408th
FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(Rs.150 crore and above)
November, 2019

PORT TRUST - SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN

सत्यमेव जयते

Government of India

Ministry of Statistics and Programme Implementation

Infrastructure and Project Monitoring Division

R.K.Puarm, East Block 6, Level 7

New Delhi-110066

Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexiing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Enivronment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministrial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECF	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vaccum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

EXECUTIVE SUMMARY

1. The Flash Report for November 2019 contains information on the status of the 1698 Central Sector Infrastructure Projects costing ₹150 crore and above. During November 2019, 5 projects (all from Road Transport & Highways sector) have reported completion with completion Cost of Rs 1759.78 crore.

2. During the reference month, out of 1698 projects, 578 projects are delayed with respect to their original schedules and 93 projects have reported additional delays vis-à-vis their date of completion reported in the previous month. Of these 93 projects, 26 are Mega Projects costing ₹1000 crore and above.

S.No.	Sector	Projects on monitor (No.)	Delayed Projects w.r.t original schedule (No.)	Additionally delayed during the month under report (No.)	Additionally delayed Mega Projects (No.)
1	ROAD TRANSPORT AND HIGHWAYS	866	221	40	7
2	RAILWAYS	312	150	11	8
3	PETROLEUM	150	55	10	4
4	COAL	107	39	1	0
5	URBAN DEVELOPMENT	75	28	8	2
6	POWER	70	50	9	3
7	WATER RESOURCES	51	1	0	0
8	HEALTH AND FAMILY WELFARE	21	11	11	0
9	CIVIL AVIATION	13	5	0	0
10	STEEL	9	8	3	2
11	FERTILISERS	5	0	0	0
12	MINES	5	1	0	0
13	ATOMIC ENERGY	4	4	0	0
14	TELECOMMUNICATIONS	4	2	0	0
15	INFORMATION AND BROADCASTING	3	1	0	0
16	HEAVY INDUSTRY	1	1	0	0
17	SHIPPING AND PORTS	1	0	0	0
18	HUMAN RESOURCE DEPARTMENT	1	1	0	0
Total		**1698**	**578**	**93**	**26**

3. Total original cost of implementation of the 1698 projects was ₹20,41,114.88 crore and their anticipated completion cost is likely to be ₹24,41,837.32crore, which reflects overall cost overruns of ₹4,00,722.44 crore (19.63% of original cost). The expenditure incurred on these projects till November 2019 is ₹10,50,331.59 crore, which is 43.01% of the anticipated cost of the projects. The

sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns is as follows:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost Overruns (as on 01-12-2019)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (%)
	ATOMIC ENERGY				
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6840.00	95.88
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	44.69
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12320.00	17079.00	38.63
	CIVIL AVIATION				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	441.33	40.28
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	859.86	860.00	0.02
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	09/2015	338.93	339.00	0.02
	COAL				
1	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	201.44
2	BHANEGAON OC	02/2015	187.94	409.68	117.98
3	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	349.28	114.60
4	RANIGANJ MASTER PLAN	08/2009	2661.73	5173.26	94.36
5	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	249.03	448.86	80.24
	FERTILISERS				
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	5.89
	HEALTH AND FAMILY WELFARE				
1	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204.44	270.00	32.07
2	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	499.23	20.55
3	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	07/2016	152.95	177.92	16.33
4	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	585.00	15.71
5	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	168.90	191.20	13.20
	HUMAN RESOURCE DEPARTMENT				
1	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	484.32	626.26	29.31
	PETROLEUM				
1	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	1683.06	95.30
2	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	70.49
3	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	06/2010	202.94	345.92	70.45
4	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	2915.00	4915.00	68.61

5	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	1823.00	3027.90	66.09
	POWER				
1	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	7927.34	217.49
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19496.34	210.19
3	TEHRI PUMPED STORAGE PLANT(1000MW)	07/2006	1657.00	5024.35	203.22
4	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9997.11	155.05
5	BARH STPP(3X660MW) NTPC	02/2005	8692.97	21312.11	145.16
	RAILWAYS				
1	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	8248.50	3230.57
2	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	04/2011	120.70	1800.00	1391.30
3	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	1017.96
4	BIHTA-AURANGABAD (NL)	04/2008	326.20	2995.01	818.15
5	ATTIPPATTU PUTTUR	04/2008	151.84	1105.00	627.74
	ROAD TRANSPORT AND HIGHWAYS				
1	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	655.17	234.27
2	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2967.50	167.82
3	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	167.64	408.77	143.84
4	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	08/2010	195.04	377.99	93.80
5	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	03/2012	207.03	389.45	88.11
	SHIPPING AND PORTS				
1	JAL MARG VIKAS PROJECT	01/2018	4200.00	5369.18	27.84
	STEEL				
1	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	23140.00	49.05
	TELECOMMUNICATIONS				
1	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	84.97
2	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	01/2018	231.80	240.10	3.58
	URBAN DEVELOPMENT				
1	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	114.26	266.00	132.80
2	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	2000.00	64.04
3	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	44.80
4	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	19058.00	30.53
5	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	02/2014	388.00	488.28	25.85
	WATER RESOURCES				
1	POLAVARAM IRRIGATION PROJECT	02/2009	10151.04	55548.87	447.22

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overrun.

4. The sector wise list of projects (maximum five in numbers) having maximum cost overruns (COR) in absolute term is as below:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns (COR)

(as on 01-12-2019)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (Rs.crore)
	ATOMIC ENERGY				
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	5121.00
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12320.00	17079.00	4759.00
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6840.00	3348.00
	CIVIL AVIATION				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	441.33	126.72
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	859.86	860.00	0.14
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	09/2015	338.93	339.00	0.07
	COAL				
1	RANIGANJ MASTER PLAN	08/2009	2661.73	5173.26	2511.53
2	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	5907.11	7080.41	1173.30
3	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	307.06
4	BHANEGAON OC	02/2015	187.94	409.68	221.74
5	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	249.03	448.86	199.83
	FERTILISERS				
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	11.65
	HEALTH AND FAMILY WELFARE				
1	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	499.23	85.12
2	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	585.00	79.42
3	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204.44	270.00	65.56
4	AIIMS - OPD(NEW)	08/2014	293.65	325.00	31.35
5	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	07/2016	152.95	177.92	24.97
	HUMAN RESOURCE DEPARTMENT				
1	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	484.32	626.26	141.94
	PETROLEUM				
1	VISAKH REFINERY MODERNISATION PROJECT	07/2016	20928.00	26264.00	5336.00
2	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	2915.00	4915.00	2000.00
3	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	05/2016	4497.00	6025.00	1528.00
4	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	1823.00	3027.90	1204.90
5	PARADIP HYDERABAD PIPLEINE	01/2015	2321.00	3338.00	1017.00
	POWER				
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19496.34	13211.01

2	BARH STPP(3X660MW) NTPC	02/2005	8692.97	21312.11	12619.14
3	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9997.11	6077.52
4	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	7927.34	5430.44
5	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	01/2013	12964.60	17304.00	4339.40
	RAILWAYS				
1	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	16592.00	51101.00	34509.00
2	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	25449.00
3	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	11589.00	28181.00	16592.00
4	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	4454.17	12524.00	8069.83
5	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	8248.50	8000.84
	ROAD TRANSPORT AND HIGHWAYS				
1	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2967.50	1859.50
2	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	03/2016	1587.49	2982.00	1394.51
3	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	08/2016	1388.34	2587.50	1199.16
4	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	1928.22	2945.00	1016.78
5	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	03/2018	1532.62	2499.00	966.38
	SHIPPING AND PORTS				
1	JAL MARG VIKAS PROJECT	01/2018	4200.00	5369.18	1169.18
	STEEL				
1	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	23140.00	7615.00
	TELECOMMUNICATIONS				
1	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	11330.00
2	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	01/2018	231.80	240.10	8.30
	URBAN DEVELOPMENT				
1	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	19058.00	4458.00
2	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	2000.00	780.79
3	KOCHI METRO RAIL PROJECT	07/2012	5181.79	5687.79	506.00
4	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	344.46
5	REDEVELOPMENT OF EAST KIDWAI NAGAR	06/2012	4264.00	4439.23	175.23
	WATER RESOURCES				
1	POLAVARAM IRRIGATION PROJECT	02/2009	10151.04	55548.87	45397.83

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overruns.

5. Out of the 1698 projects, 374 are on schedule, 578 are delayed, 400 projects reported cost overrun and 202 projects reported both time and cost overrun with respect to their original project implementation schedules. However, the number of delayed projects decreases to 484 if delay is calculated on the basis of latest schedule of completion. Further, for 728 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 578 delayed projects, 190 (32.87%) projects have overall delay in the range of 1 to 12 months, 121 (20.93%) projects have delay in the range of 13 to 24 months, 146 (25.26%) projects have delay in the range of 25 to 60 months and 121 (20.93%) projects have delay of 61 months and above. **The average time overrun in**

these 578 delayed projects is 38.84 months. The sector wise list of projects (maximum five in numbers) having maximum time overruns (TOR) are as below:

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (TOR)

(as on 01-12-2019)

SN	PROJECT	DOA	DOC ORIGINAL	DOC ANTICIPATED	TOR (IN MONTHS)
	ATOMIC ENERGY				
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	09/2010	10/2021	133
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	06/2020	54
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016	12/2020	48
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	03/2013	11/2020	11/2023	36
	CIVIL AVIATION				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	09/2018	06/2020	21
2	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	01/2016	03/2020	12/2020	9
3	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	04/2020	12/2020	8
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	09/2015	06/2019	12/2019	6
5	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	06/2018	02/2022	08/2022	6
	COAL				
1	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	03/2010	03/2022	144
2	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	03/2012	03/2024	144
3	RAMAGUNDAM OC-II EXTENSION	12/2009	03/2012	03/2023	132
4	KULDA OCP (MAHANADI COALFIELDS LTD)	01/2005	03/2010	03/2020	120
5	CHURI BENTI UG (0.81 MTY)	08/2007	03/2011	03/2021	120
	HEALTH AND FAMILY WELFARE				
1	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	11/2013	09/2020	82
2	AIIMS - MOTHER AND CHILD BLOCK	12/2013	05/2017	06/2020	37
3	AIIMS - OPD(NEW)	08/2014	05/2017	01/2020	32
4	NEIGRIHMS SHILLONG MEGHALYA	10/2016	05/2018	07/2020	26
5	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	07/2016	02/2018	03/2020	25
	HEAVY INDUSTRY				
1	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	08/2016	09/2019	03/2020	6
	HUMAN RESOURCE DEPARTMENT				
1	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	09/2014	12/2020	75
	INFORMATION AND BROADCASTING				

1	FILM AND TELEVISION INSTITUTE ARUNACHAL PRADESH	11/2016	02/2019	11/2019	9
	MINES				
1	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU	09/2017	06/2019	03/2020	9
	PETROLEUM				
1	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	12/2012	02/2022	110
2	ASSAM RENEWAL PROJECT FOR GROUP A	03/2009	03/2013	12/2019	81
3	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	05/2013	12/2019	79
4	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	06/2010	01/2014	11/2019	70
5	INTEGRATED DEVELOPMENT OF B-127 FIELDS	12/2011	03/2015	12/2019	57
	POWER				
1	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	09/2009	12/2021	147
2	BARH STPP(3X660MW) NTPC	02/2005	10/2011	08/2021	118
3	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	08/2008	06/2013	12/2022	114
4	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	02/2009	08/2013	03/2022	103
5	BRBCL-NABINAGAR TPP- JV (4X250 MW)	01/2007	07/2012	09/2020	98
	RAILWAYS				
1	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	04/1998	03/2003	03/2030	324
2	BANGLORE - SATYAMANGALAM (NL)(SWR)	04/1996	03/2002	03/2024	264
3	MUNEERABAD-MAHABOOBNAGAR(NL),SCR	04/1997	03/2000	03/2021	252
4	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	04/2010	03/2005	03/2025	240
5	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	11/2002	06/2022	235
	ROAD TRANSPORT AND HIGHWAYS				
1	SONAPUR TO GUWAHTI (AS-3)	12/2003	03/2008	08/2020	149
2	NALBARI T BIJNI (AS-7)	12/2003	04/2008	03/2020	143
3	GWALIOR-JHANSI, NH-75	12/2003	12/2009	03/2020	123
4	DELHI/ HARYANA BORDER TO ROHTAK	04/2007	05/2010	03/2020	118
5	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	08/2010	10/2010	06/2020	116
	STEEL				
1	NMDC INTEGRATED STEEL PLANT	01/2010	05/2015	07/2020	62
2	NEW SINTER PLANT AT BOKARO STEEL PLANT	03/2015	10/2017	06/2020	32
3	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	05/2015	12/2017	01/2020	25
4	COKE OVEN BATTERY-5	12/2011	12/2017	12/2019	24
5	INSTALLATION OF NEW HOT STRIP MILL AT RSP	04/2015	04/2018	01/2020	21
	TELECOMMUNICATIONS				
1	NETWORK FOR SPECTRUM	03/2012	07/2015	05/2020	58
2	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	01/2018	10/2018	12/2019	14
	URBAN DEVELOPMENT				

1	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	06/2010	03/2012	12/2019	93
2	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	10/2012	03/2020	89
3	IRRIGATION WORK OF BAGMATI	10/2005	03/2015	03/2021	72
4	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	02/2014	03/2015	10/2020	67
5	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	01/2015	05/2020	64
	WATER RESOURCES				
1	POLAVARAM IRRIGATION PROJECT	02/2009	03/2020	06/2021	15

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further time overruns.

6. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in obtaining forest/environment clearances, lack of infrastructure support & linkages, delay in tie-up of project financing, delay in finalization of detailed engineering, change in scope, delay in tendering, ordering & equipment supply, law & order problems, geological surprises, pre-commissioning teething troubles and contractual issues.

7. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The sector wise list of earliest projects (maximum five in numbers) without milestones are as below:-

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Milestones (as on 01-12-2019)

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST ANTICIPATED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
	CIVIL AVIATION						
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	441.33	85.79	09/2018	06/2020
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	09/2015	338.93	339.00	213.50	06/2019	12/2019
3	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	01/2016	219.91	219.91	65.45	03/2020	12/2020
4	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	233.38	233.38	84.73	04/2020	12/2020

5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	859.86	860.00	232.44	03/2021	03/2021
	COAL						
6	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	03/2015	513.63	513.63	175.30	12/2019	12/2019
7	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	03/2015	522.45	522.45	9.88	09/2019	N.A.
8	COAL PROJECT NAME JAMUNIA UG (0.84 MTY)	07/2016	409.87	409.87	19.05	03/2022	03/2022
9	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	07/2016	17237.00	17237.80	8032.77	11/2021	11/2021
10	KOLAR PIMPRI EXTENSION OC	03/2017	362.73	362.73	322.07	03/2020	03/2020
	HEALTH AND FAMILY WELFARE						
11	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	499.23	302.02	11/2013	09/2020
12	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	07/2016	703.00	557.48	283.12	06/2020	10/2020
13	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	07/2016	785.00	715.06	345.41	04/2020	10/2020
14	CNCI KOLKATA WEST BENGAL	08/2016	244.00	248.00	224.92	09/2018	05/2019
15	NEIGRIHMS SHILLONG MEGHALYA	10/2016	363.99	363.99	208.29	05/2018	07/2020
	HEAVY INDUSTRY						
16	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	08/2016	1554.00	1554.00	665.35	09/2019	03/2020
	HUMAN RESOURCE DEPARTMENT						
17	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	484.32	626.26	0.00	09/2014	12/2020
	INFORMATION AND BROADCASTING						
18	NATIONAL FILM HERITAGE MISSION	11/2014	597.41	597.41	29.80	N.A.	N.A.
19	FILM AND TELEVISION INSTITUTE ARUNACHAL PRADESH	11/2016	204.32	204.32	0.00	02/2019	11/2019
20	NATIONAL CENTRE OF EXCELLENCE FOR ANIMATION VISUAL EFFECTS GAMING AND COMICS	12/2016	167.70	167.70	0.00	03/2020	03/2020
	PETROLEUM						
21	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	1549.85	01/2012	N.A.
22	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	07/2011	350.00	350.00	2.06	01/2019	N.A.
23	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	678.00	678.00	7.28	02/2017	10/2021
24	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	711.00	711.00	11.12	06/2020	06/2020

25	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM	07/2014	247.00	247.00	0.00	03/2021	03/2021
	POWER						
26	LOKTAK D/S HEP(NHPC)	12/1999	578.62	578.62	0.00	06/2006	N.A.
27	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19496.34	11098.20	09/2010	N.A.
28	PAKRI BARWADIH COAL MINING PROJECT	10/2004	4237.96	4552.00	3293.00	10/2017	N.A.
29	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	01/2014	374.63	374.63	214.62	04/2016	12/2019
30	COMPREHENSIVE SCHEME FOR THE STRENGHTENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	4754.42	9072.36	1352.46	12/2018	12/2020
	RAILWAYS						
31	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	393.46	1026.00	182.49	03/2007	N.A.
32	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	2200.00	666.00	07/2012	03/2024
33	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	297.32	614.00	275.07	03/2019	03/2020
34	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	406.99	545.70	148.48	03/2006	03/2025
35	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	332.15	546.71	541.43	07/2014	N.A.
	ROAD TRANSPORT AND HIGHWAYS						
36	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	01/1991	478.35	478.35	0.00	N.A.	N.A.
37	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	01/1991	319.68	369.77	113.67	N.A.	N.A.
38	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	01/1991	219.40	219.40	0.00	01/2018	N.A.
39	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	282.41	322.01	278.45	08/2016	N.A.
40	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	358.22	377.64	325.19	10/2016	N.A.
	SHIPPING AND PORTS						

41	JAL MARG VIKAS PROJECT	01/2018	4200.00	5369.18	1662.16	03/2023	03/2023
	TELECOMMUNICATIONS						
42	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	12146.00	07/2015	05/2020
43	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	06/2016	418.26	418.26	367.04	06/2017	N.A.
44	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	01/2018	231.80	240.10	117.63	10/2018	12/2019
	URBAN DEVELOPMENT						
45	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	1085.64	02/2014	N.A.
46	IRRIGATION WORK OF BAGMATI	10/2005	956.00	956.00	651.21	03/2015	03/2021
	WATER RESOURCES						
47	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	02/2011	279.91	279.91	0.00	12/2019	12/2019
48	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	02/2014	274.76	274.76	0.00	12/2019	12/2019
49	SEWERAGE WORKS IN SEWERAGE DISTRICT A OF ALLAHABAD	02/2014	288.94	288.94	0.00	09/2019	09/2019
50	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	225.77	225.77	0.00	03/2020	03/2020
51	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE	12/2014	272.32	272.32	0.00	04/2020	04/2020

N.A.: Not Available.

N.B.: The concerned administrative Ministry may like review these Projects in order to firm-up milestones.

9. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost Estimates (as on 01-12-2019)

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST REVISED(Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)
	ATOMIC ENERGY				
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	0.00	5837.84
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	0.00	14137.00
	COAL				
1	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	249.03	0.00	296.17
2	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	172.08	0.00	347.93
3	KANIHA OCP, MCL, (10.0 MTY)	12/2007	457.77	0.00	539.88
4	BHUBANESWARI OCP, MCL (20.0 MTY)	12/2007	490.10	0.00	508.91

5	ANANTA OC EXPANSION PH-III (15.0 MTY)	08/2008	207.28	0.00	296.22
	HEALTH AND FAMILY WELFARE				
1	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204.44	0.00	204.70
2	AIIMS - OPD(NEW)	08/2014	293.65	0.00	297.16
3	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	0.00	586.96
4	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	168.90	0.00	169.51
	PETROLEUM				
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	0.00	1549.85
2	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	0.00	1356.33
3	DEVELOPMENT OF BSE-11 BLOCK	02/2017	511.30	0.00	523.88
	POWER				
1	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	0.00	7715.06
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	0.00	11098.20
3	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	05/2005	1779.29	0.00	2237.45
4	TEHRI PUMPED STORAGE PLANT(1000MW)	07/2006	1657.00	0.00	3118.00
5	DHUKWAN SMALL HYDRO PROJECT	05/2011	195.42	0.00	321.11
	RAILWAYS				
1	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	04/1991	329.39	803.11	1053.89
2	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	09/1995	303.98	0.00	681.66
3	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	02/1996	268.87	0.00	927.86
4	NANDYAL-YERRAGUNTLA(NL),SCR	03/1996	164.36	0.00	999.64
5	HARIDASPUR-PARADEEP(NL)	04/1996	1185.64	0.00	1829.53
	ROAD TRANSPORT AND HIGHWAYS				
1	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	280.00	490.00	492.41
2	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	160.00	0.00	223.81
3	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	217.61	0.00	453.70
4	NALBARI T BIJNI (AS-7)	12/2003	208.00	0.00	339.22
5	NALBARI TO BIJNI (AS-6)	12/2003	225.00	0.00	328.47
	URBAN DEVELOPMENT				
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1070.97	1085.64
2	CONSTRUCTION AND MAINTEINANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	173.00	176.65
3	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	0.00	16352.87
4	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	02/2014	388.00	0.00	440.59
5	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	02/2014	156.57	0.00	159.35
	WATER RESOURCES				
1	POLAVARAM IRRIGATION PROJECT	02/2009	10151.04	0.00	16417.99

N.B.: The concerned administrative Ministry may like to review these Projects in order to firm-up revised cost estimates.

10. The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on 01-12-2019)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
	COAL				
1	KAKATIYA LONGWALL	12/2008	12/2012	N.A.	N.A.
2	MANUGURU OC-II EXTENSION PHASE-II	03/2010	03/2012	N.A.	N.A.
3	MURAIDIH UG TURN-KEY PROJECT	02/2011	04/2014	N.A.	N.A.
4	KAPURIA UG(PSLW)	08/2011	04/2017	N.A.	N.A.
5	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	04/2013	06/2015	N.A.	N.A.
	FERTILISERS				
6	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	11/2016	N.A.	09/2019
	HEALTH AND FAMILY WELFARE				
7	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	03/2018	N.A.	09/2019
8	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	05/2017	N.A.	07/2019
9	CNCI KOLKATA WEST BENGAL	08/2016	09/2018	N.A.	05/2019
	INFORMATION AND BROADCASTING				
10	NATIONAL FILM HERITAGE MISSION	11/2014	N.A.	N.A.	N.A.
	PETROLEUM				
11	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	01/2012	N.A.	N.A.
12	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	07/2011	01/2019	N.A.	N.A.
13	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II	11/2011	03/2013	N.A.	N.A.
14	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	09/2012	03/2015	N.A.	N.A.
15	RESID UPGRADATION PROJECT	03/2013	11/2015	N.A.	N.A.
	POWER				
16	LOKTAK D/S HEP(NHPC)	12/1999	06/2006	N.A.	N.A.
17	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	09/2010	N.A.	N.A.
18	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017	N.A.	N.A.
19	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009	10/2019	10/2019
20	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	05/2005	11/2008	N.A.	N.A.
	RAILWAYS				
21	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	03/2007	03/2007	N.A.
22	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	07/2014	N.A.	N.A.
23	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	02/1996	03/2005	N.A.	N.A.

24	NANDYAL-YERRAGUNTLA(NL),SCR	03/1996	02/2009	N.A.	N.A.
25	ETAWAH-MAINPURI (NL),NCR	04/1997	12/2008	N.A.	N.A.
	ROAD TRANSPORT AND HIGHWAYS				
26	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	01/1991	04/2014	N.A.	N.A.
27	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	08/2016	N.A.	N.A.
28	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	10/2016	N.A.	N.A.
29	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB	01/1991	10/2017	N.A.	N.A.
30	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	01/1991	01/2018	N.A.	N.A.
	TELECOMMUNICATIONS				
31	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY	09/2014	09/2014	N.A.	N.A.
32	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	06/2016	06/2017	N.A.	N.A.
	URBAN DEVELOPMENT				
33	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	02/2014	N.A.	N.A.
34	CONSTRUCTION AND MAINTEINANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	12/2015	N.A.	N.A.
35	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	08/2007	N.A.	N.A.	N.A.
36	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTEINANCE UNDER PMGSY-JHARKHAND	12/2007	06/2016	N.A.	N.A.
37	CONSTRUCTION AND MAINTEINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016	N.A.	N.A.
	WATER RESOURCES				
38	SEWERAGE WORKS IN SEWERAGE DISTRICT A OF ALLAHABAD	02/2014	09/2019	N.A.	N.A.
39	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI	03/2017	08/2019	N.A.	N.A.

N.A.: Not Available.

N.B.: The concerned administrative Ministry may like to review these Projects in order to firm-up revised commissioning schedule.

11. The status as on 01.12.2019 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

12. This has the approval of Competent Authority, Ministry of Statistics and Programme Implementation.

TABLE-1

EXECUTIVE SUMMARY COSTING Rs.150 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	866	40
2	RAILWAYS	312	11
3	PETROLEUM	150	10
4	COAL	107	1
5	URBAN DEVELOPMENT	75	8
6	POWER	70	9
7	WATER RESOURCES	51	0
8	HEALTH AND FAMILY WELFARE	21	11
9	CIVIL AVIATION	13	0
10	STEEL	9	3
11	FERTILISERS	5	0
12	MINES	5	0
13	ATOMIC ENERGY	4	0
14	TELECOMMUNICATIONS	4	0
15	INFORMATION AND BROADCASTING	3	0
16	HEAVY INDUSTRY	1	0
17	SHIPPING AND PORTS	1	0
18	HUMAN RESOURCE DEPARTMENT	1	0
	Total	1698	93

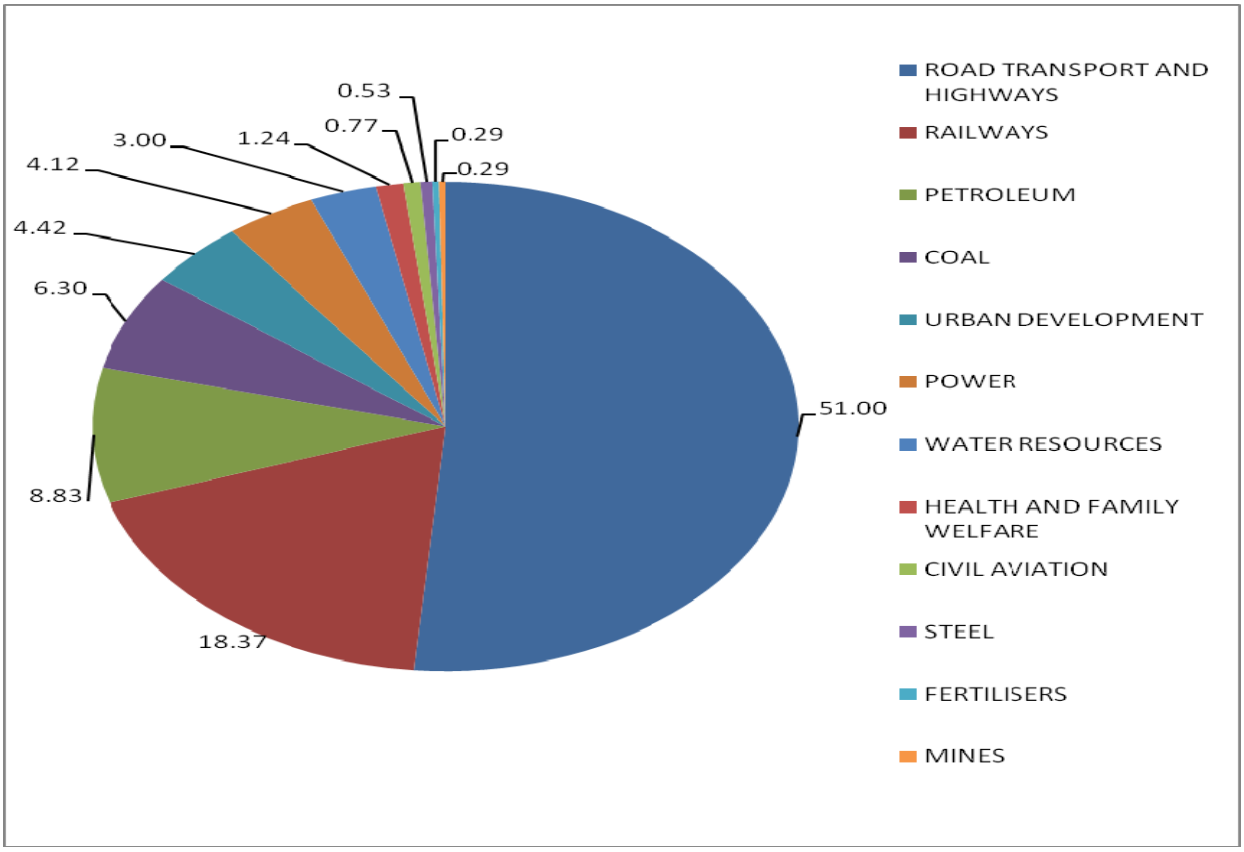

TABLE-2

Month wise List of Completed Projects Costing Rs.150 crore and above during 2019-2020				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2019			
	COAL			
1	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI (NORTHERN COAL FIELDS LIMITED) - [N06000033]	259.40	03/2012	266.38
2	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) (NORTHERN COAL FIELDS LIMITED) - [N06000091]	1,131.28	03/2018	796.85
	PETROLEUM			
3	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000175]	3,076.00	09/2017	3,450.30
	POWER			
4	BONGAIGAON THERMAL POWER PROJECT (NATIONAL THERMAL POWER CORPORATION) - [N18000041]	4,375.35	10/2011	7,000.00
5	TRIPURA GAS BASED POWER PROJECT (NORTH EAST ELECTRIC POWER CORPORATION) - [N18000071]	421.01	07/2013	963.23
	RAILWAYS			
6	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) (NORTH WESTERN RAILWAY) - [N22000113]	653.19	03/2014	862.17
	ROAD TRANSPORT AND HIGHWAYS			
7	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000357]	567.51	03/2018	421.60
	May,2019			
	COAL			
8	MAKARDHOKRA I OC (WESTERN COAL FIELDS LIMITED) - [N06000119]	266.23	03/2021	144.38
	PETROLEUM			
9	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000084]	736.65	09/2011	331.47
10	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY Central Sector Projects(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000290]	474.15	05/2019	348.64
	POWER			

Month wise List of Completed Projects Costing Rs.150 crore and above during 2019-2020				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
11	WESTERN REGION STRENGTHENING SCHEME-V (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000035]	477.69	09/2010	691.96
12	KUDGI STPP STAGE 1 (NATIONAL THERMAL POWER CORPORATION) - [N18000131]	15,166.19	01/2017	15,364.00
13	SOLAPUR STPP (NATIONAL THERMAL POWER CORPORATION) - [N18000133]	9,395.18	01/2017	8,617.00
14	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000158]	539.82	06/2016	434.33
15	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000174]	3,363.12	12/2016	2,244.00
16	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000222]	790.13	06/2019	575.24
	ROAD TRANSPORT AND HIGHWAYS			
17	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000145]	1,585.00	05/2013	2,023.33
18	JORBAT - BARAPANI PPP (ANNUITY)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000180]	536.00	01/2014	845.41
19	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S EPC() - [N24000241]	177.18	03/2016	40.51
20	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPLLY SECTIO EPC() - [N24000242]	158.65	03/2016	103.50
21	YAN TO NIRMAL SEREHABILITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW EPC() - [N24000243]	244.08	03/2016	38.32
22	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T EPC() - [N24000244]	340.00	03/2016	2.00
23	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO EPC() - [N24000246]	244.30	12/2016	2.00
24	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S () - [N24000249]	218.31	12/2015	208.28
25	REHABILATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 () - [N24000250]	260.39	11/2016	188.00
26	REHABILATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 EPC() - [N24000255]	220.72	11/2016	155.30
27	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 EPC() - [N24000261]	267.16	11/2017	308.33
28	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A EPC() - [N24000262]	201.12	02/2015	150.19
29	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) () - [N24000263]	241.61	02/2017	178.94
30	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN EPC() - [N24000265]	297.78	02/2017	284.89
31	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC () - [N24000266]	361.30	07/2014	203.29
32	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) EPC() - [N24000267]	258.99	07/2014	200.44

MoSPI OCMS

Month wise List of Completed Projects Costing Rs.150 crore and above during 2019-2020				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
33	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC EPC() - [N24000268]	251.55	02/2015	172.65
34	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T EPC() - [N24000269]	175.03	-	152.53
35	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP EPC() - [N24000272]	266.00	-	182.13
36	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000273]	314.43	-	216.96
37	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA ITEM RATE(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000277]	185.82	-	142.23
38	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. EPC() - [N24000278]	213.47	03/2015	182.91
39	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV EPC() - [N24000279]	298.34	03/2015	269.93
40	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I EPC() - [N24000280]	262.54	03/2015	215.11
41	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- ITEM RATE() - [N24000283]	169.26	12/2012	280.72
42	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO EPC() - [N24000284]	170.21	11/2014	140.09
43	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. EPC() - [N24000286]	394.20	-	332.62
44	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000288]	422.34	-	406.40
45	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE EPC() - [N24000289]	435.90	-	380.41
46	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 EPC() - [N24000290]	279.68	-	286.96
47	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO EPC() - [N24000291]	463.65	-	536.84
48	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM EPC() - [N24000292]	573.96	-	557.08
49	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000293]	480.21	-	372.37
50	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 EPC() - [N24000299]	224.83	05/2015	189.85
51	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDOU EPC() - [N24000300]	309.01	09/2015	391.89
52	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION EPC() - [N24000303]	417.61	06/2014	261.29

MoSPI OCMS

Month wise List of Completed Projects Costing Rs.150 crore and above during 2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
53	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 EPC() - [N24000310]	377.83	07/2017	318.66
54	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO EPC(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000329]	497.89	04/2017	735.92
55	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000330]	629.74	-	721.04
56	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000336]	227.74	10/2016	187.85
57	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000369]	269.26	10/2016	212.72
58	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI EPC() - [N24000370]	483.38	-	470.16
59	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 EPC() - [N24000372]	616.36	-	554.68
60	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(EPC() - [N24000374]	486.74	-	415.58
61	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 EPC() - [N24000377]	397.04	10/2016	368.49
62	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP BOT (TOLL)() - [N24000381]	257.80	02/2016	59.30
63	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(EPC() - [N24000383]	312.79	-	258.86
64	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K EPC() - [N24000384]	319.80	-	289.40
65	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' ITEM RATE() - [N24000387]	264.16	-	533.18
66	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA ITEM RATE() - [N24000390]	1,494.48	02/2011	2,158.50
67	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH EPC() - [N24000393]	774.57	03/2018	613.58
68	SHAHDOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 EPC() - [N24000394]	532.49	05/2017	386.02
69	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 EPC() - [N24000399]	317.76	03/2017	344.30
70	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 EPC() - [N24000403]	283.45	10/2016	285.18
71	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM EPC() - [N24000404]	578.38	-	481.30
72	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA EPC() - [N24000405]	789.83	-	608.55

MoSPI OCMS

Month wise List of Completed Projects Costing Rs.150 crore and above during 2019-2020				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
73	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI ITEM RATE(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000406]	208.87	05/2016	206.78
74	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM ITEM RATE() - [N24000409]	176.22	02/2018	0.10
75	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A EPC() - [N24000410]	641.02	12/2017	449.66
76	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 EPC() - [N24000416]	224.83	04/2015	189.85
77	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 EPC() - [N24000418]	493.94	03/2017	503.25
78	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA ITEM RATE() - [N24000419]	165.00	09/2010	174.57
79	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF ITEM RATE() - [N24000420]	104.00	09/2010	218.29
80	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 EPC(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000421]	235.08	05/2018	235.08
81	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP BOT (TOLL)() - [N24000447]	670.82	02/2015	590.00
82	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A () - [N24000474]	327.32	05/2017	301.41
83	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000476]	273.06	-	199.72
84	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000512]	207.88	-	179.58
85	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO EPC() - [N24000526]	899.21	-	748.74
86	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000529]	207.88	-	179.58
87	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000536]	377.64	03/2014	755.28
88	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO () - [N24000538]	292.98	11/2014	160.96
89	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000561]	244.00	07/2018	231.90
90	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000573]	322.01	08/2014	267.00
91	FUNDED)2 LANING FROM CHANGLANG DISTRICT BOUNDARY - KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000615]	334.22	06/2016	334.22

Month wise List of Completed Projects Costing Rs.150 crore and above during 2019-2020				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
92	WIDENING AND STRENFTHENING OF EXISITNG SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000647]	162.51	05/2016	136.31
93	WIDENING TO 2 LANE WITH PAVED SHOULDER AND STRENGTHENING FROM KM 88 TO 130 ON NH-86 () - [N24000856]	170.00	02/2015	115.57
94	REHABILITATION AND UPGRADATION OF PURANPUR - KHUTAR SECTION FROM KM 38.00 TO KM 82.00 OF NH-730 TO 2 () - [N24001142]	225.96	06/2018	174.63
	June,2019			
	RAILWAYS			
95	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) (NORTH CENTRAL RAILWAY) - [220100007]	158.77	03/1994	682.34
96	AMRAVATI-NARKHER NL(CR) (CENTRAL RAILWAYS) - [220100118]	663.01	06/1999	726.33
97	CALICUT-MANGALORE (DL) (SR) (SOUTHERN RAILWAY) - [220100151]	240.00	-	0.01
98	MANDARHILL-DUMKA-RAMPURHAT (NL),ER (EASTERN RAILWAYS) - [220100168]	1,125.89	03/2016	1,180.08
99	KARUR-SALEM(NL),SR (SOUTHERN RAILWAY) - [220100191]	155.55	-	863.54
100	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR (NORTH CENTRAL RAILWAY) - [220100243]	108.00	12/2009	455.39
101	KATIHAR - JOGBANI (GC)(NEFR) (NORTH EAST FRONTIER RAILWAY) - [220100247]	792.46	12/2010	944.80
102	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) (NORTH EASTERN RAILWAY) - [220100256]	744.71	-	917.49
103	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) (SOUTHERN RAILWAY) - [220100263]	280.00	-	942.28
104	JIND-SONEPAT (NL),NR (NORTHERN RAILWAY) - [220100280]	238.56	03/2012	785.75
105	KODERMA GIRIDH (NL), ECR (EAST CENTRAL RAILWAYS) - [220100306]	768.87	-	988.38
106	MAHARAJGANJ-MASRAKH (NL) - NER (NORTH EASTERN RAILWAY) - [220100316]	218.19	06/2018	380.50
107	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) (RAIL VIKAS NIGAM LTD.) - [N22000049]	732.81	03/2008	2,191.46
108	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE (SOUTHERN RAILWAY) - [N22000080]	343.17	-	1,110.44
109	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) (NORTHERN RAILWAY) - [N22000088]	369.90	03/2010	891.24
110	AGARTALA SABROOM, NL, NEFR (NORTH EAST FRONTIER RAILWAY) - [N22000099]	1,142.00	03/2014	3,354.18
111	DAKSHIN-BARASAL-LAKSHMIKANTAPUR (EASTERN RAILWAYS) - [N22000116]	259.51	02/2012	148.37
112	GHUTIASHARIF-CANNING (ER) (EASTERN RAILWAYS) - [N22000117]	193.08	12/2011	154.30
113	PANDABESWAR-CHINPAI DOUBLING (ER) (EASTERN RAILWAYS) - [N22000118]	293.74	12/2010	128.78
114	BHOJIPUR TANAKPUR VIA PILIBHIT (NORTH EASTERN RAILWAY) - [N22000132]	195.64	-	450.62

Month wise List of Completed Projects Costing Rs.150 crore and above during 2019-2020				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
115	AUNRIHAR MANDUADIH (NORTH EASTERN RAILWAY) - [N22000133]	199.75	08/2018	287.33
116	DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING (SOUTH EASTERN RAILWAY) - [N22000164]	309.44	12/2015	529.27
117	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC (SOUTHERN RAILWAY) - [N22000188]	271.24	-	468.58
118	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA (NORTH EAST FRONTIER RAILWAY) - [N22000194]	895.00	03/2007	1,566.57
119	CHENGANNUR-CHINGAVANAM (SOUTHERN RAILWAY) - [N22000203]	191.72	-	447.03
120	LUMDING-HOJAI PATCH DOUBLING PROJECT (NORTH EAST FRONTIER RAILWAY) - [N22000211]	246.07	03/2019	490.29
121	MEERUT-MUZAFARNAGAR PATCH DL (NORTHERN RAILWAY) - [N22000267]	377.44	-	430.12
122	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH (NORTHERN RAILWAY) - [N22000290]	338.54	-	384.61
123	JAKHAL-MANSA DOUBLING ON SPR SECTION (NORTHERN RAILWAY) - [N22000291]	162.96	-	160.25
124	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI (SOUTHERN RAILWAY) - [N22000303]	460.94	01/1999	0.01
125	MADURAI - RAMESWARAM (161 KM) GAUGE CONVERSION (SOUTHERN RAILWAY) - [N22000439]	458.63	03/2015	367.71
126	TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION (SOUTHERN RAILWAY) - [N22000440]	200.84	03/2014	394.51
127	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION (SOUTHERN RAILWAY) - [N22000446]	600.00	03/2010	673.80
128	MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANNAL ROAD) (62.05 KM) DOUBLING (SOUTHERN RAILWAY) - [N22000450]	199.55	03/2009	238.61
129	MANAMADURAI - VIRUDHUNAGAR (66.55 KM) GAUGE CONVERSION. (SOUTHERN RAILWAY) - [N22000453]	208.00	03/2012	206.20
130	MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING. (SOUTHERN RAILWAY) - [N22000454]	241.00	03/2014	293.37
131	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW (NORTH EASTERN RAILWAY) - [N22000455]	233.00	04/1999	349.37
132	MANDHANA - BRAHMAWART NEW LINE PROJECT. (NORTH EASTERN RAILWAY) - [N22000458]	609.04	04/1999	1,806.84
133	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM (EAST CENTRAL RAILWAYS) - [N22000474]	624.47	02/2016	3,376.08
	July,2019			
	COAL			
134	NORTH URIMARI OCP (3.0 MTY) (CENTRAL COAL FIELDS LIMITED) - [N06000084]	179.87	03/2012	163.23
	STEEL			
135	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) (RASTRIYA ISPAT NIGAM LIMITED) - [N12000120]	465.85	07/2018	390.25

Month wise List of Completed Projects Costing Rs.150 crore and above during 2019-2020				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	PETROLEUM			
136	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I (GAS AUTHORITY OF INDIA LIMITED) - [N16000072]	3,957.00	12/2018	2,707.26
137	PARADIP-RAIPUR- RANCHI PIPELINE (INDIAN OIL CORPORATION LIMITED) - [N16000088]	1,793.00	12/2016	1,788.86
138	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) (INDIAN OIL CORPORATION LIMITED) - [N16000187]	191.96	05/2015	76.28
139	REPLACEMENT OF KV SECTION OF KSPL Central Sector Projects(INDIAN OIL CORPORATION LIMITED) - [N16000287]	279.00	08/2018	200.05
	POWER			
140	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) (SATLUJ JAL VIDYUT NIGAM LIMITED) - [N18000235]	330.00	11/2017	331.46
	ROAD TRANSPORT AND HIGHWAYS			
141	BHOPAL-BIORA (4L) OF NH-12 IN MP BOT (TOLL)() - [N24000380]	704.26	05/2015	5.21
	TELECOMMUNICATIONS			
142	MADHYA PRADESH ACCESS (LOT1) Central Sector Projects(BHARAT SANCHAR NIGAM LIMITED) - [N26000110]	215.30	05/2018	33.46
	August,2019			
	COAL			
143	AMLAI OC EXPANSION SECTOR B (1.50 MTY) (SOUTH-EASTERN COAL FIELDS LIMITED) - [N06000082]	198.59	03/2016	169.15
144	GOKUL (WESTERN COAL FIELDS LIMITED) - [N06000120]	267.67	03/2018	209.47
	ROAD TRANSPORT AND HIGHWAYS			
145	IMPROVEMENT FROM KM 0/0 TO 68/0 EPC() - [N24000413]	319.80	10/2016	268.01
146	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000642]	226.31	10/2017	137.43
147	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000643]	319.80	05/2016	268.27
148	WIDENING TO 2L/2LPS FROM 131/0 TO 192/0 (BHOJPUR TO CHHATABAR) OF NH-200 UNDER NHIIP IN ODISHA (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000918]	251.92	10/2015	225.98

Month wise List of Completed Projects Costing Rs.150 crore and above during 2019-2020				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
149	WIDENING TO 2L/2LPS FROM 25/0 TO 80/0 (NABARANGPUR TO KOKSARA) OF NH-201 UNDER NHIIP IN ODISHA (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000919]	265.35	10/2015	247.56
150	WIDENING TO 2L FROM 228/70 TO 258/70 AND 286/70 TO 327/70 OF VR ROUTE UNDER VRC IN ODISHA (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000924]	229.29	11/2015	163.40
151	REHABILITATION AND UPGRADATION OF EEPURUPALEM-ONGOLE SECTION FROM KM195.000 TO 254.500 OF NH214A(NH2 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000971]	574.19	07/2017	456.98
	September,2019			
	PETROLEUM			
152	URAN CHAKAN SHIKRAPUR LPG PIPELINE (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000155]	309.81	10/2014	712.26
153	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000237]	407.00	09/2019	391.85
	October,2019			
154	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000248]	822.66	11/2018	822.02
155	BRANCH PIPELINE OF PAJPL TO UNA (INDIAN OIL CORPORATION LIMITED) - [N16000250]	151.00	09/2019	147.35
156	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000280]	420.76	09/2018	239.45
	POWER			
157	EASTERN REGION STRENGTHENING SCHEME -IX (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000171]	196.58	02/2016	165.87
158	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000180]	268.80	03/2018	259.49
159	TRAMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000227]	1,429.38	01/2019	1,050.46
160	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000236]	251.60	06/2019	192.74
161	WESTERN REGION STRENGTHENING SCHEME XVIII (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000241]	195.05	02/2020	120.83
	November,2019			
	ROAD TRANSPORT AND HIGHWAYS			
162	2 LANNING OF MOKAMA-MUNGER PPP (ANNUITY)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000166]	351.54	05/2013	329.40

Month wise List of Completed Projects Costing Rs.150 crore and above during				
2019-2020				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
163	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000446]	788.51	03/2018	103.37
164	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000450]	785.78	03/2018	839.00
165	NAGPUR - KONDHALI (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000472]	168.00	06/2006	226.24
166	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000609]	771.18	-	261.77

TABLE-3

Month wise List of Deleted Projects Costing Rs.150 crore and above during 2019-2020				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	June,2019			
	RAILWAYS			
1	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL (RAIL VIKAS NIGAM LTD.) - [220100149]	631.78	12/2012	762.72
2	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR (NORTHERN RAILWAY) - [220100258]	625.30	06/2007	848.84
3	TAMLUK DIGHA,LINE DOUBLING (SER) (SOUTH EASTERN RAILWAY) - [N22000097]	293.97	06/2005	0.00
4	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) (NORTH WESTERN RAILWAY) - [N22000112]	829.74	03/2015	823.85
5	SANTOSHPUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE (EASTERN RAILWAYS) - [N22000248]	268.52	-	0.00
6	MUNIRABAD (GINGERA) -RAICHUR NL (SOUTH WESTERN RAILWAY) - [N22000257]	179.65	-	940.47
7	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL (NORTHERN RAILWAY) - [N22000268]	396.04	-	225.18
8	CHANDIGARH-BADDI NL (NORTHERN RAILWAY) - [N22000296]	328.14	-	233.84
9	MM FROM BURAMARA-CHAKULIA (SOUTH EASTERN RAILWAY) - [N22000305]	466.48	-	0.83
10	MIRAJ-LONDA (SOUTH WESTERN RAILWAY) - [N22000327]	1,830.00	-	254.57
11	CHHINDWARA-MANDLA FORT GC (SOUTH EAST CENTRAL RAILWAY) - [N22000481]	556.54	03/2012	0.00
12	KENDRI-DHAMTARI INCLUDING ABHANPUR-RAJIM (SOUTH EAST CENTRAL RAILWAY) - [N22000482]	1,471.93	03/2022	0.00
	WATER RESOURCES			
13	PAGLADIYA DAM PROJECT (MINISTRY OF WATER RESOURCES) - [300100001]	542.90	12/2007	0.00
	July,2019			
	STEEL			
14	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000085]	188.93	04/2015	138.83
15	REVAMPING OF SINTER MACHINES - 1 AND 2 (RASTRIYA ISPAT NIGAM LIMITED) - [N12000091]	343.00	10/2016	254.65
16	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000097]	4,749.00	09/2017	110.95

Month wise List of Deleted Projects Costing Rs.150 crore and above during 2019-2020				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
17	2 MTPA PELLET PLANT AT NAGARNAR (NATIONAL MINERAL DEVELOPMENT CORPORATION (NMDC)) - [N12000115]	818.00	06/2020	31.60
	RAILWAYS			
18	BHADUTOLA-JHARGRAM VIA LALGARH (NL) (SOUTH EASTERN RAILWAY) - [N22000161]	289.64	-	0.13
19	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI (NORTHERN RAILWAY) - [N22000270]	654.00	-	0.00
20	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR (NORTHERN RAILWAY) - [N22000271]	1,239.00	-	0.00
21	HISSAR-SIRSA VIA AGROHA AND FATEHABAD (NORTHERN RAILWAY) - [N22000292]	400.00	-	0.00
22	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH (NORTHERN RAILWAY) - [N22000293]	876.00	-	0.00
23	MM FROM PANSKURA-GHATAL NL (SOUTH EASTERN RAILWAY) - [N22000309]	276.69	-	0.00
24	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI(SOUTH EASTERN RAILWAY) - [N22000397]	1,013.45	12/2021	0.01
25	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO(SOUTH EASTERN RAILWAY) - [N22000398]	524.43	12/2021	184.33
	August,2019			
	SHIPPING AND PORTS			
26	SETHUSAMUDRAM SHIP CHANNEL PROJECT (PORT TRUST) - [250100175]	2,427.40	10/2008	0.00
27	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) (PORT TRUST) - [N25000035]	150.00	03/2006	0.00
28	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB(MUMBAI PORT TRUST) - [N25000063]	366.39	12/2010	0.00
29	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED (KAMARAJAR PORT LIMITED) - [N25000066]	244.50	12/2017	0.00
30	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT (KAMARAJAR PORT LIMITED) - [N25000070]	600.00	12/2017	0.00
31	NEW LARGE DRY DOCK AT COCHIN SHIPYARD LIMITED PREMISES AT KOCHI KERALA (COCHIN SHIPYARD LTD) - [N25000073]	1,799.00	05/2021	347.03
32	INTERNATIONAL SHIP REPAIR FACILITY PROJECT AT COCHIN PORT TRUST PREMISES (COCHIN SHIPYARD LTD) - [N25000074]	970.00	05/2020	322.54
	DEFENCE PRODUCTION			
33	CONSTRUCTION WORKS PHASE 4 (GOA SHIPYARD LIMITED) - [N39000001]	167.69	05/2018	141.83
34	CONSTRUCTION WORKS PHASE 3B (GOA SHIPYARD LIMITED) - [N39000002]	285.95	08/2020	84.40

Month wise List of Deleted Projects Costing Rs.150 crore and above during				
2019-2020				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	October,2019			
	RAILWAYS			
35	CONSTRUCTION OF ROBS IN THE STATE OF BIHAR (NEW ROBS-12) (SOUTH EASTERN RAILWAY) - [N22000337]	400.00	03/2014	0.00
36	CONSTRUCTION OF ROBS IN THE STATE OF BIHAR (EAST CENTRAL RAILWAYS) - [N22000344]	599.63	12/2007	0.00

TABLE-4

Projects Added / Completed / Dropped / Frozen Rs.150 Crore and above

No of Projects in Previous Month	1636
No of Projects Completed/Dropped/Frozen in Current Month	5
No of Projects Down in Current Month	2
No of Projects added in Current Month	69
No of Projects in Current Month	1698

Project status Rs.150 Crore and above

Number of Projects

With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	578 (34.04%)	18 (1.06%)	374(22.03%)	163 (9.60%)	565(3.27%)	1698
Latest Approved (Date)	484 (28.50%)	24 (1.41%)	497(29.27%)	122 (7.18%)	571(3.63%)	1698

Project cost Rs.150 Crore and above

(All Cost/ Expenditure in Rs. crore)

						Cost overrun	
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	1301	15,92,644.31	17,87,772.81	7,07,270.85	39.60	1,95,128.50	12.30
Project with Revision in Cost	397	6,61,297.01	6,54,064.51	3,43,060.74	52.50	-7,232.50	-1.10
Total	1,698	22,53,941.32	24,41,837.32	10,50,331.59	43.01	1,87,896.00	8.34
Original Cost of All Projects							
Original Cost	1,698	20,41,114.88	24,41,837.32	10,50,331.59	43.01	4,00,722.44	19.63

Delayed Project cost Rs.150 Crore and above

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Cost overrun Rs crore	Cost overrun %
Original (OCE)	578	9,01,882.21	11,52,697.20	6,17,252.32	53.50	2,50,814.99	27.81
Latest Approved (RCE)	484	7,62,367.48	8,82,773.42	4,33,698.19	49.10	1,20,405.94	15.79

Additional Delayed Project cost Rs.150 Crore and above

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Cost overrun Rs crore	Cost overrun %
Latest Approved	93	93,885.47	1,07,753.14	74,020.83	68.70	13,867.67	14.80
Total	93	93,885.47	1,07,753.14	74,020.83	68.69	13,867.67	14.77

TABLE-5

Extent of cost overrun in projects with respect to original schedule(Sector Wise) Rs. 150 Crore and above

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48.51
2	CIVIL AVIATION	13	8,607.51	8,734.44	1.47	3	1,513.40	1,640.33	8.39
3	COAL	107	1,04,997.33	1,07,962.20	2.82	12	28,387.67	33,210.81	16.99
4	FERTILISERS	5	1,299.07	1,310.72	0.90	1	197.79	209.44	5.89
5	INFORMATION AND BROADCASTING	3	969.43	969.43	0.00	0	0.00	0.00	0.00
6	MINES	5	7,078.62	7,075.17	-0.05	0	0.00	0.00	0.00
7	STEEL	9	26,228.23	33,485.23	27.67	1	15,525.00	23,140.00	49.05
8	PETROLEUM	150	2,49,934.93	2,65,162.48	6.09	29	65,454.64	82,875.34	26.61
9	POWER	70	2,79,157.68	3,53,357.42	26.58	29	1,63,552.55	2,38,269.34	45.68
10	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0.00
11	HEALTH AND FAMILY WELFARE	21	9,473.56	9,444.06	-0.31	9	2,412.38	2,725.54	12.98
12	RAILWAYS	312	4,59,394.75	6,67,846.32	45.38	191	1,87,179.52	4,06,704.48	117.28
13	ROAD TRANSPORT AND HIGHWAYS	866	5,13,255.97	5,27,964.98	2.87	103	69,830.87	90,339.87	29.37
14	SHIPPING AND PORTS	1	4,200.00	5,369.18	27.84	1	4,200.00	5,369.18	27.84
15	TELECOMMUNICATIONS	4	16,095.23	27,333.53	69.82	2	13,565.80	24,904.10	83.58
16	URBAN DEVELOPMENT	75	2,63,975.80	2,70,607.62	2.51	14	29,058.09	35,689.91	22.82
17	WATER RESOURCES	51	27,288.45	72,686.28	166.36	1	10,151.04	55,548.87	447.22
18	HUMAN RESOURCE DEPARTMENT	1	484.32	626.26	29.31	1	484.32	626.26	29.31
Total		1698	20,41,114.88	24,41,837.32	19.63	400	6,18,784.07	10,41,752.47	68.35

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-6

Extent of cost overrun in projects with respect to original schedule(State Wise) Rs. 150 Crore and above

(All Cost/ Expenditure in Rs. Crore)

						Projects with cost overrun^			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	74	1,18,848.70	1,74,108.08	46.50	15	45,732.17	1,01,830.48	122.67
2	ARUNACHAL PRADESH	40	21,795.08	40,754.39	86.99	5	9,284.82	28,244.13	204.20
3	ASSAM	47	26,040.46	30,700.77	17.90	18	6,570.68	11,631.28	77.02
4	BIHAR	104	92,846.83	1,28,078.55	37.95	32	39,704.06	75,820.97	90.97
5	GOA	10	5,325.87	5,336.30	0.20	1	280.16	290.59	3.72
6	GUJARAT	58	82,316.29	88,517.56	7.53	9	15,988.90	23,005.55	43.88
7	HARYANA	42	34,417.90	37,813.53	9.87	7	4,921.98	8,728.09	77.33
8	HIMACHAL PRADESH	13	18,162.17	28,272.70	55.67	2	6,886.58	16,997.11	146.82
9	JAMMU AND KASHMIR	14	17,539.64	43,215.89	146.39	2	4,659.00	30,468.00	553.96
10	KARNATAKA	63	73,084.28	76,779.37	5.06	15	13,979.23	18,026.74	28.95
11	KERALA	20	36,309.60	39,755.52	9.49	9	16,705.01	20,346.47	21.80
12	MADHYA PRADESH	81	88,525.62	95,334.06	7.69	11	30,236.25	39,158.47	29.51
13	MAHARASHTRA	257	2,36,001.10	2,46,416.14	4.41	35	42,158.12	57,859.73	37.24
14	MANIPUR	5	6,002.36	14,012.39	133.45	1	4,454.17	12,524.00	181.17
15	MEGHALAYA	7	3,245.09	8,480.57	161.34	2	1,390.78	6,626.26	376.44
16	MIZORAM	13	7,757.62	11,189.69	44.24	5	3,593.57	7,025.64	95.51
17	NAGALAND	26	14,842.43	17,115.91	15.32	1	2,326.52	4,600.00	97.72
18	ODISHA	93	1,08,391.06	1,10,827.71	2.25	17	27,343.52	33,359.70	22.00
19	PUNJAB	27	13,539.35	15,616.61	15.34	7	4,225.58	6,503.12	53.90
20	RAJASTHAN	62	45,915.93	53,484.84	16.48	15	19,419.85	26,988.76	38.98
21	SIKKIM	9	3,476.73	6,368.17	83.17	3	1,909.76	4,801.20	151.40
22	TAMIL NADU	65	1,16,109.47	1,34,523.74	15.86	23	39,899.68	59,915.02	50.16
23	TRIPURA	7	1,977.29	2,159.55	9.22	5	1,436.39	1,618.65	12.69
24	UTTAR PRADESH	133	1,51,214.21	1,57,530.32	4.18	23	51,237.70	59,673.04	16.46
25	WEST BENGAL	76	61,377.53	78,388.96	27.72	25	27,245.03	44,592.75	63.67
26	A & N ISLANDS	9	2,786.01	2,893.59	3.86	2	552.41	679.33	22.98
27	CHANDIGARH	2	349.15	570.00	63.25	2	349.15	570.00	63.25
28	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	0.00
29	DELHI	34	85,373.97	86,552.63	1.38	7	6,708.62	7,887.28	17.57
30	CHHATISGARH	44	77,990.97	89,713.27	15.03	9	35,322.59	47,475.45	34.41
31	JHARKHAND	48	62,232.07	67,540.06	8.53	9	23,217.46	28,529.23	22.88
32	UTTARAKHAND	33	36,092.70	44,984.12	24.64	9	10,197.17	19,115.09	87.45
33	TELANGANA	55	39,236.69	41,643.90	6.14	10	5,264.17	8,324.65	58.14
34	MULTI STATE	126	3,45,904.63	4,57,316.12	32.21	64	1,15,582.99	2,28,535.69	97.72
Total		1698	20,41,114.88	24,41,837.32	19.63	400	6,18,784.07	10,41,752.47	68.35

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-7

Extent of time overrun in projects with respect to original schedule Rs.150 Crore and above

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	4	67,120.00	80,348.00	36 - 133
2	CIVIL AVIATION	13	8,607.51	8,734.44	1.47	5	3,573.83	3,700.62	6 - 21
3	COAL	107	1,04,997.33	1,07,962.20	2.82	39	22,430.74	26,905.00	12 - 144
4	FERTILISERS	5	1,299.07	1,310.72	0.90	0	0.00	0.00	-
5	INFORMATION AND BROADCASTING	3	969.43	969.43	0.00	1	204.32	204.32	9 - 9
6	MINES	5	7,078.62	7,075.17	-0.05	1	166.62	163.17	9 - 9
7	STEEL	9	26,228.23	33,485.23	27.67	8	25,964.87	33,221.87	12 - 62
8	PETROLEUM	150	2,49,934.93	2,65,162.48	6.09	55	1,33,765.59	1,45,532.53	1 - 110
9	POWER	70	2,79,157.68	3,53,357.42	26.58	50	1,96,297.55	2,51,376.75	1 - 147
10	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	1	1,554.00	1,554.00	6 - 6
11	HEALTH AND FAMILY WELFARE	21	9,473.56	9,444.06	-0.31	11	4,693.67	4,558.36	4 - 82
12	RAILWAYS	312	4,59,394.75	6,67,846.32	45.38	150	1,84,312.90	2,77,298.11	1 - 324
13	ROAD TRANSPORT AND HIGHWAYS	866	5,13,255.97	5,27,964.98	2.87	221	1,40,429.64	1,48,178.67	1 - 149
14	SHIPPING AND PORTS	1	4,200.00	5,369.18	27.84	0	0.00	0.00	-
15	TELECOMMUNICATIONS	4	16,095.23	27,333.53	69.82	2	13,565.80	24,904.10	14 - 58
16	URBAN DEVELOPMENT	75	2,63,975.80	2,70,607.62	2.51	28	97,167.32	98,576.57	3 - 93
17	WATER RESOURCES	51	27,288.45	72,686.28	166.36	1	10,151.04	55,548.87	15 - 15
18	HUMAN RESOURCE DEPARTMENT	1	484.32	626.26	29.31	1	484.32	626.26	75 - 75
Total		1698	20,41,114.88	24,41,837.32	19.63	578	9,01,882.21	11,52,697.20	

$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-8

Extent of time overrun in projects with respect to original schedule(State Wise) Rs.150 Crore and above

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	74	1,18,848.70	1,74,108.08	46.50	39	91,146.37	1,44,438.06	1 - 168
2	ARUNACHAL PRADESH	40	21,795.08	40,754.39	86.99	9	3,010.03	3,208.52	21 - 91
3	ASSAM	47	26,040.46	30,700.77	17.90	18	12,122.51	13,703.13	3 - 149
4	BIHAR	104	92,846.83	1,28,078.55	37.95	21	38,931.25	64,002.02	7 - 118
5	GOA	10	5,325.87	5,336.30	0.20	0	0.00	0.00	-
6	GUJARAT	58	82,316.29	88,517.56	7.53	19	37,509.71	43,754.11	3 - 120
7	HARYANA	42	34,417.90	37,813.53	9.87	9	7,113.24	9,342.62	1 - 118
8	HIMACHAL PRADESH	13	18,162.17	28,272.70	55.67	3	7,339.98	13,417.50	15 - 147
9	JAMMU AND KASHMIR	14	17,539.64	43,215.89	146.39	5	9,893.33	35,342.33	18 - 235
10	KARNATAKA	63	73,084.28	76,779.37	5.06	24	49,572.17	51,260.54	3 - 264
11	KERALA	20	36,309.60	39,755.52	9.49	10	17,312.43	19,048.63	8 - 89
12	MADHYA PRADESH	81	88,525.62	95,334.06	7.69	37	44,138.04	51,236.22	1 - 54
13	MAHARASHTRA	257	2,36,001.10	2,46,416.14	4.41	80	1,16,565.39	1,20,801.51	1 - 204
14	MANIPUR	5	6,002.36	14,012.39	133.45	3	5,188.43	13,198.46	36 - 132
15	MEGHALAYA	7	3,245.09	8,480.57	161.34	2	848.31	990.25	26 - 75
16	MIZORAM	13	7,757.62	11,189.69	44.24	5	3,593.57	7,025.64	63 - 116
17	NAGALAND	26	14,842.43	17,115.91	15.32	2	2,723.04	4,996.52	46 - 79
18	ODISHA	93	1,08,391.06	1,10,827.71	2.25	38	50,026.63	52,463.13	3 - 183
19	PUNJAB	27	13,539.35	15,616.61	15.34	10	5,798.28	7,278.04	1 - 31
20	RAJASTHAN	62	45,915.93	53,484.84	16.48	14	18,794.55	24,458.56	1 - 48
21	SIKKIM	9	3,476.73	6,368.17	83.17	2	333.87	420.73	76 - 82
22	TAMIL NADU	65	1,16,109.47	1,34,523.74	15.86	25	72,370.75	80,907.15	6 - 133
23	TRIPURA	7	1,977.29	2,159.55	9.22	2	908.56	1,009.00	6 - 18
24	UTTAR PRADESH	133	1,51,214.21	1,57,530.32	4.18	33	46,557.81	50,082.39	1 - 70
25	WEST BENGAL	76	61,377.53	78,388.96	27.72	27	33,724.91	45,662.15	7 - 324
26	A & N ISLANDS	9	2,786.01	2,893.59	3.86	1	314.61	441.33	21 - 21
27	CHANDIGARH	2	349.15	570.00	63.25	0	0.00	0.00	-
28	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	-
29	DELHI	34	85,373.97	86,552.63	1.38	11	6,300.43	7,263.25	3 - 82
30	CHHATISGARH	44	77,990.97	89,713.27	15.03	14	40,094.59	51,518.00	3 - 84
31	JHARKHAND	48	62,232.07	67,540.06	8.53	18	23,203.33	24,598.55	9 - 120
32	UTTARAKHAND	33	36,092.70	44,984.12	24.64	9	25,104.47	33,357.06	3 - 114
33	TELANGANA	55	39,236.69	41,643.90	6.14	24	20,046.49	20,105.58	2 - 156
34	MULTI STATE	126	3,45,904.63	4,57,316.12	32.21	64	1,11,295.13	1,57,366.22	2 - 252
Total		1698	20,41,114.88	24,41,837.32	19.63	578	9,01,882.21	11,52,697.20	

$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-9

Extent of time overrun in projects with respect to latest schedule Rs.150 Crore and above

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	4	67,120.00	80,348.00	36 - 133
2	CIVIL AVIATION	13	8,607.51	8,734.44	1.47	5	3,573.83	3,700.62	6 - 21
3	COAL	107	1,05,421.52	1,07,962.20	2.41	38	22,357.05	25,658.01	0 - 144
4	FERTILISERS	5	1,299.07	1,310.72	0.90	0	0.00	0.00	-
5	INFORMATION AND BROADCASTING	3	969.43	969.43	0.00	1	204.32	204.32	9 - 9
6	MINES	5	7,075.17	7,075.17	0.00	0	0.00	0.00	-
7	STEEL	9	33,843.23	33,485.23	-1.06	2	4,281.48	4,281.48	21 - 25
8	PETROLEUM	150	2,64,039.11	2,65,162.48	0.43	33	75,327.77	75,196.99	1 - 70
9	POWER	70	3,11,677.01	3,53,357.42	13.37	34	1,16,984.89	1,40,218.16	1 - 147
10	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	1	1,554.00	1,554.00	6 - 6
11	HEALTH AND FAMILY WELFARE	21	9,593.56	9,444.06	-1.56	10	3,818.67	3,810.56	4 - 82
12	RAILWAYS	312	5,89,996.53	6,67,846.32	13.20	126	2,15,044.18	2,43,218.94	1 - 264
13	ROAD TRANSPORT AND HIGHWAYS	866	5,38,445.99	5,27,964.98	-1.95	202	1,45,681.41	1,40,399.42	0 - 149
14	SHIPPING AND PORTS	1	5,369.18	5,369.18	0.00	0	0.00	0.00	-
15	TELECOMMUNICATIONS	4	16,103.53	27,333.53	69.74	1	13,334.00	24,664.00	58 - 58
16	URBAN DEVELOPMENT	75	2,65,053.71	2,70,607.62	2.10	25	82,450.52	83,343.79	0 - 93
17	WATER RESOURCES	51	27,288.45	72,686.28	166.36	1	10,151.04	55,548.87	15 - 15
18	HUMAN RESOURCE DEPARTMENT	1	484.32	626.26	29.31	1	484.32	626.26	75 - 75
Total		1698	22,53,941.32	24,41,837.32	8.34	484	7,62,367.48	8,82,773.42	

$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-10

Extent of cost overrun in projects with respect to latest schedule Rs. 150 Crore and above

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48.51
2	CIVIL AVIATION	13	8,607.51	8,734.44	1.47	3	1,513.40	1,640.33	8.39
3	COAL	107	1,05,421.52	1,07,962.20	2.41	11	22,480.56	26,130.40	16.24
4	FERTILISERS	5	1,299.07	1,310.72	0.90	1	197.79	209.44	5.89
5	INFORMATION AND BROADCASTING	3	969.43	969.43	0.00	0	0.00	0.00	0.00
6	MINES	5	7,075.17	7,075.17	0.00	0	0.00	0.00	0.00
7	STEEL	9	33,843.23	33,485.23	-1.06	0	0.00	0.00	0.00
8	PETROLEUM	150	2,64,039.11	2,65,162.48	0.43	13	14,699.80	17,731.51	20.62
9	POWER	70	3,11,677.01	3,53,357.42	13.37	19	1,20,532.75	1,62,730.21	35.01
10	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0.00
11	HEALTH AND FAMILY WELFARE	21	9,593.56	9,444.06	-1.56	9	2,412.38	2,725.54	12.98
12	RAILWAYS	312	5,89,996.53	6,67,846.32	13.20	142	1,35,455.70	2,27,563.72	68.00
13	ROAD TRANSPORT AND HIGHWAYS	866	5,38,445.99	5,27,964.98	-1.95	123	76,549.56	90,540.72	18.28
14	SHIPPING AND PORTS	1	5,369.18	5,369.18	0.00	0	0.00	0.00	0.00
15	TELECOMMUNICATIONS	4	16,103.53	27,333.53	69.74	1	13,334.00	24,664.00	84.97
16	URBAN DEVELOPMENT	75	2,65,053.71	2,70,607.62	2.10	9	23,159.81	28,742.94	24.11
17	WATER RESOURCES	51	27,288.45	72,686.28	166.36	1	10,151.04	55,548.87	447.22
18	HUMAN RESOURCE DEPARTMENT	1	484.32	626.26	29.31	1	484.32	626.26	29.31
Total		1698	22,53,941.32	24,41,837.32	8.34	336	4,48,242.11	6,79,352.94	51.56

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-11

Extent of time & cost overrun in projects with respect to latest schedule Rs.150 Crore and above

(All Cost/ Expenditure in Rs. crore)

						Projects with time$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Antici pated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Antici pated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48- 133
2	CIVIL AVIATION	13	8,607.51	8,734.44	1.47	2	653.54	780.33	6- 21
3	COAL	107	1,05,421.52	1,07,962.20	2.41	9	5,055.62	8,482.92	12- 144
4	FERTILISERS	5	1,299.07	1,310.72	0.90	0	0.00	0.00	0- 0
5	INFORMATION AND BROADCASTING	3	969.43	969.43	0.00	0	0.00	0.00	0- 0
6	MINES	5	7,075.17	7,075.17	0.00	0	0.00	0.00	0- 0
7	STEEL	9	33,843.23	33,485.23	-1.06	0	0.00	0.00	0- 0
8	PETROLEUM	150	2,64,039.11	2,65,162.48	0.43	0	0.00	0.00	0- 0
9	POWER	70	3,11,677.01	3,53,357.42	13.37	11	72,085.85	95,319.12	1- 147
10	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0- 0
11	HEALTH AND FAMILY WELFARE	21	9,593.56	9,444.06	-1.56	5	1,337.34	1,544.69	12- 82
12	RAILWAYS	312	5,89,996.53	6,67,846.32	13.20	57	65,516.21	1,03,596.27	6- 240
13	ROAD TRANSPORT AND HIGHWAYS	866	5,38,445.99	5,27,964.98	-1.95	36	23,257.74	29,452.31	1- 143
14	SHIPPING AND PORTS	1	5,369.18	5,369.18	0.00	0	0.00	0.00	0- 0
15	TELECOMMUNICATIONS	4	16,103.53	27,333.53	69.74	1	13,334.00	24,664.00	58- 58
16	URBAN DEVELOPMENT	75	2,65,053.71	2,70,607.62	2.10	4	2,894.00	3,787.27	3- 45
17	WATER RESOURCES	51	27,288.45	72,686.28	166.36	1	10,151.04	55,548.87	15- 15
18	HUMAN RESOURCE DEPARTMENT	1	484.32	626.26	29.31	1	484.32	626.26	75- 75
Total		1698	22,53,941.32	24,41,837.32	8.34	130	2,22,040.66	3,64,301.04	

^ - Cost Overrun = Anticipated Cost minus Original Cost

$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-12

Extent of time & cost overrun in projects with respect to original schedule Rs.150 Crore and above

(All Cost/ Expenditure in Rs. crore)

						Projects with time$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48- 133
2	CIVIL AVIATION	13	8,607.51	8,734.44	1.47	2	653.54	780.33	6- 21
3	COAL	107	1,04,997.33	1,07,962.20	2.82	10	10,962.73	15,563.33	12- 144
4	FERTILISERS	5	1,299.07	1,310.72	0.90	0	0.00	0.00	0- 0
5	INFORMATION AND BROADCASTING	3	969.43	969.43	0.00	0	0.00	0.00	0- 0
6	MINES	5	7,078.62	7,075.17	-0.05	0	0.00	0.00	0- 0
7	STEEL	9	26,228.23	33,485.23	27.67	1	15,525.00	23,140.00	62- 62
8	PETROLEUM	150	2,49,934.93	2,65,162.48	6.09	16	50,740.50	63,520.42	1- 110
9	POWER	70	2,79,157.68	3,53,357.42	26.58	24	1,47,226.07	2,02,305.27	1- 147
10	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0- 0
11	HEALTH AND FAMILY WELFARE	21	9,473.56	9,444.06	-0.31	5	1,337.34	1,544.69	12- 82
12	RAILWAYS	312	4,59,394.75	6,67,846.32	45.38	93	95,636.86	1,97,579.52	3- 324
13	ROAD TRANSPORT AND HIGHWAYS	866	5,13,255.97	5,27,964.98	2.87	38	27,110.31	36,600.27	1- 143
14	SHIPPING AND PORTS	1	4,200.00	5,369.18	27.84	0	0.00	0.00	0- 0
15	TELECOMMUNICATIONS	4	16,095.23	27,333.53	69.82	2	13,565.80	24,904.10	14- 58
16	URBAN DEVELOPMENT	75	2,63,975.80	2,70,607.62	2.51	6	8,625.28	10,034.53	3- 45
17	WATER RESOURCES	51	27,288.45	72,686.28	166.36	1	10,151.04	55,548.87	15- 15
18	HUMAN RESOURCE DEPARTMENT	1	484.32	626.26	29.31	1	484.32	626.26	75- 75
Total		1698	20,41,114.88	24,41,837.32	19.63	202	4,09,289.79	6,72,646.59	

^ - Cost Overrun = Anticipated Cost minus Original Cost

$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-13

State-Wise Position of Central Sector Projects costing Rs.150 Crore and above showing Both Time and Cost Overruns

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	74	1,18,848.70	1,74,108.08	46.50	10	39,330.79	93,325.81	1 - 168
2	ARUNACHAL PRADESH	40	21,795.08	40,754.39	86.99	2	345.96	544.45	36 - 91
3	ASSAM	47	26,040.46	30,700.77	17.90	5	1,654.05	3,518.82	4 - 143
4	BIHAR	104	92,846.83	1,28,078.55	37.95	11	31,377.45	56,455.93	12 - 118
5	GOA	10	5,325.87	5,336.30	0.20	0	0.00	0.00	-
6	GUJARAT	58	82,316.29	88,517.56	7.53	5	13,479.15	19,879.88	12 - 120
7	HARYANA	42	34,417.90	37,813.53	9.87	2	1,395.00	3,661.50	100 - 111
8	HIMACHAL PRADESH	13	18,162.17	28,272.70	55.67	1	3,919.59	9,997.11	147 - 147
9	JAMMU AND KASHMIR	14	17,539.64	43,215.89	146.39	1	2,500.00	27,949.00	235 - 235
10	KARNATAKA	63	73,084.28	76,779.37	5.06	6	6,128.21	8,130.00	3 - 36
11	KERALA	20	36,309.60	39,755.52	9.49	5	12,261.94	14,022.18	16 - 33
12	MADHYA PRADESH	81	88,525.62	95,334.06	7.69	8	28,472.46	35,667.94	1 - 36
13	MAHARASHTRA	257	2,36,001.10	2,46,416.14	4.41	21	25,111.48	34,502.45	1 - 204
14	MANIPUR	5	6,002.36	14,012.39	133.45	1	4,454.17	12,524.00	132 - 132
15	MEGHALAYA	7	3,245.09	8,480.57	161.34	1	484.32	626.26	75 - 75
16	MIZORAM	13	7,757.62	11,189.69	44.24	5	3,593.57	7,025.64	63 - 116
17	NAGALAND	26	14,842.43	17,115.91	15.32	1	2,326.52	4,600.00	79 - 79
18	ODISHA	93	1,08,391.06	1,10,827.71	2.25	15	24,857.95	30,794.02	3 - 183
19	PUNJAB	27	13,539.35	15,616.61	15.34	5	3,131.12	4,756.40	1 - 31
20	RAJASTHAN	62	45,915.93	53,484.84	16.48	7	14,217.88	19,881.89	6 - 48
21	SIKKIM	9	3,476.73	6,368.17	83.17	1	182.28	269.14	82 - 82
22	TAMIL NADU	65	1,16,109.47	1,34,523.74	15.86	7	15,872.04	24,411.89	12 - 133
23	TRIPURA	7	1,977.29	2,159.55	9.22	2	908.56	1,009.00	6 - 18
24	UTTAR PRADESH	133	1,51,214.21	1,57,530.32	4.18	7	23,525.00	27,657.33	3 - 70
25	WEST BENGAL	76	61,377.53	78,388.96	27.72	13	21,957.91	33,910.18	12 - 324
26	A & N ISLANDS	9	2,786.01	2,893.59	3.86	1	314.61	441.33	21 - 21
27	CHANDIGARH	2	349.15	570.00	63.25	0	0.00	0.00	-
28	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	-
29	DELHI	34	85,373.97	86,552.63	1.38	4	2,131.41	3,094.23	17 - 82
30	CHHATISGARH	44	77,990.97	89,713.27	15.03	7	33,816.43	45,670.40	3 - 62
31	JHARKHAND	48	62,232.07	67,540.06	8.53	4	16,497.75	17,892.97	9 - 37
32	UTTARAKHAND	33	36,092.70	44,984.12	24.64	4	7,732.90	16,011.99	19 - 114
33	TELANGANA	55	39,236.69	41,643.90	6.14	6	2,307.59	3,019.95	12 - 144
34	MULTI STATE	126	3,45,904.63	4,57,316.12	32.21	34	65,001.70	1,11,394.90	9 - 252
Total		1698	20,41,114.88	24,41,837.32	19.63	202	4,09,289.79	6,72,646.59	

^ - Cost Overrun = Anticipated Cost minus Original Cost

$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-14

EXECUTIVE SUMMARY COSTING Rs.1000 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	154	8
2	ROAD TRANSPORT AND HIGHWAYS	151	7
3	PETROLEUM	59	4
4	POWER	41	3
5	URBAN DEVELOPMENT	22	2
6	COAL	16	0
7	STEEL	6	2
8	ATOMIC ENERGY	4	0
9	CIVIL AVIATION	2	0
10	TELECOMMUNICATIONS	2	0
11	MINES	1	0
12	HEAVY INDUSTRY	1	0
13	HEALTH AND FAMILY WELFARE	1	0
14	SHIPPING AND PORTS	1	0
15	WATER RESOURCES	1	0
	Total	462	26

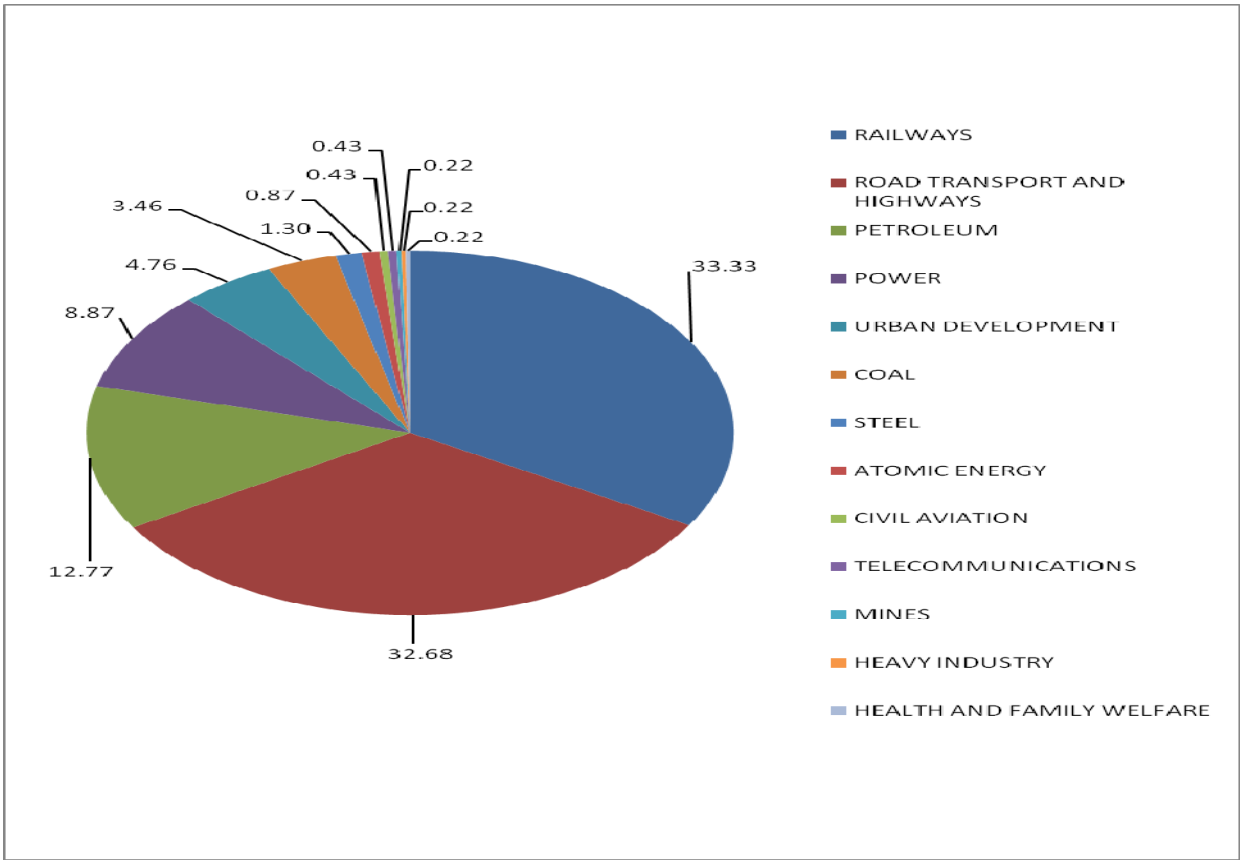

TABLE-15

Projects Added / Completed / Dropped / Frozen Rs.1000 Crore and above

No of Projects in Previous Month	460
No of Projects Completed/Dropped/Frozen in Current Month	1
No of Projects down in Current Month	1
No of Projects added in Current Month	4
No of Projects in Current Month	462

Project status Rs.1000 Crore and above

Number of Projects

With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	208 (45.02%)	6 (1.30%)	86 (18.61%)	54 (11.69%)	108(3.38%)	462
Latest Approved (Date)	163 (35.28%)	7 (1.52%)	139(30.09%)	43 (9.31%)	110(3.81%)	462

Project cost Rs.1000 Crore and above

(All Cost/ Expenditure in Rs. crore)

						Cost overrun	
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	330	11,95,068.40	13,84,403.36	5,46,410.64	39.50	1,89,334.96	15.80
Project with Revision in Cost	132	5,41,474.38	5,40,350.92	2,86,222.52	53.00	-1,123.46	-.20
Total	462	17,36,542.78	19,24,754.28	8,32,633.16	43.26	1,88,211.50	10.84
Original Cost of All Projects							
Original Cost	462	15,39,306.21	19,24,754.28	8,32,633.16	43.26	3,85,448.07	25.04

Delayed Project cost Rs. 1000 Crore and above

(All Cost/ Expenditure in Rs. crore)

						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	208	7,45,209.76	9,91,210.11	5,29,758.11	53.40	2,46,000.35	33.01
Latest Approved (RCE)	163	6,18,372.59	7,42,583.42	3,57,854.80	48.20	1,24,210.83	20.09

Additional Delayed Project cost Rs. 1000 Crore and above

(All Cost/ Expenditure in Rs. crore)

						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Latest Approved	26	65,099.55	79,113.41	52,559.48	66.40	14,013.86	21.50
Total	26	65,099.55	79,113.41	52,559.48	66.44	14,013.86	21.53

TABLE-16

Extent of cost overrun in projects with respect to original schedule(Sector Wise) Rs.1000 Crore and above

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48.51
2	CIVIL AVIATION	2	3,850.00	3,850.00	0.00	0	0.00	0.00	0.00
3	COAL	16	66,016.48	69,702.11	5.58	3	25,805.84	29,491.47	14.28
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
5	STEEL	6	25,381.34	32,638.34	28.59	1	15,525.00	23,140.00	49.05
6	PETROLEUM	59	2,12,049.29	2,26,555.48	6.84	17	59,689.90	76,219.46	27.69
7	POWER	41	2,66,808.74	3,40,676.51	27.69	25	1,62,144.07	2,36,528.89	45.88
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0.00
9	HEALTH AND FAMILY WELFARE	1	1,351.00	1,351.00	0.00	0	0.00	0.00	0.00
10	RAILWAYS	154	3,91,155.69	5,87,757.30	50.26	101	1,55,626.99	3,57,581.48	129.77
11	ROAD TRANSPORT AND HIGHWAYS	151	2,20,881.10	2,33,121.48	5.54	33	42,475.56	55,676.92	31.08
12	SHIPPING AND PORTS	1	4,200.00	5,369.18	27.84	1	4,200.00	5,369.18	27.84
13	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	84.97
14	URBAN DEVELOPMENT	22	2,47,802.36	2,54,066.84	2.53	5	26,033.88	32,298.36	24.06
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	447.22
Total		462	15,39,306.21	19,24,754.28	25.04	191	5,42,257.28	9,37,017.63	72.80

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-17

Extent of cost overrun in projects with respect to original schedule(State Wise) Rs. 1000 Crore and above

(All Cost/ Expenditure in Rs. Crore)

						Projects with cost overrun^			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	20	97,962.39	1,53,647.17	56.84	10	44,401.22	1,00,444.00	126.22
2	ARUNACHAL PRADESH	5	13,732.92	32,374.37	135.74	2	8,782.23	27,423.68	212.26
3	ASSAM	8	11,678.49	14,282.38	22.30	3	2,127.51	4,868.01	128.81
4	BIHAR	23	57,179.10	90,364.87	58.04	13	31,489.79	64,675.56	105.39
5	GUJARAT	20	64,112.23	69,558.16	8.49	4	14,316.57	20,421.55	42.64
6	HARYANA	15	21,618.98	24,638.36	13.97	3	2,699.20	5,718.58	111.86
7	HIMACHAL PRADESH	7	15,497.19	25,607.72	65.24	2	6,886.58	16,997.11	146.82
8	JAMMU AND KASHMIR	8	15,337.84	41,014.09	167.40	2	4,659.00	30,468.00	553.96
9	KARNATAKA	19	55,423.75	58,845.64	6.17	8	10,837.45	14,275.34	31.72
10	KERALA	9	30,871.86	34,193.65	10.76	6	14,996.96	18,342.79	22.31
11	MADHYA PRADESH	21	59,593.54	67,463.72	13.21	9	29,414.20	37,802.42	28.52
12	MAHARASHTRA	52	1,54,949.73	1,67,985.94	8.41	19	36,356.65	50,164.73	37.98
13	MANIPUR	1	4,454.17	12,524.00	181.17	1	4,454.17	12,524.00	181.17
14	MEGHALAYA	1	906.46	6,000.00	561.92	1	906.46	6,000.00	561.92
15	MIZORAM	1	2,393.47	5,021.45	109.80	1	2,393.47	5,021.45	109.80
16	NAGALAND	3	7,896.52	10,170.00	28.79	1	2,326.52	4,600.00	97.72
17	ODISHA	35	84,344.16	86,328.70	2.35	10	25,048.54	30,532.65	21.89
18	PUNJAB	3	3,627.54	4,826.70	33.06	1	1,388.34	2,587.50	86.37
19	RAJASTHAN	10	22,632.33	28,820.49	27.34	4	15,115.90	21,304.06	40.94
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	204.95
21	TAMIL NADU	25	97,234.18	1,13,562.51	16.79	13	36,705.21	53,730.54	46.38
22	UTTAR PRADESH	43	1,12,731.46	1,18,937.71	5.51	12	46,866.04	54,013.42	15.25
23	WEST BENGAL	24	43,267.91	59,250.43	36.94	12	22,816.12	38,829.67	70.19
24	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	0.00
25	DELHI	9	76,967.38	77,923.40	1.24	2	5,483.21	6,439.23	17.44
26	CHHATISGARH	14	65,083.62	76,559.60	17.63	7	34,693.96	46,471.96	33.95
27	JHARKHAND	13	49,100.48	53,989.92	9.96	5	21,821.72	26,711.16	22.41
28	UTTARAKHAND	7	27,696.84	36,133.38	30.46	4	8,654.06	17,090.60	97.49
29	TELANGANA	5	18,567.06	20,644.30	11.19	2	2,378.60	4,455.84	87.33
30	MULTI STATE	59	3,17,019.05	4,24,158.62	33.80	33	1,02,898.12	2,11,019.09	105.08
Total		462	15,39,306.21	19,24,754.28	25.04	191	5,42,257.28	9,37,017.63	72.80

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-18

Extent of time overrun in projects with respect to original schedule Rs.1000 Crore and above

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	4	67,120.00	80,348.00	36 - 133
2	CIVIL AVIATION	2	3,850.00	3,850.00	0.00	1	2,467.00	2,467.00	6 - 6
3	COAL	16	66,016.48	69,702.11	5.58	4	10,854.16	14,538.99	31 - 84
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
5	STEEL	6	25,381.34	32,638.34	28.59	6	25,381.34	32,638.34	15 - 62
6	PETROLEUM	59	2,12,049.29	2,26,555.48	6.84	24	1,19,763.79	1,31,234.26	1 - 110
7	POWER	41	2,66,808.74	3,40,676.51	27.69	27	1,86,754.55	2,41,501.78	1 - 147
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	1	1,554.00	1,554.00	6 - 6
9	HEALTH AND FAMILY WELFARE	1	1,351.00	1,351.00	0.00	0	0.00	0.00	-
10	RAILWAYS	154	3,91,155.69	5,87,757.30	50.26	87	1,52,011.13	2,42,566.72	3 - 324
11	ROAD TRANSPORT AND HIGHWAYS	151	2,20,881.10	2,33,121.48	5.54	44	65,233.61	72,276.22	1 - 100
12	SHIPPING AND PORTS	1	4,200.00	5,369.18	27.84	0	0.00	0.00	-
13	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58 - 58
14	URBAN DEVELOPMENT	22	2,47,802.36	2,54,066.84	2.53	8	90,585.14	91,871.93	4 - 64
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	15 - 15
Total		462	15,39,306.21	19,24,754.28	25.04	208	7,45,209.76	9,91,210.11	

$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-19

Extent of time overrun in projects with respect to original schedule(State Wise) Rs.1000 Crore and above

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	20	97,962.39	1,53,647.17	56.84	11	80,526.89	1,34,140.38	1 - 168
2	ARUNACHAL PRADESH	5	13,732.92	32,374.37	135.74	1	1,253.10	1,253.10	60 - 60
3	ASSAM	8	11,678.49	14,282.38	22.30	4	6,654.35	7,714.86	3 - 81
4	BIHAR	23	57,179.10	90,364.87	58.04	9	32,035.52	56,487.05	12 - 118
5	GUJARAT	20	64,112.23	69,558.16	8.49	8	32,495.53	38,097.02	3 - 87
6	HARYANA	15	21,618.98	24,638.36	13.97	2	4,637.00	6,496.50	7 - 100
7	HIMACHAL PRADESH	7	15,497.19	25,607.72	65.24	2	6,405.52	12,483.04	15 - 147
8	JAMMU AND KASHMIR	8	15,337.84	41,014.09	167.40	5	9,893.33	35,342.33	18 - 235
9	KARNATAKA	19	55,423.75	58,845.64	6.17	11	41,542.14	43,242.71	3 - 264
10	KERALA	9	30,871.86	34,193.65	10.76	5	15,319.19	16,962.71	8 - 33
11	MADHYA PRADESH	21	59,593.54	67,463.72	13.21	10	33,703.42	40,513.91	1 - 36
12	MAHARASHTRA	52	1,54,949.73	1,67,985.94	8.41	26	90,172.06	97,693.35	1 - 204
13	MANIPUR	1	4,454.17	12,524.00	181.17	1	4,454.17	12,524.00	132 - 132
14	MEGHALAYA	1	906.46	6,000.00	561.92	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	5,021.45	109.80	1	2,393.47	5,021.45	96 - 96
16	NAGALAND	3	7,896.52	10,170.00	28.79	1	2,326.52	4,600.00	79 - 79
17	ODISHA	35	84,344.16	86,328.70	2.35	17	41,720.08	43,704.61	3 - 183
18	PUNJAB	3	3,627.54	4,826.70	33.06	2	2,457.93	3,657.09	6 - 14
19	RAJASTHAN	10	22,632.33	28,820.49	27.34	1	12,320.00	17,079.00	48 - 48
20	SIKKIM	1	1,339.48	4,084.69	204.95	0	0.00	0.00	-
21	TAMIL NADU	25	97,234.18	1,13,562.51	16.79	12	66,688.04	74,507.46	6 - 133
22	UTTAR PRADESH	43	1,12,731.46	1,18,937.71	5.51	14	37,768.58	41,652.37	2 - 40
23	WEST BENGAL	24	43,267.91	59,250.43	36.94	15	29,646.46	41,166.81	7 - 324
24	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	-
25	DELHI	9	76,967.38	77,923.40	1.24	3	4,167.73	4,948.52	6 - 31
26	CHHATISGARH	14	65,083.62	76,559.60	17.63	8	38,121.02	49,365.91	3 - 62
27	JHARKHAND	13	49,100.48	53,989.92	9.96	5	19,509.24	20,575.75	9 - 84
28	UTTARAKHAND	7	27,696.84	36,133.38	30.46	4	23,343.06	31,505.53	3 - 114
29	TELANGANA	5	18,567.06	20,644.30	11.19	2	11,759.46	11,759.46	7 - 156
30	MULTI STATE	59	3,17,019.05	4,24,158.62	33.80	28	93,895.95	1,38,715.19	3 - 252
Total		462	15,39,306.21	19,24,754.28	25.04	208	7,45,209.76	9,91,210.11	

$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-20

Extent of time overrun in projects with respect to latest schedule Rs.1000 Crore and above

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	4	67,120.00	80,348.00	36 - 133
2	CIVIL AVIATION	2	3,850.00	3,850.00	0.00	1	2,467.00	2,467.00	6 - 6
3	COAL	16	67,189.78	69,702.11	3.74	3	10,797.19	13,308.72	31 - 60
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
5	STEEL	6	32,996.34	32,638.34	-1.09	2	4,281.48	4,281.48	21 - 25
6	PETROLEUM	59	2,25,870.19	2,26,555.48	0.30	10	65,165.09	65,165.09	1 - 26
7	POWER	41	2,99,095.28	3,40,676.51	13.90	18	1,09,907.77	1,33,041.86	1 - 147
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	1	1,554.00	1,554.00	6 - 6
9	HEALTH AND FAMILY WELFARE	1	1,471.00	1,351.00	-8.16	0	0.00	0.00	-
10	RAILWAYS	154	5,15,590.65	5,87,757.30	14.00	72	1,85,647.30	2,14,421.72	3 - 264
11	ROAD TRANSPORT AND HIGHWAYS	151	2,36,689.70	2,33,121.48	-1.51	44	72,046.58	71,100.75	0 - 100
12	SHIPPING AND PORTS	1	5,369.18	5,369.18	0.00	0	0.00	0.00	-
13	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58 - 58
14	URBAN DEVELOPMENT	22	2,48,610.45	2,54,066.84	2.19	6	75,901.14	76,681.93	13 - 64
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	15 - 15
Total		462	17,36,542.78	19,24,754.28	10.84	163	6,18,372.59	7,42,583.42	

$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-21

Extent of cost overrun in projects with respect to latest schedule Rs. 1000 Crore and above

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48.51
2	CIVIL AVIATION	2	3,850.00	3,850.00	0.00	0	0.00	0.00	0.00
3	COAL	16	67,189.78	69,702.11	3.74	2	19,898.73	22,411.06	12.63
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
5	STEEL	6	32,996.34	32,638.34	-1.09	0	0.00	0.00	0.00
6	PETROLEUM	59	2,25,870.19	2,26,555.48	0.30	6	10,892.27	13,333.12	22.41
7	POWER	41	2,99,095.28	3,40,676.51	13.90	18	1,20,337.33	1,62,435.61	34.98
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0.00
9	HEALTH AND FAMILY WELFARE	1	1,471.00	1,351.00	-8.16	0	0.00	0.00	0.00
10	RAILWAYS	154	5,15,590.65	5,87,757.30	14.00	72	1,10,001.47	1,91,026.20	73.66
11	ROAD TRANSPORT AND HIGHWAYS	151	2,36,689.70	2,33,121.48	-1.51	30	40,583.61	49,130.46	21.06
12	SHIPPING AND PORTS	1	5,369.18	5,369.18	0.00	0	0.00	0.00	0.00
13	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	84.97
14	URBAN DEVELOPMENT	22	2,48,610.45	2,54,066.84	2.19	4	21,154.18	26,610.57	25.79
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	447.22
Total		462	17,36,542.78	19,24,754.28	10.84	137	3,73,623.63	5,85,658.89	56.75

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-22

Extent of time & cost overrun in projects with respect to latest schedule Rs.1000 Crore and above

(All Cost/ Expenditure in Rs. crore)

						Projects with time$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48- 133
2	CIVIL AVIATION	2	3,850.00	3,850.00	0.00	0	0.00	0.00	0- 0
3	COAL	16	67,189.78	69,702.11	3.74	1	2,661.73	5,173.26	60- 60
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
5	STEEL	6	32,996.34	32,638.34	-1.09	0	0.00	0.00	0- 0
6	PETROLEUM	59	2,25,870.19	2,26,555.48	0.30	0	0.00	0.00	0- 0
7	POWER	41	2,99,095.28	3,40,676.51	13.90	10	71,890.43	95,024.52	1- 147
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0- 0
9	HEALTH AND FAMILY WELFARE	1	1,471.00	1,351.00	-8.16	0	0.00	0.00	0- 0
10	RAILWAYS	154	5,15,590.65	5,87,757.30	14.00	30	54,305.79	88,331.04	9- 204
11	ROAD TRANSPORT AND HIGHWAYS	151	2,36,689.70	2,33,121.48	-1.51	14	15,203.04	19,624.10	2- 62
12	SHIPPING AND PORTS	1	5,369.18	5,369.18	0.00	0	0.00	0.00	0- 0
13	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58- 58
14	URBAN DEVELOPMENT	22	2,48,610.45	2,54,066.84	2.19	1	1,219.21	2,000.00	17- 17
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	15- 15
Total		462	17,36,542.78	19,24,754.28	10.84	61	1,96,036.24	3,30,864.79	

^ - Cost Overrun = Anticipated Cost minus Original Cost

$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-23

Extent of time & cost overrun in projects with respect to original schedule Rs.1000 Crore and above (All Cost/ Expenditure in Rs. Crore)									
						Projects with time$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48- 133
2	CIVIL AVIATION	2	3,850.00	3,850.00	0.00	0	0.00	0.00	0- 0
3	COAL	16	66,016.48	69,702.11	5.58	2	8,568.84	12,253.67	48- 60
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
5	STEEL	6	25,381.34	32,638.34	28.59	1	15,525.00	23,140.00	62- 62
6	PETROLEUM	59	2,12,049.29	2,26,555.48	6.84	11	48,513.94	60,866.61	1- 110
7	POWER	41	2,66,808.74	3,40,676.51	27.69	20	1,45,817.59	2,00,564.82	1- 147
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0- 0
9	HEALTH AND FAMILY WELFARE	1	1,351.00	1,351.00	0.00	0	0.00	0.00	0- 0
10	RAILWAYS	154	3,91,155.69	5,87,757.30	50.26	56	81,294.69	1,75,832.90	3- 324
11	ROAD TRANSPORT AND HIGHWAYS	151	2,20,881.10	2,33,121.48	5.54	16	19,612.68	26,655.29	1- 100
12	SHIPPING AND PORTS	1	4,200.00	5,369.18	27.84	0	0.00	0.00	0- 0
13	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58- 58
14	URBAN DEVELOPMENT	22	2,47,802.36	2,54,066.84	2.53	2	6,401.00	7,687.79	17- 32
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	15- 15
Total		462	15,39,306.21	19,24,754.28	25.04	113	3,76,489.78	6,27,712.95	

^ - Cost Overrun = Anticipated Cost minus Original Cost

$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-24

State-Wise Position of Central Sector Projects costing Rs.1000 Crore and above showing Both Time and Cost Overruns

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	20	97,962.39	1,53,647.17	56.84	7	38,490.89	92,462.38	1 - 168
2	ARUNACHAL PRADESH	5	13,732.92	32,374.37	135.74	0	0.00	0.00	-
3	ASSAM	8	11,678.49	14,282.38	22.30	1	385.20	1,532.00	12 - 12
4	BIHAR	23	57,179.10	90,364.87	58.04	7	29,343.85	53,795.38	12 - 118
5	GUJARAT	20	64,112.23	69,558.16	8.49	2	12,288.74	17,890.23	12 - 54
6	HARYANA	15	21,618.98	24,638.36	13.97	1	1,108.00	2,967.50	100 - 100
7	HIMACHAL PRADESH	7	15,497.19	25,607.72	65.24	1	3,919.59	9,997.11	147 - 147
8	JAMMU AND KASHMIR	8	15,337.84	41,014.09	167.40	1	2,500.00	27,949.00	235 - 235
9	KARNATAKA	19	55,423.75	58,845.64	6.17	4	4,902.43	6,619.00	3 - 16
10	KERALA	9	30,871.86	34,193.65	10.76	4	12,006.19	13,673.75	16 - 33
11	MADHYA PRADESH	21	59,593.54	67,463.72	13.21	7	27,975.41	34,786.89	1 - 26
12	MAHARASHTRA	52	1,54,949.73	1,67,985.94	8.41	13	22,229.53	30,522.69	1 - 204
13	MANIPUR	1	4,454.17	12,524.00	181.17	1	4,454.17	12,524.00	132 - 132
14	MEGHALAYA	1	906.46	6,000.00	561.92	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	5,021.45	109.80	1	2,393.47	5,021.45	96 - 96
16	NAGALAND	3	7,896.52	10,170.00	28.79	1	2,326.52	4,600.00	79 - 79
17	ODISHA	35	84,344.16	86,328.70	2.35	9	22,712.87	28,196.97	3 - 183
18	PUNJAB	3	3,627.54	4,826.70	33.06	1	1,388.34	2,587.50	6 - 6
19	RAJASTHAN	10	22,632.33	28,820.49	27.34	1	12,320.00	17,079.00	48 - 48
20	SIKKIM	1	1,339.48	4,084.69	204.95	0	0.00	0.00	-
21	TAMIL NADU	25	97,234.18	1,13,562.51	16.79	5	15,380.80	23,200.22	12 - 133
22	UTTAR PRADESH	43	1,12,731.46	1,18,937.71	5.51	5	23,116.58	27,149.38	3 - 40
23	WEST BENGAL	24	43,267.91	59,250.43	36.94	9	20,992.37	32,527.75	14 - 324
24	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	-
25	DELHI	9	76,967.38	77,923.40	1.24	1	1,219.21	2,000.00	17 - 17
26	CHHATISGARH	14	65,083.62	76,559.60	17.63	6	33,664.00	45,210.91	3 - 62
27	JHARKHAND	13	49,100.48	53,989.92	9.96	2	16,090.78	17,157.29	9 - 33
28	UTTARAKHAND	7	27,696.84	36,133.38	30.46	3	7,127.06	15,289.53	76 - 114
29	TELANGANA	5	18,567.06	20,644.30	11.19	0	0.00	0.00	-
30	MULTI STATE	59	3,17,019.05	4,24,158.62	33.80	20	58,153.78	1,02,973.02	9 - 252
Total		462	15,39,306.21	19,24,754.28	25.04	113	3,76,489.78	6,27,712.95	

^ - Cost Overrun = Anticipated Cost minus Original Cost

$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-25

List of projects completed/dropped/Frozen during current month Rs.150 Crore and above

(All Cost/ Expenditure in Rs. crore)

			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	ROAD TRANSPORT AND HIGHWAYS						
1	2 LANNING OF MOKAMA-MUNGER PPP (ANNUITY)	05/2011	351.54	05/2013	351.54	N.A.	329.40
2	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III)	09/2015	788.51	03/2018	788.51	N.A.	103.37
3	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II)	09/2015	785.78	03/2018	785.78	N.A.	839.00
4	NAGPUR - KONDHALI	09/2005	168.00	06/2006	168.00	N.A.	226.24
5	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW	09/2015	771.18	N.A.	7,558.00	N.A.	261.77

TABLE-26

List of projects added Rs.150 Crore and above					(November 2019)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	PETROLEUM					
1	LAB REVAMP AT GUJARAT REFINERY Central Sector Projects	10/2019	403.00	12/2021	403.00	12/2021
	ROAD TRANSPORT AND HIGHWAYS					
2	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I	12/2016	196.00	9/2021	196.00	9/2021
3	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180	1/2016	497.14	8/2016	497.14	8/2016
4	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V	1/2016	476.20	9/2016	544.00	9/2016
5	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 127.500 TO 178.944 DARRIGHAT TO BANARI SECTION	3/2016	491.52	9/2016	491.52	9/2016
6	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION	11/2015	335.32	6/2017	335.32	6/2017
7	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	1/2016	624.98	10/2016	624.98	10/2016
8	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO	3/2017	423.79	1/2018	423.79	1/2018
9	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1	12/2010	169.26	1/2019	299.00	1/2019
10	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A	11/2017	188.80	5/2019	188.80	5/2019
11	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331	12/2014	379.16	11/2017	379.16	11/2017
12	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION	12/2014	496.02	3/2015	496.02	3/2015
13	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221	3/2010	179.89	3/2013	271.00	3/2013
14	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI	3/2016	452.94	7/2016	452.94	7/2016
	URBAN DEVELOPMENT					

List of projects added Rs.150 Crore and above					(November 2019)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
15	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P.	2/2019	186.00	9/2020	186.00	9/2020
16	DELHI GHAZIABAD MEERUT RRTS CORRIDOR	3/2019	30,274.00	6/2025	30,274.00	6/2025
17	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS	7/2019	24,948.65	3/2025	24,948.65	3/2025
18	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND	5/2017	565.00	12/2020	565.00	12/2020
19	SURAT METRO RAIL PROJECT	3/2019	12,020.32	3/2024	12,020.32	3/2024
20	AHMEDABAD METRO RAIL PROJECT PHASE II	3/2019	5,384.17	3/2024	5,384.17	3/2024
	WATER RESOURCES					
21	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI	3/2017	273.37	8/2019	273.37	8/2019
22	INTERCEPTION AND DIVERSION (I&D)WITH STP AT RISHIKESH	3/2017	158.00	11/2019	158.00	11/2019
23	SEWERAGE WORKS IN SEWERAGE DISTRICT A OF ALLAHABAD	2/2014	288.94	9/2019	288.94	9/2019
24	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA	5/2017	767.59	9/2021	767.59	9/2021
25	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS	3/2018	904.00	9/2021	904.00	9/2021
26	FARRUKHABAD I AND D AND STP WORKS HAM	10/2017	213.62	3/2022	213.62	3/2022
27	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR	10/2016	370.40	8/2020	370.40	8/2020
28	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS	3/2018	967.23	9/2021	967.23	9/2021
29	SEWERAGE TREATMENT PLANT AT PAHARI PATNA	5/2017	191.62	11/2020	191.62	11/2020
30	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA	5/2017	184.86	5/2021	184.86	5/2021
31	SEWERAGE SCHEME AT PAHARI ZONE V PATNA	5/2017	356.37	4/2021	356.37	4/2021
32	SAIDPUR SEWER NETWORK PATNA	4/2015	268.63	1/2021	268.63	1/2021
33	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR	4/2015	184.93	4/2020	184.93	4/2020
34	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	225.77	3/2020	225.77	3/2020
35	SEWER NETWORKS, SPS AND STP, MUNGER	3/2018	294.02	10/2021	294.02	10/2021
36	SEWER NETWORKS SPS AND STP HAJIPUR	3/2018	305.19	8/2021	305.19	8/2021
37	INTERCEPTION DIVERSION AND TREATMENT WORKS AT TOLLY'S NULLAH ADI GANGA	8/2017	307.12	9/2022	307.12	9/2022
38	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA	8/2017	824.00	6/2022	824.00	6/2022
39	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA	8/2017	578.89	6/2022	578.89	6/2022

List of projects added Rs.150 Crore and above					(November 2019)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
40	INTERCEPTION AND DIVERSION WITH STP AT BALLY	10/2017	164.93	12/2021	164.93	12/2021
41	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI	1/2018	172.10	12/2021	172.10	12/2021
42	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE	12/2014	272.32	4/2020	272.32	4/2020
43	SEWERAGE SYSTEM & STP WORKS AT HALISHAHR	2/2014	274.76	12/2019	274.76	12/2019
44	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH	8/2017	185.22	12/2021	185.22	12/2021
45	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK	3/2017	277.42	5/2021	277.42	5/2021
46	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH	5/2018	160.00	2/2022	160.00	2/2022
47	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS	3/2018	165.16	6/2022	165.16	6/2022
48	INTERCEPTION & DIVERSION WITH STP AT MAHESHTALA	5/2018	198.43	2/2022	198.43	2/2022
49	I AND D AND STP WORKS AT BURDWAN WEST BENGAL	12/2018	234.31	4/2022	234.31	4/2022
50	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPURL	3/2019	287.53	4/2022	287.53	4/2022
51	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS	1/2019	384.96	4/2022	384.96	4/2022
52	I AND D AND STP AT CHAPPRA	11/2018	236.15	12/2020	236.15	12/2020
53	I AND D AND STP WORKS FOR BHAGALPUR	10/2017	254.13	9/2020	254.13	9/2020
54	SEWER NETWORK SPS AND STP BEGUSARAI	3/2018	230.06	7/2021	230.06	7/2021
55	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH	3/2019	298.12	7/2021	298.12	7/2021
56	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH	2/2019	681.78	6/2022	681.78	6/2022
57	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS AT AGRA	2/2019	317.19	8/2021	317.19	8/2021
58	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH	1/2019	206.05	10/2021	206.05	10/2021
59	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH	1/2019	231.79	12/2021	231.79	12/2021
60	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	2/2011	279.91	12/2019	279.91	12/2019
61	MATHURA SEWERAGE SCHEME	12/2017	460.45	12/2020	460.45	12/2020
62	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO	5/2017	344.81	5/2020	344.81	5/2020

List of projects added Rs.150 Crore and above					(November 2019)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
63	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O&M AT CORONATION PILLAR DELHI	12/2018	515.07	1/2021	515.07	1/2021
64	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S	5/2016	239.11	2/2022	239.11	2/2022
65	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2	5/2016	211.79	12/2021	211.79	12/2021
66	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L	3/2017	665.78	12/2022	665.78	12/2022
67	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA	2/2017	161.31	11/2019	161.31	11/2019
68	REHABILITATION RENOVATION OF AGRA SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS IN AGRA UTTAR PR	12/2018	857.26	8/2021	857.26	8/2021
69	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH	3/2019	271.39	8/2021	271.39	8/2021

TABLE-27

Milestones (Cumulative due & achieved) Rs.150 Crore and above

Total	5620
Achieved up to month	2882

TABLE-28

List of projects reporting additional delayed Rs.150 Crore and above							(November 2019)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Antici pated	Original	Last month	This month	Delay (in months)
	COAL						
1	PATHERDIH NLW WASHERY BCCL	269.82	269.82	04/2014	11/2019	01/2020	2
	STEEL						
2	INSTALLATION OF NEW HOT STRIP MILL AT RSP SAIL	3,127.30	3,127.30	04/2018	11/2019	01/2020	2
3	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT SAIL	1,154.18	1,154.18	12/2017	11/2019	01/2020	2
4	CENTRAL DISPATCH YARD RINL	320.66	320.66	08/2018	10/2019	12/2019	2
	PETROLEUM						
5	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY BPCL	4,588.29	5,245.96	08/2018	11/2019	12/2019	1
6	BS-VI PROJECT AT BONGAIGAON REFINERY IOCL	1,222.00	1,222.00	09/2019	02/2020	04/2020	2
7	BS-VI PROJECT AT PANIPAT REFINERY IOCL	3,529.00	3,529.00	07/2019	12/2019	02/2020	2
8	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN OIL	352.56	438.84	03/2017	03/2020	06/2020	3
9	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY IOCL	2,934.40	2,934.40	09/2019	01/2020	04/2020	3
10	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY BPCL	554.00	554.00	02/2020	10/2019	02/2020	4
11	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP IOCL	384.58	384.58	04/2021	04/2020	09/2020	5
12	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II OIL	571.66	571.66	12/2019	12/2019	06/2020	6
13	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY IOCL	429.00	429.00	01/2019	12/2019	06/2020	6
14	MMPL PIPELINE REROUTING PROJECT BPCL	449.58	449.58	12/2019	12/2019	07/2020	7
	POWER						

MoSPI OCMS

List of projects reporting additional delayed Rs.150 Crore and above

(November 2019)

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Antici pated	Original	Last month	This month	
15	SYTEM STRENGTHENING XIII OF SR GRID PGCIL	487.49	639.46	06/2014	11/2019	12/2019	1
16	EASTERN REGION STRENGTHENING SCHEME-V PGCIL	1,364.52	1,891.41	04/2016	11/2019	12/2019	1
17	SOUTHERN REGION STRENGTHENING SCHEME-XXI PGCIL	562.25	562.25	03/2019	11/2019	12/2019	1
18	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI PGCIL	608.24	608.24	04/2019	11/2019	12/2019	1
19	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI PGCIL Central Sector Projects	3,654.00	3,654.00	04/2019	11/2019	12/2019	1
20	TRANSMISSION SYSTEM FOR EVACUTION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY PGCIL Central Sector Projects	186.17	186.17	07/2019	12/2019	01/2020	1
21	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ PGCIL	322.30	322.30	02/2019	12/2019	03/2020	3
22	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII PGCIL	379.95	379.95	12/2019	12/2019	03/2020	3
23	RAMMAM-III HEPP (3X40 MW) NTPC	1,381.84	1,592.34	09/2019	02/2022	05/2024	27
	HEALTH AND FAMILY WELFARE						
24	AIIMS - MOTHER AND CHILD BLOCK HSCC	204.44	270.00	05/2017	05/2020	06/2020	1
25	AIIMS - OPD(NEW) HSCC	293.65	325.00	05/2017	12/2019	01/2020	1
26	NEIGRIHMS SHILLONG MEGHALYA HSCC	363.99	363.99	05/2018	06/2020	07/2020	1
27	HOSPITAL AND TEACHING- AIIMS GUNTUR HSCC Central Sector Projects	601.02	601.02	N.A.	06/2020	07/2020	1
28	HOSPITAL AND TEACHING- AIIMS KALYANI HSCC	651.99	651.99	N.A.	06/2020	07/2020	1
29	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL HSCC Central Sector Projects	355.15	355.15	03/2019	05/2020	07/2020	2
30	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB HITES	703.00	557.48	06/2020	08/2020	10/2020	2
31	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB HSCC	152.95	177.92	02/2018	12/2019	03/2020	3
32	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA HSCC Central Sector Projects	274.19	274.19	03/2019	12/2019	03/2020	3

MoSPI OCMS

List of projects reporting additional delayed Rs.150 Crore and above

(November 2019)

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Antici pated	Original	Last month	This month	
33	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH HSCC Central Sector Projects	272.19	272.54	03/2019	12/2019	03/2020	3
34	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) HITES	785.00	715.06	04/2020	06/2020	10/2020	4
	RAILWAYS						
35	GONDIA-JABALPUR(GC),(SECR) SECR	511.86	1,756.00	04/2020	12/2020	01/2021	1
36	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND SER	148.77	377.00	12/2016	12/2019	01/2020	1
37	NEW BG LINE FROM JAGBANI TO BIRATNAGAR NFR	241.52	373.87	N.A.	03/2021	06/2021	3
38	JHARSUGUDA-BILASPUR 4TH LINE SECR	1,973.00	1,973.64	03/2021	12/2022	03/2023	3
39	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) RVNL	133.41	385.00	03/2009	12/2019	06/2020	6
40	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT SECR	585.93	1,268.32	02/2019	06/2020	12/2020	6
41	ANUPPUR-KATNI SECR	1,370.00	1,370.94	12/2021	12/2021	11/2022	11
42	KATNI - SINGRAULI DOUBLING PROJECT WCR	1,763.93	1,762.94	03/2020	03/2022	03/2023	12
43	PUNE-MIRAJ-LONDA (467 KM) CR	3,627.47	3,627.47	03/2024	03/2022	03/2023	12
44	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) NFR	4,454.17	12,524.00	03/2011	03/2020	03/2022	24
45	RAYADURGA-TUMKUR NL RVNL	2,062.30	2,062.30	N.A.	03/2022	03/2025	36
	ROAD TRANSPORT AND HIGHWAYS						
46	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 NHAI	574.28	537.16	07/2018	10/2019	11/2019	1
47	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 NHAI	248.97	248.97	05/2019	12/2019	01/2020	1
48	REHABILITATION AND UPGRADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE MoRTH	208.50	208.50	11/2019	11/2019	12/2019	1
49	2 LANING WITH PS OF GULABPURA - UNIARA NHAI	597.00	597.00	10/2017	01/2020	03/2020	2
50	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II NHAI	795.76	622.00	N.A.	10/2019	12/2019	2

MoSPI OCMS

List of projects reporting additional delayed Rs.150 Crore and above

(November 2019)

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Antici pated	Original	Last month	This month	
51	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I NHAI	794.30	622.00	N.A.	10/2019	12/2019	2
52	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM NHAI	1,232.21	1,087.00	N.A.	03/2020	05/2020	2
53	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH MoRTH	196.52	196.52	10/2019	10/2019	12/2019	2
54	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO MoRTH	208.88	208.88	10/2019	10/2019	12/2019	2
55	6-LANING OF DHANKUNI-KHARAGPUR SECTION NHAI PPP (BOT)	1,396.18	1,396.18	09/2014	12/2019	03/2020	3
56	DELHI AGRA APPROVED LENGTH 180.0 KM NHAI PPP (BOT)	1,928.22	2,945.00	04/2015	03/2020	06/2020	3
57	FOUR LANING OF YADGIRI - WARANGAL NHAI	1,423.96	897.03	11/2018	12/2019	03/2020	3
58	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ MoRTH	248.83	248.83	03/2019	12/2019	03/2020	3
59	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION MoRTH	300.00	300.00	05/2019	12/2019	03/2020	3
60	4-LANNING OF OTTANCHATRAM BYPASS NHAI Central Sector Projects	244.27	244.27	09/2017	12/2019	04/2020	4
61	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT MoRTH	359.27	359.27	05/2019	08/2019	12/2019	4
62	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 MoRTH	249.50	249.50	05/2019	11/2019	03/2020	4
63	4-LANING OF FARAKA-RAIGANJ NHAI PPP (BOT)	1,078.84	1,078.84	08/2013	12/2019	05/2020	5
64	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 NHAI PPP (BOT)	972.50	972.50	07/2017	10/2019	03/2020	5
65	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I NHAI	1,100.19	1,145.31	N.A.	12/2019	05/2020	5
66	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) NHAI	1,388.34	2,587.50	09/2019	09/2019	03/2020	6
67	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM MoRTH	877.79	877.79	06/2019	06/2020	12/2020	6
68	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS MoRTH	247.25	247.25	03/2019	09/2019	03/2020	6

MoSPI OCMS

List of projects reporting additional delayed Rs.150 Crore and above

(November 2019)

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Antici pated	Original	Last month	This month	
69	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 MoRTH	170.57	170.57	11/2020	11/2020	05/2021	6
70	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 MoRTH	376.25	376.25	08/2017	08/2019	02/2020	6
71	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON MoRTH	298.32	298.32	02/2019	12/2019	06/2020	6
72	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD MoRTH	319.28	319.28	08/2017	08/2019	03/2020	7
73	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER NHAI	648.32	512.72	03/2020	07/2019	03/2020	8
74	4-LANING OF BRAHAMPORE-FARAKA NHAI PPP (BOT)	998.79	998.79	08/2013	06/2020	03/2021	9
75	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU MoRTH	372.68	372.68	02/2017	02/2019	12/2019	10
76	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 MoRTH	290.15	290.15	05/2017	05/2019	03/2020	10
77	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 MoRTH	1,069.59	1,069.59	10/2019	10/2019	12/2020	14
78	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 MoRTH	263.45	263.45	09/2017	09/2019	12/2020	15
79	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 MoRTH	444.84	444.84	09/2016	09/2018	03/2020	18
80	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 MoRTH	386.09	386.09	05/2016	05/2018	12/2019	19
81	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT MoRTH	348.95	348.95	08/2016	08/2018	03/2020	19
82	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD MoRTH	350.61	350.61	01/2017	07/2018	04/2020	21
83	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O MoRTH	995.09	995.09	05/2016	05/2018	07/2020	26
84	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES MoRTH EPC	271.45	271.45	10/2015	10/2017	01/2020	27

MoSPI OCMS

List of projects reporting additional delayed Rs.150 Crore and above

(November 2019)

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Antici pated	Original	Last month	This month	
85	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 MoRTH	333.21	355.89	12/2015	12/2016	12/2020	48
	URBAN DEVELOPMENT						
86	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB CPWD	388.00	488.28	05/2017	11/2019	12/2019	1
87	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN CPWD	549.31	559.47	07/2019	03/2020	04/2020	1
88	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI CPWD	223.37	223.37	07/2020	09/2020	11/2020	2
89	PUNE METRO RAIL PROJECT (PHASE 1) MMRC	11,420.00	11,420.00	11/2021	01/2022	03/2022	2
90	KOCHI METRO RAIL PROJECT KMRCL	5,181.79	5,687.79	07/2017	12/2019	03/2020	3
91	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR CPWD	790.79	800.00	03/2022	03/2022	06/2022	3
92	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI CPWD	209.00	209.00	10/2019	03/2020	07/2020	4
93	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITIUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST CPWD	150.29	150.29	03/2020	03/2020	03/2021	12

TABLE-29

Sector wise analysis of projects Rs.150 Crore and above					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	67,120.00	671,20.00	80,348.00	47,067.84
CIVIL AVIATION	13	8,607.51	86,07.51	8,734.44	1,357.47
COAL	107	1,04,997.33	1,054,21.52	1,07,962.20	37,121.19
FERTILISERS	5	1,299.07	12,99.07	1,310.72	840.40
INFORMATION AND BROADCASTING	3	969.43	9,69.43	969.43	29.80
MINES	5	7,078.62	70,75.17	7,075.17	653.40
STEEL	9	26,228.23	338,43.23	33,485.23	23,942.27
PETROLEUM	150	2,49,934.93	2,640,39.11	2,65,162.48	99,549.90
POWER	70	2,79,157.68	3,116,77.01	3,53,357.42	2,22,975.18
HEAVY INDUSTRY	1	1,554.00	15,54.00	1,554.00	665.35
HEALTH AND FAMILY WELFARE	21	9,473.56	95,93.56	9,444.06	4,742.85
RAILWAYS	312	4,59,394.75	5,899,96.53	6,67,846.32	1,99,661.27
ROAD TRANSPORT AND HIGHWAYS	866	5,13,255.97	5,384,45.99	5,27,964.98	2,90,564.48
SHIPPING AND PORTS	1	4,200.00	53,69.18	5,369.18	1,662.16
TELECOMMUNICATIONS	4	16,095.23	161,03.53	27,333.53	12,884.57
URBAN DEVELOPMENT	75	2,63,975.80	2,650,53.71	2,70,607.62	90,163.27
WATER RESOURCES	51	27,288.45	272,88.45	72,686.28	16,450.19
HUMAN RESOURCE DEPARTMENT	1	484.32	4,84.32	626.26	0.00
Grand total	1698	20,41,114.88	22,53,941.32	24,41,837.32	10,50,331.59

Graphical Presentation of All Projects w.r.t. Original Schedule

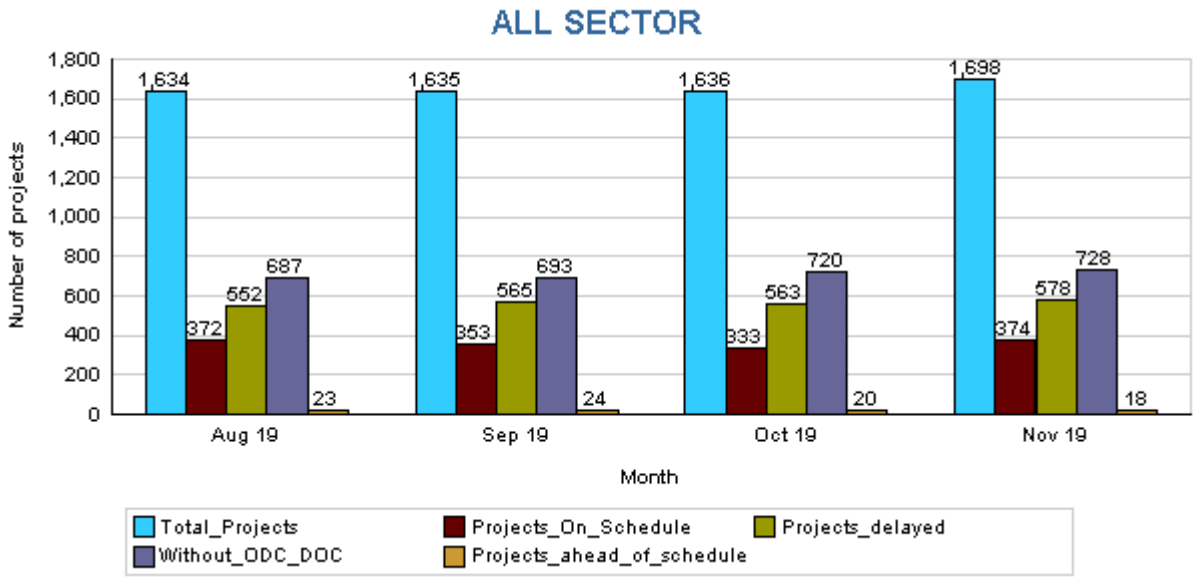

Break-up of 578 Delayed projects in November 2019

Delay in Months | 1-12 | 13-24 | 25-60 | 60 and Above

Graphical Presentation of All Projects w.r.t. Original Schedule

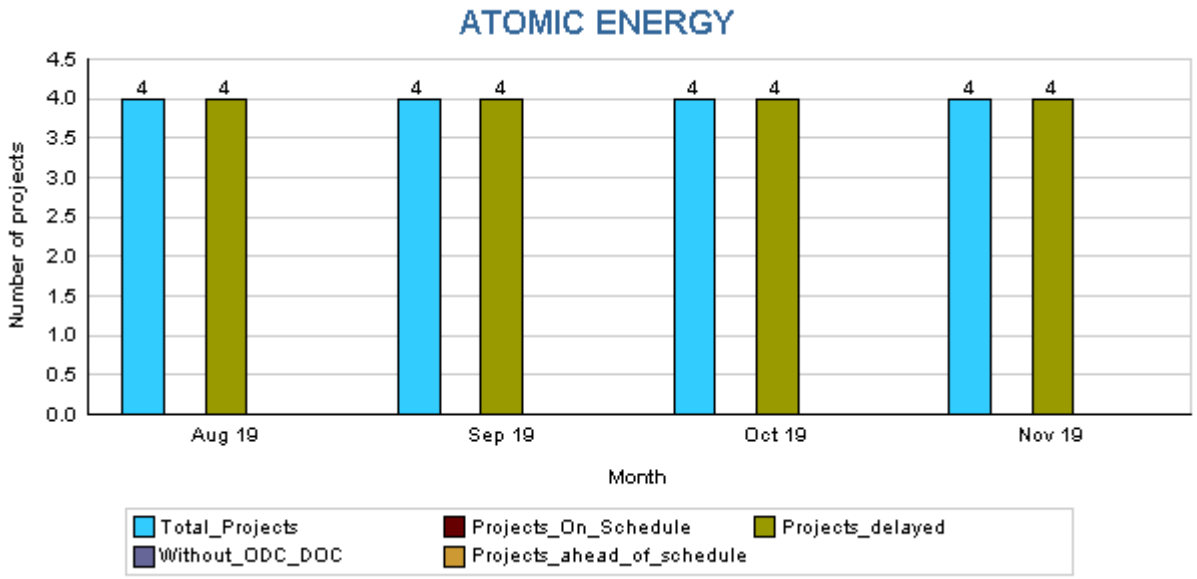

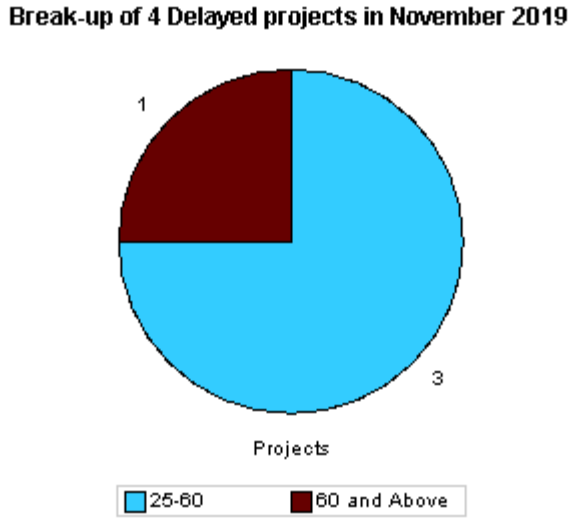

Graphical Presentation of All Projects w.r.t. Original Schedule

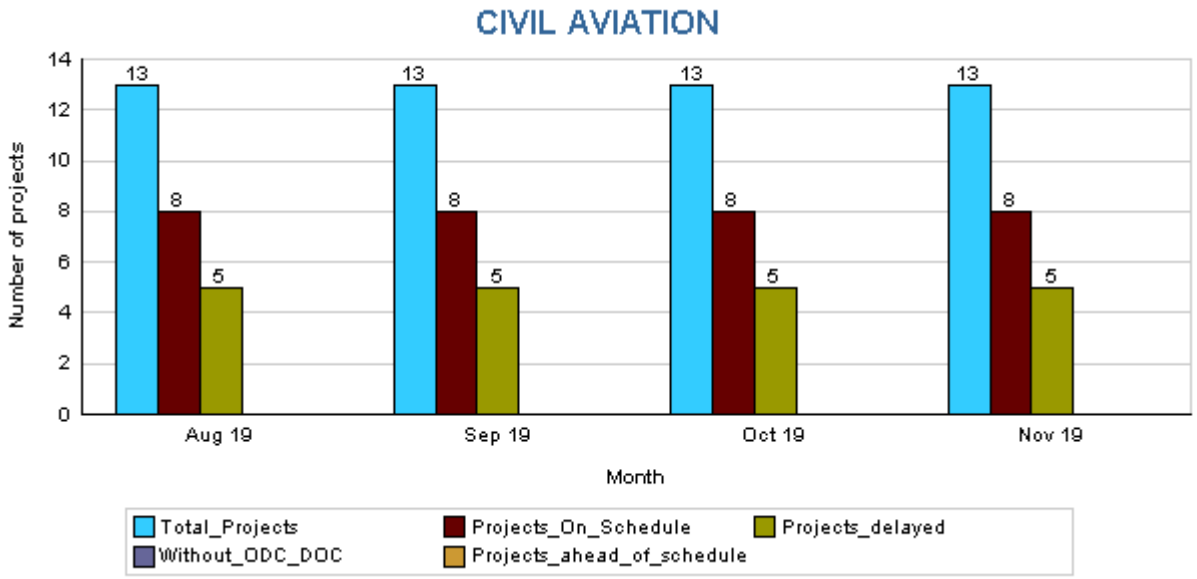

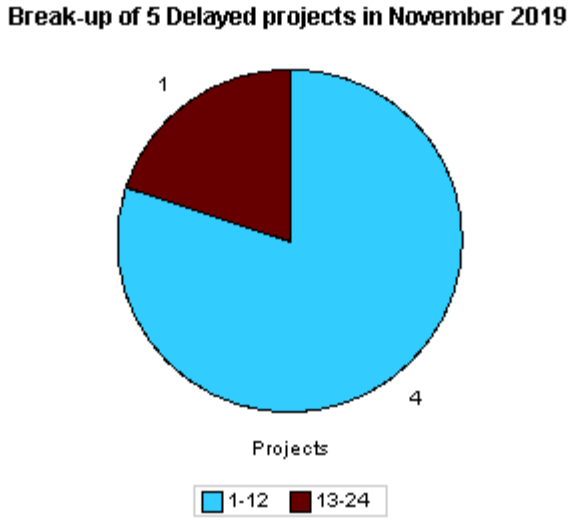

Graphical Presentation of All Projects w.r.t. Original Schedule

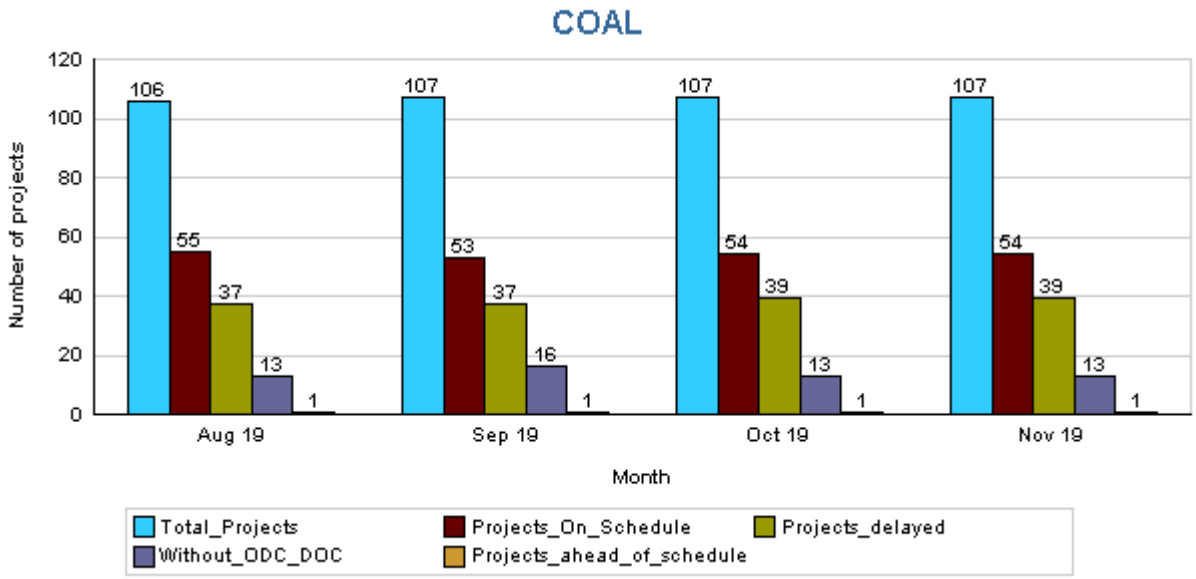

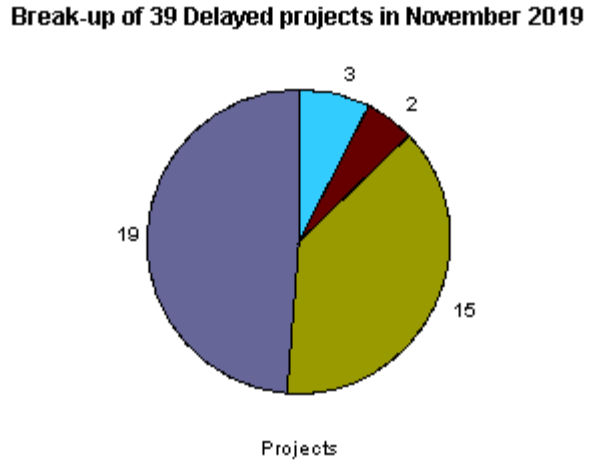

Graphical Presentation of All Projects w.r.t. Original Schedule

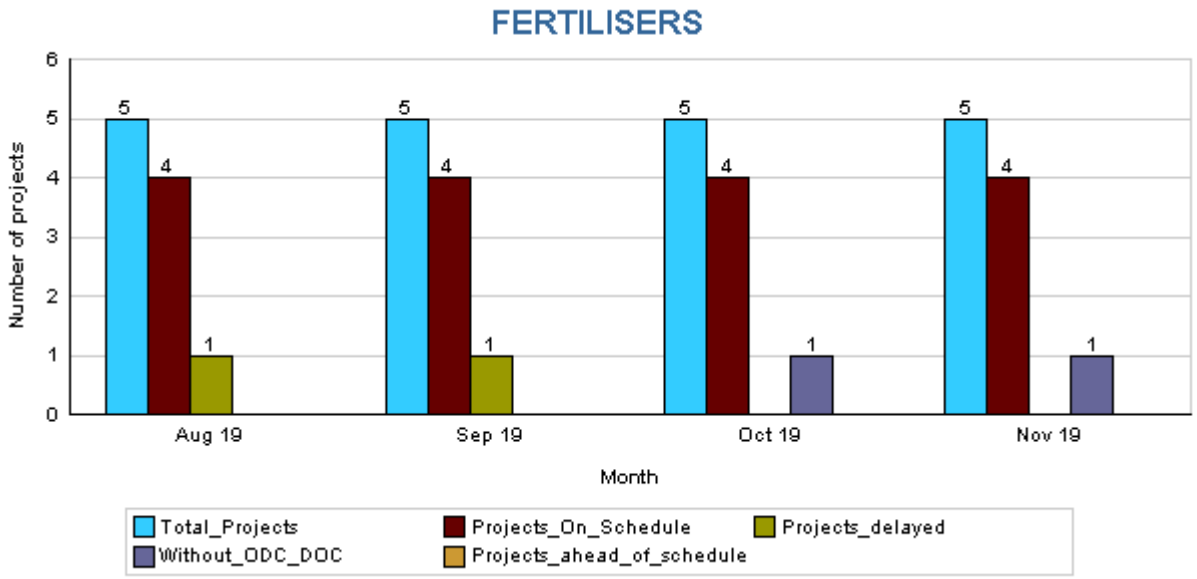

Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

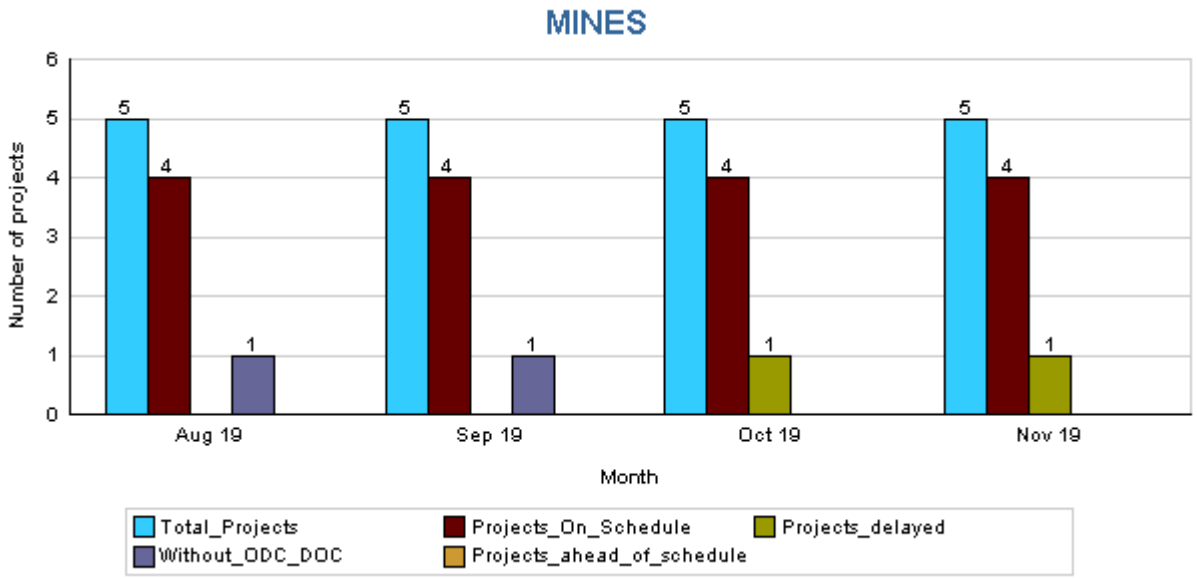

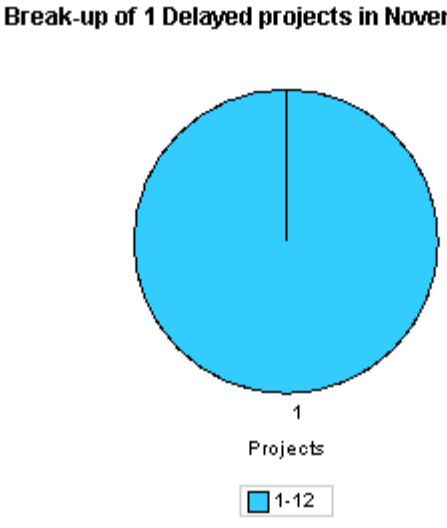

Graphical Presentation of All Projects w.r.t. Original Schedule

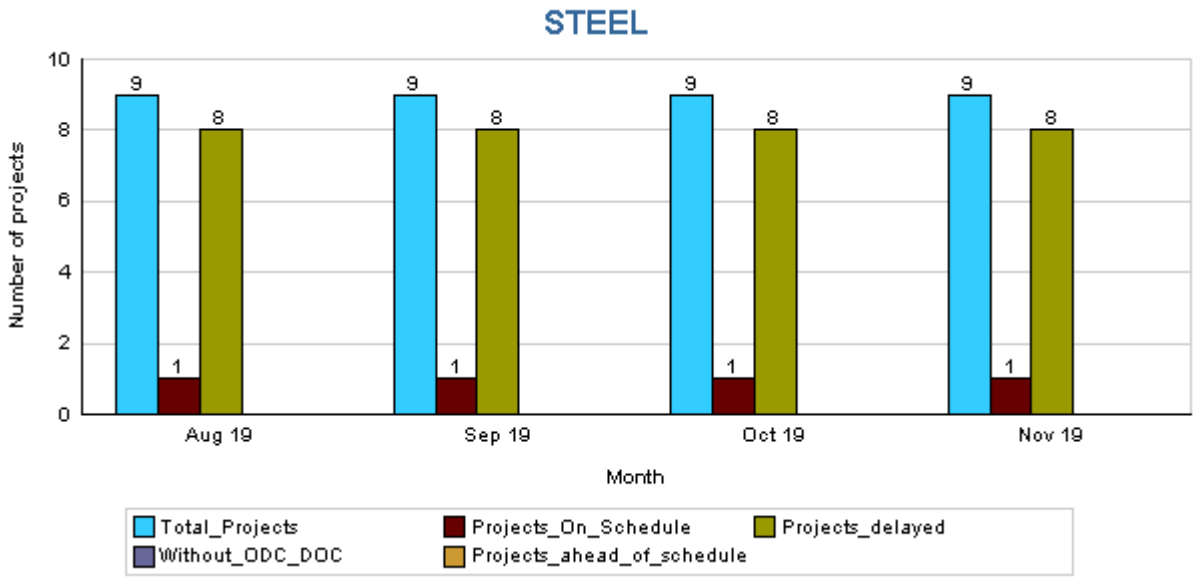

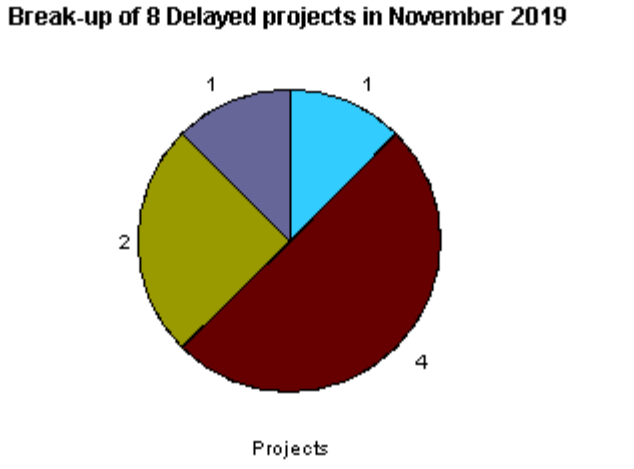

Graphical Presentation of All Projects w.r.t. Original Schedule

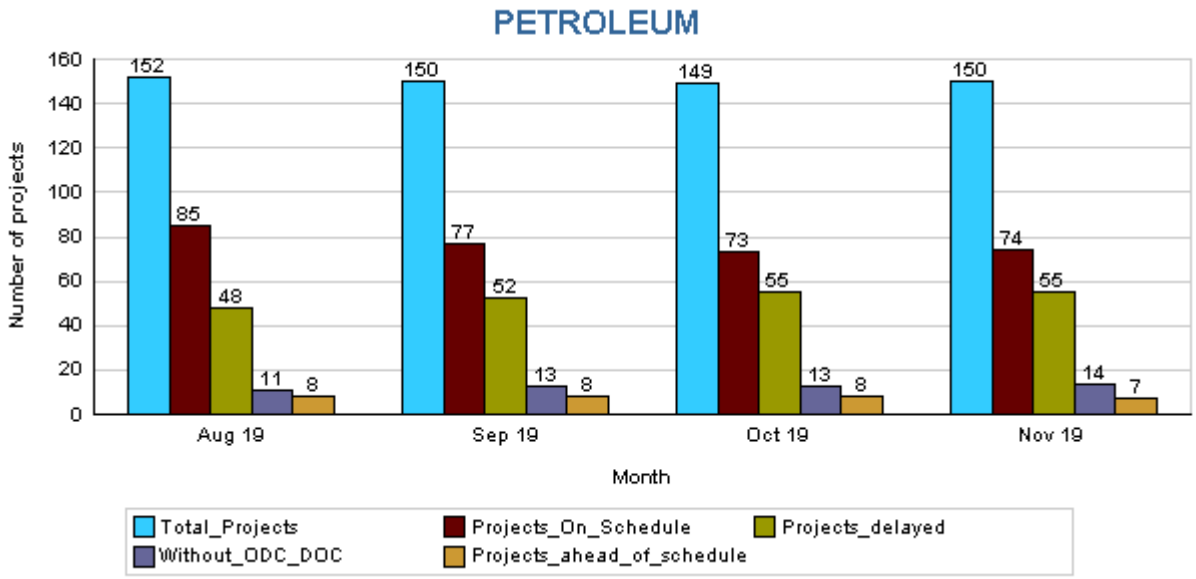

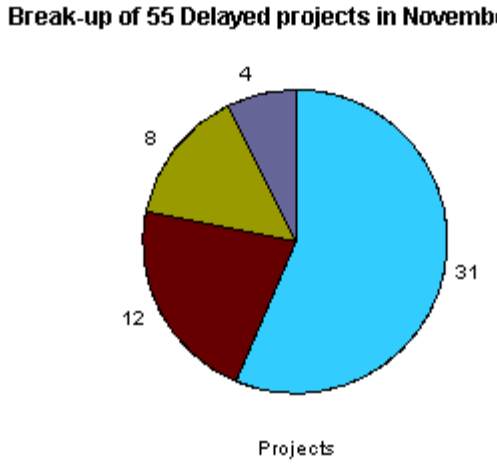

Graphical Presentation of All Projects w.r.t. Original Schedule

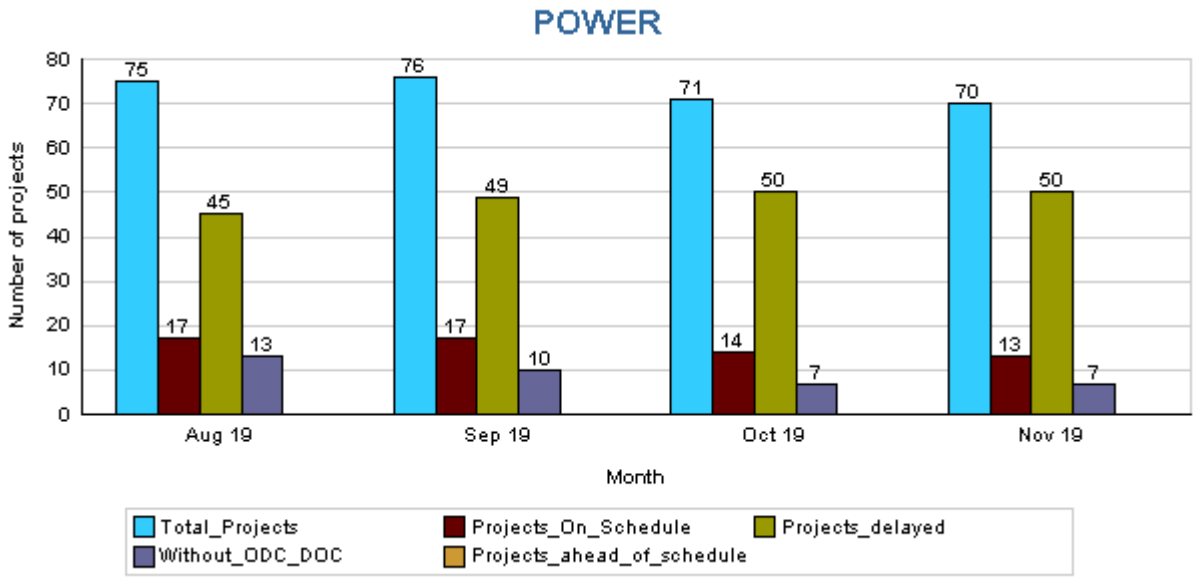

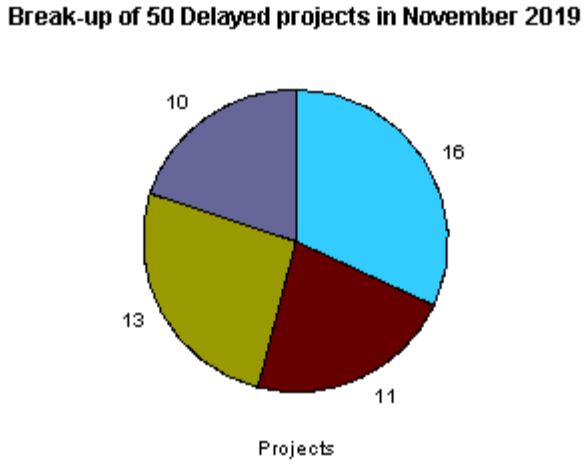

Graphical Presentation of All Projects w.r.t. Original Schedule

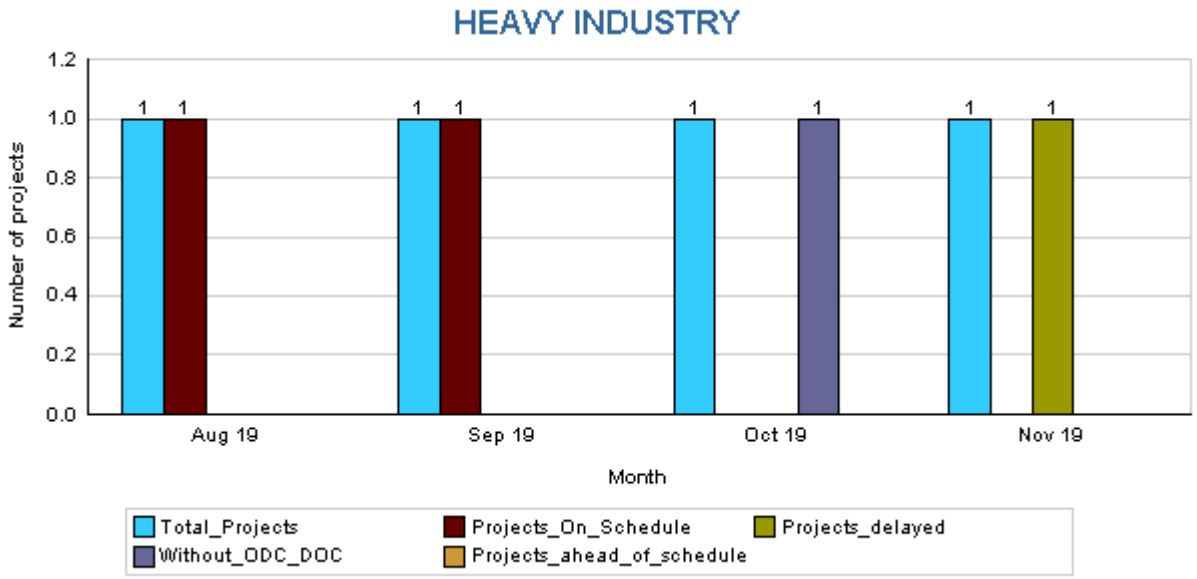

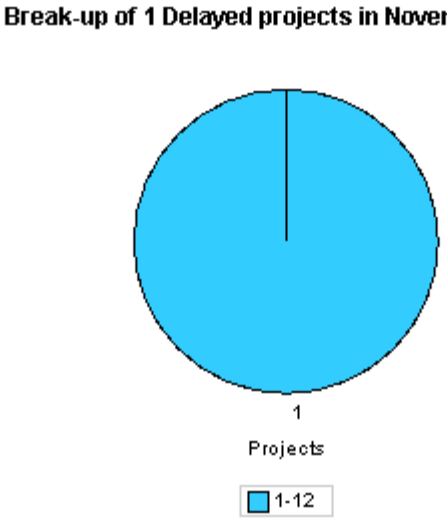

Graphical Presentation of All Projects w.r.t. Original Schedule

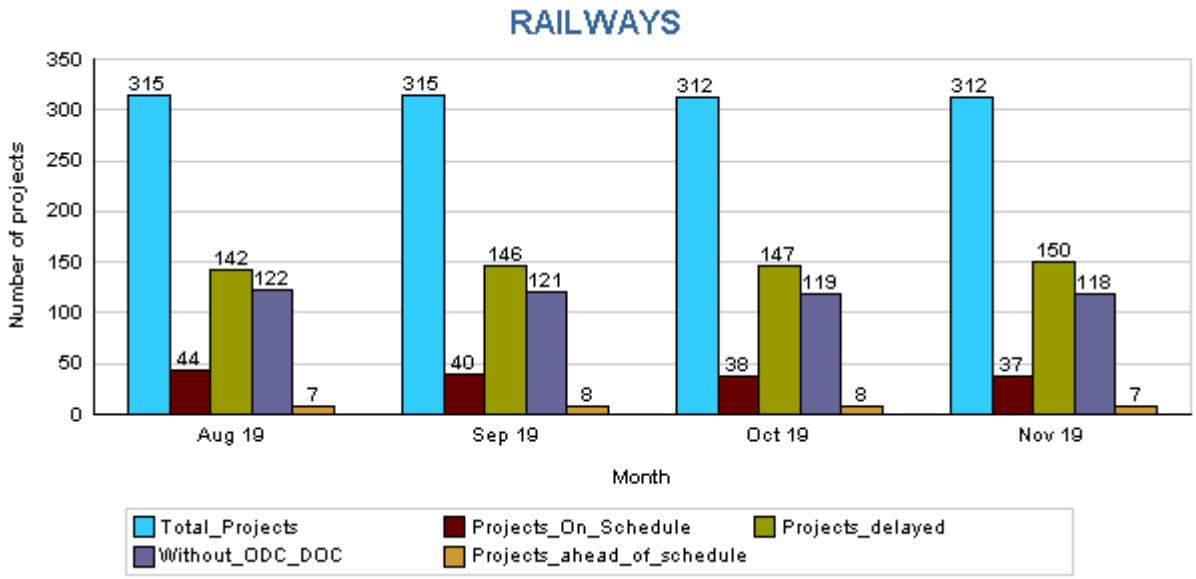

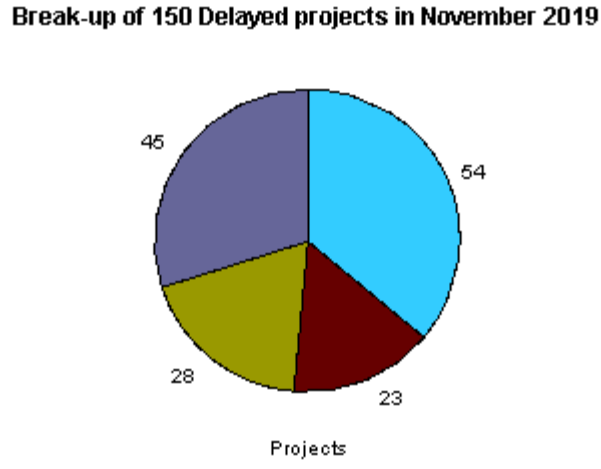

Graphical Presentation of All Projects w.r.t. Original Schedule

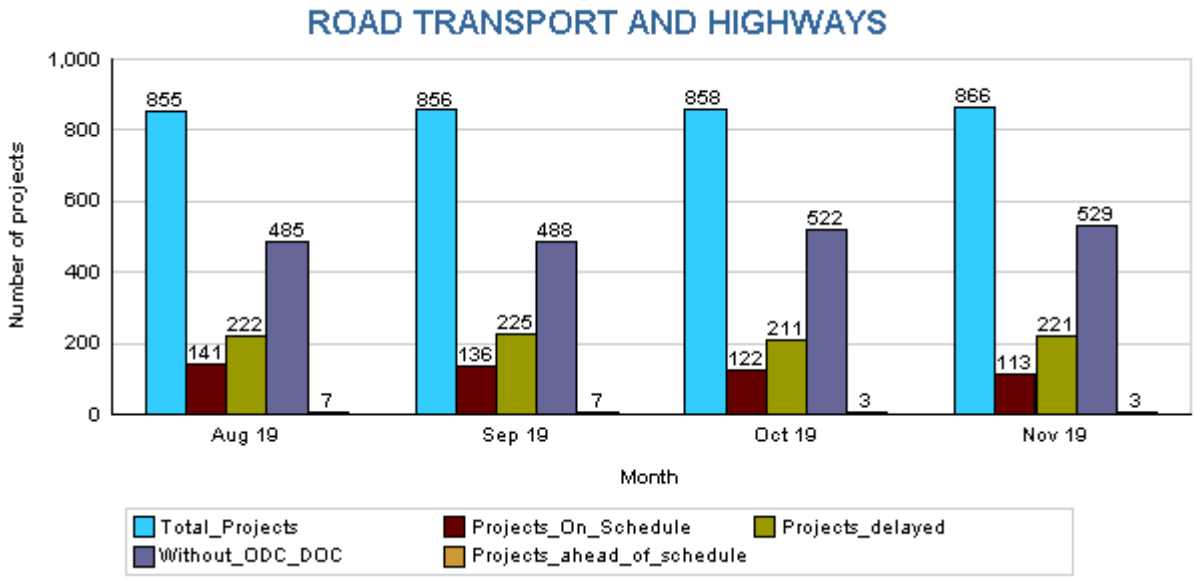

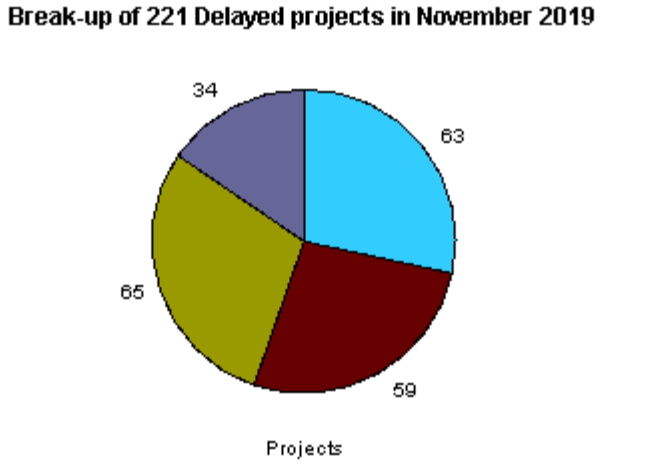

Graphical Presentation of All Projects w.r.t. Original Schedule

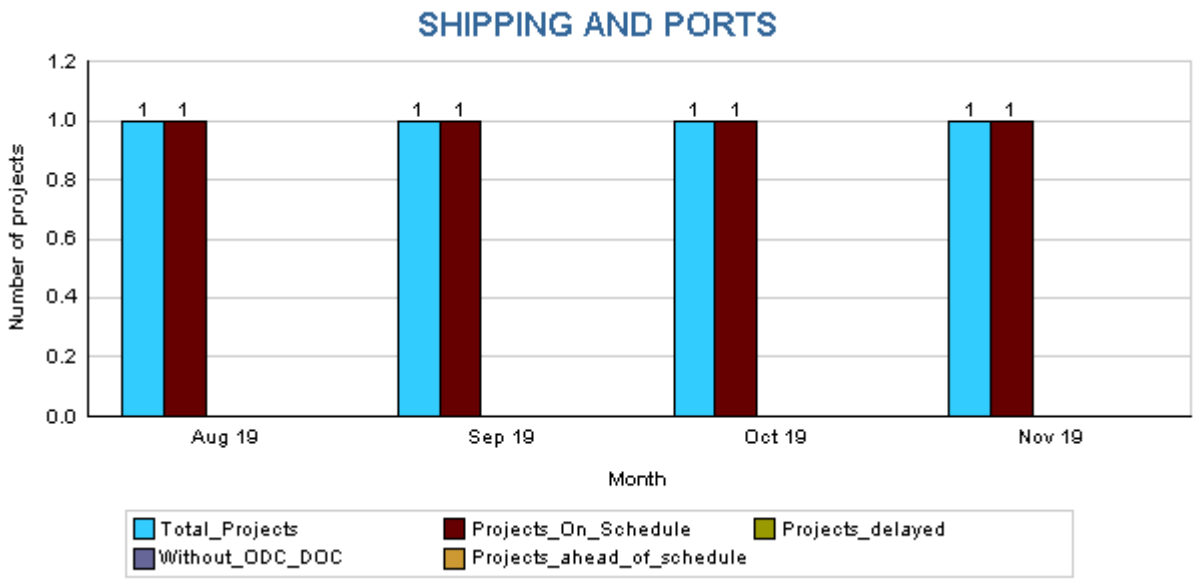

Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

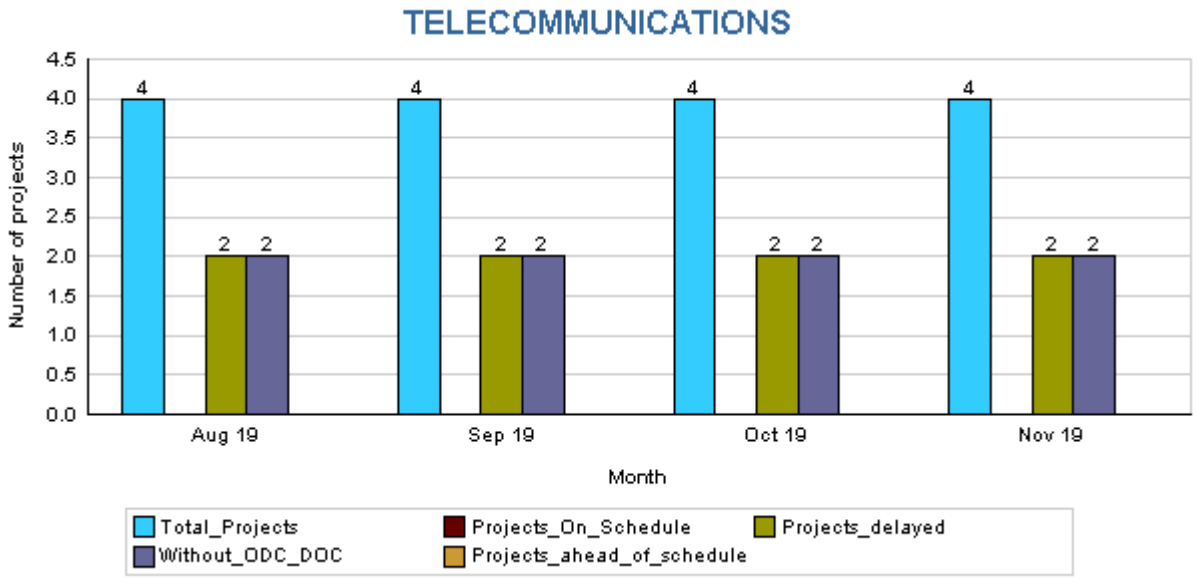

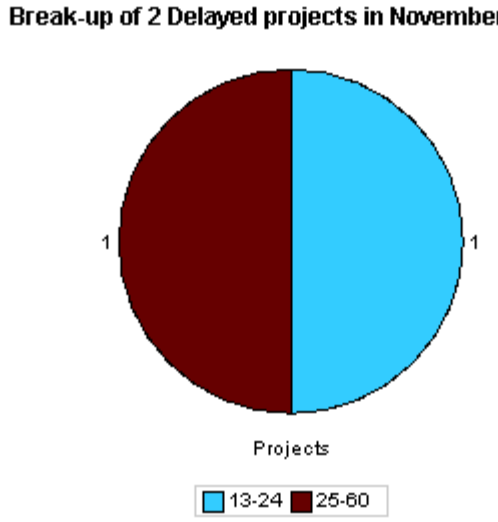

Graphical Presentation of All Projects w.r.t. Original Schedule

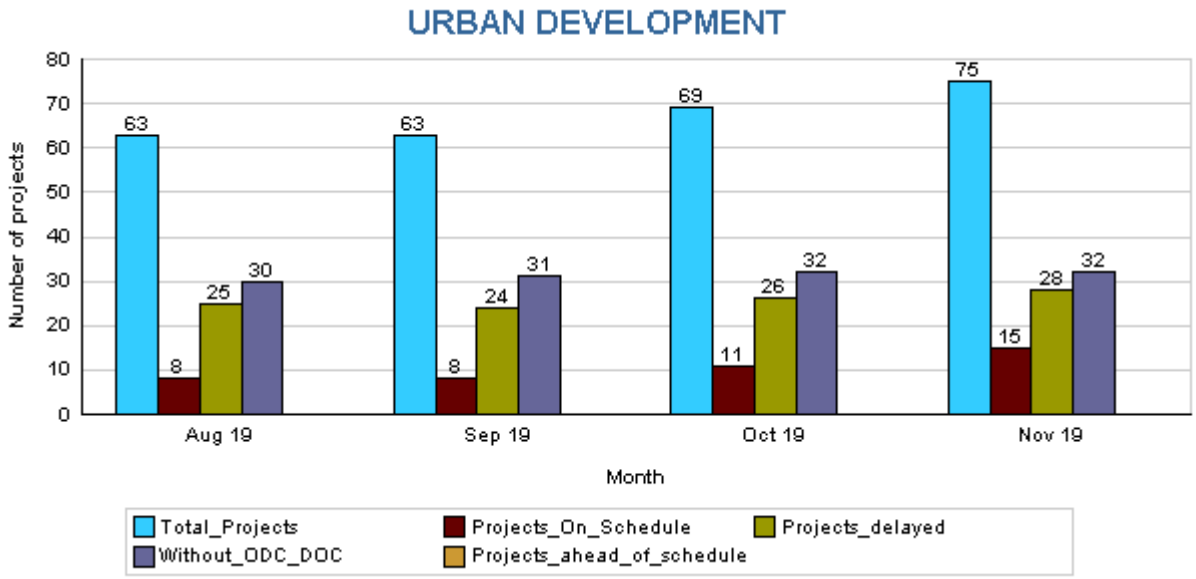

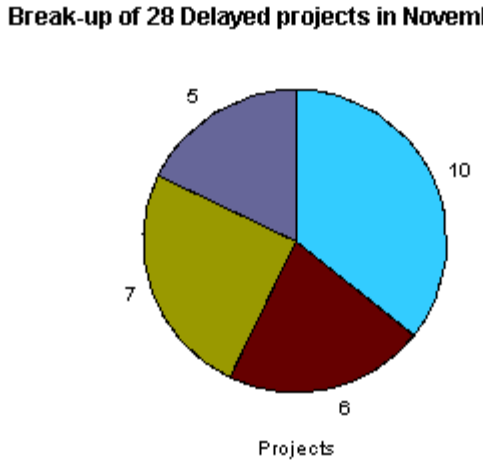

Table-30

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	ATOMIC ENERGY								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT ,	10/2009	11,459.00 -	16,580.00	14,137.00	12/2015 -	06/2020	54(O) -	53/70
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN ,	10/2009	12,320.00 -	17,079.00	11,387.00	12/2016 -	12/2020	48(O) -	40/68
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI 500 MWE) - [020100044]BHAVNI,TAMIL NADU ,	09/2003	3,492.00 -	6,840.00	5,837.84	09/2010 -	10/2021	133(O) -	83/87
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU , Central Sector Projects	03/2013	39,849.00 -	39,849.00	15,706.00	11/2020 -	11/2023	36(O) -	23/76
	Total		67,120.00 -	80,348.00	47,067.84				199/301
	CIVIL AVIATION								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT PORTBLAIR - [N04000073]AAI,A & N ISLANDS ,	10/2013	314.61 -	441.33	85.79	09/2018 -	06/2020	21(O) -	0/0
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM ,	12/2016	859.86 -	860.00	232.44	03/2021 -	03/2021	0(O) -	0/0
7	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES PHASE I AND II - [N04000082]AAI,BIHAR ,	05/2018	539.20 -	539.20	25.64	10/2022 -	10/2022	0(O) -	0/0
8	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA BCAS AAIB AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI ,	11/2016	233.38 -	233.38	84.73	04/2020 -	12/2020	8(O) -	0/0
9	CONSTRUCTION OF TERMINAL BUILDING & ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]AAI,JAMMU AND KASHMIR ,	07/2018	323.19 -	323.19	10.14	09/2021 -	09/2021	0(O) -	0/0
10	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING RECONSTRUCTION OF OLD TERMINAL BUILDING MODIFICAT - [N04000079]AAI,MAHARASHTRA ,	03/2017	358.89 -	358.89	29.73	04/2021 -	04/2021	0(O) -	0/0
11	MODERNIZATION OF CHENNAI AIRPORT PHASE II CHENNAI - [N04000074]AAI,TAMIL NADU ,	06/2018	2,467.00 -	2,467.00	213.17	02/2022 -	08/2022	6(O) -	0/0
12	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI,TAMIL NADU ,	08/2018	951.28 -	951.28	71.55	10/2021 -	10/2021	0(O) -	0/0
13	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI,TRIPURA ,	09/2015	338.93 -	339.00	213.50	06/2019 -	12/2019	6(O) -	0/0
14	CCS INTERNATIONAL AIRPORT LUCKNOW - [N04000077]AAI,UTTAR PRADESH ,	06/2018	1,383.00 -	1,383.00	210.62	09/2021 -	09/2021	0(O) -	0/0

MoSPI OCMS

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
15	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT DEHRADUN - [N04000085]AAI,UTTARAKHAND ,	07/2018	353.27 -	353.27	114.29	09/2020 -	09/2020	0(O) -	0/0
16	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA - [N04000080]AAI,WEST BENGAL ,	01/2016	219.91 -	219.91	65.45	03/2020 -	12/2020	9(O) -	0/0
17	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT KOLKATA - [N04000081]AAI,WEST BENGAL ,	01/2019	264.99 -	264.99	.42	11/2021 -	11/2021	0(O) -	0/0
	Total		8,607.51 -	8,734.44	1,357.47				0/0
	COAL								
18	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL,CHHATISGARH ,	06/2010	11,816.40 -	11,816.40	2,891.13	03/2023 -	03/2023	0(O) -	14/19
19	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH ,	08/2013	7,612.33 -	7,612.33	2,116.58	03/2023 -	03/2023	0(O) -	7/21
20	PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATISGARH ,	11/2014	1,624.59 -	1,624.59	6.50	03/2023 -	03/2023	0(O) -	1/12
21	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH ,	09/2008	152.43 -	459.49	193.35	03/2015 -	03/2020	60(O) -	6/10
22	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH ,	07/2008	178.44 -	178.44	2.92	03/2014 -	03/2020	72(O) -	2/8
23	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH ,	12/2009	321.50 -	321.50	197.28	03/2014 -	03/2021	84(O) -	0/5
24	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH ,	04/2012	258.56 -	258.56	181.44	03/2016 -	03/2020	48(O) -	4/7
25	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH ,	12/2013	610.63 -	610.63	105.36	03/2022 -	03/2022	0(O) -	2/10
26	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH ,	05/2014	164.49 -	164.49	82.91	03/2020 -	03/2020	0(O) -	5/9
27	AMERA OC RCE - [N06000123]SECL,CHHATISGARH ,	02/2015	335.97 -	335.97	51.21	03/2018 -	03/2020	24(O) -	1/7
28	AMGAON OPENCAST PROJECT RCE - [N06000135]SECL,CHHATISGARH ,	07/2015	316.10 -	316.10	86.43	03/2020 -	03/2020	0(O) -	1/6
29	DURGAPUR OPENCAST PROJECT - [N06000136]SECL,CHHATISGARH ,	02/2015	916.24 -	916.24	4.11	03/2023 -	03/2023	0(O) -	1/11
30	MADANNAGAR OPENCAST PROJECT - [N06000140]SECL,CHHATISGARH ,	10/2015	1,875.32 -	1,875.32	.00	03/2024 -	03/2024	0(O) -	1/5
31	VIJAY WEST OPENCAST PROJECT - [N06000158]SECL,CHHATISGARH ,	05/2017	976.95 -	976.95	75.96	03/2026 -	03/2026	0(O) -	0/1
32	MAHAMAYA OPENCAST PROJECT - [N06000164]SECL,CHHATISGARH ,	05/2018	410.26 -	410.26	9.53	03/2026 -	03/2026	0(O) -	0/1
33	JHIRIA WEST OPENCAST PROJECT - [N06000166]SECL,CHHATISGARH ,	11/2018	389.97 -	389.97	.00	03/2026 -	03/2026	0(O) -	1/1
34	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND ,	08/2008	706.40 -	706.40	432.82	07/2012 -	03/2022	116(O) -	6/6
35	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND ,	08/2007	163.51 -	163.51	106.41	03/2011 -	03/2021	120(O) -	6/6
36	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND ,	08/2008	264.68 -	264.68	181.17	03/2012 -	03/2021	108(O) -	5/6

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
37	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND ,	12/2009	510.85 -	510.85	365.62	03/2016 -	03/2021	60(O) -	5/6
38	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND ,	06/2009	162.46 -	162.46	90.75	03/2014 -	03/2021	84(O) -	6/6
39	MURAIDIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND ,	02/2011	339.88 -	339.88	12.08	04/2014 -	-	-	4/7
40	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND ,	08/2011	1,230.27 -	1,230.27	401.81	04/2015 04/2022	04/2022	84(O) 0	2/6
41	AMRAPALI OC(12MTY) - [N06000103]CCL,JHARKHAND ,	02/2012	858.11 -	858.11	187.61	03/2020 -	03/2020	0(O) -	6/7
42	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND ,	02/2014	555.52 -	555.52	5.24	03/2021 -	03/2021	0(O) -	0/2
43	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND ,	08/2011	988.35 -	988.35	45.26	04/2017 -	-	-	1/3
44	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND ,	08/2010	289.45 -	289.45	260.10	05/2014 03/2020	03/2020	70(O) 0	0/8
45	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND ,	10/2012	269.82 -	269.82	180.83	04/2014 -	01/2020	69(O) -	0/10
46	HURA - C OC (3 MTY) - [N06000143]ECL,JHARKHAND ,	10/2015	359.69 -	359.69	84.91	03/2022 -	03/2022	0(O) -	4/22
47	CHITRA EAST (RCE) OCP - [N06000169]ECL,JHARKHAND ,	08/2018	513.98 -	513.98	92.51	03/2024 -	03/2024	0(O) -	0/16
48	NORTH URIMARI EXPANSION OCP - [N06000182]CCL,JHARKHAND ,	03/2019	1,553.06 -	1,553.06	203.46	03/2023 -	03/2023	0(O) -	0/1
49	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH ,	08/2015	1,186.64 -	203.82	123.05	03/2023 -	03/2021	-24(O) -	3/10
50	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH ,	02/2015	481.60 -	481.60	.00	03/2023 -	03/2023	0(O) -	2/9
51	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH ,	12/2014	357.80 -	357.80	104.66	03/2021 -	03/2021	0(O) -	3/10
52	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH ,	12/2014	371.04 -	371.04	48.13	03/2021 -	03/2021	0(O) -	3/8
53	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH ,	07/2015	231.92 -	231.92	.00	03/2022 -	03/2022	0(O) -	1/8
54	MALACHUA OPENCAST PROJECT - [N06000139]SECL,MADHYA PRADESH ,	10/2015	488.33 -	488.33	27.33	03/2023 -	03/2023	0(O) -	0/4
55	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH ,	03/2016	869.44 -	869.44	116.75	03/2021 -	03/2021	0(O) -	2/5
56	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH ,	07/2016	409.87 -	409.87	19.05	03/2022 -	03/2022	0(O) -	0/0
57	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH , Central Sector Projects	05/2017	1,783.09 -	1,783.09	267.80	03/2021 -	03/2021	0(O) -	2/9
58	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL,MADHYA PRADESH ,	11/2017	1,255.17 -	1,255.17	95.24	03/2022 -	03/2022	0(O) -	1/9
59	SEMARIA OPENCAST PROJECT - [N06000176]NCL,MADHYA PRADESH ,	05/2019	396.58 -	396.58	.00	03/2026 -	03/2026	0(O) -	1/5
60	VISHNUPURI UG TO OC MINE - [N06000178]WCL,MADHYA PRADESH ,	07/2018	195.57 -	195.57	2.94	03/2025 -	03/2025	0(O) -	0/7
61	GANDHIGRAM UG MINE - [N06000183]WCL,MADHYA PRADESH ,	08/2019	414.16 -	414.16	.01	03/2026 -	03/2026	0(O) -	0/7

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
62	BLOCK-B EXPANSION OPENCAST PROJECT - [N06000184]NCL,MADHYA PRADESH ,	07/2019	998.71 -	998.71	.00	03/2023 -	03/2023	0(O) -	0/7
63	PENGANGA OCP(REVISED) - [N06000066]WCL,MAHARASHTRA ,	09/2014	441.82 -	441.82	215.48	03/2020 -	03/2020	0(O) -	8/11
64	DINESH OCP - [N06000118]WCL,MAHARASHTRA ,	11/2014	611.16 -	611.16	413.02	03/2020 -	03/2020	0(O) -	3/8
65	BHANEGAON OC - [N06000121]WCL,MAHARASHTRA ,	02/2015	187.94 -	409.68	127.70	03/2023 -	03/2023	0(O) -	7/11
66	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA ,	05/2015	295.56 -	295.56	120.81	03/2019 -	-	-	10/13
67	SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA ,	06/2015	205.49 -	205.49	117.56	03/2020 -	03/2020	0(O) -	6/10
68	AMALGAMATED PAUNI-II III OC MINE - [N06000131]WCL,MAHARASHTRA ,	06/2015	483.69 -	483.69	219.00	03/2021 -	03/2021	0(O) -	3/6
69	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL,MAHARASHTRA ,	08/2015	727.28 -	727.28	260.88	03/2025 -	03/2025	0(O) -	6/13
70	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA ,	08/2015	288.90 -	333.43	27.21	03/2023 -	03/2024	12(O) -	3/10
71	KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA ,	11/2015	277.65 -	313.34	117.85	03/2021 -	03/2024	36(O) -	3/6
72	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]WCL,MAHARASHTRA ,	11/2015	498.42 -	498.42	189.52	03/2020 -	03/2020	0(O) -	2/6
73	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA ,	02/2016	198.68 -	198.68	185.01	03/2019 -	-	-	3/9
74	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA ,	02/2016	304.52 -	304.52	153.54	03/2019 -	-	-	4/8
75	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA ,	03/2017	362.73 -	362.73	322.07	03/2020 -	03/2020	0(O) -	0/0
76	SAONER I UG TO OC PHASE I - [N06000177]WCL,MAHARASHTRA ,	11/2016	162.10 -	162.10	50.64	03/2022 -	03/2022	0(O) -	0/6
77	UKNI DEEP OC - [N06000179]WCL,MAHARASHTRA ,	11/2018	318.14 -	318.14	143.90	03/2021 -	03/2021	0(O) -	0/4
78	BELLORA-NAIGAON DEEP OC - [N06000180]WCL,MAHARASHTRA ,	11/2018	252.71 -	252.71	45.09	03/2021 -	03/2021	0(O) -	0/3
79	GAURI DEEP OC - [N06000181]WCL,MAHARASHTRA ,	10/2016	164.96 -	164.96	93.86	03/2019 -	-	-	1/3
80	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]WCL,MULTI STATE ,	08/2016	319.76 -	319.76	238.99	03/2022 -	03/2022	0(O) -	0/3
81	DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE ,	09/2016	458.07 -	458.07	20.86	03/2022 -	03/2022	0(O) -	1/12
82	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE ,	02/2017	328.00 -	328.00	167.00	03/2021 -	03/2021	0(O) -	2/6
83	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA ,	01/2005	302.96 -	302.96	272.73	03/2010 -	03/2020	120(O) -	10/10
84	BHUBANESWARI OCP MCL (20.0 MTY) - [N06000034]MCL,ODISHA ,	12/2007	490.10 -	490.10	508.91	03/2017 -	03/2021	48(O) -	11/12
85	KANIHA OCP MCL (10.0 MTY) - [N06000035]MCL,ODISHA ,	12/2007	457.77 -	457.77	539.88	03/2013 -	03/2022	108(O) -	8/9
86	BALRAM OCP EXTENSION MCL 8.00 MTY - [N06000044]MCL,ODISHA ,	12/2007	172.08 -	172.08	347.93	03/2010 -	03/2022	144(O) -	3/4

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
87	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA ,	08/2008	207.28 -	207.28	296.22	03/2012 -	03/2021	108(O) -	5/7
88	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA ,	11/2008	479.53 -	479.53	389.52	03/2013 -	03/2021	96(O) -	6/9
89	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA ,	05/2014	479.15 -	479.15	211.71	03/2019 -	03/2024	60(O) -	2/9
90	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA ,	05/2014	3,756.36 -	3,756.36	1,205.32	03/2026 -	03/2026	0(O) -	7/15
91	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA ,	05/2014	337.66 -	337.66	188.48	03/2019 -	03/2020	12(O) -	5/6
92	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA ,	06/2014	289.03 -	289.03	.00	03/2018 -	03/2021	36(O) -	5/6
93	GARJANBAHAL OCP - [N06000117]MCL,ODISHA ,	11/2014	1,375.38 -	1,375.38	445.39	03/2021 -	03/2021	0(O) -	6/9
94	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]MCL,ODISHA ,	05/2018	2,434.75 -	2,434.75	123.99	03/2027 -	03/2027	0(O) -	2/12
95	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]MCL,ODISHA ,	11/2018	2,838.87 -	2,838.87	1,157.99	03/2029 -	03/2029	0(O) -	0/9
96	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN , Central Sector Projects	03/2015	522.45 -	522.45	9.88	09/2019 -	-	-	0/0
97	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN , Central Sector Projects	03/2015	513.63 -	513.63	175.30	12/2019 -	12/2019	0(O) -	0/0
98	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU ,	06/2011	5,907.11 7,080.41	7,080.41	6,867.42	12/2015 -	12/2019	48(O) -	31/35
99	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU ,	04/2013	1,458.17 709.06	709.06	461.66	06/2015 -	-	-	5/7
100	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA ,	10/2006	249.03 -	448.86	296.17	03/2012 -	03/2024	144(O) -	35/42
101	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA ,	12/2008	453.63 -	453.63	121.91	12/2012 -	-	-	11/44
102	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA ,	12/2009	418.97 -	489.62	353.10	03/2012 -	03/2023	132(O) -	1/2
103	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA ,	03/2010	209.78 -	209.78	143.61	03/2015 -	03/2020	60(O) -	30/31
104	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA ,	03/2010	181.19 -	181.19	170.60	03/2012 -	-	-	6/6
105	KISTARAM OCP - [N06000089]SCCL,TELANGANA ,	11/2010	242.29 -	164.04	119.85	03/2015 -	03/2021	72(O) -	3/5
106	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA ,	07/2011	162.76 -	349.28	7.49	03/2015 -	03/2021	72(O) -	5/29
107	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA ,	07/2011	447.06 -	473.22	18.35	03/2015 -	03/2021	72(O) -	8/13
108	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA ,	06/2012	365.01 -	365.01	159.81	06/2015 -	03/2020	57(O) -	36/36
109	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA ,	07/2012	417.33 -	384.32	112.52	07/2016 -	03/2020	44(O) -	26/28
110	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA ,	11/2012	430.45 -	415.37	187.89	03/2016 -	03/2020	48(O) -	38/39
111	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]SCCL,TELANGANA ,	05/2015	397.09 -	442.42	99.42	03/2019 -	03/2020	12(O) -	15/18

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
112	KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL,TELANGANA , Central Sector Projects	10/2015	426.79 -	426.79	.72	03/2018 -	03/2020	24(O) -	0/9
113	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]SCCL,TELANGANA ,	12/2015	477.65 -	477.65	2.11	03/2020 -	03/2020	0(O) -	5/17
114	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA ,	03/2017	413.84 -	413.84	56.86	03/2019 -	03/2022	36(O) -	1/11
115	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL,TELANGANA ,	11/2016	272.73 -	272.73	162.62	- 04/2017	03/2020	- 0	1/6
116	RAMPURAM SHAFT BLOCK - [N06000174]SCCL,TELANGANA ,	08/2016	431.92 -	431.92	.00	- 03/2023	-	-	0/9
117	SRAVANAPALLI OPENCAST PROJECT - [N06000175]SCCL,TELANGANA ,	02/2018	412.70 -	412.70	.11	- 03/2023	-	-	0/7
118	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH ,	07/2016	17,237.00 -	17,237.80	8,032.77	11/2021 -	11/2021	0(O) -	0/0
119	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]ECL,WEST BENGAL ,	11/2015	602.86 -	602.86	317.12	03/2022 -	03/2022	0(O) -	9/13
120	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL ,	08/2012	1,055.05 -	1,055.05	528.96	03/2018 -	10/2020	31(O) -	11/16
121	RANIGANJ MASTER PLAN - [N06000163]ECL,WEST BENGAL ,	08/2009	2,661.73 -	5,173.26	336.63	08/2019 -	08/2024	60(O) -	0/19
122	SIDULI MINE (OC AND UG) - [N06000165]ECL,WEST BENGAL ,	05/2018	535.18 -	535.18	.00	03/2026 -	03/2026	0(O) -	1/22
123	NAKRAKONDA KUMARDIH B OCP - [N06000170]ECL,WEST BENGAL ,	08/2018	502.68 -	502.68	.00	03/2029 -	03/2029	0(O) -	0/22
124	TILABONI UG MINE - [N06000172]ECL,WEST BENGAL ,	02/2019	916.62 -	916.62	.00	03/2027 -	03/2027	0(O) -	0/27
	Total		1,04,997.33 -	1,07,962.20	37,121.19				519/1121
	FERTILISERS								
125	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL,HARYANA ,	01/2018	215.92 -	215.92	128.60	11/2019 -	11/2019	0(O) -	0/2
126	NEW SEWAGE TREATMENT PLANT PACKAGE RCF TROMBAY - [N08000009]RCF,MAHARASHTRA ,	10/2014	197.79 -	209.44	185.68	11/2016 -	09/2019	-	9/13
127	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]RCF,MAHARASHTRA ,	04/2018	426.72 -	426.72	249.06	04/2020 -	04/2020	0(O) -	1/14
128	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL,PUNJAB ,	01/2018	218.83 -	218.83	131.34	11/2019 -	11/2019	0(O) -	0/2
129	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL,PUNJAB ,	01/2018	239.81 -	239.81	145.72	11/2019 -	11/2019	0(O) -	0/2
	Total		1,299.07 -	1,310.72	840.40				10/33
	INFORMATION AND BROADCASTING								

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
130	FILM AND TELEVISION INSTITUTE ARUNACHAL PRADESH - [N09000002]CPWD,ANDHRA PRADESH ,	11/2016	204.32 -	204.32	.00	02/2019 -	11/2019	9(O) -	0/0
131	NATIONAL FILM HERITAGE MISSION - [N09000001]NFAI,MAHARASHTRA ,	11/2014	597.41 -	597.41	29.80	- -	-	-	0/0
132	NATIONAL CENTRE OF EXCELLENCE FOR ANIMATION VISUAL EFFECTS GAMING AND COMICS - [N09000003]NBCC,MAHARASHTRA ,	12/2016	167.70 -	167.70	.00	03/2020 -	03/2020	0(O) -	0/0
	Total		969.43 -	969.43	29.80				0/0
	MINES								
133	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA ,	12/2014	5,540.00 5,540.00	5,540.00	114.95	04/2021 04/2021	04/2021	0(O) 0	3/4
134	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA ,	05/2016	534.00 -	534.00	320.18	01/2020 -	01/2020	0(O) -	1/3
135	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO,ODISHA , Central Sector Projects	12/2015	355.00 -	355.00	82.07	11/2020 -	11/2020	0(O) -	2/3
136	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]NALCO,ODISHA , Central Sector Projects	11/2017	483.00 483.00	483.00	1.20	04/2021 04/2021	04/2021	0(O) 0	1/2
137	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO,TAMIL NADU ,	09/2017	166.62 163.17	163.17	135.00	06/2019 03/2020	03/2020	9(O) 0	1/1
	Total		7,078.62 -	7,075.17	653.40				8/13
	STEEL								
138	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH ,	12/2011	2,858.00 -	2,500.00	1,482.76	12/2017 12/2019	12/2019	24(O) 0	5/6
139	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH ,	08/2015	320.66 -	320.66	253.54	08/2018 12/2019	12/2019	16(O) 2	3/4
140	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH ,	01/2010	15,525.00 23,140.00	23,140.00	16,244.05	05/2015 07/2020	07/2020	62(O) 0	65/86
141	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND ,	03/2015	1,034.01 -	1,034.01	447.34	10/2017 06/2020	06/2020	32(O) 0	0/2
142	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND ,	05/2015	1,154.18 -	1,154.18	978.83	12/2017 11/2019	01/2020	25(O) 2	1/2
143	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND ,	11/2016	262.87 -	262.87	130.11	06/2019 06/2020	06/2020	12(O) 0	0/1
144	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA ,	04/2015	3,127.30 -	3,127.30	3,119.34	04/2018 11/2019	01/2020	21(O) 2	3/3
145	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH ,	04/2014	1,682.85 -	1,682.85	1,270.63	09/2018 12/2019	12/2019	15(O) 0	4/5
146	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121]SAIL,WEST BENGAL ,	12/2018	263.36 -	263.36	15.67	09/2020 -	09/2020	0(O) -	0/4

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Total		26,228.23 -	33,485.23	23,942.27				81/113
	PETROLEUM								
147	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH ,	07/2016	20,928.00 26,264.00	26,264.00	7,245.30	07/2020 07/2022	07/2022	24(O) 0	86/111
148	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH ,	03/2016	34,012.00 -	34,012.00	4,204.96	06/2020 -	08/2021	14(O) -	15/20
149	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL,ANDHRA PRADESH ,	01/2015	342.00 -	342.00	.00	03/2021 -	03/2021	0(O) -	0/0
150	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL,ANDHRA PRADESH ,	07/2014	247.00 -	247.00	.00	03/2021 -	03/2021	0(O) -	0/0
151	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL AP - [N16000302]IOCL,ANDHRA PRADESH ,	08/2017	384.58 -	384.58	105.36	04/2021 -	09/2020	-7(O) -	0/0
152	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH ,	08/2018	466.00 -	466.00	96.28	04/2021 -	07/2021	3(O) -	0/0
153	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH ,	04/2018	355.00 -	355.00	14.89	04/2022 -	02/2023	10(O) -	0/0
154	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL,ANDHRA PRADESH ,	10/2018	316.20 -	316.20	14.78	10/2021 -	10/2021	0(O) -	0/0
155	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]BPCL,ANDHRA PRADESH ,	07/2017	580.20 -	580.20	47.41	02/2021 -	02/2021	0(O) -	0/16
156	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM ,	03/2009	2,465.15 -	2,378.86	2,147.00	03/2013 12/2019	12/2019	81(O) 0	6/15
157	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM ,	06/2010	202.94 345.92	345.92	155.61	01/2014 -	11/2019	70(O) -	7/7
158	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) CACHAR ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM ,	06/2016	423.00 -	423.00	282.50	08/2019 -	12/2020	16(O) -	6/13
159	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]IOCL,ASSAM ,	02/2016	2,582.00 -	2,582.00	1,613.96	11/2019 -	02/2020	3(O) -	13/17
160	PIPELINE NETWORK PROJECT GELEKI ASSAM - [N16000278]ONGC,ASSAM ,	07/2016	249.85 265.49	265.49	180.20	05/2020 -	05/2020	0(O) -	4/5
161	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM ,	07/2011	350.00 -	350.00	2.06	01/2019 -	-	-	0/0
162	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]IOCL,ASSAM ,	05/2018	1,222.00 -	1,222.00	606.24	09/2019 -	04/2020	7(O) -	6/7
163	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM ,	01/2018	543.91 -	682.90	71.46	02/2020 06/2020	06/2020	4(O) 0	1/14
164	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM ,	08/2018	557.00 -	557.00	249.46	02/2020 -	06/2020	4(O) -	4/5
165	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS MADHUBAN - [N16000356]OIL,ASSAM ,	06/2016	224.75 -	224.75	69.99	08/2020 -	08/2020	0(O) -	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
166	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM ,	09/2012	871.35 -	1,200.00	565.63	03/2015 -	-	-	0/5
167	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]IOCL,BIHAR ,	05/2016	664.00 -	729.40	663.70	12/2020 -	02/2020	-10(O) -	4/5
168	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]IOCL,BIHAR ,	09/2015	324.00 -	324.00	192.32	06/2020 -	03/2020	-3(O) -	3/4
169	LPG BP PROJECT MOTIHARI - [N16000317]IOCL,BIHAR ,	05/2018	206.50 -	206.50	21.62	03/2021 -	03/2021	0(O) -	14/26
170	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]IOCL,BIHAR ,	12/2017	199.36 -	199.36	9.39	10/2020 -	10/2020	0(O) -	2/2
171	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL,BIHAR ,	10/2017	359.25 -	359.25	75.57	10/2022 -	10/2022	0(O) -	0/0
172	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]IOCL,BIHAR ,	07/2018	189.00 -	189.00	23.10	01/2021 -	01/2021	0(O) -	4/8
173	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI BIHAR - [N16000344]IOCL,BIHAR ,	04/2018	522.00 -	522.00	158.65	03/2021 -	03/2021	0(O) -	0/0
174	FUEL QUALITY UPGRADATION (NSU NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY - [N16000348]IOCL,BIHAR ,	06/2017	951.64 -	951.64	490.98	10/2019 -	05/2020	7(O) -	9/11
175	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH - [N16000311]HPCL,CHHATISGARH ,	12/2016	300.00 -	300.00	1.09	04/2021 -	04/2021	0(O) -	0/0
176	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI ,	08/2014	6,086.08 5,842.31	5,842.31	4,784.88	05/2019 10/2019	10/2019	-	13/14
177	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT ,	04/2016	327.78 -	200.00	150.72	04/2018 -	12/2019	20(O) -	18/20
178	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]ONGC,GUJARAT ,	02/2017	1,162.56 -	1,162.56	412.79	03/2026 -	03/2026	0(O) -	7/10
179	INFRASTRUCTURE DEVLOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]IOCL,GUJARAT , Central Sector Projects	09/2016	208.35 -	208.35	126.98	07/2020 -	07/2020	0(O) -	10/10
180	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]IOCL,GUJARAT ,	08/2017	1,342.00 -	1,342.00	6.30	08/2020 -	08/2020	0(O) -	1/1
181	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]IOCL,GUJARAT ,	03/2018	3,380.00 -	3,380.00	2,238.63	09/2019 -	03/2020	6(O) -	8/9
182	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT ,	10/2017	906.00 -	906.00	98.97	02/2020 -	10/2020	8(O) -	4/8
183	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA GUJARAT - [N16000336]IOCL,GUJARAT ,	03/2018	588.20 -	588.20	1.24	- -	08/2022	- -	8/17
184	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL,GUJARAT ,	09/2018	225.54 -	225.54	2.35	02/2021 -	02/2021	0(O) -	3/8
185	LAB REVAMP AT GUJARAT REFINERY - [N16000377]IOCL,GUJARAT , Central Sector Projects	10/2019	403.00 -	403.00	43.50	12/2021 -	12/2021	0(O) -	0/0
186	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]HPCL,HARYANA ,	11/2017	255.00 -	255.00	94.33	11/2020 -	11/2020	0(O) -	20/46

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
187	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]IOCL,HARYANA ,	04/2018	206.63 -	206.63	19.25	02/2020 -	02/2020	0(O) -	5/6
188	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]IOCL,HARYANA ,	12/2017	3,529.00 -	3,529.00	1,895.18	07/2019 -	02/2020	7(O) -	9/9
189	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL,HARYANA ,	08/2018	1,636.00 -	1,636.00	152.56	08/2020 -	08/2020	0(O) -	5/6
190	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]IOCL,HARYANA ,	01/2019	909.00 -	909.00	22.76	01/2021 -	01/2021	0(O) -	0/0
191	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]IOCL,HARYANA ,	10/2018	598.00 -	598.00	17.37	02/2020 -	02/2020	0(O) -	3/4
192	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL,HARYANA ,	08/2018	286.42 -	286.42	1.92	08/2020 09/2020	09/2020	1(O) 0	8/16
193	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV PANIPAT - [N16000363]IOCL,HARYANA ,	12/2018	278.60 -	278.60	.00	06/2021 -	06/2021	0(O) -	0/3
194	R and D CAMPUS II AT FARIDABAD - [N16000375]IOCL,HARYANA ,	06/2019	2,281.94 -	2,281.94	.00	12/2022 -	12/2022	0(O) -	0/0
195	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]IOCL,HARYANA ,	08/2019	1,255.00 -	1,255.00	99.93	10/2021 -	10/2021	0(O) -	0/0
196	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC,JHARKHAND ,	12/2015	823.27 910.23	910.23	403.18	03/2023 03/2022	03/2022	-12(O) 0	6/10
197	120 TMTPA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND ,	06/2017	161.50 -	161.50	17.78	06/2020 -	09/2021	15(O) -	0/12
198	CITY GAS DISTRIBUTION (CGD) NETWORK RANCHI - [N16000329]GAIL,JHARKHAND ,	10/2017	226.45 -	226.45	56.99	10/2022 -	10/2022	0(O) -	11/17
199	CITY GAS DISTRIBUTION (CGD) NETWORK JAMSHEDPUR - [N16000330]GAIL,JHARKHAND ,	10/2017	221.45 -	221.45	51.10	10/2022 -	10/2022	0(O) -	0/0
200	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]BPCL,JHARKHAND ,	11/2018	248.55 -	248.55	23.38	06/2022 -	06/2022	0(O) -	0/0
201	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KARNATAKA ,	01/2006	993.00 -	1,693.00	1,549.85	01/2012 -	-	-	0/0
202	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA , Central Sector Projects	02/2015	749.00 -	842.00	606.89	02/2020 -	02/2020	0(O) -	0/0
203	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]MANGALORE REFIN,KARNATAKA ,	05/2015	224.00 207.00	185.00	164.61	04/2019 -	-	-	8/8
204	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]MANGALORE REFIN,KARNATAKA ,	10/2015	135.00 170.70	170.70	156.65	03/2019 10/2019	10/2019	-	11/11
205	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA ,	09/2016	1,810.00 1,810.00	1,810.00	940.45	12/2019 07/2020	07/2020	7(O) 0	8/9
206	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA , Central Sector Projects	11/2017	581.00 -	621.00	102.99	03/2020 11/2020	11/2020	8(O) 0	2/3
207	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]BPCL,KARNATAKA ,	10/2018	206.26 -	206.26	2.84	03/2021 -	03/2021	0(O) -	0/15
208	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]HPCL,KARNATAKA ,	06/2019	2,166.38 -	2,166.38	15.61	06/2022 -	06/2022	0(O) -	0/18

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
209	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]HPCL,KARNATAKA ,	12/2018	854.00 -	854.00	38.34	12/2022 -	12/2022	0(O) -	0/19
210	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA ,	10/2015	607.06 -	714.25	356.46	10/2017 -	-	-	39/52
211	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA ,	11/2014	4,588.29 5,245.96	5,245.96	3,877.61	08/2018 11/2019	12/2019	16(O) 1	0/20
212	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA ,	02/2016	3,313.00 3,288.96	3,288.96	1,349.99	02/2020 10/2020	10/2020	8(O) 0	0/20
213	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA ,	12/2015	1,112.00 1,507.24	1,507.24	555.00	06/2019 02/2022	02/2022	32(O) 0	0/0
214	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]BPCL,KERALA ,	09/2018	11,130.00 -	11,130.00	54.40	03/2023 -	03/2023	0(O) -	0/0
215	PROVISION OF 2ND SPUR FOR TWL GANTRY TWD FACILITY FOR MS AND HSD ADDITIONAL TANKS FOR MS HSD AND - [N16000304]IOCL,MADHYA PRADESH ,	08/2017	236.00 -	236.00	30.20	06/2020 -	08/2020	2(O) -	0/0
216	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA ,	03/2011	861.79 -	1,683.06	1,356.33	05/2013 12/2019	12/2019	79(O) 0	4/8
217	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA ,	12/2011	2,059.63 2,665.65	2,665.65	1,932.09	03/2015 12/2019	12/2019	57(O) 0	15/18
218	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA ,	11/2014	6,068.80 -	5,296.93	4,767.31	04/2019 12/2019	12/2019	8(O) 0	8/9
219	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA ,	08/2015	2,818.88 -	2,818.88	2,302.10	03/2019 05/2020	05/2020	14(O) 0	4/5
220	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA , Central Sector Projects	01/2015	4,619.94 -	4,619.94	4,444.58	12/2017 03/2020	03/2020	27(O) 0	4/5
221	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA , Central Sector Projects	12/2015	3,190.69 -	3,247.19	2,298.77	04/2018 05/2020	05/2020	25(O) 0	13/15
222	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA ,	05/2016	1,945.00 -	1,945.00	1,004.75	08/2021 -	08/2021	0(O) -	5/5
223	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]BPCL,MAHARASHTRA ,	02/2016	554.00 -	554.00	375.80	02/2020 -	02/2020	0(O) -	0/10
224	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA ,	04/2013	449.58 -	449.58	192.13	12/2019 07/2020	07/2020	7(O) 7	0/17
225	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA ,	05/2016	212.00 -	212.00	46.99	01/2021 -	04/2021	3(O) -	0/0
226	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA ,	05/2016	348.00 -	348.00	37.01	01/2021 -	10/2021	9(O) -	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
227	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI - [N16000276]IOCL,MAHARASHTRA ,	05/2016	261.00 -	261.00	52.11	01/2021 -	01/2021	0(O) -	0/0
228	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA ,	09/2015	4,199.00 5,060.00	5,060.00	3,071.60	03/2020 -	03/2020	0(O) -	108/135
229	DEVELOPMENT OF B-147 FIELD - [N16000292]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	546.15 565.15	565.15	449.96	11/2019 03/2020	03/2020	4(O) 0	4/5
230	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	511.30 -	511.30	523.88	11/2019 -	11/2019	0(O) -	5/5
231	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	968.61 -	1,033.95	968.11	11/2019 -	11/2019	0(O) -	5/5
232	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC,MAHARASHTRA ,	02/2017	4,006.83 -	4,475.92	2,869.89	05/2021 12/2021	12/2021	7(O) 0	11/15
233	PUNE POL STORAGE DEPOT - [N16000313]BPCL,MAHARASHTRA ,	08/2016	282.64 -	282.64	145.83	08/2020 -	08/2020	0(O) -	0/15
234	180 TMTPA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD) MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA ,	06/2017	249.26 -	249.26	60.45	06/2020 -	09/2021	15(O) -	0/12
235	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335]ONGC,MAHARASHTRA ,	04/2018	766.37 -	766.37	465.86	12/2019 -	12/2019	0(O) -	4/5
236	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3 D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]ONGC,MAHARASHTRA ,	02/2019	2,292.46 -	2,292.46	402.18	05/2021 -	05/2021	0(O) -	4/6
237	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]ONGC,MAHARASHTRA ,	04/2019	3,228.80 -	3,228.80	497.01	03/2022 -	03/2022	0(O) -	4/6
238	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]ONGC,MAHARASHTRA ,	02/2019	3,660.71 3,740.05	3,740.05	274.07	04/2021 -	05/2021	1(O) -	4/6
239	HEERA REDEVELOPMENT - PHASE III - [N16000360]ONGC,MAHARASHTRA ,	05/2019	2,494.68 -	2,494.68	48.07	12/2021 -	03/2022	3(O) -	4/6
240	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]ONGC,MAHARASHTRA ,	05/2019	763.92 -	763.92	116.82	12/2020 -	12/2020	0(O) -	4/5
241	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE ,	07/2011	352.56 -	438.84	249.73	03/2017 06/2020	06/2020	39(O) 3	2/15
242	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE ,	01/2015	1,823.00 3,027.90	3,027.90	955.36	12/2020 -	12/2020	0(O) -	4/5
243	PARADIP HYDERABAD PIPLEINE - [N16000194]IOCL,MULTI STATE ,	01/2015	2,321.00 3,338.00	3,338.00	1,912.90	12/2020 -	08/2020	-4(O) -	4/5
244	JAIPUR-PANIPAT NAPTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE ,	02/2015	890.00 -	887.00	609.28	10/2019 -	12/2019	2(O) -	5/6
245	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE ,	01/2015	690.00 -	690.00	326.08	07/2018 -	10/2020	27(O) -	24/36
246	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]HPCL,MULTI STATE ,	09/2016	1,879.00 -	1,879.00	1,536.16	06/2020 -	06/2020	0(O) -	21/24

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
247	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE ,	05/2016	406.00 -	406.00	91.19	10/2020 -	10/2020	0(O) -	6/12
248	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE ,	09/2016	571.66 -	571.66	297.66	12/2019 06/2020	06/2020	6(O) 6	6/22
249	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE ,	07/2015	2,881.40 -	2,000.00	1,293.26	12/2020 -	12/2020	0(O) -	19/24
250	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE ,	03/2017	2,433.00 -	2,433.00	1,496.03	12/2020 -	12/2020	0(O) -	16/24
251	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE ,	03/2017	3,437.00 -	3,437.00	1,309.83	12/2020 -	12/2020	0(O) -	17/24
252	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE , Central Sector Projects	06/2009	2,915.00 4,915.00	4,915.00	2,742.24	12/2012 02/2022	02/2022	110(O) 0	21/42
253	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL,MULTI STATE ,	09/2017	2,677.00 -	2,677.00	971.81	03/2021 -	03/2021	0(O) -	11/26
254	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE ,	11/2015	500.00 -	500.00	.00	06/2017 -	-	-	0/0
255	BARAUNI-GUWAHATI PIPELINE - [N16000334]GAIL,MULTI STATE ,	06/2018	3,308.00 -	3,308.00	1,349.36	12/2021 -	12/2021	0(O) -	11/20
256	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA ,	03/2014	3,150.00 -	3,150.00	2,573.02	09/2017 -	-	-	6/6
257	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA ,	03/2017	1,933.00 -	1,933.00	1,055.91	12/2020 -	12/2020	0(O) -	18/24
258	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]IOCL,ODISHA ,	05/2016	429.00 -	429.00	318.90	01/2019 -	06/2020	17(O) -	6/6
259	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA , Central Sector Projects	12/2016	161.59 -	161.59	38.65	12/2019 -	07/2021	19(O) -	17/26
260	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA , Central Sector Projects	07/2017	243.53 -	243.53	55.03	07/2022 -	07/2022	0(O) -	0/0
261	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]IOCL,ODISHA ,	08/2017	315.00 -	315.00	116.26	12/2021 -	12/2020	-12(O) -	2/3
262	CITY GAS DISTRIBUTION (CGD) NETWORK CUTTACK - [N16000328]GAIL,ODISHA ,	07/2017	182.20 -	182.20	32.85	07/2022 -	07/2022	0(O) -	0/0
263	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]IOCL,ODISHA ,	04/2018	5,654.00 -	5,654.00	467.39	10/2021 -	10/2021	0(O) -	3/10
264	2G ETHANOL BIO REFINERY AT BARGARH - [N16000341]BPCL,ODISHA ,	08/2017	750.00 -	750.00	34.73	12/2020 -	12/2020	0(O) -	0/14
265	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL,ODISHA ,	10/2018	1,297.50 -	1,297.50	18.30	10/2021 -	10/2021	0(O) -	0/1
266	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]IOCL,ODISHA ,	11/2018	462.30 -	462.30	.00	09/2021 -	09/2021	0(O) -	0/0
267	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]IOCL,ODISHA ,	05/2019	3,361.00 -	3,361.00	372.43	08/2021 -	08/2021	0(O) -	5/11
268	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]IOCL,ODISHA ,	06/2019	371.00 -	371.00	.00	09/2022 -	09/2022	0(O) -	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
269	2ND GENERATION LIGNOCELLUOSIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA) - [N16000374]BPCL,ODISHA ,	08/2019	1,607.00 -	1,607.00	37.49	08/2022 -	08/2022	0(O) -	0/21
270	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN ,	11/2011	310.00 -	370.00	17.84	03/2013 -	-	-	0/24
271	LPG BP PROJECT JODHPUR - [N16000318]IOCL,RAJASTHAN ,	03/2018	229.80 -	229.80	74.26	- -	03/2021	- -	11/26
272	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU ,	05/2013	711.00 -	711.00	11.12	06/2020 -	06/2020	0(O) -	0/0
273	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU ,	03/2013	3,110.36 -	3,110.36	2,915.00	11/2015 -	-	-	52/52
274	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU ,	11/2012	678.00 -	678.00	7.28	02/2017 -	10/2021	56(O) -	0/0
275	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU ,	11/2015	650.82 -	650.82	415.38	03/2019 05/2020	05/2020	14(O) 0	4/5
276	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU ,	05/2016	4,497.00 6,025.00	6,025.00	990.22	12/2018 -	02/2021	26(O) -	4/5
277	AUGMENTATION OF CTMPL - [N16000286]IOCL,TAMIL NADU , Central Sector Projects	12/2016	228.00 -	228.00	24.50	06/2020 -	06/2020	0(O) -	4/5
278	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU ,	09/2017	1,858.00 -	1,858.00	1,119.38	12/2019 -	12/2019	0(O) -	0/0
279	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU ,	08/2017	421.00 -	421.00	159.94	08/2020 -	08/2020	0(O) -	0/0
280	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR TAMIL NADU - [N16000305]IOCL,TAMIL NADU ,	12/2017	466.43 -	466.43	35.01	10/2020 -	08/2021	10(O) -	0/0
281	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA ,	12/2018	611.00 -	611.00	13.11	04/2022 -	04/2022	0(O) -	0/0
282	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]GAIL,UTTAR PRADESH , Central Sector Projects	04/2017	287.49 -	287.49	133.40	04/2022 -	04/2022	0(O) -	36/43
283	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH ,	08/2017	318.80 -	318.80	52.67	08/2021 -	11/2021	3(O) -	0/0
284	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]IOCL,UTTAR PRADESH ,	01/2018	666.64 -	666.64	468.46	09/2019 -	01/2020	4(O) -	5/6
285	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL,UTTAR PRADESH ,	08/2017	255.40 -	255.40	4.07	08/2020 -	08/2020	0(O) -	1/1
286	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]IOCL,UTTAR PRADESH ,	03/2018	676.00 -	676.00	251.64	12/2021 -	12/2021	0(O) -	2/3
287	120 TMTPA LPG BOTTLING PLANT AT GORAKHPUR UP - [N16000354]IOCL,UTTAR PRADESH ,	03/2014	204.00 -	204.00	148.58	09/2019 -	-	-	6/6
288	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365]BPCL,UTTAR PRADESH ,	12/2017	1,524.06 -	1,524.06	20.02	12/2021 -	12/2021	0(O) -	0/21
289	REDEVELOPMENT/ EXPANSION OF MEERUT DEPOT FOR ENHANCING PRODUCT HANDLING CAPACITY - [N16000366]HPCL,UTTAR PRADESH ,	08/2016	154.84 -	154.84	128.71	11/2019 -	11/2019	0(O) -	40/40

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
290	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND , Central Sector Projects	02/2017	160.10 -	160.10	51.57	02/2020 -	10/2020	8(O) -	18/26
291	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL,WEST BENGAL ,	03/2015	694.00 1,097.54	1,097.54	722.99	10/2018 12/2019	12/2019	14(O) 0	0/15
292	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL,WEST BENGAL ,	04/2016	1,021.00 -	1,021.00	4.45	12/2020 -	12/2020	0(O) -	0/0
293	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL ,	03/2017	1,740.00 -	1,740.00	462.88	12/2020 -	12/2020	0(O) -	12/24
294	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL,WEST BENGAL ,	04/2017	163.02 -	163.02	54.53	04/2020 -	03/2021	11(O) -	17/26
295	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]IOCL,WEST BENGAL ,	05/2018	2,934.40 -	2,934.40	1,780.52	09/2019 -	04/2020	7(O) -	10/11
296	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]IOCL,WEST BENGAL ,	03/2018	3,712.00 -	3,696.00	683.33	09/2022 -	06/2021	-15(O) -	1/3
	Total		2,49,934.93 -	2,65,162.48	99,549.90				1048/1759
	POWER								
297	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH ,	09/2003	6,285.33 -	19,496.34	11,098.20	09/2010 -	-	-	0/0
298	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH ,	12/2004	2,496.90 7,927.34	7,927.34	7,599.10	12/2009 10/2019	10/2019	-	30/30
299	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR ,	02/2005	8,692.97 21,312.11	21,312.11	16,756.64	10/2011 08/2021	08/2021	118(O) 0	29/47
300	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR ,	01/2007	5,353.00 7,998.00	9,583.00	7,981.46	07/2012 -	09/2020	98(O) -	12/25
301	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR , Joint Venture	01/2013	12,964.60 17,304.00	17,304.00	14,229.00	05/2018 12/2021	06/2021	37(O) 0	36/45
302	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]SJVN,BIHAR ,	03/2019	10,439.09 10,439.09	10,439.09	836.81	01/2024 -	01/2024	0(O) -	16/19
303	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH ,	12/2012	11,846.00 -	12,739.82	12,839.84	10/2017 03/2020	03/2020	29(O) 0	38/41
304	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH ,	09/2015	3,004.00 -	3,004.00	1,782.00	11/2019 -	11/2019	0(O) -	0/0
305	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI ,	03/2015	1,394.52 -	1,394.52	431.80	05/2017 06/2019	12/2019	31(O) 0	4/9
306	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT , Central Sector Projects	05/2017	175.64 -	175.64	101.85	09/2018 03/2020	03/2020	18(O) 0	0/0
307	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT ,	12/2017	193.14 -	193.14	100.18	06/2019 03/2020	03/2020	9(O) 0	0/0
308	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH ,	09/2002	3,919.59 -	9,997.11	7,715.06	09/2009 -	12/2021	147(O) -	3/5
309	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND ,	02/2014	14,366.58 -	15,164.05	9,861.12	06/2019 09/2019	03/2022	33(O) 0	24/28

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
310	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND ,	10/2004	4,237.96 4,238.00	4,552.00	3,293.00	10/2017 -	-	-	0/0
311	PATRATU STPP-I (3X800MW) - [N18000275]NTPC,JHARKHAND ,	11/2017	18,668.00 -	18,668.00	2,078.50	03/2023 -	03/2023	0(O) -	1/1
312	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA , Central Sector Projects	05/2017	445.89 -	445.89	295.78	02/2019 12/2019	03/2020	13(O) 0	0/0
313	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH ,	03/2013	11,638.55 -	12,865.92	12,361.29	01/2018 03/2020	03/2020	26(O) 0	39/42
314	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH ,	03/2015	9,870.51 -	11,148.86	9,055.78	01/2020 -	02/2020	1(O) -	37/40
315	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH , Central Sector Projects	01/2017	2,104.21 -	1,587.16	308.34	09/2020 -	09/2020	0(O) -	9/16
316	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA ,	03/2012	7,921.47 -	7,921.47	5,302.00	09/2016 -	-	-	41/41
317	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR ,	12/1999	578.62 -	578.62	.00	06/2006 -	-	-	0/0
318	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE ,	10/2008	4,824.12 5,071.94	5,071.94	4,570.22	10/2012 12/2019	03/2020	89(O) 0	8/11
319	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE ,	02/2009	11,130.19 14,719.10	14,719.10	12,816.90	08/2013 03/2022	03/2022	103(O) 0	23/26
320	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE ,	10/2011	487.49 639.46	639.46	568.44	06/2014 09/2019	12/2019	66(O) 1	10/12
321	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE ,	10/2013	1,364.52 1,891.41	1,891.41	1,280.93	04/2016 08/2019	12/2019	44(O) 1	8/12
322	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE ,	01/2014	374.63 374.63	374.63	214.62	04/2016 12/2017	12/2019	44(O) 0	0/0
323	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE ,	05/2014	522.29 546.36	546.36	470.50	11/2016 06/2020	03/2020	40(O) 0	8/12
324	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE ,	06/2014	5,151.37 5,151.37	5,151.37	3,216.41	03/2018 12/2019	12/2019	21(O) 0	9/12
325	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE ,	01/2015	871.62 -	871.62	584.94	10/2017 09/2019	11/2019	25(O) 0	0/5
326	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE ,	01/2015	203.28 260.03	260.03	199.56	07/2017 06/2019	11/2019	28(O) 0	3/5
327	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE ,	03/2015	197.40 197.40	197.40	83.94	03/2018 -	12/2019	21(O) -	0/0
328	TRANSMISSION SYSTEM STRENTHENNING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE ,	03/2016	808.63 -	808.63	534.82	01/2018 03/2020	03/2020	26(O) 0	0/0
329	GREEN ENERGY CORRIDORS - INTER STATE TRANSSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE ,	05/2016	3,519.59 -	3,519.59	2,534.01	05/2019 -	12/2019	7(O) -	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
330	HVDC BIPOLE LINK BETWEEN WR (RAIGARH CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE ,	05/2016	14,733.37 -	14,733.37	9,317.26	11/2019 -	02/2020	3(O) -	0/0
331	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE ,	09/2016	562.25 -	562.25	420.20	03/2019 -	12/2019	9(O) -	0/0
332	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE ,	03/2017	283.72 -	283.72	196.10	11/2019 -	11/2019	0(O) -	0/0
333	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE ,	10/2016	408.46 -	408.46	311.82	01/2019 09/2019	01/2020	12(O) 0	0/0
334	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE ,	10/2016	608.24 -	608.24	416.24	04/2019 -	12/2019	8(O) -	0/0
335	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE ,	02/2017	322.30 -	322.30	164.09	02/2019 04/2020	03/2020	13(O) 3	0/0
336	EASTERN REGION STRENTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE ,	02/2017	235.53 -	235.53	130.55	06/2019 -	03/2020	9(O) -	0/0
337	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE ,	03/2017	379.95 -	379.95	93.48	12/2019 -	03/2020	3(O) -	0/0
338	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH CHATTISGARH) AND SOUTHERN REGION (PUGALAR TM) NOR - [N18000247]PGCIL,MULTI STATE ,	02/2017	5,070.13 -	5,070.13	3,042.59	04/2020 -	04/2020	0(O) -	0/0
339	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE ,	03/2017	337.75 -	337.75	99.94	06/2019 -	12/2019	6(O) -	0/0
340	COMPREHENSIVE SCHEME FOR THE STRENGHTENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE ,	12/2014	4,754.42 -	9,072.36	1,352.46	12/2018 -	12/2020	24(O) -	0/0
341	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE ,	12/2014	5,111.33 -	6,880.36	1,779.00	12/2018 -	12/2020	24(O) -	0/0
342	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE , Central Sector Projects	12/2015	3,654.00 -	3,654.00	3,485.19	04/2019 -	12/2019	8(O) -	0/0
343	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE , Central Sector Projects	03/2017	3,500.00 3,500.00	3,500.00	1,949.00	07/2020 -	07/2020	0(O) -	0/0
344	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE , Central Sector Projects	08/2017	1,931.39 -	1,931.39	1,107.54	02/2020 -	02/2020	0(O) -	0/0
345	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE ,	09/2017	198.49 -	198.49	119.50	09/2019 02/2020	02/2020	5(O) 0	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
346	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE ,	11/2017	358.83 -	358.83	166.27	05/2020 -	05/2020	0(O) -	0/0
347	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA ,	02/2014	12,532.44 -	13,740.53	9,944.45	12/2018 02/2020	09/2020	21(O) 0	35/40
348	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA ,	04/2016	844.64 -	844.64	435.25	04/2019 04/2019	11/2019	7(O) 0	0/0
349	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA ,	05/2016	1,885.13 -	1,885.13	527.90	12/2018 -	03/2020	15(O) -	0/0
350	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU ,	05/2005	1,779.29 -	2,187.32	2,237.45	11/2008 -	-	-	20/22
351	TRANSMISSION SYSTEM FOR EVACUTION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU , Central Sector Projects	05/2017	186.17 -	186.17	110.60	07/2019 -	01/2020	6(O) -	0/0
352	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA ,	01/2016	10,598.98 -	10,598.98	5,851.67	11/2020 06/2021	06/2021	7(O) 0	24/25
353	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH ,	09/2014	9,188.98 -	10,016.10	6,633.23	07/2019 03/2020	07/2020	12(O) 0	35/37
354	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH ,	05/2011	195.42 -	294.60	321.11	02/2014 -	12/2019	70(O) -	7/8
355	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH , Joint Venture	04/2012	9,750.89 -	12,176.28	10,032.00	02/2017 06/2020	06/2020	40(O) 0	34/40
356	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH ,	03/2019	11,089.42 -	11,089.42	672.81	09/2023 -	09/2023	0(O) -	0/0
357	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]NTPC,UTTAR PRADESH ,	12/2018	587.44 -	587.44	250.00	09/2020 -	09/2020	0(O) -	0/0
358	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]NTPC,UTTAR PRADESH ,	03/2019	349.00 -	349.00	125.00	11/2020 -	11/2020	0(O) -	0/0
359	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND ,	07/2006	1,657.00 -	5,024.35	3,118.00	02/2016 -	06/2022	76(O) -	19/30
360	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND ,	11/2006	2,978.48 5,867.38	5,867.38	4,264.84	03/2013 12/2020	01/2021	94(O) 0	7/15
361	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND ,	08/2008	2,491.58 -	4,397.80	1,823.10	06/2013 -	12/2022	114(O) -	10/13
362	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND ,	07/2012	1,527.00 -	1,801.07	148.93	08/2017 -	-	-	0/15
363	NAITWAR MORI HEP - [N18000265]SJVN,UTTARAKHAND ,	10/2017	648.33 -	648.33	284.44	12/2021 -	12/2021	0(O) -	5/32
364	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL ,	09/2014	1,381.84 -	1,592.34	502.87	09/2019 05/2024	05/2024	56(O) 27	5/9
365	EASTERN REGION STRENGTHENNING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL ,	04/2016	454.11 -	454.11	297.16	04/2018 01/2020	01/2020	21(O) 0	0/0
366	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL ,	12/2016	529.68 -	529.68	140.10	11/2018 -	03/2020	16(O) -	0/0
	Total		2,79,157.68 -	3,53,357.42	2,22,975.18				589/770
	HEAVY INDUSTRY								

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
367	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI , Central Sector Projects	08/2016	1,554.00 -	1,554.00	665.35	09/2019 -	03/2020	6(O) -	0/0
	Total		1,554.00 -	1,554.00	665.35				0/0
	HEALTH AND FAMILY WELFARE								
368	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS-MNAGLAGIRI GUNTUR ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH , Central Sector Projects	08/2017	272.19 -	272.54	191.86	03/2019 -	03/2020	12(O) -	0/0
369	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH , Central Sector Projects	03/2018	601.02 -	601.02	169.38	- -	07/2020	- -	0/0
370	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI ASSAM - [N21000027]HITES,ASSAM ,	05/2017	875.00 -	747.80	110.70	05/2021 10/2021	10/2021	5(O) 0	0/0
371	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI ,	02/2013	414.11 -	499.23	302.02	11/2013 -	09/2020	82(O) -	0/0
372	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI ,	12/2013	204.44 -	270.00	204.70	05/2017 -	06/2020	37(O) -	2/2
373	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI ,	08/2014	293.65 -	325.00	297.16	05/2017 -	01/2020	32(O) -	3/5
374	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI ,	12/2017	156.56 -	156.65	76.53	- -	05/2020	- -	0/0
375	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA , Central Sector Projects	01/2018	249.01 -	249.01	126.78	- -	05/2020	- -	0/0
376	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA ,	09/2014	505.58 -	585.00	586.96	03/2018 -	09/2019	-	1/2
377	AIIMS BILASPUR - [N21000028]NBCC,HIMACHAL PRADESH ,	04/2018	1,351.00 1,471.00	1,351.00	245.85	09/2021 -	09/2021	0(O) -	0/0
378	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA , Central Sector Projects	08/2017	274.19 -	274.19	241.58	03/2019 -	03/2020	12(O) -	0/0
379	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA , Central Sector Projects	03/2018	582.99 -	582.99	211.20	- -	06/2020	- -	0/0
380	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA ,	10/2016	363.99 -	363.99	208.29	05/2018 -	07/2020	26(O) -	0/0
381	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB ,	07/2016	152.95 -	177.92	139.70	02/2018 -	03/2020	25(O) -	1/1
382	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA PUNJAB - [N21000026]HITES,PUNJAB ,	07/2016	703.00 -	557.48	283.12	06/2020 08/2020	10/2020	4(O) 2	0/0
383	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH , Central Sector Projects	03/2018	268.84 -	268.84	157.76	- -	04/2020	- -	0/0
384	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH ,	07/2016	785.00 -	715.06	345.41	04/2020 06/2020	10/2020	6(O) 4	0/0
385	CONSTRUCTION OF HOSPITAL BLOCK IIT KHARAGPUR - [N21000010]HSCC,WEST BENGAL ,	12/2014	168.90 -	191.20	169.51	05/2017 -	07/2019	-	3/3

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
386	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL ,	08/2016	244.00 -	248.00	224.92	09/2018 -	05/2019	-	0/0
387	RESIDENTIALCOMPLEX AND OPD BLOCK AIIMS KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL , Central Sector Projects	08/2017	355.15 -	355.15	217.00	03/2019 -	07/2020	16(O) -	0/0
388	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL ,	04/2018	651.99 -	651.99	232.42	- -	07/2020	- -	0/0
	Total		9,473.56 -	9,444.06	4,742.85				10/13
	RAILWAYS								
389	NANDYAL-YERRAGUNTLA(NL) SCR - [220100192]SCR,ANDHRA PRADESH ,	03/1996	164.36 -	1,050.00	999.64	02/2009 -	-	-	0/0
390	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH ,	12/2001	1,045.20 2,120.16	2,120.16	524.57	03/2009 -	03/2023	168(O) -	0/0
391	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH ,	04/2011	761.37 761.37	761.37	.52	- -	-	-	0/0
392	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH ,	04/2013	829.00 829.00	829.00	.94	- -	-	-	1/1
393	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH ,	04/2011	2,288.70 2,643.25	2,643.25	810.35	03/2021 -	03/2024	36(O) -	0/1
394	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH ,	03/2012	1,503.71 -	2,200.00	1,722.18	03/2020 -	03/2022	24(O) -	0/0
395	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH ,	04/2015	3,873.07 3,873.07	3,873.07	.38	- -	-	-	0/0
396	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH ,	04/2016	3,631.00 3,631.00	3,631.00	617.19	03/2022 -	03/2023	12(O) -	0/0
397	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH ,	04/2015	3,246.26 -	3,548.67	1,211.97	12/2023 -	12/2023	0(O) -	0/0
398	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH ,	04/2015	2,499.71 2,499.71	3,382.95	397.90	03/2022 -	03/2022	0(O) -	0/0
399	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH ,	01/2013	387.70 -	387.70	323.91	03/2018 -	-	-	0/0
400	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH ,	08/2016	234.50 -	235.00	10.88	03/2019 -	12/2020	21(O) -	0/0
401	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT) NEFR - [N22000086]NFR,ASSAM ,	09/2006	385.20 1,532.00	1,532.00	642.09	03/2019 -	03/2020	12(O) -	0/0
402	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM ,	04/2011	314.00 728.00	728.00	727.55	03/2019 -	03/2020	12(O) -	0/0
403	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM ,	04/2015	2,232.32 -	2,182.00	756.32	03/2022 -	03/2020	-24(O) -	0/0
404	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM ,	04/2015	870.96 -	2,136.01	580.01	03/2021 -	03/2021	0(O) -	0/0
405	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC) ECR - [220100240]ECR,BIHAR ,	04/1997	324.73 898.53	1,050.00	1,043.03	03/2012 -	03/2020	96(O) -	0/0
406	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR ,	04/1997	162.87 614.45	614.45	309.76	- -	03/2022	- -	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
407	HAJIPUR-SUGAULI VIA VAISHALI (NL) ECR - [220100303]ECR,BIHAR ,	04/2003	528.65 2,066.78	2,066.78	1,441.80	- -	03/2023	- -	0/0
408	KOSI BRIDGE (NL) ECR - [220100304]ECR,BIHAR ,	04/2002	499.41 516.02	516.02	402.55	03/2020 -	03/2020	0(O) -	0/0
409	DANIAWAN-BIHARSARIF (NL) ECR - [220100311]ECR,BIHAR ,	04/2001	406.92 -	339.00	200.00	- -	-	-	0/0
410	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR ,	04/1996	477.88 751.55	751.55	674.58	03/2012 -	03/2020	96(O) -	0/0
411	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) NEFR - [N22000087]NFR,BIHAR ,	09/2006	532.87 2,145.00	2,145.00	935.60	03/2019 -	03/2020	12(O) -	0/0
412	KISHANGANJ JALALGARH NL NEFR - [N22000101]NFR,BIHAR ,	04/2008	333.76 -	360.00	6.74	- 03/2022	03/2022	- 0	0/0
413	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR ,	04/2008	633.87 -	633.87	.40	- -	-	-	0/0
414	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR ,	04/2008	620.57 -	620.57	.32	- -	-	-	0/0
415	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR ,	04/2008	445.25 -	445.25	1.15	- -	-	-	0/0
416	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR ,	04/2008	326.20 -	2,995.01	1.94	- -	03/2024	- -	0/0
417	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR ,	04/1999	325.00 735.20	735.20	363.83	- -	03/2021	- -	0/0
418	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR ,	04/2006	378.56 -	1,858.75	377.77	- -	03/2022	- -	0/0
419	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR ,	04/2005	205.00 -	205.00	5.21	- -	-	-	0/0
420	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR ,	04/2006	211.00 -	1,006.00	24.16	- -	-	-	0/0
421	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR ,	04/2008	678.62 -	678.62	17.20	- -	-	-	0/0
422	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR ,	04/2008	228.05 -	228.05	1.53	- -	03/2024	- -	0/0
423	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR ,	04/2008	1,605.17 1,605.17	1,605.17	23.49	- 03/2023	03/2023	- 0	0/0
424	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR ,	04/2008	192.56 -	192.56	.39	- -	-	-	0/0
425	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR ,	04/2008	281.30 -	281.30	.60	- -	-	-	0/0
426	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR ,	04/2004	372.14 1,470.50	1,470.50	824.49	- -	03/2021	- -	0/0
427	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR ,	04/2009	548.00 819.01	819.01	489.11	03/2020 -	03/2022	24(O) -	0/0
428	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR ,	04/2013	213.01 367.17	425.17	423.55	- -	01/2020	- -	0/1
429	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR ,	05/2015	380.00 519.33	519.33	164.77	- -	02/2023	- -	0/0
430	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR ,	12/2015	1,200.20 1,200.20	1,200.20	397.15	03/2020 -	10/2021	19(O) -	0/1

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
431	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR ,	12/2015	1,491.47 -	1,491.47	443.64	03/2020 -	12/2022	33(O) -	1/1
432	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR ,	01/1991	332.15 546.71	546.71	541.43	07/2014 -	-	-	0/0
433	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR ,	04/2016	744.04 1,215.54	1,215.54	79.18	03/2021 -	03/2022	12(O) -	0/0
434	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR ,	04/2016	731.64 1,185.73	1,185.73	35.74	03/2021 -	03/2022	12(O) -	0/0
435	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR ,	04/1998	180.82 726.31	726.31	510.91	- -	10/2019	-	0/0
436	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA DANIYAWAN-BIHARSHARIF - [N22000476]ECR,BIHAR ,	04/1991	329.39 803.11	1,483.14	1,053.89	- -	12/2021	- -	0/0
437	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH ,	12/2012	1,160.00 1,160.83	1,160.83	699.40	03/2020 -	03/2023	36(O) -	1/1
438	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH ,	03/2007	1,402.02 -	1,100.00	1,088.23	03/2020 -	06/2020	3(O) -	0/0
439	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH ,	05/2014	207.00 -	207.00	153.83	03/2018 -	-	-	0/0
440	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH ,	04/2008	872.00 1,226.51	1,226.51	1,062.76	12/2019 03/2020	03/2020	3(O) 0	0/0
441	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH ,	04/2015	1,973.00 1,973.64	1,973.64	174.40	03/2021 03/2023	03/2023	24(O) 3	0/1
442	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH ,	02/2014	2,288.00 -	4,970.11	628.61	03/2022 -	12/2022	9(O) -	0/1
443	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH ,	04/2013	3,055.00 -	3,055.00	1,951.07	09/2018 -	12/2020	27(O) -	0/1
444	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]RITES,CHHATISGARH ,	02/2016	393.98 -	393.98	290.45	03/2020 -	03/2020	0(O) -	0/2
445	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI ,	04/1999	156.65 -	197.17	106.97	- 03/2024	03/2024	- 0	0/0
446	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI ,	04/2012	295.68 -	295.68	92.91	- -	03/2023	- -	0/0
447	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT ,	04/2008	829.74 1,215.34	1,310.23	1,450.40	03/2020 03/2021	03/2021	12(O) 0	0/0
448	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT ,	04/2008	318.24 321.62	321.62	125.76	03/2012 03/2022	03/2022	120(O) 0	0/0
449	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT ,	04/2006	117.36 196.95	202.35	809.40	03/2011 03/2017	03/2017	-	0/0
450	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT ,	04/2012	975.62 -	1,082.32	1,054.93	12/2021 -	12/2021	0(O) -	0/0
451	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT ,	04/2012	644.38 -	644.38	418.93	03/2021 -	03/2021	0(O) -	0/0
452	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT ,	04/2011	844.10 844.10	844.10	107.52	- 03/2021	03/2021	- 0	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
453	RAJKOT-VERAVAL WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT ,	04/1994	320.66 858.56	858.96	534.00	03/2019 03/2022	03/2022	36(O) 0	0/0
454	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT ,	04/2013	1,548.66 -	1,548.66	1,339.35	12/2021 -	03/2022	3(O) -	0/0
455	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT ,	04/2011	1,037.15 1,037.15	1,037.15	1,017.75	03/2021 03/2022	03/2022	12(O) 0	0/0
456	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT ,	04/2015	1,002.39 1,002.39	1,002.39	396.54	03/2021 03/2021	03/2021	0(O) 0	0/0
457	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT ,	10/2013	343.00 -	343.00	222.83	03/2019 -	12/2019	9(O) -	0/0
458	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT ,	03/2017	243.60 -	243.60	.00	- -	-	-	0/0
459	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT ,	03/2012	248.26 -	248.26	.00	- -	-	-	0/0
460	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT ,	03/2012	153.83 -	153.83	.00	- -	-	-	0/0
461	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT ,	02/1991	551.51 809.07	809.07	641.51	03/2019 03/2020	03/2020	12(O) 0	0/0
462	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT ,	04/2017	691.84 663.29	663.29	180.20	03/2020 03/2021	03/2021	12(O) 0	0/0
463	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA ,	04/2012	287.00 -	694.00	220.42	12/2011 -	03/2021	111(O) -	0/0
464	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA ,	12/2015	346.32 -	346.32	288.65	03/2019 -	03/2020	12(O) -	0/0
465	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH ,	04/2008	2,966.99 -	7,000.00	446.46	12/2026 -	12/2025	-12(O) -	0/0
466	UDHAMPUR-SRINAGAR-BARAMULLA (NL) NR - [220100133]NR,JAMMU AND KASHMIR ,	03/1995	2,500.00 27,949.00	27,949.00	19,767.15	11/2002 -	06/2022	235(O) -	0/0
467	KODERMA-RANCHI VIA BARKAKANA (NL) ECR - [220100222]ECR,JHARKHAND ,	03/1999	1,033.07 3,020.95	3,376.00	3,328.43	- -	03/2021	- -	0/0
468	KODERMA-TILAIYA (NL) ECR - [220100305]ECR,JHARKHAND ,	04/2002	459.91 1,625.87	1,625.87	544.36	- -	03/2021	- -	0/0
469	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND ,	04/2012	258.20 358.68	358.68	265.54	12/2018 -	06/2020	18(O) -	0/0
470	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND ,	04/2012	148.77 -	377.00	182.63	12/2016 08/2018	01/2020	37(O) 1	0/0
471	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND ,	03/2016	1,724.20 -	1,993.24	411.64	03/2021 03/2021	12/2021	9(O) 0	0/0
472	GARHWA ROAD-RAMNA - [N22000465]ECR,JHARKHAND ,	03/2015	348.23 -	348.23	187.91	03/2021 -	12/2020	-3(O) -	0/0
473	HUBLI-ANKOLA(NL) SWR - [220100193]SWR,KARNATAKA ,	04/1997	2,315.00 -	2,315.00	149.76	- -	12/2024	- -	0/0
474	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA ,	04/1996	1,382.78 1,382.78	1,382.78	7.35	03/2002 -	03/2024	264(O) -	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

(November 2019)

Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning: Original / Revised	Date of Commissioning: Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
475	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA ,	04/2011	1,801.01 1,801.01	1,801.01	48.41	- -	12/2023	- -	0/0
476	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA ,	04/2010	986.30 986.30	986.30	302.38	03/2016 -	12/2023	93(O) -	1/1
477	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA ,	04/2013	558.00 692.43	692.43	.00	- -	12/2023	- -	0/0
478	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA ,	04/2011	832.47 832.47	832.47	.94	03/2016 -	03/2024	96(O) -	0/0
479	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA ,	04/2011	348.85 348.85	348.85	.36	- -	12/2023	- -	0/0
480	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA ,	04/2010	2,127.00 -	2,900.00	1,737.30	03/2023 -	03/2024	12(O) -	0/1
481	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA ,	04/2011	146.75 146.75	167.50	.34	- -	12/2023	- -	0/0
482	GADAG-WADI NL - [N22000299]SWR,KARNATAKA ,	04/2013	2,841.84 2,841.84	2,841.84	169.45	12/2018 -	12/2024	72(O) -	0/0
483	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA ,	04/2013	327.25 367.77	367.77	.00	- -	12/2023	- -	0/0
484	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA ,	04/2012	279.54 279.54	279.54	30.34	03/2016 -	12/2023	93(O) -	0/0
485	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA ,	03/2015	1,156.94 1,140.94	1,140.94	773.28	03/2020 -	03/2021	12(O) -	1/5
486	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA ,	03/2015	578.00 578.00	578.00	525.85	03/2020 -	03/2020	0(O) -	1/2
487	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA ,	03/1996	644.78 644.78	890.00	443.52	03/2017 -	03/2020	36(O) -	0/0
488	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA ,	10/1998	1,566.00 -	2,815.62	264.28	- -	-	-	0/0
489	KUMBALAM-TURAVUR - [N22000191]SR,KERALA ,	04/2011	252.96 -	252.96	8.50	- -	-	-	0/0
490	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA ,	04/2010	189.24 -	189.24	6.72	- -	-	-	0/0
491	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA ,	02/2015	1,431.90 -	1,431.90	75.00	- -	-	-	0/0
492	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA ,	02/2015	1,000.00 -	828.50	.08	- -	-	-	0/0
493	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA ,	02/2012	550.00 -	550.00	.00	03/2016 -	-	-	0/0
494	RAMGANJMUNDI-BHOPAL (NL) WCR - [220100314]WCR,MADHYA PRADESH ,	04/2001	424.60 -	2,909.99	1,975.34	03/2021 -	03/2023	24(O) -	0/14
495	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH ,	04/2005	383.79 1,473.76	1,413.76	1,351.73	- 01/2020	01/2020	- 0	0/0
496	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH ,	04/2008	3,503.69 3,975.22	3,975.22	1,758.23	03/2022 03/2023	03/2023	12(O) 0	0/0
497	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH ,	12/2015	1,763.93 -	1,762.94	847.47	03/2020 03/2023	03/2023	36(O) 12	1/1
498	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH ,	04/2011	1,485.85 -	1,485.85	1,158.89	12/2020 -	03/2021	3(O) -	0/0
499	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH ,	06/2016	2,478.23 -	2,478.23	477.93	03/2022 -	03/2023	12(O) -	0/10

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
500	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH ,	08/2016	582.13 -	1,247.64	152.01	03/2022 09/2022	09/2022	6(O) 0	1/1
501	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH ,	12/2015	174.00 -	174.00	152.48	03/2019 -	02/2020	11(O) -	0/0
502	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH ,	04/2010	585.93 1,268.32	1,268.32	669.57	02/2019 12/2020	12/2020	22(O) 6	0/1
503	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH ,	04/2015	1,370.00 1,370.94	1,370.94	311.76	12/2021 11/2022	11/2022	11(O) 11	0/0
504	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH ,	04/2016	700.00 603.69	603.69	113.47	06/2020 06/2021	06/2021	12(O) 0	0/0
505	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA ,	03/1996	495.44 1,781.98	2,980.41	1,431.38	03/2004 -	03/2021	204(O) -	0/0
506	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA ,	02/1997	2,271.50 -	3,712.50	2,434.24	03/2021 -	03/2022	12(O) -	0/0
507	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA ,	04/2008	5,300.00 -	918.53	284.75	03/2014 -	03/2021	84(O) -	0/0
508	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA ,	04/2012	714.10 -	714.10	65.20	04/2016 -	-	-	0/0
509	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA ,	04/2008	3,168.29 -	3,168.29	1,202.21	03/2023 -	03/2023	0(O) -	0/0
510	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA ,	04/2011	792.89 -	1,377.48	316.79	03/2021 -	03/2022	12(O) -	0/0
511	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA ,	04/2011	184.06 199.12	312.00	275.98	03/2019 12/2019	12/2019	9(O) 0	0/0
512	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA ,	04/2012	540.02 -	540.02	252.82	03/2022 -	03/2024	24(O) -	0/0
513	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA ,	02/2016	9,968.00 -	9,968.00	.00	03/2024 -	03/2024	0(O) -	0/0
514	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA ,	02/2016	2,425.00 -	5,341.68	.00	03/2024 -	03/2024	0(O) -	0/0
515	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA ,	02/2016	2,750.00 -	3,438.51	.00	03/2024 -	-	-	0/0
516	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA ,	02/2015	1,272.19 -	1,272.19	319.94	03/2022 -	03/2023	12(O) -	0/0
517	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA ,	02/2015	2,449.91 -	2,449.91	180.76	03/2023 -	03/2023	0(O) -	0/0
518	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA ,	02/2015	3,627.47 3,627.00	3,627.47	761.03	03/2024 -	03/2023	-12(O) -	0/0
519	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA ,	02/2016	1,876.00 -	2,081.27	187.09	03/2023 -	03/2023	0(O) -	0/0
520	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA ,	02/2016	1,035.16 -	1,035.16	117.02	03/2022 -	03/2024	24(O) -	0/0
521	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA ,	02/2016	637.95 -	637.95	73.16	03/2023 -	03/2024	12(O) -	0/0
522	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA ,	03/2009	713.48 -	2,300.00	2,056.99	03/2020 -	03/2021	12(O) -	0/0
523	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA ,	04/2015	723.78 -	723.78	.19	12/2025 -	03/2025	-9(O) -	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
524	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA ,	09/2016	1,908.51 2,686.63	2,686.63	515.29	03/2023 03/2023	03/2023	0(O) 0	0/1
525	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA ,	10/2013	305.00 -	305.00	261.28	03/2019 -	12/2019	9(O) -	0/0
526	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA ,	03/2010	265.88 -	265.88	.00	- -	-	-	0/0
527	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA ,	03/2012	217.38 -	217.38	.00	- -	-	-	0/0
528	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA ,	06/2018	229.00 852.50	852.50	39.69	12/2021 03/2023	03/2023	15(O) 0	0/1
529	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR ,	04/2003	4,454.17 13,809.00	12,524.00	9,541.58	03/2011 -	03/2022	132(O) -	0/0
530	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA ,	04/2010	906.46 -	6,000.00	263.12	03/2021 -	03/2021	0(O) -	0/0
531	BHAIRABI SAIRONG NL NEFR - [N22000100]NFR,MIZORAM ,	04/2008	2,393.47 4,968.00	5,021.45	3,131.89	03/2014 03/2022	03/2022	96(O) 0	0/0
532	GONDIA-JABALPUR(GC) (SECR) - [220100186]SECR,MULTI STATE ,	02/1997	511.86 1,756.00	1,756.00	1,668.96	04/2020 01/2021	01/2021	9(O) 1	0/1
533	NANGALDAM-TALWARA(NL) NR - [220100188]NR,MULTI STATE ,	03/1981	450.00 2,010.00	2,200.00	666.00	07/2012 -	03/2024	140(O) -	0/0
534	MUNEERABAD-MAHABOOBNAGAR(NL) SCR - [220100205]SCR,MULTI STATE ,	04/1997	1,723.00 1,780.29	1,780.09	1,478.40	03/2000 -	03/2021	252(O) -	0/0
535	LALITPUR-SATNA-REWA-SINGRULI NL (NCR) - [220100232]WCR,MULTI STATE ,	09/1998	247.66 6,672.85	8,248.50	1,986.78	05/2008 03/2022	03/2023	178(O) 0	0/9
536	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) NEFR - [220100266]NFR,MULTI STATE ,	04/2000	1,180.19 3,300.00	4,541.00	3,344.19	12/2008 -	03/2021	147(O) -	0/0
537	DEOGHAR - SULTANGANJ (INL) ER - [220100273]ER,MULTI STATE ,	04/2000	607.09 -	1,425.44	637.54	02/2013 -	03/2024	133(O) -	0/0
538	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE ,	04/2005	230.03 -	230.03	277.14	12/2022 -	12/2022	0(O) -	0/0
539	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE ,	03/2007	243.78 -	895.00	106.55	12/2021 -	12/2021	0(O) -	0/0
540	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE ,	03/2013	295.00 -	477.31	336.89	01/2019 -	01/2020	12(O) -	0/0
541	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE ,	04/2007	1,347.26 1,347.26	1,347.26	741.93	03/2022 03/2022	03/2022	0(O) 0	0/0
542	DAHOD-INDORE VIA SARDARPUR JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE ,	04/2007	1,640.04 1,640.04	1,640.04	739.31	03/2022 03/2023	03/2023	12(O) 0	0/0
543	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE ,	04/2011	2,082.75 -	4,079.15	185.30	- -	-	-	0/1
544	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE ,	04/2011	2,912.96 -	3,845.60	148.26	03/2022 -	12/2024	33(O) -	0/3
545	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE ,	04/2010	2,030.50 -	2,030.50	19.07	- -	-	-	0/0
546	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE ,	04/2010	651.00 -	1,009.00	7.96	03/2015 03/2025	03/2025	120(O) 0	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
547	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE ,	04/2008	415.67 -	549.75	15.58	- -	-	-	0/0
548	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE ,	04/2013	1,798.00 -	2,496.67	.00	03/2019 -	-	-	0/0
549	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE ,	04/2008	523.52 -	2,300.00	2.28	- -	-	-	0/0
550	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE ,	04/2007	270.14 -	457.08	373.51	- -	-	-	0/0
551	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE ,	04/2010	242.22 -	471.00	69.09	03/2020 -	03/2020	0(O) -	0/0
552	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE ,	04/2010	241.52 -	373.87	273.20	- -	06/2021	- -	0/0
553	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE ,	04/2011	414.84 -	661.00	122.93	03/2020 -	03/2020	0(O) -	0/0
554	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE ,	04/1999	819.23 -	1,871.00	1,082.01	- -	-	-	0/0
555	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]SR,MULTI STATE ,	04/2011	120.70 -	1,800.00	187.30	03/2019 -	12/2019	9(O) -	0/0
556	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE ,	04/1987	406.99 -	545.70	148.48	03/2006 -	03/2025	228(O) -	0/0
557	SULTANGANJ-KATURIA VIA ASARGANJ TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE ,	04/2007	450.00 -	1,261.34	.00	- -	03/2025	- -	0/0
558	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE ,	04/2010	172.03 -	260.10	10.73	- -	03/2025	- -	0/0
559	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE ,	04/2013	915.98 -	2,137.81	297.68	03/2022 -	03/2025	36(O) -	0/0
560	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE ,	04/2011	288.35 -	393.00	393.00	- -	03/2020	- -	0/0
561	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE ,	04/2011	261.38 -	478.08	478.08	- -	05/2019	-	0/0
562	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE ,	04/2001	923.52 -	995.10	501.00	03/2016 -	03/2025	108(O) -	0/0
563	CHINPAI-SAINTHIA DOUBLING MM FOR PRANTI-SURI CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE ,	04/2005	595.51 -	769.40	103.08	03/2017 -	03/2025	96(O) -	0/0
564	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE ,	04/2010	174.56 -	174.56	71.42	- -	03/2025	- -	0/0
565	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE ,	04/2010	277.28 -	266.32	162.57	03/2016 -	03/2025	108(O) -	0/0
566	DANKUNI-CHANDANPUR 4TH LINE 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE ,	04/2010	365.17 -	296.43	248.70	03/2017 -	03/2025	96(O) -	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
567	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE ,	04/2010	157.94 -	157.94	51.75	11/2018 -	03/2021	28(O) -	0/0
568	BARIARPIUR-MANANPURVIA KHARAGPUER LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE ,	04/2007	450.55 -	250.55	20.12	- -	03/2025	- -	0/0
569	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE ,	04/2010	365.17 -	527.54	1.76	- -	03/2025	- -	0/0
570	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE ,	04/2011	542.18 -	693.80	458.91	03/2020 -	03/2021	12(O) -	0/0
571	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE ,	04/2011	175.80 -	251.18	251.18	- -	03/2021	- -	0/0
572	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE ,	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108(O) -	0/0
573	NEW ALIPUR TO AKRA MM FOR BUDGE BUDGE-PUJALI NL PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE ,	04/2010	494.54 -	494.59	32.00	03/2005 -	03/2025	240(O) -	0/0
574	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE ,	04/2000	297.47 -	298.22	52.09	- -	03/2025	- -	0/0
575	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE ,	04/2003	337.96 -	336.96	70.20	- -	03/2025	- -	0/0
576	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE ,	04/2009	499.96 -	680.68	159.45	02/2012 -	03/2025	157(O) -	0/0
577	LILUAH-DANKUNI 3RD LINE MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE ,	04/2009	257.42 -	257.42	107.49	03/2014 -	03/2025	132(O) -	0/0
578	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE ,	04/2011	166.89 -	166.89	.02	- -	03/2025	- -	0/0
579	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE ,	04/2012	1,856.95 2,200.00	2,200.00	290.92	03/2023 -	03/2024	12(O) -	0/0
580	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE ,	04/2012	923.23 2,184.83	2,184.83	2.46	- -	-	-	1/1
581	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE ,	04/2007	336.91 791.39	791.39	517.05	- 03/2022	03/2022	- 0	0/0
582	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE ,	04/2013	296.00 466.65	466.65	.00	- -	12/2023	- -	0/0
583	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE ,	04/2007	2,062.30 2,062.30	2,062.30	903.96	- -	03/2025	- -	2/2
584	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE ,	04/2010	704.31 952.16	952.16	303.24	03/2020 03/2020	03/2020	0(O) 0	1/1
585	KADAPA-BANGALORE (NL) KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE ,	04/2008	2,132.77 2,132.77	2,132.77	331.15	03/2014 -	03/2024	120(O) -	1/1
586	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE ,	04/2012	250.93 -	310.70	275.20	- -	03/2024	- -	0/0
587	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE ,	05/2015	600.00 -	685.99	74.80	03/2020 -	04/2022	25(O) -	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
588	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE ,	05/2015	860.43 -	958.00	756.85	03/2020 -	03/2020	0(O) -	0/0
589	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE ,	03/2015	1,614.59 1,870.41	1,870.41	885.55	03/2019 -	03/2021	24(O) -	0/0
590	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE ,	05/2015	678.54 678.54	678.54	495.04	03/2019 -	02/2021	23(O) -	0/38
591	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE , Central Sector Projects	10/2006	11,589.00 30,357.00	28,181.00	.00	- -	-	-	0/0
592	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE ,	04/2015	2,063.03 2,063.03	2,063.03	792.70	03/2021 -	03/2023	24(O) -	0/0
593	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE ,	04/2015	636.38 -	636.38	.00	- -	-	-	0/0
594	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE ,	12/2015	1,08,000.00 -	1,08,000.00	5,969.41	12/2023 12/2023	12/2023	0(O) 0	0/0
595	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE ,	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	03/2020	0(O) -	0/0
596	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE ,	04/2007	328.14 -	1,540.00	234.79	03/2023 -	03/2023	0(O) -	0/0
597	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE ,	03/2002	625.00 781.00	859.00	835.35	03/2016 -	03/2021	60(O) -	0/0
598	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND ,	04/2006	2,326.52 -	4,600.00	842.42	03/2015 -	10/2021	79(O) -	0/0
599	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND ,	04/2013	4,274.00 -	4,274.00	.00	03/2020 -	03/2020	0(O) -	0/0
600	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA ,	04/1994	2,923.13 3,791.66	3,791.66	1,243.45	03/2009 -	06/2024	183(O) -	0/0
601	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA ,	04/1996	1,185.64 -	1,844.47	1,829.53	12/2017 -	03/2020	27(O) -	0/0
602	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA ,	04/1998	1,202.70 -	1,202.70	947.96	02/2015 -	12/2021	82(O) -	0/0
603	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA ,	04/2000	133.41 207.00	385.00	387.92	03/2009 03/2009	06/2020	135(O) 6	1/1
604	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA ,	04/2005	810.78 198.07	1,928.07	770.82	06/2021 -	06/2024	36(O) -	0/0
605	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA ,	04/2010	149.90 -	230.00	54.46	03/2015 -	-	-	0/0
606	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA ,	03/2011	1,111.99 1,539.28	1,539.28	937.49	02/2019 -	03/2022	37(O) -	0/0
607	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA ,	03/2013	843.04 843.04	843.04	141.96	10/2020 03/2023	03/2023	29(O) 0	0/0
608	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA ,	03/2012	155.81 -	238.03	204.79	03/2020 -	03/2021	12(O) -	0/0
609	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA ,	04/2015	1,547.38 1,547.38	1,547.38	366.66	03/2022 -	03/2023	12(O) -	0/0
610	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA ,	04/2015	2,361.74 2,361.74	2,361.74	208.19	03/2022 -	03/2025	36(O) -	0/0
611	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA ,	04/2015	701.61 701.61	810.02	129.40	11/2018 -	03/2022	40(O) -	0/0

MoSPI OCMS

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
612	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA ,	04/2015	1,172.92 1,172.92	1,172.92	546.12	12/2018 03/2022	03/2022	39(O) 0	0/0
613	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA ,	11/2015	969.83 1,312.96	1,312.96	562.50	03/2020 03/2020	06/2020	3(O) 0	0/0
614	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA ,	01/1991	2,335.67 -	2,335.68	647.54	12/2024 -	12/2024	0(O) -	0/0
615	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA ,	03/2006	948.04 -	1,500.00	1,374.96	03/2020 -	03/2021	12(O) -	0/0
616	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA ,	03/2009	942.95 -	1,120.00	1,028.76	03/2019 -	06/2022	39(O) -	0/0
617	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA ,	04/2016	5,200.00 -	1,700.43	48.00	03/2020 -	06/2023	39(O) -	0/0
618	QADIAN-BEAS - [N22000295]NR,PUNJAB ,	04/2011	205.22 -	841.90	1.73	- -	03/2024	- -	0/0
619	DAUSA-GANGAPUR CITY(NL) NWR - [220100184]NWR,RAJASTHAN ,	02/1997	410.08 780.98	886.41	559.84	02/2019 -	03/2021	25(O) -	0/0
620	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN ,	04/2012	246.08 -	348.55	229.00	12/2019 -	06/2020	6(O) -	0/0
621	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN ,	04/2013	236.93 -	294.90	226.61	10/2018 -	12/2019	14(O) -	0/0
622	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN ,	04/2013	822.00 -	1,099.54	.00	- -	-	-	0/1
623	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN ,	04/2013	323.00 -	432.22	.00	- -	-	-	0/0
624	MAVLI JUNCTION-BARI SADRI MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN ,	04/2013	420.18 -	420.18	184.64	03/2020 -	06/2020	3(O) -	0/0
625	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN ,	04/2011	213.39 -	303.56	274.18	11/2019 -	05/2020	6(O) -	0/0
626	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN ,	04/2013	242.09 281.03	410.00	362.96	02/2019 -	03/2020	13(O) -	0/0
627	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN ,	05/2015	873.71 -	1,980.21	4.60	- -	-	-	0/0
628	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN ,	01/2011	493.17 -	493.17	441.09	03/2018 -	03/2020	24(O) -	0/0
629	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN ,	08/2018	808.85 -	808.85	60.28	08/2022 -	09/2022	1(O) -	0/0
630	SEVOK RANGPO NEFR - [N22000102]NFR,SIKKIM ,	04/2008	1,339.48 -	4,084.69	332.23	12/2015 -	-	-	0/0
631	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU ,	09/1995	303.98 -	980.00	681.66	03/2020 -	03/2021	12(O) -	0/0
632	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS MTP - [N22000028]MRTP,TAMIL NADU ,	04/2006	495.74 -	734.01	445.91	06/2013 -	-	-	1/4
633	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU ,	09/2007	724.69 -	2,072.50	1,440.83	02/2019 -	02/2020	12(O) -	0/0
634	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU ,	09/2006	227.40 -	900.00	63.28	- -	-	-	0/0
635	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU ,	09/2006	582.83 -	2,300.00	241.58	- -	-	-	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
636	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU ,	04/2008	151.84 -	1,105.00	3.34	02/2019 -	-	-	0/0
637	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU ,	04/2013	839.00 -	1,500.00	.62	- -	-	-	0/0
638	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU ,	04/1999	198.68 -	556.64	304.22	- -	-	-	0/0
639	ERODE-PALANI - [N22000199]SR,TAMIL NADU ,	04/2008	288.57 -	1,140.00	1.63	- -	-	-	0/0
640	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU ,	04/2008	164.41 -	450.00	167.49	- -	03/2020	- -	0/0
641	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU ,	04/2007	931.98 -	951.24	738.83	- -	03/2020	- -	0/0
642	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU ,	10/2013	187.26 -	231.67	162.06	04/2014 -	03/2020	71(O) -	0/0
643	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU ,	02/1996	268.87 -	950.00	927.86	03/2005 -	-	-	0/0
644	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU ,	02/1999	257.00 257.00	257.00	268.31	03/2018 -	-	-	0/0
645	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU ,	02/2017	1,567.00 -	1,567.00	.00	03/2024 -	03/2026	24(O) -	0/0
646	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU ,	02/2015	1,700.00 -	1,003.00	252.02	03/2022 -	03/2022	0(O) -	0/0
647	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU ,	02/2015	760.00 -	1,182.31	446.00	03/2020 -	06/2021	15(O) -	0/0
648	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA ,	07/1998	458.25 458.25	458.26	3.83	- -	-	-	0/0
649	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA ,	04/2006	1,160.48 1,160.48	1,160.48	323.09	03/2010 -	03/2023	156(O) -	1/1
650	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA ,	04/2012	632.68 -	816.55	701.83	03/2016 -	12/2020	57(O) -	0/0
651	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA ,	04/2013	1,112.00 2,911.84	2,911.84	.92	- -	-	-	1/1
652	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA ,	03/2015	636.38 -	636.38	281.85	03/2021 -	03/2021	0(O) -	3/3
653	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA ,	04/2015	773.94 -	773.94	475.85	12/2024 -	12/2024	0(O) -	0/0
654	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA ,	04/2017	119.73 185.00	390.60	342.54	03/2022 -	03/2022	0(O) -	0/0
655	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA ,	04/2012	569.63 670.00	670.00	107.83	03/2020 09/2021	09/2021	18(O) -3	2/3
656	ETAWAH-MAINPURI (NL) NCR - [220100318]NCR,UTTAR PRADESH ,	04/1997	120.00 -	346.00	345.51	12/2008 -	-	-	0/0
657	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH ,	02/2008	171.10 -	275.08	141.55	03/2012 -	-	-	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
658	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH ,	03/2013	307.00 -	1,409.09	.00	- -	-	-	0/0
659	KAPILVASTU-BASTI VIA BANSI SIDHARTHNAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH ,	03/2013	643.00 -	644.00	.00	- -	-	-	0/0
660	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH ,	04/2012	1,229.00 -	1,230.00	103.72	- -	03/2023	- -	0/0
661	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH ,	04/2014	182.92 -	197.73	.00	- -	-	-	0/0
662	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH ,	03/2015	1,295.42 -	1,295.42	350.85	03/2022 -	12/2019	-27(O) -	0/0
663	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH ,	04/2015	668.70 668.00	680.00	330.00	03/2020 -	03/2020	0(O) -	4/6
664	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH ,	04/2015	943.60 -	750.56	409.09	03/2022 -	12/2024	33(O) -	0/0
665	LUCKNOW- PILIBHIT VIA SITAPUR LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH ,	04/2011	927.01 -	1,200.00	1,178.67	03/2019 -	03/2020	12(O) -	0/0
666	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH ,	04/2015	1,765.92 -	1,765.92	650.11	03/2023 -	12/2024	21(O) -	0/0
667	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH ,	03/2012	1,183.25 -	1,183.25	1,136.44	12/2020 -	12/2022	24(O) -	0/0
668	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH ,	08/2015	2,436.21 -	2,436.21	597.94	03/2020 -	03/2021	12(O) -	0/0
669	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH ,	08/2015	528.57 -	528.57	118.49	03/2019 -	12/2019	9(O) -	0/0
670	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH ,	04/2016	213.00 -	213.35	9.62	04/2016 -	06/2020	50(O) -	0/0
671	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH ,	04/2016	1,900.00 -	1,277.06	.00	01/2022 -	01/2022	0(O) -	0/0
672	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH ,	04/2017	150.00 -	150.00	.00	04/2017 -	10/2022	66(O) -	0/0
673	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH ,	04/2017	1,343.00 -	1,476.15	.00	01/2018 -	-	-	0/0
674	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH ,	04/2017	622.50 427.00	426.74	195.35	04/2017 -	01/2020	33(O) -	0/0
675	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH ,	04/2017	276.90 -	276.90	.00	04/2017 -	04/2022	60(O) -	0/0
676	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH ,	04/2016	602.50 -	714.34	18.40	- -	-	-	0/0
677	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH ,	04/2016	600.00 -	600.00	31.72	01/2022 -	01/2022	0(O) -	0/0
678	SHAHGANJ-BHATNI-PHEPHNA-INDARA MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH ,	04/2016	1,177.96 -	1,028.95	26.06	12/2019 -	04/2021	16(O) -	0/0
679	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH ,	03/2018	4,329.53 -	4,329.53	3.90	03/2023 -	03/2023	0(O) -	0/0
680	JHANSI BINA DOUBLING - [N22000496]NCR,UTTAR PRADESH ,	09/2016	2,001.00 -	2,001.00	416.59	03/2021 -	03/2021	0(O) -	0/6
681	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND ,	04/2003	142.45 -	228.40	.15	- -	-	-	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
682	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND ,	04/2012	219.83 346.63	346.63	233.23	- -	06/2020	- -	0/0
683	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND ,	04/2011	16,216.00 -	16,216.00	1,790.80	12/2024 -	03/2025	3(O) -	0/0
684	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL) NEFR - [220100135]NFR,WEST BENGAL ,	04/1983	297.32 -	614.00	275.07	03/2019 -	03/2020	12(O) -	0/0
685	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL ,	04/1974	393.46 154.30	1,026.00	182.49	03/2007 03/2007	-	-	0/0
686	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL ,	03/2000	1,049.69 -	3,404.92	3,837.57	12/2006 -	-	-	0/0
687	TARAKESWAR - BISHNUPUR NEW BG LINE (NL) ER - [220100272]ER,WEST BENGAL ,	04/2000	1,188.91 -	1,619.48	871.86	03/2019 12/2009	03/2025	72(O) 0	0/0
688	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL ,	04/2007	1,106.62 -	1,091.59	860.08	12/2010 12/2017	03/2025	171(O) 0	7/7
689	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL,WEST BENGAL ,	04/2010	2,397.72 -	2,397.72	197.20	03/2016 -	-	-	0/0
690	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL ,	04/2010	2,298.42 -	2,733.86	40.13	03/2014 -	12/2025	141(O) -	0/0
691	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL ,	04/2010	3,951.98 -	4,724.30	2,278.26	03/2016 -	03/2025	108(O) -	0/0
692	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL ,	04/2010	2,913.51 -	4,639.00	855.74	03/2016 -	03/2025	108(O) -	0/0
693	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL ,	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	63(O) -	0/0
694	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL ,	04/2010	267.37 -	620.00	40.99	- 03/2025	03/2025	- 0	0/0
695	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL ,	04/2010	221.42 -	380.00	38.18	- 03/2022	03/2022	- 0	0/0
696	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSHPUR - [N22000212]MRTP,WEST BENGAL ,	04/2009	573.78 -	268.52	.03	- -	03/2025	- -	0/0
697	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL ,	04/2012	255.64 -	272.20	177.61	- -	09/2021	- -	0/0
698	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR,WEST BENGAL ,	04/2016	602.27 -	612.00	336.17	12/2021 -	03/2020	-21(O) -	0/0
699	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL ,	04/1998	1,027.40 1,966.70	2,373.00	485.04	03/2003 03/2030	03/2030	324(O) 0	0/0
700	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]NFR,WEST BENGAL ,	02/1999	380.60 -	1,871.00	1,087.60	04/2010 -	-	-	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Total		4,59,394.75 -	6,67,846.32	1,99,661.27				33/139
	HUMAN RESOURCE DEPARTMENT								
701	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES,MEGHALAYA ,	09/2013	484.32 -	626.26	.00	09/2014 -	12/2020	75(O) -	0/0
	Total		484.32 -	626.26	.00				0/0
	ROAD TRANSPORT AND HIGHWAYS								
702	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS ,	03/2015	262.97 -	262.97	.00	10/2018 -	-	-	0/4
703	2 LANE WITH HARD SHOLDER REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS ,	03/2017	409.85 -	409.85	21.11	12/2017 -	-	-	0/4
704	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS ,	03/2015	277.17 -	277.17	158.36	04/2017 -	-	-	3/4
705	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS ,	02/2018	391.00 -	391.00	22.17	10/2018 -	-	-	0/4
706	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS ,	03/2018	234.27 -	234.27	11.03	10/2018 -	-	-	0/4
707	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS ,	11/2017	237.80 -	238.00	7.48	11/2019 -	11/2019	0(O) -	0/0
708	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS ,	11/2017	257.34 -	238.00	41.09	11/2019 -	11/2019	0(O) -	0/0
709	AJANTHA TO BULDHANA - [N24001008]MoRTH,A & N ISLANDS ,	02/2017	401.00 401.00	401.00	107.81	07/2019 -	07/2019	-	0/4
710	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH , PPP (BOT)	04/2011	571.00 -	571.00	582.53	10/2013 -	-	-	0/0
711	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2011	1,535.00 -	1,535.00	3,225.15	05/2014 12/2019	12/2019	67(O) 0	0/0
712	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]MoRTH,ANDHRA PRADESH ,	07/2015	333.21 333.21	333.21	256.11	12/2015 -	-	-	0/2

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
713	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]MoRTH,ANDHRA PRADESH , EPC	01/2014	195.45 -	195.45	.00	11/2014 -	-	-	0/4
714	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]MoRTH,ANDHRA PRADESH , EPC	03/2015	271.45 -	271.45	159.15	10/2015 01/2020	01/2020	51(O) 27	3/4
715	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]MoRTH,ANDHRA PRADESH ,	07/2015	333.21 -	333.21	256.11	12/2015 -	-	-	0/2
716	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]MoRTH,ANDHRA PRADESH , EPC	10/2015	333.21 -	353.89	256.11	11/2015 -	-	-	0/0
717	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH ,	01/2016	1,134.97 -	1,134.97	783.67	11/2018 -	-	-	0/0
718	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH ,	09/2014	1,684.00 -	1,684.00	54.13	02/2017 -	-	-	0/0
719	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI,ANDHRA PRADESH ,	03/2017	648.32 -	512.72	501.52	03/2020 -	03/2020	0(O) -	0/0
720	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH ,	03/2017	1,041.62 -	1,187.10	807.76	03/2020 -	05/2020	2(O) -	0/0
721	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH , Central Sector Projects	06/2017	648.33 -	306.00	152.56	06/2017 -	07/2020	37(O) -	0/0
722	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH ,	12/2017	328.67 -	328.67	176.29	- -	11/2019	- -	0/0
723	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH ,	12/2017	1,323.15 -	1,323.15	403.93	- -	07/2021	- -	0/0
724	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH ,	12/2017	357.00 -	357.00	70.71	- -	-	-	0/0
725	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH ,	02/2018	1,959.00 -	1,959.00	657.85	- -	07/2021	- -	0/0
726	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH ,	03/2018	1,532.62 2,499.00	2,499.00	584.50	03/2021 -	04/2021	1(O) -	1/4
727	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH ,	03/2018	1,550.98 -	1,550.98	673.04	- -	07/2021	- -	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
728	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH ,	03/2018	565.09 -	565.09	167.77	- -	02/2021	- -	0/0
729	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH ,	03/2018	314.43 -	314.43	24.90	- -	12/2020	- -	0/0
730	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH ,	03/2018	557.30 -	557.30	208.96	- -	03/2020	- -	0/0
731	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MoRTH,ANDHRA PRADESH ,	10/2015	333.21 -	355.89	265.48	12/2015 01/2020	12/2020	60(O) 48	2/3
732	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]MoRTH,ANDHRA PRADESH ,	09/2016	372.68 -	372.68	185.04	02/2017 12/2019	12/2019	34(O) 10	2/4
733	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO - [N24000930]MoRTH,ANDHRA PRADESH ,	11/2016	378.24 -	378.24	287.63	01/2018 01/2020	01/2020	24(O) 0	3/4
734	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]MoRTH,ANDHRA PRADESH ,	11/2016	290.15 -	290.15	70.35	05/2017 03/2020	03/2020	34(O) 10	1/4
735	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MoRTH,ANDHRA PRADESH ,	01/2017	319.28 -	319.28	108.34	08/2017 03/2020	03/2020	31(O) 7	1/4
736	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MoRTH,ANDHRA PRADESH ,	02/2017	429.43 -	429.43	209.09	11/2017 03/2020	11/2019	24(O) 0	3/4
737	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MoRTH,ANDHRA PRADESH ,	03/2018	228.32 -	228.32	47.96	08/2018 03/2020	03/2020	19(O) 0	2/4
738	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU - [N24000936]MoRTH,ANDHRA PRADESH ,	03/2018	244.95 245.00	244.95	126.99	08/2018 02/2020	02/2020	18(O) 0	2/3
739	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MoRTH,ANDHRA PRADESH ,	03/2018	289.67 290.00	289.67	103.90	08/2018 02/2020	02/2020	18(O) 0	2/4
740	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938]MoRTH,ANDHRA PRADESH ,	03/2018	297.12 294.00	294.12	291.57	07/2018 01/2020	01/2020	18(O) 0	4/4

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
741	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MoRTH,ANDHRA PRADESH ,	03/2018	504.19 504.00	504.19	226.14	11/2018 05/2020	05/2020	18(O) 0	2/4
742	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]MoRTH,ANDHRA PRADESH ,	03/2016	995.09 995.00	995.09	410.28	05/2016 07/2020	07/2020	50(O) 26	2/4
743	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963]MoRTH,ANDHRA PRADESH ,	01/2018	418.03 -	418.03	170.05	08/2018 08/2020	08/2020	24(O) 0	2/4
744	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MoRTH,ANDHRA PRADESH ,	08/2016	350.61 -	350.61	310.25	01/2017 04/2020	04/2020	39(O) 21	3/4
745	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MoRTH,ANDHRA PRADESH ,	01/2016	386.09 -	386.09	183.00	05/2016 12/2019	12/2019	43(O) 19	2/4
746	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]MoRTH,ANDHRA PRADESH ,	01/2016	348.95 -	348.95	161.26	08/2016 03/2020	03/2020	43(O) 19	2/4
747	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MoRTH,ANDHRA PRADESH ,	03/2016	444.84 -	444.84	251.28	09/2016 03/2020	03/2020	42(O) 18	2/4
748	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MoRTH,ANDHRA PRADESH ,	11/2016	376.25 -	376.25	201.42	08/2017 02/2020	02/2020	30(O) 6	2/4
749	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]MoRTH,ANDHRA PRADESH ,	01/2017	263.45 -	263.45	59.79	09/2017 12/2020	12/2020	39(O) 15	0/4
750	REHABILITAITON AND UPGRADATION OF REPALLE TO EEPPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MoRTH,ANDHRA PRADESH ,	01/2017	576.48 -	576.48	228.31	01/2018 12/2020	01/2020	24(O) 0	1/4
751	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S - [N24001183]MoRTH,ANDHRA PRADESH ,	07/2014	251.55 -	251.55	7.74	02/2015 -	-	-	0/0
752	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]MoRTH,ARUNACHAL PRADESH , ITEM RATE	12/2011	156.63 276.00	276.00	147.65	02/2012 -	-	-	0/0
753	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]MoRTH,ARUNACHAL PRADESH , ITEM RATE	11/2010	305.49 -	305.49	131.08	03/2011 -	-	-	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
754	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]MoRTH,ARUNACHAL PRADESH , ITEM RATE	03/2012	207.03 389.45	389.45	291.55	05/2012 05/2015	12/2019	91(O) 0	0/0
755	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	194.11 -	194.11	181.03	05/2018 -	08/2019	-	3/4
756	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL,ARUNACHAL PRADESH , EPC	10/2015	179.82 -	179.82	197.77	01/2019 -	-	-	4/4
757	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH , EPC	07/2015	197.16 197.16	197.16	75.57	10/2018 09/2015	09/2018	-	1/4
758	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	394.00 -	394.00	272.92	06/2018 -	03/2020	21(O) -	1/3
759	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROMKM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH ,	01/2016	183.65 -	183.65	107.04	11/2016 -	-	-	3/4
760	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH ,	04/2016	245.79 -	245.79	105.26	- -	09/2020	- -	2/4
761	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH ,	04/2016	198.00 -	198.00	184.62	10/2016 -	10/2019	-	3/4
762	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH ,	11/2015	434.06 -	434.06	133.38	- -	12/2020	- -	2/4
763	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH ,	12/2016	138.93 155.00	155.00	75.99	01/2017 -	01/2020	36(O) -	2/4
764	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH ,	01/2017	1,253.10 -	1,253.10	158.90	03/2017 -	03/2022	60(O) -	1/4
765	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH ,	03/2017	284.09 284.09	284.09	77.42	04/2017 03/2018	03/2021	47(O) 0	1/4
766	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH ,	02/2017	195.23 -	195.23	49.25	04/2017 -	-	-	1/4
767	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH ,	02/2017	203.36 -	203.36	62.53	04/2017 -	-	-	1/4

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

(November 2019)

Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning: Original / Revised	Date of Commissioning: Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
768	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH ,	01/2017	194.66 -	194.66	83.66	04/2017 -	-	-	1/4
769	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH ,	02/2017	168.32 168.32	168.32	34.87	04/2017 02/2018	02/2021	46(O) 0	1/4
770	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH ,	02/2017	180.57 180.57	180.57	14.27	04/2017 02/2018	02/2021	46(O) 0	0/4
771	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH ,	02/2017	216.71 216.71	216.71	19.67	04/2017 02/2018	02/2021	46(O) 0	0/4
772	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH ,	02/2017	167.28 167.28	167.28	19.83	04/2017 02/2018	02/2021	46(O) 0	1/1
773	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH ,	01/2017	198.22 -	198.22	83.66	04/2017 -	-	-	1/4
774	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH ,	03/2018	392.60 -	392.60	.00	- -	-	-	0/0
775	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH ,	12/2016	200.44 -	200.44	75.98	- -	-	-	0/0
776	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH ,	03/2017	1,718.59 -	1,718.59	158.90	- -	-	-	0/0
777	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM - [N24000947]NHIDCL,ARUNACHAL PRADESH ,	05/2016	259.52 -	259.52	184.51	- -	-	-	0/0
778	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH ,	09/2016	568.92 -	568.92	134.41	- -	-	-	0/0
779	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH ,	12/2016	188.78 -	188.78	38.37	- -	-	-	0/0
780	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH ,	02/2017	175.06 175.06	175.06	14.08	- 04/2019	04/2022	- 0	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
781	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH ,	02/2017	176.12 176.12	176.12	14.79	- 04/2019	04/2022	- 0	0/0
782	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D - [N24000974]NHIDCL,ARUNACHAL PRADESH ,	02/2017	199.02 199.02	199.02	11.87	- 02/2018	02/2021	- 0	0/0
783	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D - [N24000975]NHIDCL,ARUNACHAL PRADESH ,	02/2017	184.88 184.88	184.88	97.50	- 02/2018	02/2021	- 0	0/0
784	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH ,	10/2015	210.50 210.50	210.50	120.60	- 01/2016	01/2019	-	0/0
785	BORDUMSA NAMCHIK (BURIDEHING - JAIRAMPUR) ROAD ON NH-52B (NEW NH-215) FROM KM. 0.15 (STARTING CHAIN - [N24000977]NHIDCL,ARUNACHAL PRADESH ,	07/2015	189.91 -	189.91	154.43	- -	-	-	4/4
786	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN - [N24000978]NHIDCL,ARUNACHAL PRADESH ,	03/2015	172.75 -	172.75	118.30	- -	-	-	3/4
787	TWO-LANING OF HAYULIANG– HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI - [N24000979]NHIDCL,ARUNACHAL PRADESH ,	01/2017	256.66 -	256.66	24.14	- -	-	-	1/4
788	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH ,	09/2011	1,979.00 -	1,979.00	1,143.00	- 03/2020	-	-	0/0
789	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH ,	11/2016	243.89 -	243.89	121.47	- -	09/2020	- -	0/0
790	HARANGAJO TO MAIBANG (AS-23) KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM ,	12/2003	280.00 490.00	525.00	492.41	02/2009 07/2019	07/2019	-	0/0
791	MAIBANG TO LUMDING (AS-25) KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM ,	12/2003	199.81 340.14	340.14	319.96	04/2009 03/2011	08/2019	-	0/0
792	MAIBANG TO LUMDING (AS-26) KM.60.500 TO KM.83.400 NH-54 - [240106279]NHAI,ASSAM ,	12/2003	167.64 408.77	408.77	395.78	11/2008 07/2011	01/2014	-	0/0
793	MAIBANG TO LUMDING (AS-24) KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM ,	12/2003	155.04 255.23	255.23	251.39	11/2008 01/2011	08/2013	-	0/0
794	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM ,	12/2003	245.00 -	174.34	225.34	03/2008 -	08/2020	149(O) -	0/0
795	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM ,	12/2003	225.00 -	225.00	328.47	06/2008 -	09/2019	-	0/0
796	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM ,	12/2003	208.00 -	230.00	339.22	04/2008 -	03/2020	143(O) -	0/0
797	DHARAMTUL TO SONAPUR KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM ,	12/2003	160.00 -	167.98	223.81	05/2008 -	06/2019	-	0/0
798	HARANGAJO TO MAIBANG NH-54 - [N24000062]NHAI,ASSAM ,	12/2003	196.00 655.17	655.17	655.17	07/2009 10/2018	10/2018	-	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
799	BRAHMPUTRA BRIDGE NH NO-31 - [N24000063]NHAI,ASSAM ,	12/2003	217.61 -	360.84	453.70	04/2010 -	07/2019	-	0/0
800	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM , EPC	05/2015	454.89 -	454.89	123.20	05/2018 05/2020	12/2020	31(O) 0	2/4
801	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM , EPC	06/2015	437.39 -	437.39	9.30	06/2018 12/2020	12/2021	42(O) 0	0/4
802	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM , EPC	06/2015	463.49 -	463.49	22.32	06/2018 01/2021	12/2021	42(O) 0	0/4
803	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM , EPC	06/2016	829.00 -	829.00	304.25	01/2019 -	-	-	2/4
804	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM , EPC	03/2015	168.39 -	168.39	73.37	11/2018 -	-	-	4/4
805	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM , EPC	10/2014	588.95 -	588.95	382.22	11/2018 -	-	-	2/4
806	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM , EPC	11/2010	268.08 -	268.08	203.15	05/2017 -	-	-	0/0
807	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]MoRTH,ASSAM , ITEM RATE	11/2010	470.20 -	630.36	344.32	02/2011 -	-	-	0/0
808	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]MoRTH,ASSAM , EPC	11/2014	218.31 -	307.47	263.85	02/2018 -	-	-	0/0
809	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM , EPC	12/2015	225.02 -	159.20	26.00	12/2018 -	-	-	1/4
810	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM , EPC	12/2015	223.30 -	223.30	73.39	06/2018 -	-	-	3/4
811	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM , EPC	01/1991	520.01 -	520.01	50.38	- -	-	-	1/4
812	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM , EPC	12/2015	289.99 -	289.99	13.26	12/2018 -	-	-	0/4
813	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM , EPC	01/2016	294.17 -	294.17	63.00	01/2016 02/2019	04/2021	63(O) 0	1/4
814	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM , EPC	01/2016	252.00 -	252.00	4.74	01/2016 12/2021	12/2021	71(O) 0	0/4
815	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM ,	03/2015	829.00 -	829.00	304.27	01/2016 -	-	-	2/3

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
816	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL,ASSAM ,	10/2017	818.00 -	818.00	62.91	- -	06/2020	- -	0/4
817	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0 KM 54/0 TO KM 61/0 KM 69/0 TO KM 80/0 AN - [N24001152]MoRTH,ASSAM ,	09/2018	160.00 -	160.00	.50	09/2021 -	09/2021	0(O) -	0/0
818	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]MoRTH,ASSAM ,	11/2010	197.37 -	197.37	88.86	02/2014 -	12/2019	70(O) -	0/0
819	OUR LANNNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM ,	03/2017	1,049.51 -	1,049.51	89.16	- -	-	-	0/0
820	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR , PPP (ANNUITY)	08/2010	671.30 -	671.30	1,132.48	02/2013 -	03/2020	85(O) -	3/4
821	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR , PPP (BOT)	09/2011	574.00 -	574.00	768.73	03/2014 -	-	-	0/0
822	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR ,	10/2011	375.09 -	375.09	494.33	04/2014 -	-	-	0/0
823	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR , PPP (ANNUITY)	01/2011	575.00 -	575.00	850.24	07/2013 -	03/2020	80(O) -	2/3
824	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR , PPP (ANNUITY)	05/2011	511.54 585.00	591.00	571.22	11/2013 12/2019	03/2020	76(O) 0	0/0
825	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR , EPC	01/1991	675.00 -	675.00	154.56	- -	-	-	0/0
826	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MoRTH,BIHAR , ITEM RATE	01/1991	282.41 -	322.01	278.45	08/2016 -	-	-	0/0
827	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MoRTH,BIHAR , ITEM RATE	01/1991	358.22 -	377.64	325.19	10/2016 -	-	-	0/0
828	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR ,	08/2015	556.07 -	556.07	.00	- -	-	-	0/0
829	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR ,	12/2015	1,041.10 -	1,041.10	214.34	04/2019 -	-	-	0/0
830	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR ,	08/2015	814.04 -	825.17	646.72	- 07/2017	01/2020	- 0	2/3
831	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR ,	08/2015	322.09 247.00	322.09	77.53	04/2018 -	12/2020	32(O) -	0/0
832	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR ,	01/1991	642.41 -	681.67	402.94	- 04/2018	10/2020	- 0	1/2
833	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR ,	12/2015	1,167.45 -	1,167.45	113.26	- -	12/2019	- -	0/0
834	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR ,	08/2015	399.54 -	297.27	509.75	04/2019 10/2017	10/2019	-	3/4
835	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MoRTH,BIHAR ,	01/1991	478.35 -	478.35	.00	- -	-	-	0/0
836	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR ,	08/2015	854.80 -	854.80	558.04	- -	-	-	3/4

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
837	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR ,	08/2015	516.13 -	516.13	395.25	04/2018 -	-	-	4/4
838	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]MoRTH,BIHAR , EPC	01/1991	154.62 -	154.62	.00	- -	-	-	0/0
839	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH,BIHAR , EPC	01/1991	319.68 -	369.77	113.67	- -	-	-	0/0
840	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MoRTH,BIHAR ,	10/2013	278.39 -	278.39	.00	08/2014 -	-	-	0/0
841	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH,BIHAR ,	11/2013	683.83 -	560.70	597.00	07/2016 -	-	-	0/0
842	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MoRTH,BIHAR ,	02/2014	665.50 -	665.50	.00	07/2016 -	-	-	0/0
843	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH,BIHAR ,	02/2016	178.85 -	152.62	40.44	05/2016 -	-	-	0/0
844	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MoRTH,BIHAR ,	02/2016	369.77 -	369.77	.00	06/2016 -	-	-	0/0
845	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH,BIHAR ,	02/2016	553.30 -	478.35	289.14	05/2016 -	-	-	0/0
846	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR ,	01/2014	1,408.85 -	925.87	586.18	10/2016 -	-	-	0/0
847	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPR - [N24000580]MoRTH,BIHAR ,	03/2015	206.80 -	206.80	74.04	07/2016 -	-	-	0/0
848	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MoRTH,BIHAR ,	08/2015	288.24 -	288.24	286.46	11/2015 -	-	-	0/0
849	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR ,	05/2015	581.84 -	581.84	89.69	05/2017 04/2019	04/2019	-	0/0
850	REHABILIATION OF 4-LANE 5.575 KM LONG 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR ,	08/2016	1,742.01 -	1,742.01	1,034.37	12/2016 -	-	-	0/0
851	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR ,	03/2017	672.89 -	736.01	.00	03/2020 -	03/2020	0(O) -	0/0
852	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR ,	03/2017	235.48 -	227.77	11.00	03/2020 -	05/2021	14(O) -	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
853	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR , Central Sector Projects	08/2017	950.64 -	950.64	102.51	08/2017 -	02/2022	54(O) -	0/0
854	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR ,	12/2017	2,598.00 -	2,598.00	.00	- -	-	-	0/0
855	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR ,	01/2018	573.70 -	573.70	.00	- -	-	-	0/0
856	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR ,	01/2018	895.39 -	895.39	.00	- -	-	-	0/0
857	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR ,	03/2018	496.20 -	496.20	.00	- -	-	-	0/0
858	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR ,	09/2018	1,478.40 -	1,478.40	.00	- -	-	-	0/0
859	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999]MoRTH,BIHAR ,	11/2016	230.34 -	230.34	178.39	10/2019 -	-	-	0/0
860	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR ,	03/2018	153.24 -	153.24	2.06	- -	-	-	0/0
861	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]MoRTH,BIHAR ,	05/2014	199.98 -	199.98	153.43	08/2016 -	12/2020	52(O) -	0/0
862	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR ,	02/2019	2,926.42 -	2,926.42	.00	- -	-	-	0/0
863	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221 - [N24001223]MoRTH,CHANDIGARH ,	03/2010	179.89 271.00	271.00	.00	03/2013 -	03/2013	-	0/0
864	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1 - [N24001225]MoRTH,CHANDIGARH ,	12/2010	169.26 299.00	299.00	.00	01/2019 -	01/2019	-	0/0
865	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]MoRTH,CHHATISGARH , EPC	12/2015	291.05 -	291.05	182.16	- -	-	-	0/0
866	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]MoRTH,CHHATISGARH , EPC	11/2015	485.44 -	485.44	447.13	12/2015 -	-	-	0/0
867	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH ,	12/2015	596.67 -	596.67	399.92	05/2018 10/2019	10/2019	-	0/0
868	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH ,	12/2015	509.13 -	509.13	412.66	04/2018 08/2018	08/2018	-	0/0
869	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH ,	12/2015	726.67 598.13	598.13	414.73	04/2018 03/2020	03/2020	23(O) 0	0/0
870	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH ,	03/2018	1,029.96 -	1,261.05	97.55	- 03/2021	03/2021	- 0	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
871	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH,CHHATISGARH ,	01/2016	497.14 -	497.14	.00	08/2016 -	08/2016	-	0/0
872	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATISGARH ,	11/2015	335.32 -	335.32	.00	06/2017 -	06/2017	-	0/0
873	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]MoRTH,CHHATISGARH ,	01/2016	476.20 544.00	544.00	.00	09/2016 -	09/2016	-	0/0
874	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 127.500 TO 178.944 DARRIGHAT TO BANARI SECTION - [N24001220]MoRTH,CHHATISGARH ,	03/2016	491.52 -	491.52	.00	09/2016 -	09/2016	-	0/0
875	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATISGARH ,	01/2016	624.98 -	624.98	.00	10/2016 -	10/2016	-	0/0
876	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH,CHHATISGARH ,	03/2016	452.94 -	452.94	.00	07/2016 -	07/2016	-	0/0
877	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224]MoRTH,CHHATISGARH ,	03/2017	423.79 -	423.79	.00	01/2018 -	01/2018	-	0/0
878	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226]MoRTH,CHHATISGARH ,	12/2014	496.02 -	496.02	.00	03/2015 -	03/2015	-	0/0
879	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH,CHHATISGARH ,	11/2017	188.80 -	188.80	.00	05/2019 -	05/2019	-	0/0
880	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229]MoRTH,CHHATISGARH ,	12/2014	379.16 -	379.16	.00	11/2017 -	11/2017	-	0/0
881	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 - [N24001184]NHIDCL,DELHI ,	07/2017	269.69 -	269.69	.00	09/2019 -	12/2019	3(O) -	0/0
882	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDEAPAR BRIDGE - [N24000251]MoRTH,GOA , EPC	03/2015	297.00 -	297.00	290.64	04/2018 -	-	-	0/1
883	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]MoRTH,GOA ,	03/2015	298.33 -	298.33	160.33	- -	-	-	0/4
884	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]MoRTH,GOA , EPC	03/2015	184.05 -	184.05	96.58	- -	-	-	2/4
885	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]MoRTH,GOA , EPC	03/2015	280.16 -	290.59	219.47	- -	-	-	3/4
886	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA , EPC	10/2015	936.40 -	936.40	262.25	- -	-	-	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
887	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA , EPC	12/2015	773.98 -	773.98	259.66	- -	-	-	0/0
888	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH,GOA , EPC	12/2015	819.95 -	819.95	193.63	- -	-	-	0/0
889	PATRADEVI TO KARASWADA 4L - [N24001004]MoRTH,GOA ,	03/2017	634.32 634.32	634.32	109.33	05/2020 -	05/2020	0(O) -	1/4
890	KARASWADA TO BAMBOLIM - [N24001005]MoRTH,GOA ,	03/2017	852.67 852.67	852.67	86.04	12/2019 -	12/2019	0(O) -	1/4
891	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT , PPP (BOT)	03/2010	1,509.10 3,787.21	1,509.10	3,684.44	09/2012 12/2019	12/2019	87(O) 0	2/3
892	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT , PPP (BOT)	01/2011	953.88 -	953.88	976.79	07/2013 11/2020	11/2020	88(O) 0	0/0
893	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT , PPP (BOT)	01/2013	2,125.24 2,125.24	2,125.24	4,669.71	12/2015 -	-	-	3/3
894	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT ,	03/2014	503.16 -	503.16	389.50	08/2016 -	10/2017	-	0/0
895	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT ,	05/2016	998.18 -	998.18	441.80	- -	-	-	2/2
896	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT ,	05/2016	834.64 -	834.64	319.33	- -	-	-	1/1
897	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT ,	05/2016	723.64 -	723.64	313.19	- -	-	-	2/2
898	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT ,	05/2016	763.08 -	763.08	386.86	- -	-	-	2/2
899	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT ,	05/2016	425.60 241.41	425.60	103.13	- -	-	-	0/0
900	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT ,	05/2016	364.56 -	392.00	260.72	- -	12/2019	- -	0/0
901	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT ,	07/2016	829.97 -	829.97	192.41	- -	01/2020	- -	0/0
902	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT ,	12/2016	417.19 -	417.19	262.83	- -	09/2019	-	0/3
903	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT ,	01/2017	1,251.11 -	1,251.11	1,084.26	- -	01/2021	- -	0/0
904	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT ,	06/2017	1,958.88 -	1,958.88	1,116.85	06/2020 02/2018	02/2021	8(O) 0	0/3
905	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT , Central Sector Projects	10/2017	232.49 -	232.49	.00	10/2017 -	11/2019	25(O) -	0/0
906	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT ,	02/2018	1,052.21 1,449.00	1,449.00	336.43	- -	01/2021	- -	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
907	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT ,	03/2018	2,702.05 -	2,043.00	.00	- 05/2018	01/2021	- 0	0/0
908	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT ,	03/2018	1,437.64 1,687.00	1,437.64	564.11	- 12/2018	07/2021	- 0	0/0
909	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT ,	03/2018	1,161.39 1,404.00	1,161.39	.00	- 11/2021	-	-	0/0
910	WIDENING FROM TWO LANE TO FOUR LANE WITH PAVED SHOULDER AND STRENGTHNING OF EXISTING PAVEMENT BETWEE - [N24000920]MoRTH,GUJARAT ,	03/2016	223.67 -	223.67	112.81	02/2017 -	-	-	4/4
911	UPGRADATION TO 2 LANE WITH PAVED SHOULDER WITH RIGID PAVEMETS FROM 37/400 TO KM 66/700 ON NH 848 ON - [N24000921]MoRTH,GUJARAT , EPC	03/2016	208.34 -	208.34	112.87	02/2016 -	-	-	0/4
912	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]MoRTH,GUJARAT , EPC	12/2017	867.97 -	867.97	172.70	11/2018 -	-	-	0/1
913	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEE - [N24000923]MoRTH,GUJARAT , EPC	03/2018	464.07 -	464.07	125.89	11/2018 -	-	-	0/1
914	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPIR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]MoRTH,GUJARAT , EPC	10/2018	400.76 -	400.76	29.00	05/2019 -	-	-	0/0
915	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]MoRTH,GUJARAT , EPC	08/2017	962.43 -	962.43	81.55	03/2018 -	-	-	0/1
916	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197]MoRTH,GUJARAT ,	03/2018	351.00 -	351.00	.49	06/2021 -	06/2021	0(O) -	0/0
917	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA , PPP (BOT)	04/2007	486.00 -	486.00	470.01	05/2010 -	03/2020	118(O) -	0/0
918	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA , PPP (BOT)	05/2009	1,108.00 2,967.50	2,967.50	3,990.72	11/2011 -	03/2020	100(O) -	0/0
919	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA ,	08/2015	723.54 1,286.84	1,286.84	1,163.65	02/2018 10/2017	-	-	0/0
920	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA ,	12/2015	602.95 507.70	507.70	496.22	06/2016 -	10/2019	-	0/0
921	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA ,	01/2016	574.28 537.16	537.16	503.20	07/2018 -	11/2019	16(O) -	0/0
922	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA , PPP (BOT)	07/2015	2,128.72 -	2,128.72	971.24	04/2019 -	-	-	0/0
923	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA ,	11/2015	867.66 1,464.24	1,464.24	1,255.55	05/2018 02/2018	-	-	0/0
924	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA ,	08/2016	248.97 -	248.97	236.19	05/2019 -	01/2020	8(O) -	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
925	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA ,	09/2016	1,004.67 -	813.45	577.21	05/2019 -	02/2019	-	0/0
926	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA ,	03/2017	639.79 -	552.90	558.40	03/2020 -	-	-	0/0
927	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA ,	03/2018	1,484.30 -	1,484.30	111.66	- -	12/2020	- -	0/0
928	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA ,	03/2018	275.12 -	275.12	129.75	- -	03/2020	- -	0/0
929	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROMEXISTI - [N24000837]NHAI,HARYANA ,	03/2018	307.79 -	307.79	147.50	- -	03/2020	- -	0/0
930	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA ,	03/2018	634.70 931.21	931.21	125.31	- -	07/2021	- -	0/0
931	SIX LANING AND STREGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA ,	03/2018	795.50 -	799.30	115.56	- -	07/2021	- -	0/0
932	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA ,	03/2018	198.05 -	198.05	98.90	- -	03/2020	- -	0/0
933	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA ,	03/2018	181.78 -	181.78	66.03	- -	06/2020	- -	0/0
934	REDESIGNING REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA ,	03/2018	551.58 -	551.58	305.46	- -	03/2020	- -	0/0
935	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA ,	01/2017	247.25 -	247.25	144.71	03/2019 03/2020	03/2020	12(O) 6	0/0
936	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]MoRTH,HARYANA ,	01/2017	276.01 -	276.01	187.39	03/2019 07/2019	-	-	0/0
937	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA ,	01/2019	1,051.91 -	1,051.91	213.79	- -	-	-	0/0
938	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA ,	01/2019	1,120.06 -	1,120.06	228.53	- -	-	-	0/0
939	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA ,	01/2019	1,137.42 -	1,137.42	305.85	- -	-	-	0/0
940	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA ,	01/2019	1,033.19 -	1,033.19	209.69	- -	-	-	0/0
941	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA ,	01/2019	1,243.45 -	1,243.45	357.82	- -	-	-	0/0
942	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA ,	01/2019	889.36 -	889.36	284.61	- -	-	-	0/0
943	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA ,	01/2019	1,018.79 -	1,018.79	226.56	- -	-	-	0/0
944	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA ,	01/2019	996.65 -	996.65	320.30	- -	-	-	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
945	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH , PPP (BOT)	11/2013	1,916.79 -	1,916.79	1,948.92	11/2016 -	-	-	0/0
946	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH ,	09/2015	934.46 1,302.98	934.46	531.34	03/2018 -	03/2020	24(O) -	0/0
947	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH ,	02/2016	273.20 725.87	273.20	659.81	02/2019 -	06/2019	-	0/0
948	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH ,	08/2016	1,583.18 2,170.44	1,583.18	271.06	- -	09/2020	- -	0/0
949	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH ,	09/2016	1,273.71 1,464.12	1,273.71	573.04	- -	07/2020	- -	0/0
950	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH ,	10/2016	447.75 1,238.21	447.75	1,028.99	- -	11/2019	- -	0/0
951	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH ,	06/2017	2,485.93 2,946.82	2,485.93	359.79	06/2020 -	09/2021	15(O) -	0/0
952	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050 ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH ,	03/2018	478.74 1,071.75	478.74	15.06	- -	05/2021	- -	0/0
953	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,987.00 -	1,987.00	2,864.02	07/2015 12/2019	09/2020	62(O) 0	0/0
954	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	05/2011	2,159.00 -	2,519.00	4,706.90	06/2015 -	-	-	0/0
955	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,813.76 -	1,813.76	2,393.99	07/2013 -	-	-	0/0
956	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	06/2011	1,100.70 -	1,100.70	2,898.25	06/2014 09/2017	10/2020	76(O) 0	0/0
957	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR ,	12/2015	2,168.66 -	2,168.66	684.57	06/2019 -	12/2020	18(O) -	0/0
958	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR ,	12/2015	2,136.97 -	2,136.97	1,214.48	12/2018 -	07/2020	19(O) -	0/0
959	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR ,	12/2017	1,471.75 1,339.00	1,339.00	399.89	- -	01/2021	- -	1/3
960	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR ,	03/2018	404.17 -	404.17	46.34	08/2018 -	-	-	2/4
961	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR ,	03/2018	216.00 -	216.00	12.70	11/2018 -	-	-	0/4
962	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR ,	03/2018	253.44 -	253.44	.00	07/2019 -	-	-	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
963	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND , PPP (ANNUITY)	12/2012	1,479.00 -	1,479.00	740.26	06/2015 -	-	-	0/0
964	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND ,	02/2016	997.15 -	997.15	728.62	03/2019 -	-	-	0/0
965	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND ,	07/2016	458.03 -	458.03	325.89	- 12/2017	12/2019	- 0	0/0
966	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND ,	08/2016	323.72 -	323.72	232.58	08/2018 -	01/2020	17(O) -	0/0
967	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI,JHARKHAND ,	03/2017	165.50 -	172.16	117.09	03/2020 -	03/2020	0(O) -	0/0
968	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND ,	03/2017	239.68 -	235.90	91.24	03/2020 -	03/2020	0(O) -	0/0
969	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND ,	01/2018	273.46 -	273.46	.00	- -	-	-	0/0
970	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND ,	01/2018	1,155.16 999.00	1,155.16	30.13	- 06/2019	-	-	0/0
971	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND ,	03/2018	1,005.08 1,073.10	1,005.08	.00	- 03/2019	03/2021	- 0	0/0
972	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131]MoRTH,JHARKHAND ,	03/2018	212.99 -	212.99	93.80	06/2020 -	06/2020	0(O) -	0/0
973	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216]MoRTH,JHARKHAND ,	12/2016	196.00 -	196.00	.00	09/2021 -	09/2021	0(O) -	0/0
974	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA ,	09/2010	946.00 -	946.00	818.53	06/2018 -	12/2019	18(O) -	3/3
975	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA , EPC	03/2015	165.67 -	165.67	.00	11/2015 -	-	-	0/0
976	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MoRTH,KARNATAKA , EPC	03/2015	159.12 -	159.12	.00	11/2015 -	-	-	0/0
977	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MoRTH,KARNATAKA , EPC	01/1991	219.40 -	219.40	.00	01/2018 -	-	-	0/0
978	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA , PPP (BOT)	05/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020	52(O) -	0/0
979	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA , PPP (BOT)	03/2015	1,388.00 -	1,388.00	1,185.00	08/2018 -	03/2020	19(O) -	0/0
980	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA ,	03/2016	701.40 -	701.40	29.48	03/2019 -	11/2020	20(O) -	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
981	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA ,	03/2016	870.00 -	870.00	36.30	03/2019 -	11/2020	20(O) -	0/0
982	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA ,	08/2016	1,664.20 -	1,664.20	721.93	04/2020 -	04/2020	0(O) -	0/0
983	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA ,	08/2016	1,167.42 870.00	870.00	265.48	03/2019 03/2017	08/2020	17(O) 0	0/0
984	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA ,	09/2016	950.69 1,008.00	1,108.00	1,385.71	08/2019 -	12/2020	16(O) -	0/0
985	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA ,	03/2017	831.58 -	1,177.00	657.59	03/2020 -	07/2020	4(O) -	0/0
986	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA ,	03/2017	993.16 -	1,434.00	695.33	03/2020 -	06/2020	3(O) -	0/0
987	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA ,	02/2018	486.78 -	486.78	113.59	- -	-	-	0/0
988	SIX-LANING OF BANGALORE – NIDAGATTA SECTION KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA ,	02/2018	1,995.34 2,190.00	2,400.00	1,558.83	- 05/2019	11/2021	- 0	0/0
989	SIX LANING OF NIDAGATTA-MYSORE SECTION KM 74.20 TO KM 135.304 OF NH-275 IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA ,	02/2018	2,177.80 2,283.50	2,450.00	898.52	- 10/2019	-	-	0/0
990	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT - [N24001154]MoRTH,KARNATAKA ,	08/2016	367.44 -	367.44	61.95	01/2017 -	-	-	0/0
991	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT - [N24001155]MoRTH,KARNATAKA ,	08/2016	175.20 -	175.20	113.38	01/2017 -	-	-	0/0
992	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA - [N24001156]MoRTH,KARNATAKA ,	01/2017	166.67 -	166.67	117.05	09/2017 -	-	-	0/0
993	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA ,	08/2016	175.50 -	175.50	86.54	02/2017 -	-	-	0/0
994	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA ,	03/2018	159.97 -	159.97	.00	06/2019 -	-	-	0/0
995	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]MoRTH,KARNATAKA ,	01/2018	159.70 -	159.70	22.79	07/2018 -	-	-	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
996	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA ,	09/2017	191.60 -	191.60	26.24	10/2018 -	-	-	0/0
997	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]MoRTH,KARNATAKA ,	12/2017	297.30 -	297.30	.00	01/2019 -	-	-	0/0
998	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA ,	03/2018	325.86 -	325.86	62.54	10/2018 -	-	-	0/0
999	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA ,	08/2016	329.01 -	329.01	135.50	02/2017 -	-	-	0/0
1000	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA ,	10/2016	396.96 -	396.96	113.98	03/2017 -	-	-	0/0
1001	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA ,	11/2016	314.90 -	314.90	104.40	03/2017 -	-	-	0/0
1002	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA ,	03/2015	159.12 -	159.12	96.22	01/2016 -	-	-	0/0
1003	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776) - [N24001167]MoRTH,KARNATAKA ,	03/2015	165.67 -	165.67	87.63	01/2016 -	-	-	0/0
1004	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA ,	05/2018	171.60 -	171.60	.86	05/2018 -	05/2020	24(O) -	0/0
1005	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM. - [N24001170]MoRTH,KARNATAKA ,	01/2014	471.16 -	471.16	128.32	08/2014 -	-	-	0/0
1006	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA ,	01/2017	291.49 -	291.49	130.00	08/2017 -	-	-	0/0
1007	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA ,	02/2017	157.32 188.00	157.32	.00	05/2019 -	05/2021	24(O) -	0/0
1008	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA , PPP (BOT)	02/2010	617.00 -	617.00	943.17	08/2012 -	12/2019	88(O) -	0/0
1009	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH,KERALA , EPC	01/2014	255.75 348.00	348.43	290.12	09/2017 -	12/2019	27(O) -	0/0
1010	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA ,	06/2015	845.24 -	941.00	847.81	- -	01/2020	- -	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1011	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA ,	04/2016	804.97 -	804.97	456.79	06/2018 -	04/2020	22(O) -	0/0
1012	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA , Central Sector Projects	09/2017	1,124.11 -	1,232.76	292.23	09/2017 -	06/2020	33(O) -	0/0
1013	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA ,	02/2018	1,424.77 -	1,853.42	14.19	- -	-	-	0/0
1014	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH , PPP (BOT)	10/2010	1,175.00 -	1,175.00	1,509.96	04/2013 -	-	-	4/4
1015	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH , PPP (BOT)	11/2010	325.00 -	475.00	469.54	05/2013 -	-	-	3/3
1016	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]MoRTH,MADHYA PRADESH , BOT (TOLL)	01/2012	320.48 -	320.48	189.49	08/2015 -	-	-	0/0
1017	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH , EPC	06/2015	390.51 -	390.51	198.91	- -	03/2020	- -	0/0
1018	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]MoRTH,MADHYA PRADESH , EPC	11/2013	497.05 -	881.05	544.84	05/2017 -	05/2020	36(O) -	0/0
1019	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]MoRTH,MADHYA PRADESH , BOT (TOLL)	08/2015	257.80 -	257.00	12.38	- -	-	-	0/0
1020	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]MoRTH,MADHYA PRADESH , BOT (TOLL)	11/2011	954.43 -	954.43	235.61	09/2015 -	03/2020	54(O) -	0/0
1021	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH , BOT (TOLL)	01/2012	410.72 -	410.72	216.14	04/2015 -	10/2019	-	0/0
1022	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH ,	03/2015	795.76 622.00	622.00	638.13	- -	12/2019	- -	0/0
1023	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH ,	03/2015	794.30 622.00	622.00	592.72	- -	12/2019	- -	0/0
1024	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH , EPC	11/2015	628.45 -	628.45	259.33	01/2020 -	01/2020	0(O) -	0/0
1025	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH , EPC	12/2015	957.54 -	957.54	503.38	02/2020 -	02/2020	0(O) -	0/0
1026	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH ,	03/2015	928.83 -	928.83	630.61	- 06/2015	06/2015	-	0/0
1027	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH , PPP (BOT)	05/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	-	-	0/0
1028	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH ,	06/2015	1,012.90 -	1,012.90	226.10	03/2016 -	-	-	0/0
1029	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH ,	03/2015	810.22 -	810.22	695.69	- 06/2015	06/2015	-	0/0
1030	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH , PPP (BOT)	06/2015	1,583.79 -	1,583.79	1,648.90	01/2019 10/2019	10/2019	-	0/3

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

(November 2019)

Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning: Original / Revised	Date of Commissioning: Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1031	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH , EPC	03/2015	511.83 -	511.83	261.31	08/2017 -	02/2020	30(O) -	0/0
1032	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH ,	08/2016	227.49 -	227.49	129.93	01/2019 -	12/2019	11(O) -	3/4
1033	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH , Central Sector Projects	10/2017	639.97 -	639.97	331.84	10/2017 -	01/2020	27(O) -	2/4
1034	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	374.40 218.85	204.65	155.83	09/2017 -	-	-	3/4
1035	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	990.61 -	990.61	397.89	09/2017 -	01/2021	40(O) -	0/4
1036	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH ,	12/2017	950.27 -	950.27	168.05	- -	-	-	2/4
1037	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH ,	01/2018	960.24 -	960.24	328.34	- -	-	-	0/0
1038	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH ,	01/2018	770.73 -	770.73	59.45	- -	-	-	0/0
1039	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH ,	03/2018	162.56 -	162.56	88.47	03/2018 -	03/2020	24(O) -	0/0
1040	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH ,	03/2018	166.21 -	166.21	40.28	08/2018 -	06/2020	22(O) -	0/0
1041	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH ,	02/2018	169.63 -	169.63	11.39	03/2018 -	07/2020	28(O) -	0/0
1042	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]MoRTH,MADHYA PRADESH ,	11/2017	235.91 -	235.91	144.76	02/2018 -	03/2020	25(O) -	0/0
1043	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH ,	11/2017	184.62 -	184.62	65.06	02/2018 -	03/2020	25(O) -	0/0
1044	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]MoRTH,MADHYA PRADESH ,	03/2018	191.21 -	191.21	72.02	11/2019 -	06/2020	7(O) -	0/0
1045	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH ,	01/2017	205.05 -	205.05	79.65	03/2017 -	06/2020	39(O) -	0/0
1046	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH ,	03/2018	214.69 -	214.69	25.88	03/2018 -	06/2020	27(O) -	0/0
1047	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH ,	03/2018	217.22 -	217.22	45.76	08/2018 -	06/2020	22(O) -	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1048	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH ,	03/2018	233.04 -	233.04	109.26	03/2018 -	03/2020	24(O) -	0/0
1049	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH ,	11/2017	249.05 -	249.05	127.30	07/2018 -	03/2020	20(O) -	0/0
1050	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH ,	11/2017	254.17 -	254.17	152.81	02/2018 -	03/2020	25(O) -	0/0
1051	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH ,	02/2018	279.44 -	279.44	76.00	03/2018 -	04/2020	25(O) -	0/0
1052	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]MoRTH,MADHYA PRADESH ,	09/2016	287.34 -	287.34	148.65	01/2019 -	12/2019	11(O) -	0/0
1053	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH ,	01/2017	373.82 -	373.82	116.34	09/2019 -	05/2020	8(O) -	0/0
1054	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH ,	01/2016	809.16 -	809.16	236.96	07/2018 -	02/2020	19(O) -	0/0
1055	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH ,	03/2016	877.79 -	877.79	436.12	06/2019 -	12/2020	18(O) -	0/0
1056	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]MoRTH,MADHYA PRADESH ,	09/2016	178.23 -	178.23	114.16	09/2018 -	08/2019	-	0/0
1057	ANJANGAON TO MAH/MP BORDER - [N24001007]MoRTH,MADHYA PRADESH ,	01/2017	359.00 359.00	359.00	201.80	06/2019 -	-	-	0/4
1058	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH ,	11/2017	392.33 -	392.33	242.88	03/2018 -	06/2020	27(O) -	0/0
1059	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MoRTH,MADHYA PRADESH ,	01/2019	264.50 -	264.50	.00	03/2021 -	03/2021	0(O) -	0/0
1060	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH ,	10/2019	743.88 -	743.88	.00	- -	-	-	0/0
1061	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]NHAI,MADHYA PRADESH ,	12/2017	656.98 -	656.98	2.48	- -	-	-	0/0
1062	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213]NHAI,MADHYA PRADESH ,	12/2017	1,094.97 -	1,094.97	1.51	- -	-	-	0/0
1063	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]NHAI,MADHYA PRADESH ,	12/2017	217.96 -	217.96	.50	- -	-	-	0/0
1064	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA , PPP (BOT)	10/2010	1,724.55 -	1,724.55	2,401.00	03/2013 -	12/2019	81(O) -	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1065	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA , PPP (BOT)	05/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	-	-	2/2
1066	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]MoRTH,MAHARASHTRA , EPC	03/2015	168.30 -	168.30	52.00	- -	-	-	0/4
1067	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]MoRTH,MAHARASHTRA , EPC	08/2014	187.79 -	187.79	76.62	07/2016 -	-	-	0/12
1068	REHABILATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]MoRTH,MAHARASHTRA , EPC	01/2014	446.77 -	446.77	278.50	- -	-	-	3/4
1069	WIDENING NH-848 FROM KM 16.000 TO 34.000 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MoRTH,MAHARASHTRA , EPC	10/2015	289.60 -	289.60	90.65	- -	-	-	0/0
1070	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MoRTH,MAHARASHTRA , ITEM RATE	12/2011	156.26 227.00	247.95	175.00	- -	-	-	0/0
1071	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA , EPC	01/2015	225.81 -	225.81	85.11	- -	-	-	0/0
1072	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	2,288.18 -	2,288.18	487.81	05/2019 -	-	-	0/0
1073	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA ,	09/2015	414.51 414.00	414.00	532.46	05/2018 05/2020	05/2020	24(O) 0	0/1
1074	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA ,	10/2015	531.13 -	727.00	509.85	05/2018 -	09/2020	28(O) -	0/0
1075	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA , EPC	07/2015	1,885.74 -	1,885.74	1,636.02	05/2019 -	-	-	0/0
1076	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA ,	10/2015	593.26 41.54	636.24	461.85	05/2018 06/2020	06/2020	25(O) 0	0/1
1077	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB SERVICE ROADS FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA ,	12/2015	649.50 -	649.50	137.85	03/2019 04/2021	04/2021	25(O) 0	0/0
1078	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA ,	08/2015	505.00 -	504.00	235.19	05/2018 04/2019	09/2020	28(O) 0	0/1
1079	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA , PPP (BOT)	01/2015	972.50 -	972.50	3,512.79	07/2017 12/2019	03/2020	32(O) 5	0/0
1080	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA , PPP (BOT)	06/2014	923.04 -	923.04	764.07	11/2016 -	05/2020	42(O) -	0/0
1081	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	1,871.34 67.34	1,871.34	3,512.79	01/2018 12/2018	12/2019	23(O) 0	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1082	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA ,	04/2010	1,170.52 -	1,170.52	2,051.36	06/2012 -	-	-	0/0
1083	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA ,	03/2016	197.69 151.11	197.69	151.11	07/2018 -	-	-	0/0
1084	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA ,	03/2016	546.00 -	546.00	269.67	07/2019 12/2020	12/2020	17(O) 0	0/0
1085	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA ,	03/2016	591.66 -	591.66	310.56	07/2019 12/2020	12/2020	17(O) 0	0/0
1086	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA ,	03/2016	1,142.62 -	1,142.62	813.85	- -	-	-	0/0
1087	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA ,	03/2016	1,101.58 -	1,101.58	315.00	- -	-	-	0/0
1088	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA ,	11/2016	1,071.61 -	1,071.61	404.89	- -	07/2021	- -	1/4
1089	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA ,	11/2016	1,064.88 -	1,064.88	.00	- -	07/2021	- -	0/4
1090	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA ,	11/2016	400.25 -	400.25	64.89	03/2019 -	02/2021	23(O) -	0/0
1091	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA ,	11/2016	446.17 -	446.17	38.97	03/2019 -	03/2021	24(O) -	0/0
1092	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA ,	11/2016	290.73 315.00	315.00	234.43	- 03/2020	03/2019	-	0/0
1093	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA ,	01/2017	244.90 -	244.90	251.87	05/2019 -	12/2019	7(O) -	0/0
1094	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA ,	02/2017	904.16 911.07	904.16	854.25	02/2020 11/2017	05/2020	3(O) 0	0/0
1095	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA ,	03/2017	247.02 -	157.49	30.60	03/2020 02/2021	02/2020	-1(O) 0	0/0
1096	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA ,	03/2017	744.64 -	982.00	.00	03/2020 -	03/2020	0(O) -	0/0
1097	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA ,	03/2017	1,030.44 -	1,065.51	1,005.76	03/2020 -	05/2020	2(O) -	0/3
1098	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA ,	03/2017	988.34 988.00	1,043.28	1,034.00	03/2020 -	08/2020	5(O) -	3/3
1099	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA ,	03/2017	1,059.73 -	1,071.00	582.87	03/2017 05/2018	11/2020	44(O) 0	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1100	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA ,	03/2017	296.19 -	254.00	254.85	03/2020 -	09/2019	-	0/0
1101	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA ,	03/2017	1,098.06 -	1,160.64	1,056.76	03/2020 -	08/2020	5(O) -	0/3
1102	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA ,	12/2017	404.94 448.18	448.18	165.51	- -	10/2020	- -	0/0
1103	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA ,	01/2018	607.00 512.99	607.00	163.98	- 02/2019	08/2021	- 0	0/1
1104	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA ,	01/2018	621.00 565.02	621.00	327.15	- 10/2018	04/2021	- 0	2/3
1105	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA , EPC	03/2018	291.53 -	291.53	46.60	- 11/2020	11/2020	- 0	0/0
1106	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA , EPC	03/2018	289.21 -	289.21	27.87	- -	11/2020	- -	0/0
1107	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA ,	03/2018	1,162.92 -	1,162.92	14.76	- -	07/2021	- -	0/0
1108	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA ,	03/2018	642.13 -	807.00	341.71	- -	12/2020	- -	0/0
1109	SARSAM TO KOTHARI - [N24001002]MoRTH,MAHARASHTRA ,	02/2016	545.64 -	545.64	99.01	07/2019 -	-	-	0/4
1110	AKOLA TO AKOT - [N24001003]MoRTH,MAHARASHTRA ,	01/2017	313.95 -	313.95	41.05	06/2019 -	-	-	0/4
1111	AKOT TO ANJANGAON - [N24001006]MoRTH,MAHARASHTRA ,	01/2017	245.77 246.00	245.77	119.98	06/2019 -	-	-	0/4
1112	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA ,	02/2017	203.21 203.00	203.21	109.79	05/2019 -	12/2019	7(O) -	0/0
1113	SHEGAON TO DEORI PHATA - [N24001010]MoRTH,MAHARASHTRA ,	02/2017	373.10 373.00	373.10	143.43	05/2019 -	12/2019	7(O) -	0/4
1114	MEHKAR TO CHIKALI - [N24001011]MoRTH,MAHARASHTRA ,	02/2017	322.48 322.00	322.48	185.08	05/2019 -	-	-	0/4
1115	CHIKALI TO KHAMGAON - [N24001012]MoRTH,MAHARASHTRA ,	02/2017	548.03 548.00	548.03	319.00	06/2019 -	10/2019	-	0/4
1116	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA ,	01/2017	391.06 391.00	391.06	107.00	06/2019 -	06/2020	12(O) -	0/0
1117	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA ,	01/2017	385.87 386.00	385.87	203.75	06/2019 -	12/2019	6(O) -	0/0
1118	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA ,	01/2017	341.16 341.00	341.16	156.29	06/2019 -	12/2019	6(O) -	0/0
1119	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA ,	01/2017	471.61 472.00	471.61	259.90	06/2019 -	-	-	0/0
1120	DAHEGAON TO KUHI - [N24001017]MoRTH,MAHARASHTRA ,	01/2017	228.89 228.89	228.89	115.00	06/2019 -	-	-	3/4

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1121	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA ,	01/2017	392.83 393.00	392.83	286.60	06/2019 -	-	-	0/0
1122	KATOL TO WARUD - [N24001019]MoRTH,MAHARASHTRA ,	01/2017	463.62 664.00	463.62	125.34	06/2019 -	08/2019	-	0/4
1123	AMDI TO SAONER - [N24001021]MoRTH,MAHARASHTRA ,	01/2017	396.91 396.91	396.91	254.48	06/2019 -	08/2019	-	3/4
1124	WADI TO ASOLA - [N24001022]MoRTH,MAHARASHTRA ,	01/2017	363.82 363.82	363.82	41.10	09/2019 -	09/2020	12(O) -	1/4
1125	NAGAJ TO VAIJAPUR - [N24001023]MoRTH,MAHARASHTRA ,	01/2017	376.72 377.00	376.72	183.81	06/2019 -	12/2019	6(O) -	0/4
1126	MANGAON TO DIGHI PORT - [N24001024]MoRTH,MAHARASHTRA ,	01/2017	457.52 457.52	457.52	277.98	07/2019 -	07/2020	12(O) -	2/4
1127	INDAPAUR TO AGARDANDA - [N24001025]MoRTH,MAHARASHTRA ,	01/2017	355.17 -	355.17	164.87	07/2019 -	12/2019	5(O) -	3/4
1128	WAKAN PALI KHOPOLI - [N24001026]MoRTH,MAHARASHTRA ,	01/2017	376.19 376.19	376.19	34.03	05/2019 -	05/2020	12(O) -	1/4
1129	SHAHPUR PATGAON SECTION I - [N24001027]MoRTH,MAHARASHTRA ,	01/2018	150.79 150.79	150.79	21.42	12/2019 -	12/2019	0(O) -	1/4
1130	PATGAON KHOPOLI SECTION I - [N24001028]MoRTH,MAHARASHTRA ,	01/2018	170.00 -	170.00	56.57	12/2019 -	12/2019	0(O) -	0/4
1131	AHMADPUR TO PIMPLA - [N24001029]MoRTH,MAHARASHTRA ,	01/2017	422.38 422.38	422.38	169.58	08/2019 -	08/2019	-	2/4
1132	PIMPLA TO MANJARSUMBHA - [N24001030]MoRTH,MAHARASHTRA ,	01/2017	595.77 595.77	595.77	151.44	08/2019 -	08/2019	-	2/4
1133	MANJUSUMBA TO CHUMBALI - [N24001031]MoRTH,MAHARASHTRA ,	01/2017	228.54 228.54	228.54	102.30	08/2019 -	08/2019	-	2/4
1134	DEORI TO AMGAON - [N24001032]MoRTH,MAHARASHTRA ,	01/2017	409.62 410.00	409.62	181.78	05/2019 -	05/2020	12(O) -	0/4
1135	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]MoRTH,MAHARASHTRA ,	01/2017	486.19 486.19	486.19	218.55	07/2019 -	07/2019	-	2/4
1136	PARTUR TO MAJALGAON - [N24001034]MoRTH,MAHARASHTRA ,	01/2017	420.57 420.57	420.57	176.39	07/2019 -	07/2019	-	2/4
1137	MANSAR TO SALAIKHURD - [N24001035]MoRTH,MAHARASHTRA ,	01/2018	418.36 -	418.36	125.13	12/2019 -	12/2019	0(O) -	0/4
1138	MAJALGAON TO KAIJ - [N24001036]MoRTH,MAHARASHTRA ,	01/2017	413.99 -	413.99	299.33	07/2019 -	07/2019	-	0/0
1139	KAIJ TO KUSALAM - [N24001037]MoRTH,MAHARASHTRA ,	01/2017	554.78 554.78	554.78	163.90	07/2019 -	07/2019	-	2/4
1140	MAHAD TO RAIGAD FORT - [N24001038]MoRTH,MAHARASHTRA ,	07/2018	237.40 -	237.40	8.34	05/2020 -	05/2020	0(O) -	0/4
1141	JINTUR TO PARBHANI - [N24001039]MoRTH,MAHARASHTRA ,	01/2017	356.66 356.66	356.66	33.88	- -	-	-	0/4
1142	JAHIRABAD TO LATUR - [N24001040]MoRTH,MAHARASHTRA ,	01/2017	461.96 461.96	461.96	160.43	11/2019 -	11/2019	0(O) -	2/4
1143	SHIROD SHAHPURER TO NANDED - [N24001041]MoRTH,MAHARASHTRA ,	01/2017	211.34 211.34	211.34	107.83	07/2019 -	07/2019	-	2/4
1144	SALAIKHURD TO TIRORA - [N24001042]MoRTH,MAHARASHTRA ,	01/2018	415.25 415.25	415.25	96.22	12/2019 -	12/2019	0(O) -	0/4
1145	NILAJPHATA TO BHANDARA - [N24001043]MoRTH,MAHARASHTRA ,	01/2018	420.63 421.00	420.63	31.60	05/2020 -	05/2020	0(O) -	0/4

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1146	KALMAB TO RALEGAON - [N24001044]MoRTH,MAHARASHTRA ,	01/2017	467.78 -	467.78	301.91	06/2019 -	-	-	0/4
1147	JALGAON TO BHADGAON - [N24001045]MoRTH,MAHARASHTRA ,	01/2018	307.54 308.00	307.54	124.59	11/2019 -	11/2019	0(O) -	0/4
1148	RALEGAON TO RAMTIRTH - [N24001046]MoRTH,MAHARASHTRA ,	01/2017	210.81 -	210.81	114.69	07/2019 -	-	-	0/4
1149	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA ,	01/2018	259.55 260.00	259.55	145.00	11/2019 -	11/2019	0(O) -	0/0
1150	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA ,	01/2017	232.77 -	232.77	89.51	07/2019 -	-	-	0/0
1151	KARAD TO VITA - [N24001049]MoRTH,MAHARASHTRA ,	01/2018	344.85 245.00	344.85	96.04	12/2019 -	12/2019	0(O) -	0/4
1152	VITA TO NAGAJ - [N24001050]MoRTH,MAHARASHTRA ,	03/2018	304.58 305.00	304.58	24.16	12/2019 -	12/2019	0(O) -	0/4
1153	NALDURG TO AKKALKOT - [N24001051]MoRTH,MAHARASHTRA ,	02/2018	274.50 275.00	274.50	65.39	12/2019 -	12/2019	0(O) -	0/4
1154	SANGOLA TO JATH - [N24001052]MoRTH,MAHARASHTRA ,	01/2018	257.38 257.00	257.38	84.15	12/2019 -	12/2019	0(O) -	0/4
1155	KARAD TO TAGAON - [N24001053]MoRTH,MAHARASHTRA ,	01/2017	537.81 538.00	537.81	89.97	06/2019 -	06/2020	12(O) -	0/4
1156	TASGAON TO SHIRDHON - [N24001054]MoRTH,MAHARASHTRA ,	01/2017	195.64 196.00	195.64	169.73	11/2019 -	11/2019	0(O) -	0/4
1157	HELWAK TO KARAD - [N24001055]MoRTH,MAHARASHTRA ,	02/2017	416.99 -	416.99	127.40	07/2019 -	-	-	0/4
1158	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA ,	02/2017	422.02 422.00	422.02	247.01	07/2019 -	-	-	0/0
1159	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MoRTH,MAHARASHTRA ,	02/2017	407.19 407.00	407.19	25.00	06/2019 -	06/2020	12(O) -	0/4
1160	KARWANDI TO RAJURI - [N24001058]MoRTH,MAHARASHTRA ,	03/2018	276.95 277.00	276.95	87.47	12/2019 -	12/2019	0(O) -	0/4
1161	SHIVUR TO YEOLA - [N24001059]MoRTH,MAHARASHTRA ,	03/2018	181.08 -	181.08	7.50	12/2019 -	12/2019	0(O) -	0/4
1162	PALPHATA TO PHULAMBARI - [N24001060]MoRTH,MAHARASHTRA ,	03/2018	227.19 227.00	227.19	74.23	12/2019 -	12/2019	0(O) -	0/4
1163	CHIKALI TO DHAD - [N24001061]MoRTH,MAHARASHTRA ,	03/2018	189.46 189.00	189.46	35.54	12/2019 -	12/2019	0(O) -	0/4
1164	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]MoRTH,MAHARASHTRA ,	03/2018	336.21 336.00	336.21	71.66	12/2019 -	12/2019	0(O) -	0/4
1165	WADIGODRI TO DHANGRIPIMPRI - [N24001063]MoRTH,MAHARASHTRA ,	03/2018	194.23 194.00	194.23	86.23	02/2020 -	02/2020	0(O) -	0/4
1166	DHANGIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]MoRTH,MAHARASHTRA ,	03/2018	217.14 217.00	217.14	99.77	02/2020 -	02/2020	0(O) -	0/4
1167	PARBHANI TO GANGKHED - [N24001065]MoRTH,MAHARASHTRA ,	03/2018	238.19 238.00	238.19	45.85	12/2019 -	12/2019	0(O) -	0/4
1168	LATUR TO PANGAON - [N24001066]MoRTH,MAHARASHTRA ,	03/2018	336.47 336.00	336.47	123.48	12/2019 -	12/2019	0(O) -	0/4
1169	OMREGA TO AUSA - [N24001067]MoRTH,MAHARASHTRA ,	03/2018	272.04 272.00	272.04	137.24	12/2019 -	12/2019	0(O) -	0/4

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1170	WASHIM TO DASTAPUR - [N24001068]MoRTH,MAHARASHTRA ,	03/2018	165.51 -	165.51	34.45	12/2019 -	12/2019	0(O) -	1/4
1171	NANDED TO JALKOT - [N24001069]MoRTH,MAHARASHTRA ,	12/2017	456.93 457.00	456.93	78.50	09/2019 -	09/2019	-	1/4
1172	DASTAPUR TO KARANJA - [N24001070]MoRTH,MAHARASHTRA ,	03/2018	182.63 -	182.63	82.40	12/2019 -	12/2019	0(O) -	2/4
1173	JALKOT TO TOGRI - [N24001071]MoRTH,MAHARASHTRA ,	07/2018	299.92 300.00	299.92	19.20	08/2020 -	08/2020	0(O) -	0/4
1174	KHERDA TO NAGZARI - [N24001072]MoRTH,MAHARASHTRA ,	03/2018	181.30 -	181.30	72.50	12/2019 -	12/2019	0(O) -	0/4
1175	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA ,	09/2018	301.38 301.00	301.38	41.00	08/2020 -	08/2020	0(O) -	0/0
1176	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA ,	03/2018	249.29 -	249.29	97.20	12/2019 -	12/2019	0(O) -	0/0
1177	OSMANNAGAR TO KUNDRAL - [N24001075]MoRTH,MAHARASHTRA ,	09/2017	344.25 344.00	344.25	61.02	08/2020 -	08/2020	0(O) -	0/4
1178	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA ,	03/2018	219.91 -	219.91	126.76	12/2019 -	12/2019	0(O) -	0/0
1179	KUNDRAL TO WAZAR - [N24001077]MoRTH,MAHARASHTRA ,	01/2018	225.25 225.00	225.25	148.75	12/2019 -	12/2019	0(O) -	2/4
1180	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA ,	03/2018	228.31 -	228.31	13.50	12/2019 -	12/2019	0(O) -	0/0
1181	ARDHAPUR TO HIMAYATNAGAR - [N24001079]MoRTH,MAHARASHTRA ,	12/2017	426.06 426.00	426.06	66.97	06/2020 -	06/2020	0(O) -	1/4
1182	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA ,	03/2018	256.15 -	256.15	36.50	12/2019 -	12/2019	0(O) -	0/0
1183	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]MoRTH,MAHARASHTRA ,	03/2018	294.87 295.00	294.87	36.30	12/2019 -	12/2019	0(O) -	1/4
1184	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA ,	03/2018	223.46 -	223.46	21.42	12/2019 -	12/2019	0(O) -	0/0
1185	CHIKLI TO TAKARKHED - [N24001083]MoRTH,MAHARASHTRA ,	03/2018	393.10 393.10	393.10	153.97	12/2019 -	12/2019	0(O) -	2/4
1186	PAHUR TO BODHWAD - [N24001084]MoRTH,MAHARASHTRA ,	01/2017	244.93 -	244.93	59.23	05/2020 -	05/2020	0(O) -	0/4
1187	TAKARKHED TO JALNA - [N24001085]MoRTH,MAHARASHTRA ,	09/2017	417.90 418.00	417.90	119.26	06/2019 -	12/2019	6(O) -	0/4
1188	BODHWAD TO STATE BORDER - [N24001086]MoRTH,MAHARASHTRA ,	01/2017	178.26 -	178.26	118.95	07/2019 -	-	-	0/4
1189	MANGRUPHIR TO MAHAN - [N24001087]MoRTH,MAHARASHTRA ,	03/2018	222.13 222.13	222.13	78.63	11/2019 -	11/2019	0(O) -	0/4
1190	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA ,	03/2018	177.84 177.00	177.84	73.69	12/2019 -	12/2019	0(O) -	0/0
1191	MALEGAON TO RISOD - [N24001089]MoRTH,MAHARASHTRA ,	02/2018	303.24 303.24	303.24	131.97	12/2019 -	12/2019	0(O) -	0/4
1192	KOLDE TO KHETIYA - [N24001090]MoRTH,MAHARASHTRA ,	01/2017	509.18 -	509.18	205.93	07/2019 -	-	-	0/4
1193	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]MoRTH,MAHARASHTRA ,	03/2016	536.65 356.00	536.65	465.20	12/2019 -	12/2019	0(O) -	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1194	SATARA TO MHASWAD - [N24001092]MoRTH,MAHARASHTRA ,	01/2017	653.46 -	653.46	207.42	07/2019 -	-	-	0/4
1195	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA ,	12/2017	309.94 310.00	309.94	51.32	12/2019 -	12/2019	0(O) -	0/0
1196	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA ,	12/2017	244.04 244.00	244.04	40.94	03/2019 -	12/2019	9(O) -	0/0
1197	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA ,	01/2017	388.44 -	388.44	191.77	- -	-	-	0/0
1198	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA ,	01/2018	264.41 264.00	264.41	36.71	03/2019 -	12/2019	9(O) -	0/0
1199	SELDOH TO PANVAR - [N24001097]MoRTH,MAHARASHTRA ,	07/2018	404.33 404.00	404.33	30.19	05/2020 -	05/2020	0(O) -	0/4
1200	WARDHA TO HINGAGHAT - [N24001098]MoRTH,MAHARASHTRA ,	01/2018	216.90 216.90	216.90	55.00	12/2019 -	12/2019	0(O) -	1/4
1201	MHASWAD TO TEMBHURNI - [N24001099]MoRTH,MAHARASHTRA ,	01/2017	488.60 -	488.60	184.71	07/2019 -	-	-	0/4
1202	AHMEDNAGAR TO BARAMATI - [N24001100]MoRTH,MAHARASHTRA ,	01/2017	955.40 -	955.40	347.50	08/2019 -	08/2019	-	0/4
1203	KURUDWADI TO PANDHARPUR - [N24001101]MoRTH,MAHARASHTRA ,	01/2017	307.63 -	307.63	157.17	07/2019 -	-	-	0/4
1204	PANDHARPUR TO SANGOLA - [N24001102]MoRTH,MAHARASHTRA ,	07/2017	218.38 -	218.38	168.75	07/2019 -	-	-	0/4
1205	SARAD VANI PIMPALGAON - [N24001103]MoRTH,MAHARASHTRA ,	01/2017	250.46 -	250.46	105.63	07/2019 -	-	-	0/4
1206	MALEWADA TO CHIMUR - [N24001104]MoRTH,MAHARASHTRA ,	10/2016	322.55 -	322.55	156.91	06/2019 -	06/2020	12(O) -	2/4
1207	CHIMUR TO WARORA - [N24001105]MoRTH,MAHARASHTRA ,	11/2016	467.70 -	467.70	156.72	03/2019 -	-	-	0/4
1208	PEN TO KHOPOLI - [N24001106]MoRTH,MAHARASHTRA ,	03/2018	301.39 302.00	301.39	.00	03/2018 -	12/2019	21(O) -	0/4
1209	PANCHARAL TO MANDANGHAR - [N24001107]MoRTH,MAHARASHTRA ,	07/2018	381.08 302.00	381.08	13.03	05/2020 -	05/2020	0(O) -	0/4
1210	CHALISGAON TO NANDGAON - [N24001108]MoRTH,MAHARASHTRA ,	03/2018	206.97 207.00	206.97	92.89	12/2019 -	12/2019	0(O) -	0/4
1211	KUSUMBA TO MALEGAON - [N24001109]MoRTH,MAHARASHTRA ,	03/2018	243.45 244.00	243.45	80.02	12/2019 -	12/2019	0(O) -	0/4
1212	BAMNI TO NAVAEGAON - [N24001110]MoRTH,MAHARASHTRA ,	09/2017	241.69 242.00	241.69	83.29	04/2020 -	04/2020	0(O) -	1/4
1213	KOLHA TO NASRATPUR - [N24001111]MoRTH,MAHARASHTRA ,	04/2016	281.78 282.00	281.78	47.73	04/2019 -	04/2020	12(O) -	0/4
1214	NASRATPUR TO BARASGAON - [N24001112]MoRTH,MAHARASHTRA ,	07/2016	406.54 406.54	406.54	142.00	09/2019 -	09/2019	-	2/4
1215	BARASGAON TO RAHATEE - [N24001113]MoRTH,MAHARASHTRA ,	07/2016	289.11 290.00	289.11	23.82	09/2018 -	04/2021	31(O) -	0/4
1216	INDAPUR TO VADPALE - [N24001114]MoRTH,MAHARASHTRA ,	01/2017	1,202.52 1,202.52	1,202.52	635.90	12/2019 -	03/2020	3(O) -	1/4
1217	VADPALE TO BHOGAN KHURD - [N24001115]MoRTH,MAHARASHTRA ,	01/2017	1,598.47 1,560.00	1,598.47	751.91	11/2019 -	03/2020	4(O) -	1/4
1218	GADCHIROLI TO MUL - [N24001116]MoRTH,MAHARASHTRA ,	12/2016	484.15 -	484.15	160.31	06/2019 -	-	-	2/4

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1219	MUL TO CHANDRAPUR - [N24001117]MoRTH,MAHARASHTRA ,	12/2016	162.34 -	162.34	32.80	07/2019 -	07/2019	-	1/4
1220	SAKOLI TO BHANDARA - [N24001118]MoRTH,MAHARASHTRA ,	01/2017	362.96 362.96	362.96	37.83	06/2019 -	11/2019	5(O) -	0/4
1221	NAGBHID TO ARMORI - [N24001119]MoRTH,MAHARASHTRA ,	09/2016	269.05 -	269.05	221.91	07/2019 -	-	-	0/4
1222	AKKALKOT TO DHUDHNI - [N24001120]MoRTH,MAHARASHTRA ,	04/2016	211.42 -	211.42	131.85	02/2019 -	02/2020	12(O) -	0/4
1223	NASHIK TO PETH - [N24001121]MoRTH,MAHARASHTRA ,	12/2015	289.60 -	289.60	118.81	11/2018 -	11/2019	12(O) -	0/4
1224	PAITHAN TO SHIRUR - [N24001122]MoRTH,MAHARASHTRA ,	03/2017	341.80 -	341.80	107.89	06/2019 -	-	-	0/4
1225	SHIRUR TO KHARDA - [N24001123]MoRTH,MAHARASHTRA ,	02/2017	381.77 -	381.77	156.79	06/2019 -	-	-	0/4
1226	AURANGABAD TO SILLOD - [N24001124]MoRTH,MAHARASHTRA ,	02/2017	456.32 -	456.32	91.75	06/2019 -	-	-	0/4
1227	SILLOD TO FARDAPUR - [N24001125]MoRTH,MAHARASHTRA ,	02/2017	337.46 -	337.46	39.22	06/2019 -	-	-	0/4
1228	FARDAPUR TO JALGAON - [N24001126]MoRTH,MAHARASHTRA ,	02/2017	456.45 -	456.45	67.74	06/2019 -	-	-	0/4
1229	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA ,	02/2017	406.51 -	406.51	280.69	06/2019 -	-	-	0/0
1230	BHOKAR TO SARSAM - [N24001128]MoRTH,MAHARASHTRA ,	02/2017	295.09 -	295.99	162.64	07/2019 -	-	-	0/4
1231	BHOGAN KHURD TO KASHEDI - [N24001132]MoRTH,MAHARASHTRA ,	09/2017	743.21 743.00	743.21	52.87	06/2021 -	06/2021	0(O) -	1/4
1232	PARSHURAM GHAT TO ARAWALI - [N24001133]MoRTH,MAHARASHTRA ,	04/2016	983.14 983.00	983.14	655.15	12/2019 -	11/2019	-1(O) -	1/4
1233	KANTE TO WAKED - [N24001134]MoRTH,MAHARASHTRA ,	03/2016	1,230.02 1,230.00	1,230.02	555.61	11/2019 -	11/2019	0(O) -	1/4
1234	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA ,	02/2016	1,244.75 1,245.00	1,244.75	357.60	02/2019 -	-	-	0/0
1235	TALGAON TO KALMATH - [N24001136]MoRTH,MAHARASHTRA ,	10/2016	904.70 905.00	904.70	604.05	03/2020 -	03/2020	0(O) -	2/4
1236	KALMATH TO ZARAP - [N24001137]MoRTH,MAHARASHTRA ,	09/2016	1,338.13 1,338.00	1,338.13	959.51	03/2020 -	03/2020	0(O) -	3/5
1237	PARLI PIMPLA DAHIGUDA - [N24001138]MoRTH,MAHARASHTRA ,	02/2017	205.72 205.72	205.72	30.42	06/2019 -	06/2020	12(O) -	1/4
1238	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA ,	02/2018	355.99 355.99	355.99	131.97	12/2019 -	12/2019	0(O) -	0/0
1239	WARDHA TO ARVI - [N24001150]MoRTH,MAHARASHTRA ,	02/2018	313.58 313.58	313.58	12.96	04/2020 -	04/2020	0(O) -	0/4
1240	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL,MANIPUR ,	08/2017	517.57 -	457.77	137.04	10/2018 -	10/2021	36(O) -	1/4
1241	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174]MoRTH,MANIPUR ,	10/2016	235.31 -	235.31	91.38	11/2020 -	11/2020	0(O) -	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1242	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA ,	12/2015	479.20 -	479.20	711.38	05/2018 03/2018	10/2019	-	0/0
1243	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA ,	04/2017	553.51 -	553.51	32.78	- -	09/2021	- -	0/4
1244	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA ,	03/2019	306.28 -	306.28	42.66	05/2019 -	-	-	0/4
1245	WIDENING TO 2 LANE RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM , ITEM RATE	11/2010	624.41 -	992.67	853.82	03/2011 -	12/2019	105(O) -	0/0
1246	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM , ITEM RATE	08/2010	193.69 -	327.92	254.24	10/2010 -	12/2019	110(O) -	0/0
1247	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM , ITEM RATE	08/2010	195.04 -	377.99	305.38	10/2010 -	06/2020	116(O) -	0/0
1248	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM ,	04/2017	519.09 -	519.09	.00	09/2019 -	09/2019	-	0/0
1249	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM ,	04/2017	640.07 -	640.07	.00	09/2019 -	09/2019	-	0/0
1250	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM ,	04/2017	642.96 -	642.96	.00	09/2019 -	09/2019	-	0/0
1251	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM ,	04/2017	473.18 -	473.18	.00	09/2019 -	09/2019	-	0/0
1252	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM ,	04/2017	537.82 -	537.82	.00	09/2019 -	09/2019	-	0/0
1253	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM ,	04/2017	518.53 -	518.53	.00	09/2019 -	09/2019	-	0/0
1254	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM ,	04/2017	404.29 -	404.29	.00	09/2019 -	09/2019	-	0/0
1255	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM ,	04/2017	428.11 -	428.11	.00	09/2019 -	09/2019	-	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1256	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM ,	08/2010	186.96 -	305.61	275.06	09/2014 -	12/2019	63(O) -	0/0
1257	GWALIOR-JHANSI NH-75 - [N24000089]NHAI,MULTI STATE , PPP (ANNUITY)	12/2003	604.00 364.59	364.59	215.58	12/2009 08/2020	03/2020	123(O) -5	0/0
1258	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE , PPP (BOT)	02/2009	1,693.75 2,848.49	1,693.75	2,848.49	08/2011 -	-	-	2/2
1259	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE , PPP (ANNUITY)	02/2011	2,498.76 -	2,498.76	2,531.46	08/2014 -	-	-	0/0
1260	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE , PPP (BOT)	09/2011	2,848.00 -	2,848.00	1,159.10	03/2014 04/2017	06/2020	75(O) 0	0/0
1261	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE , PPP (BOT)	09/2011	754.00 -	754.00	1,364.18	03/2013 -	12/2019	81(O) -	0/0
1262	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE , PPP (BOT)	10/2012	1,928.22 -	2,945.00	2,467.00	04/2015 01/2017	06/2020	62(O) 3	0/4
1263	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE ,	09/2016	1,244.10 -	1,244.10	1,394.00	- -	02/2020	- -	0/0
1264	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE ,	03/2018	1,294.47 -	1,296.00	.00	- -	-	-	0/0
1265	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE ,	03/2018	998.70 -	962.00	.00	- -	-	-	0/0
1266	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD MON-TAMLU-MERANGKONG ROAD PHEK- PFUTSERO ROA - [N24000315]MoRTH,NAGALAND , ITEM RATE	12/2010	1,296.00 -	1,296.00	.00	02/2011 -	-	-	0/0
1267	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND ,	03/2016	373.07 387.00	373.07	211.16	08/2016 -	08/2019	-	2/4
1268	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND ,	03/2016	396.52 339.55	396.52	235.52	08/2016 -	06/2020	46(O) -	2/4
1269	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND ,	03/2016	429.52 340.00	429.52	167.54	08/2016 -	08/2019	-	2/4
1270	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND ,	02/2017	507.68 -	507.68	129.13	04/2017 -	-	-	1/4
1271	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND ,	02/2017	387.00 -	387.00	135.12	09/2018 -	-	-	1/4
1272	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND ,	03/2018	500.09 -	500.09	.00	09/2018 -	-	-	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1273	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND ,	03/2018	339.57 233.35	339.57	.00	09/2018 07/2019	-	-	0/0
1274	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND ,	03/2018	239.30 -	239.30	.00	09/2018 05/2019	-	-	0/4
1275	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND ,	03/2018	285.68 -	285.68	9.58	09/2018 -	-	-	0/4
1276	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND ,	03/2018	315.03 -	315.03	18.60	09/2018 -	-	-	0/4
1277	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND ,	03/2018	240.64 -	240.64	17.29	09/2018 -	-	-	0/4
1278	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND ,	03/2018	237.72 136.73	237.72	29.67	09/2018 11/2018	-	-	1/2
1279	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND ,	03/2018	251.97 160.10	251.97	18.66	09/2018 11/2018	-	-	0/2
1280	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND ,	03/2018	282.98 -	282.98	12.76	09/2018 11/2018	-	-	0/2
1281	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND ,	03/2018	215.12 -	215.12	12.45	09/2018 -	-	-	1/4
1282	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND ,	03/2018	215.79 -	215.79	10.21	09/2018 -	-	-	1/4
1283	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND ,	03/2018	272.89 -	272.89	.00	09/2018 -	-	-	0/4
1284	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND ,	03/2018	323.98 -	323.98	.00	09/2018 -	-	-	0/4
1285	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND ,	10/2016	167.62 -	167.62	42.15	12/2020 -	12/2020	0(O) -	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1286	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND ,	10/2016	172.63 -	172.63	45.02	12/2020 -	12/2020	0(O) -	0/0
1287	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND ,	11/2016	336.25 -	336.25	62.64	09/2019 -	09/2019	-	0/0
1288	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND ,	03/2017	217.35 -	217.35	35.10	11/2020 -	11/2020	0(O) -	0/0
1289	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180]MoRTH,NAGALAND ,	03/2019	237.51 -	237.51	.00	12/2022 -	12/2022	0(O) -	0/0
1290	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA , PPP (BOT)	03/2012	1,410.00 -	1,410.00	1,935.14	09/2014 -	-	-	0/0
1291	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA , PPP (BOT)	12/2011	1,047.00 -	1,047.00	1,874.43	06/2014 -	03/2019	-	0/0
1292	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MoRTH,ODISHA , EPC	01/1991	218.63 -	218.63	29.27	10/2017 -	-	-	0/0
1293	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MoRTH,ODISHA ,	01/1991	229.41 -	229.41	6.65	05/2018 -	-	-	0/0
1294	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]MoRTH,ODISHA , EPC	07/2014	342.05 -	342.05	258.91	01/2017 -	-	-	0/0
1295	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA ,	07/2015	1,282.94 -	1,282.94	255.43	- -	03/2021	- -	0/0
1296	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA ,	12/2015	752.28 -	752.28	76.78	- -	11/2019	- -	0/1
1297	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]MoRTH,ODISHA , EPC	12/2011	159.39 -	159.39	210.29	11/2017 -	-	-	0/0
1298	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA , EPC	12/2011	191.08 -	191.08	99.98	08/2015 -	12/2019	52(O) -	0/0
1299	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA ,	02/2016	1,069.65 -	1,069.65	526.12	- -	03/2020	- -	0/0
1300	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA ,	09/2016	2,510.04 -	2,510.04	313.18	08/2019 -	03/2021	19(O) -	0/0
1301	REHABILITAITON AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA ,	10/2016	1,008.96 -	1,008.96	506.49	- -	03/2021	- -	0/0
1302	WIDENING AND STRENFTHENING OF EXISITNG SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA ,	03/2014	191.50 192.00	192.00	136.19	05/2016 -	12/2019	43(O) -	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1303	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MoRTH,ODISHA ,	01/2015	326.63 327.00	326.63	249.26	04/2018 -	-	-	0/0
1304	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MoRTH,ODISHA ,	02/2015	239.91 240.00	160.00	147.25	10/2017 -	-	-	0/0
1305	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MoRTH,ODISHA ,	07/2014	342.05 342.00	342.00	258.91	01/2017 -	-	-	0/0
1306	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA ,	08/2013	171.96 172.00	172.00	88.30	06/2016 -	11/2019	41(O) -	0/0
1307	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MoRTH,ODISHA ,	06/2016	157.30 157.00	157.30	97.29	06/2018 -	-	-	0/0
1308	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA ,	03/2017	1,288.07 -	1,420.00	446.76	03/2020 -	03/2021	12(O) -	0/0
1309	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA , Central Sector Projects	07/2017	476.56 -	476.56	.00	07/2017 11/2020	06/2021	47(O) 0	0/0
1310	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA ,	12/2017	686.65 -	686.65	91.47	- 07/2020	06/2021	- 0	0/0
1311	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA ,	12/2017	417.51 -	417.51	35.52	- -	06/2021	- -	0/0
1312	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA ,	01/2018	953.09 -	953.09	126.71	- 05/2020	06/2021	- 0	0/0
1313	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA ,	01/2018	668.86 -	668.86	134.42	- 05/2020	06/2021	- 0	0/0
1314	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA ,	01/2018	633.68 -	633.68	.00	- -	-	-	0/0
1315	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA ,	01/2018	614.48 -	614.48	52.00	- -	08/2021	- -	0/0
1316	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA ,	01/2018	564.66 -	564.66	46.76	- -	08/2021	- -	0/0
1317	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA ,	01/2018	686.65 -	686.65	89.80	- 03/2020	06/2021	- 0	0/0
1318	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA ,	01/2018	1,522.00 -	1,522.00	132.24	- 06/2021	06/2021	- 0	0/0
1319	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA ,	01/2018	999.00 -	999.00	.00	- -	06/2021	- -	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1320	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA ,	01/2018	503.88 -	503.88	3.98	- -	06/2021	- -	0/0
1321	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA , EPC	03/2018	806.11 -	806.11	21.39	- -	04/2021	- -	0/0
1322	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. - [N24000911]MoRTH,ODISHA ,	03/2016	165.06 -	165.06	92.59	12/2016 -	-	-	0/0
1323	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA ,	08/2016	287.70 -	287.70	153.90	02/2017 -	-	-	0/0
1324	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA ,	09/2016	295.67 -	295.67	127.75	02/2017 -	-	-	0/0
1325	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA ,	12/2016	223.50 -	223.50	44.52	08/2018 -	-	-	0/0
1326	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA ,	12/2016	206.88 -	206.88	41.69	04/2018 -	-	-	0/0
1327	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA ,	03/2018	214.23 -	214.23	23.44	08/2018 -	-	-	0/0
1328	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA ,	03/2018	199.16 -	199.16	25.63	08/2018 -	-	-	0/0
1329	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]MoRTH,PUNJAB , EPC	12/2015	766.36 -	766.36	685.36	- 09/2019	-	-	0/0
1330	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]MoRTH,PUNJAB , EPC	11/2015	847.02 -	847.02	795.00	- 09/2019	-	-	0/0
1331	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB , EPC	11/2015	889.24 -	904.82	739.41	- 12/2019	-	-	0/0
1332	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB ,	09/2014	479.00 -	479.00	453.80	- -	03/2020	- -	0/0
1333	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB ,	10/2015	447.29 746.43	746.43	613.57	12/2017 06/2020	12/2019	24(O) 0	0/0
1334	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]MoRTH,PUNJAB , EPC	06/2015	892.17 -	892.17	648.44	- -	-	-	0/0
1335	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB ,	08/2016	1,388.34 2,541.32	2,587.50	1,449.00	09/2019 03/2020	03/2020	6(O) 6	0/0
1336	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB ,	08/2016	1,169.61 1,367.00	1,169.61	1,151.18	- -	04/2020	- -	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1337	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB ,	03/2017	754.54 -	756.27	181.12	03/2020 -	04/2020	1(O) -	0/0
1338	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB ,	02/2018	261.76 -	207.00	92.25	- -	01/2021	- -	0/0
1339	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB , EPC	03/2018	199.90 149.90	199.90	92.61	- -	-	-	0/0
1340	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB , EPC	03/2018	196.05 149.90	196.05	143.03	- -	01/2020	- -	0/0
1341	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905]MoRTH,PUNJAB ,	03/2018	322.48 -	322.48	120.18	07/2020 -	07/2020	0(O) -	0/0
1342	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]MoRTH,PUNJAB ,	03/2018	173.24 -	173.24	56.66	06/2020 -	06/2020	0(O) -	0/0
1343	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB ,	03/2018	293.10 -	293.10	63.14	08/2020 -	08/2020	0(O) -	0/0
1344	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB ,	10/2017	1,069.59 -	1,069.59	663.50	10/2019 12/2020	12/2020	14(O) 14	0/0
1345	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB ,	03/2018	170.57 192.48	170.57	46.23	11/2020 -	05/2021	6(O) -	0/0
1346	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927]MoRTH,PUNJAB ,	03/2018	293.64 -	293.64	28.24	08/2020 -	08/2020	0(O) -	0/0
1347	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB ,	03/2018	293.64 -	293.64	134.32	08/2020 -	08/2020	0(O) -	0/0
1348	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MoRTH,RAJASTHAN , EPC	10/2014	269.22 -	269.22	33.24	01/2015 -	-	-	0/0
1349	WIDENING AND STRENGHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MoRTH,RAJASTHAN , EPC	10/2014	257.09 -	257.09	14.18	01/2015 -	-	-	0/0
1350	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MoRTH,RAJASTHAN , EPC	10/2013	278.87 -	278.87	.00	05/2014 -	-	-	0/0
1351	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MoRTH,RAJASTHAN , ITEM RATE	01/1991	376.52 -	376.52	.00	04/2014 -	-	-	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1352	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MoRTH,RAJASTHAN , EPC	02/2015	383.40 -	383.40	244.68	03/2015 -	-	-	0/0
1353	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MoRTH,RAJASTHAN , EPC	12/2015	621.43 -	621.43	387.22	06/2018 -	-	-	0/4
1354	TWO LANING WITH PAVED SHOULDER OF KARAUlI - DHOLPUR - [N24000344]NHAI,RAJASTHAN ,	09/2014	425.19 -	425.19	276.40	09/2016 09/2014	10/2019	-	0/0
1355	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN ,	10/2015	597.00 -	597.00	587.64	10/2017 04/2018	03/2020	29(O) 2	3/4
1356	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN , PPP (BOT)	11/2012	530.07 -	530.07	556.02	08/2016 -	12/2019	40(O) -	0/0
1357	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN , PPP (BOT)	08/2014	822.90 -	822.90	844.08	04/2018 -	-	-	0/0
1358	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]MoRTH,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	2,323.04	10/2013 -	-	-	0/0
1359	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]MoRTH,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	492.00	10/2013 -	-	-	0/4
1360	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN , PPP (BOT)	02/2008	1,673.70 -	1,673.70	3,326.93	10/2011 -	-	-	0/0
1361	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN ,	08/2015	275.90 -	275.90	257.52	- 02/2016	10/2019	-	0/0
1362	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI,RAJASTHAN , PPP (BOT)	06/2016	637.18 -	637.18	588.00	06/2019 -	09/2019	-	0/0
1363	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN , PPP (BOT)	06/2016	763.23 -	763.23	439.88	06/2019 -	11/2019	5(O) -	1/1
1364	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589]NHAI,RAJASTHAN ,	06/2016	649.00 -	649.00	320.14	06/2019 -	09/2019	-	0/0
1365	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN ,	07/2016	688.70 881.00	688.70	701.76	- 05/2017	11/2019	- 0	0/0
1366	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN ,	07/2016	331.46 -	331.46	267.94	10/2018 -	-	-	0/0
1367	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN ,	08/2016	320.30 -	320.30	237.81	01/2019 -	10/2019	-	4/4

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1368	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN ,	09/2016	1,239.82 -	1,239.82	1,363.85	- -	05/2020	- -	3/4
1369	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN ,	09/2016	1,100.19 -	1,145.31	967.00	- -	05/2020	- -	0/0
1370	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN ,	12/2016	1,031.95 -	1,031.95	367.00	- -	08/2020	- -	0/0
1371	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN ,	04/2017	894.00 -	929.32	750.00	04/2020 -	11/2019	-5(O) -	0/0
1372	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN , Central Sector Projects	10/2017	964.17 -	964.17	390.91	10/2017 -	11/2020	37(O) -	0/0
1373	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAUR ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN ,	12/2017	1,308.73 -	1,308.73	99.68	- -	12/2020	- -	0/0
1374	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN ,	02/2018	1,103.88 -	1,103.88	344.06	- -	09/2020	- -	0/0
1375	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN ,	02/2018	741.86 -	741.86	.00	- -	-	-	0/0
1376	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN ,	02/2018	716.76 -	716.76	232.06	- -	-	-	0/0
1377	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN ,	03/2018	874.25 -	874.25	195.00	- -	-	-	0/0
1378	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN ,	03/2018	1,158.35 -	1,158.35	369.55	- -	-	-	0/0
1379	WIDENING STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]MoRTH,RAJASTHAN ,	11/2017	187.82 -	187.82	59.14	04/2018 -	-	-	1/4
1380	NETRA VILLAGE TO MANDORE SECTION OF NH-65 KM 267+500 TO 296+070 (4L) UNDER EPC. - [N24000951]MoRTH,RAJASTHAN ,	10/2014	382.81 -	382.81	335.93	01/2015 -	-	-	3/4
1381	UP-GRADATION TO TWO LANE WITH PAVED SHOULDER FOR SECTION FROM KM 58.000 TO KM 91.600 (BALOTRA TO SAN - [N24000952]MoRTH,RAJASTHAN ,	01/2017	179.32 -	179.32	113.12	11/2017 -	-	-	2/4
1382	CONSTRUCTION OF NAGAUR BYPASS FROM EXISTING KM 166/260 TO KM 180/500 OF NH-65 ON EPC MODE. - [N24000953]MoRTH,RAJASTHAN ,	03/2016	155.77 -	155.77	99.92	09/2016 -	-	-	3/4
1383	NAGAUR-BIKANER OF NH-11 (2L+PS) UNDER PPP. - [N24000954]MoRTH,RAJASTHAN ,	01/2012	378.07 478.73	478.73	188.98	01/2014 -	-	-	1/4

MoSPI OCMS

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1384	CITTORGARH-NEEMACH (4L) OF NH-79 AND NIMBAHARA PRATAPGARH (2L+PS) OF NH-113 UNDER PPP. - [N24000955]MoRTH,RAJASTHAN ,	10/2012	511.21 -	511.21	814.79	10/2013 -	-	-	3/4
1385	DEVELOPMENT AND OPERATION OF BIKANER-SURATGARH SECTION OF NH-15 BY 2L+PS IN THE STATE OF RAJASTHAN - [N24000956]MoRTH,RAJASTHAN ,	03/2009	501.00 671.54	671.54	659.98	09/2013 -	-	-	3/4
1386	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]MoRTH,RAJASTHAN ,	11/2017	163.95 -	163.95	67.93	04/2018 -	-	-	3/4
1387	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]MoRTH,RAJASTHAN ,	02/2018	370.30 -	370.30	207.58	06/2018 -	-	-	1/4
1388	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]MoRTH,RAJASTHAN ,	02/2018	341.79 -	341.79	120.47	05/2018 -	-	-	1/4
1389	CONSTRUCTION OF 4 LANING BY CC PAVEMENT ON KOTA-DARAH OF NH-12 FROM 256/550 TO 289/550 UNDER EPC. - [N24000960]MoRTH,RAJASTHAN ,	12/2015	621.43 -	621.43	426.67	10/2016 -	-	-	3/4
1390	UP-GRADATION TO 2 LANE WITH PAVED SHOULDER FOR SECTION FROM KM 118.900 TO KM 156.955 BALOTRA TOSANDE - [N24000961]MoRTH,RAJASTHAN ,	01/2017	163.54 -	163.54	106.15	07/2017 -	-	-	2/4
1391	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MoRTH,RAJASTHAN ,	03/2019	178.13 -	178.13	16.35	- -	-	-	0/0
1392	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]MoRTH,SIKKIM ,	04/2013	151.59 -	151.59	196.76	08/2013 -	12/2019	76(O) -	0/0
1393	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]MoRTH,SIKKIM , ITEM RATE	04/2013	166.27 -	166.27	132.27	08/2013 -	-	-	0/0
1394	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]MoRTH,SIKKIM , ITEM RATE	01/2013	182.28 -	269.14	185.49	02/2013 -	12/2019	82(O) -	0/0
1395	RHENOK-RORAHTHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM , Central Sector Projects	04/2017	388.00 -	447.37	142.95	10/2017 -	-	-	2/4
1396	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM ,	04/2017	318.42 -	318.42	66.63	11/2017 -	-	-	2/4
1397	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM ,	03/2017	375.80 -	375.80	77.39	- -	-	-	0/0
1398	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM ,	11/2017	290.05 -	290.05	35.34	11/2017 -	-	-	1/4
1399	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM ,	03/2018	264.84 -	264.84	.00	06/2018 -	-	-	0/4

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1400	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU , PPP (BOT)	09/2011	1,250.00 -	1,250.00	1,333.68	12/2013 -	06/2020	78(O) -	0/0
1401	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU ,	06/2011	600.00 -	600.00	329.92	06/2013 01/2019	08/2020	86(O) 0	0/0
1402	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU , PPP (ANNUITY)	05/2010	374.00 -	374.00	237.00	05/2013 -	-	-	0/0
1403	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU , PPP (ANNUITY)	09/2011	485.00 -	485.00	406.68	08/2013 -	-	-	0/0
1404	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHTH 170 KM) - [N24000213]NHAI,TAMIL NADU , PPP (ANNUITY)	04/2012	624.00 -	624.00	350.79	04/2014 -	-	-	0/0
1405	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MoRTH,TAMIL NADU , EPC	03/2015	258.97 -	268.92	.00	08/2015 -	-	-	0/0
1406	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MoRTH,TAMIL NADU , EPC	03/2015	157.18 162.00	162.00	.00	07/2015 -	-	-	0/0
1407	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- - [N24000318]MoRTH,TAMIL NADU , EPC	11/2015	154.14 -	154.14	.00	08/2015 -	-	-	0/0
1408	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU ,	05/2015	1,387.11 -	1,387.11	980.46	11/2017 -	07/2019	-	0/0
1409	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU ,	06/2015	563.92 -	563.92	93.53	12/2017 -	-	-	0/0
1410	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU ,	07/2014	401.11 -	401.11	273.89	01/2017 -	-	-	0/0
1411	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU , PPP (BOT)	03/2007	516.00 -	516.00	886.70	07/2008 -	-	-	0/0
1412	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU ,	02/2016	707.82 -	707.82	375.47	08/2018 -	03/2020	19(O) -	0/0
1413	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU ,	02/2016	641.17 -	641.17	369.23	07/2018 -	05/2020	22(O) -	0/0
1414	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU ,	03/2017	848.45 -	848.45	87.01	03/2020 -	03/2020	0(O) -	0/0
1415	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU , Central Sector Projects	03/2016	641.17 -	641.17	369.23	07/2016 -	05/2020	46(O) -	0/0
1416	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU , Central Sector Projects	08/2017	1,176.37 -	1,176.37	193.39	08/2017 -	09/2020	37(O) -	0/0
1417	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU , Central Sector Projects	09/2017	244.27 -	244.27	168.40	09/2017 -	04/2020	31(O) -	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1418	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU , Central Sector Projects	09/2017	1,227.87 -	1,227.87	330.29	09/2017 -	08/2020	35(O) -	0/0
1419	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU ,	12/2017	379.90 -	379.90	112.41	- -	03/2020	- -	0/0
1420	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU ,	02/2018	1,166.26 -	1,166.26	163.29	- -	02/2021	- -	0/0
1421	FOUR LANINIG OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU , EPC	03/2018	505.35 -	505.35	36.14	- -	11/2020	- -	0/0
1422	FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300) - [N24000827]NHAI,TAMIL NADU , EPC	03/2018	628.71 -	628.71	106.92	- -	11/2020	- -	0/0
1423	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU ,	03/2018	633.55 -	482.04	.00	- -	-	-	0/0
1424	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU ,	03/2018	1,016.92 -	1,071.00	.00	- -	04/2021	- -	0/0
1425	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU ,	03/2018	2,065.96 -	2,169.00	.00	- -	-	-	0/0
1426	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA , PPP (BOT)	04/2014	1,266.60 1,544.00	1,544.00	1,446.45	09/2016 -	09/2019	-	0/0
1427	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]MoRTH,TELANGANA , EPC	01/2014	270.00 -	270.00	19.84	03/2016 -	-	-	1/4
1428	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA , EPC	03/2015	153.21 -	153.21	100.10	01/2017 -	09/2019	-	0/0
1429	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA ,	12/2015	1,423.96 897.03	897.03	757.88	11/2018 07/2019	03/2020	16(O) 3	0/0
1430	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA ,	03/2017	4,429.00 -	4,429.00	.00	03/2017 -	-	-	0/0
1431	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K - [N24000804]NHAI,TELANGANA ,	03/2018	802.65 -	802.65	81.03	- -	-	-	0/0
1432	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA ,	03/2018	950.63 -	950.63	173.59	- -	-	-	0/0
1433	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA ,	03/2018	857.62 -	857.62	1.61	- -	-	-	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1434	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA ,	03/2018	828.29 998.89	828.29	.00	- 11/2019	-	-	0/0
1435	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA ,	10/2016	298.32 -	298.32	83.57	02/2019 -	06/2020	16(O) -	0/0
1436	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA ,	10/2016	248.83 -	248.83	91.52	03/2019 -	03/2020	12(O) -	0/0
1437	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA ,	01/2017	244.54 -	244.54	138.52	05/2019 09/2019	12/2019	7(O) 0	0/0
1438	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA ,	01/2017	196.52 -	196.52	103.22	10/2019 -	12/2019	2(O) -	0/0
1439	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH,TELANGANA ,	01/2017	283.00 -	283.00	166.22	12/2019 -	12/2019	0(O) -	0/0
1440	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA ,	01/2017	359.27 -	359.27	237.90	05/2019 -	12/2019	7(O) -	0/0
1441	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA ,	01/2017	300.00 -	300.00	100.33	05/2019 -	03/2020	10(O) -	0/0
1442	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH,TELANGANA ,	01/2018	283.15 -	283.15	42.22	05/2020 -	05/2020	0(O) -	0/0
1443	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH,TELANGANA ,	01/2018	230.03 -	230.03	127.98	12/2019 -	12/2019	0(O) -	0/0
1444	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH,TELANGANA ,	02/2018	206.13 -	206.13	127.86	06/2020 -	06/2020	0(O) -	0/0
1445	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH,TELANGANA ,	02/2018	294.13 -	294.13	39.44	11/2019 -	11/2019	0(O) -	0/0
1446	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH,TELANGANA ,	02/2018	220.28 -	220.28	37.58	11/2019 -	11/2019	0(O) -	0/0
1447	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH,TELANGANA ,	02/2018	426.52 -	426.52	225.51	04/2020 -	04/2020	0(O) -	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1448	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH,TELANGANA ,	03/2018	322.81 -	322.81	1.66	09/2020 -	09/2020	0(O) -	0/0
1449	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH,TELANGANA ,	03/2018	626.76 -	626.76	80.66	07/2020 -	07/2020	0(O) -	0/0
1450	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH,TELANGANA ,	01/2017	605.08 -	605.08	273.88	10/2019 -	10/2019	-	0/0
1451	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA ,	03/2018	192.67 -	192.67	107.37	07/2019 -	12/2019	5(O) -	0/0
1452	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH,TELANGANA ,	01/2019	193.19 -	193.19	.00	- -	-	-	0/0
1453	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA , EPC	10/2014	369.00 -	369.00	316.74	03/2018 12/2019	-	-	3/4
1454	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH,TRIPURA ,	10/2016	171.90 -	171.90	14.77	08/2020 -	08/2020	0(O) -	0/0
1455	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH , PPP (BOT)	02/2011	1,141.00 -	1,141.00	1,715.42	08/2013 -	-	-	0/0
1456	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH , PPP (BOT)	03/2011	1,046.00 -	1,046.00	805.19	09/2013 -	-	-	0/0
1457	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH , PPP (BOT)	07/2012	291.36 -	291.36	459.07	01/2014 -	-	-	0/0
1458	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH , PPP (BOT)	03/2013	1,573.00 -	1,573.00	2,078.25	09/2015 -	-	-	0/0
1459	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH , EPC	01/2014	282.41 -	282.41	155.53	03/2016 -	-	-	0/0
1460	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH ,	05/2015	261.09 275.00	261.09	240.96	05/2017 -	-	-	0/0
1461	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH ,	04/2014	351.34 -	351.34	433.68	01/2016 -	-	-	0/0
1462	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH ,	09/2015	368.73 -	368.73	239.04	09/2016 03/2018	03/2018	-	0/0
1463	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH ,	06/2014	301.04 -	301.04	207.94	01/2016 -	-	-	0/0
1464	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI,UTTAR PRADESH ,	04/2014	495.78 -	495.78	633.24	01/2016 -	-	-	0/0
1465	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]MoRTH,UTTAR PRADESH , EPC	10/2013	445.89 -	653.29	464.05	03/2017 -	-	-	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1466	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]MoRTH,UTTAR PRADESH , ITEM RATE	11/2010	305.49 -	305.49	131.08	03/2017 -	-	-	0/0
1467	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH , PPP (BOT)	07/2015	1,657.20 -	1,657.20	2,345.00	01/2019 -	-	-	0/0
1468	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH ,	12/2015	611.65 -	611.65	728.24	06/2016 -	-	-	0/0
1469	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH ,	01/2016	815.28 2,182.03	815.28	520.89	06/2018 -	06/2020	24(O) -	0/0
1470	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH ,	01/2016	1,027.53 2,433.38	1,027.53	601.13	06/2018 -	06/2020	24(O) -	0/0
1471	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH ,	06/2016	667.00 2,257.49	667.00	464.05	07/2018 -	04/2020	21(O) -	0/0
1472	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH ,	12/2015	667.00 3,007.86	667.00	549.07	06/2018 -	04/2020	22(O) -	0/0
1473	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH , EPC	05/2013	164.54 -	164.54	126.41	08/2015 -	12/2019	52(O) -	0/0
1474	MEERUT-BULANDSHAHAR - [N24000539]NHAI,UTTAR PRADESH ,	01/2016	683.24 868.77	987.94	727.69	- 10/2019	02/2020	- 0	0/1
1475	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH ,	01/2016	1,081.57 -	1,057.60	1,024.76	06/2019 12/2016	09/2019	-	0/0
1476	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH ,	03/2016	676.73 -	676.73	945.17	04/2019 -	-	-	0/0
1477	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKPUR) - [N24000547]NHAI,UTTAR PRADESH ,	03/2016	1,404.50 3,267.94	1,404.50	2,977.58	- 03/2017	-	-	0/0
1478	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPU - [N24000549]NHAI,UTTAR PRADESH ,	03/2016	1,396.74 -	1,396.74	227.26	- -	-	-	0/0
1479	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH ,	03/2016	1,587.49 -	2,982.00	276.87	04/2019 -	-	-	0/0
1480	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH ,	03/2016	899.00 -	899.00	561.27	04/2019 07/2020	07/2020	15(O) 0	0/0
1481	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH ,	03/2016	1,668.00 -	1,668.00	946.08	- -	01/2020	- -	0/0
1482	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH ,	03/2016	1,408.00 -	1,408.00	442.70	- -	07/2020	- -	0/0
1483	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH ,	03/2016	1,737.00 -	1,737.00	1,159.07	- -	04/2020	- -	0/0
1484	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH ,	08/2016	2,016.00 -	2,016.00	1,996.00	04/2019 -	11/2019	7(O) -	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1485	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH ,	12/2016	534.55 -	531.00	433.62	- -	09/2019	-	0/0
1486	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH ,	01/2017	450.68 -	450.68	397.62	- -	-	-	0/0
1487	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH ,	03/2017	1,373.28 -	1,373.28	571.96	03/2020 -	11/2020	8(O) -	0/4
1488	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH ,	03/2017	1,184.71 -	1,310.00	563.15	03/2020 -	08/2020	5(O) -	0/4
1489	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH ,	03/2017	1,989.00 2,602.09	1,989.00	882.41	03/2020 11/2017	05/2020	2(O) 0	0/0
1490	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH ,	03/2017	2,064.99 -	2,447.00	1,896.03	03/2020 06/2020	06/2020	3(O) 0	0/0
1491	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH ,	12/2017	1,232.21 3,207.63	1,087.00	502.12	- 02/2018	05/2020	- 2	0/0
1492	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH ,	12/2017	207.00 -	207.00	34.77	- 03/2020	12/2020	- 0	0/0
1493	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH ,	12/2017	305.00 -	305.00	.00	- -	-	-	0/0
1494	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH ,	01/2018	450.77 929.89	450.77	.00	- -	-	-	0/0
1495	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH ,	02/2018	670.50 -	670.50	25.44	- -	-	-	0/0
1496	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH ,	03/2018	809.07 1,065.70	809.07	107.50	- -	-	-	0/0
1497	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH ,	03/2018	925.40 1,197.00	1,197.00	401.68	- -	-	-	0/0
1498	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH ,	03/2018	1,117.84 -	1,117.84	.00	- -	12/2021	- -	0/0
1499	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH ,	03/2018	2,140.93 -	2,140.93	1,229.85	- -	-	-	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1500	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH ,	03/2018	1,120.57 1,332.00	1,332.00	183.54	- -	-	-	0/0
1501	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH ,	03/2018	1,025.80 -	677.07	156.01	- -	-	-	0/0
1502	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH ,	03/2018	1,115.28 -	770.04	260.94	- -	-	-	0/0
1503	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH ,	02/2018	972.77 1,444.25	972.77	494.71	- 02/2019	-	-	0/0
1504	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH ,	11/2016	326.99 327.00	326.99	.00	- -	-	-	0/0
1505	REHABILITATION AND UPGRADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942]MoRTH,UTTAR PRADESH ,	03/2016	208.50 -	208.50	139.97	11/2019 -	12/2019	1(O) -	0/0
1506	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139]MoRTH,UTTAR PRADESH ,	10/2016	218.94 219.00	218.94	103.89	03/2020 -	03/2020	0(O) -	0/0
1507	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]MoRTH,UTTAR PRADESH ,	11/2016	215.16 215.00	215.16	160.46	09/2019 -	10/2019	-	0/0
1508	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH ,	03/2016	240.30 240.00	240.30	198.06	01/2020 -	01/2020	0(O) -	0/0
1509	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]MoRTH,UTTAR PRADESH ,	10/2016	176.94 177.00	176.94	141.11	10/2018 -	09/2019	-	0/0
1510	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MoRTH,UTTAR PRADESH ,	10/2013	445.89 653.00	653.29	464.07	03/2017 -	10/2019	-	0/0
1511	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]MoRTH,UTTAR PRADESH ,	05/2013	164.54 165.00	164.54	89.14	08/2015 -	-	-	0/0
1512	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH ,	03/2016	249.50 -	249.50	156.70	05/2019 -	03/2020	10(O) -	0/0
1513	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2- - [N24001147]MoRTH,UTTAR PRADESH ,	10/2016	239.63 -	239.63	212.09	02/2019 -	07/2019	-	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1514	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148]MoRTH,UTTAR PRADESH ,	03/2016	599.34 -	599.34	485.53	01/2020 -	01/2020	0(O) -	0/0
1515	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH – 14 - [N24001185]NHAI,UTTAR PRADESH , PPP BOT (Hybrid Annuity)	11/2017	2,159.00 -	2,159.00	831.09	01/2019 -	-	-	0/0
1516	REHABILITATION AND UPGRADATION OF BARAICH - SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA - [N24001202]MoRTH,UTTAR PRADESH ,	03/2016	388.83 -	388.83	304.47	12/2019 -	12/2019	0(O) -	0/0
1517	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]MoRTH,UTTAR PRADESH ,	10/2016	218.90 -	218.90	62.69	03/2020 -	03/2020	0(O) -	0/0
1518	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH ,	07/2016	208.88 -	208.88	88.62	10/2019 -	12/2019	2(O) -	0/0
1519	R AND U FROM KM 385.00 TO KM 420.000 TO 2-LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 - [N24001205]MoRTH,UTTAR PRADESH ,	12/2016	209.10 -	209.10	159.51	10/2019 04/2020	04/2020	6(O) 0	0/0
1520	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH ,	03/2018	263.89 242.05	242.05	139.38	04/2020 -	04/2020	0(O) -	0/0
1521	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH ,	03/2018	185.18 -	185.18	65.66	02/2020 -	02/2020	0(O) -	0/0
1522	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208]MoRTH,UTTAR PRADESH ,	03/2018	288.30 -	288.30	.34	08/2020 -	08/2020	0(O) -	0/0
1523	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH ,	03/2016	296.50 -	296.50	40.27	09/2020 -	09/2020	0(O) -	0/0
1524	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH ,	03/2018	306.59 -	306.59	.00	- -	-	-	0/0
1525	IMPROVEMENT AND UP-GRADATION OF EXISITING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH ,	11/2018	281.45 -	281.45	.00	- -	-	-	0/0
1526	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND ,	11/2011	478.51 -	478.00	315.11	10/2013 -	02/2020	76(O) -	0/0
1527	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND ,	03/2016	720.00 -	720.00	322.19	- 10/2020	10/2020	- 0	0/0
1528	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND ,	03/2016	1,443.00 -	1,443.00	1,246.85	- -	02/2020	- -	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1529	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND ,	11/2012	605.84 -	722.46	723.95	07/2018 12/2019	02/2020	19(O) 0	0/0
1530	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND ,	03/2018	274.31 -	274.31	29.13	05/2018 -	-	-	1/4
1531	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND ,	03/2018	403.36 -	403.36	99.65	06/2018 -	-	-	1/4
1532	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND ,	03/2018	417.24 -	417.24	112.62	05/2018 -	-	-	1/4
1533	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH,UTTARAKHAND ,	12/2017	257.34 -	257.34	62.79	12/2019 -	12/2019	0(O) -	0/0
1534	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH,UTTARAKHAND ,	12/2017	200.34 -	200.34	31.00	12/2019 -	12/2019	0(O) -	0/0
1535	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH,UTTARAKHAND ,	12/2017	248.22 -	248.22	57.20	12/2019 -	12/2019	0(O) -	0/0
1536	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND ,	06/2017	282.08 -	282.08	77.05	06/2019 -	12/2019	6(O) -	0/0
1537	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND ,	11/2017	232.81 -	232.81	59.44	11/2019 -	11/2019	0(O) -	0/0
1538	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND ,	11/2017	283.51 -	283.51	126.38	11/2019 -	11/2019	0(O) -	0/0
1539	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND ,	11/2017	266.52 -	266.52	144.27	11/2019 -	11/2019	0(O) -	0/0
1540	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH,UTTARAKHAND ,	02/2018	418.88 -	418.88	88.00	02/2020 -	02/2020	0(O) -	0/0
1541	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH,UTTARAKHAND ,	02/2018	293.68 -	293.68	11.57	- -	-	-	0/0
1542	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH,UTTARAKHAND ,	05/2018	248.00 -	248.00	.00	05/2020 -	05/2020	0(O) -	0/0

MoSPI OCMS

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1543	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND ,	03/2018	460.73 -	461.00	.00	- -	-	-	0/0
1544	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND ,	03/2018	1,383.78 -	1,383.78	117.49	07/2018 -	-	-	1/5
1545	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND ,	08/2016	234.88 -	208.89	118.26	12/2017 -	12/2019	24(O) -	0/0
1546	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL , PPP (BOT)	02/2011	1,078.84 -	1,078.84	2,181.00	08/2013 -	05/2020	81(O) -	0/4
1547	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL , PPP (BOT)	02/2011	998.79 -	998.79	1,807.21	08/2013 -	03/2021	91(O) -	0/4
1548	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL , PPP (BOT)	04/2012	1,396.18 -	1,396.18	2,894.94	09/2014 -	03/2020	66(O) -	0/0
1549	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MoRTH,WEST BENGAL ,	01/1991	322.00 -	322.00	56.41	03/2018 -	-	-	0/0
1550	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL ,	10/2015	361.15 -	361.15	186.64	- -	01/2020	- -	0/0
1551	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL ,	12/2015	1,083.00 -	1,083.00	1,487.87	06/2018 -	12/2019	18(O) -	0/0
1552	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL , PPP (BOT)	04/2014	1,665.00 -	1,665.00	4,357.89	- -	06/2019	-	0/0
1553	CONSTRUCTION OF ROB –FLYOVER AT RANICHAK HALDIA - [N24000553]NHAI,WEST BENGAL ,	03/2016	229.37 -	229.37	110.52	11/2018 03/2020	03/2020	16(O) 0	0/0
1554	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL ,	09/2016	767.03 767.03	767.03	595.72	08/2018 -	09/2019	-	0/0
1555	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I - [N24000770]NHIDCL,WEST BENGAL ,	03/2017	158.65 -	158.65	39.06	06/2018 -	-	-	0/0
1556	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL ,	03/2018	1,261.98 -	1,261.98	793.49	- -	07/2021	- -	0/0
1557	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B NH-31C NH-31 NH-10 O - [N24000871]MoRTH,WEST BENGAL ,	08/2014	600.87 720.97	720.97	652.08	11/2017 05/2019	05/2019	-	0/0
1558	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717 NH-31 NH-31C NH-317A O - [N24000873]MoRTH,WEST BENGAL ,	08/2014	823.20 937.76	937.76	751.19	11/2017 06/2019	06/2019	-	0/0
1559	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]MoRTH,WEST BENGAL ,	03/2016	271.17 291.20	291.20	89.25	11/2018 11/2019	11/2019	12(O) 0	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1560	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH,WEST BENGAL ,	01/2017	396.86 396.86	396.86	185.31	09/2019 -	-	-	0/0
1561	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]MoRTH,WEST BENGAL ,	03/2017	202.69 202.69	202.69	103.14	11/2019 -	-	-	0/0
1562	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH,WEST BENGAL ,	02/2018	426.18 426.18	426.18	224.05	09/2020 -	-	-	0/0
1563	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH,WEST BENGAL ,	02/2018	218.70 218.70	218.70	38.81	11/2020 -	-	-	0/0
1564	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE BAGDO - [N24000883]MoRTH,WEST BENGAL ,	03/2018	254.30 254.30	254.30	53.02	10/2020 -	10/2020	0(O) -	0/0
1565	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH,WEST BENGAL ,	03/2016	160.27 213.97	213.97	20.11	08/2019 -	08/2021	24(O) -	0/0
1566	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH,WEST BENGAL ,	06/2016	236.78 263.26	263.26	59.92	08/2019 -	08/2021	24(O) -	0/0
1567	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH,WEST BENGAL ,	04/2014	279.70 398.52	398.52	322.75	08/2017 07/2019	07/2019	-	0/0
	Total		5,13,255.97 -	5,27,964.98	2,90,564.48				301/1055
	SHIPPING AND PORTS								
1568	JAL MARG VIKAS PROJECT - [N25000072]IWAI,MULTI STATE ,	01/2018	4,200.00 5,369.18	5,369.18	1,662.16	03/2023 03/2023	03/2023	0(O) 0	0/0
	Total		4,200.00 -	5,369.18	1,662.16				0/0
	TELECOMMUNICATIONS								
1569	GSM-RF EXPANSION PROJECT MTNL DELHI (3G) - [N26000105]MTNL,DELHI ,	06/2016	418.26 -	418.26	367.04	06/2017 -	-	-	0/0
1570	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]BSNL,MAHARASHTRA , Central Sector Projects	01/2018	231.80 240.10	240.10	117.63	10/2018 12/2019	12/2019	14(O) 0	0/0
1571	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE ,	03/2012	13,334.00 -	24,664.00	12,146.00	07/2015 -	05/2020	58(O) -	0/0
1572	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE , Central Sector Projects	09/2014	2,111.17 -	2,011.17	253.90	09/2014 -	-	-	0/70

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Total		16,095.23 -	27,333.53	12,884.57				0/70
	URBAN DEVELOPMENT								
1573	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH ,	07/2014	232.00 -	232.00	.00	- -	-	-	0/0
1574	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH ,	06/2014	157.84 -	169.16	163.98	03/2017 -	-	-	4/5
1575	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH ,	08/2007	246.90 -	246.90	.00	- -	-	-	0/0
1576	CONSTRACTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108]CPWD,ANDHRA PRADESH ,	01/2018	206.58 -	206.58	177.73	03/2019 -	-	-	0/7
1577	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM A.P. - [N28000133]CPWD,ANDHRA PRADESH ,	02/2019	186.00 199.00	186.00	.00	09/2020 -	09/2020	0(O) -	0/7
1578	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR ,	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72(O) -	0/0
1579	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR ,	02/2016	496.18 496.00	498.99	97.67	06/2017 -	03/2021	45(O) -	0/0
1580	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI ,	09/2011	38,585.00 -	38,585.00	34,763.00	03/2016 -	-	-	0/0
1581	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI ,	10/2013	1,219.21 -	2,000.00	408.23	10/2019 -	03/2021	17(O) -	0/7
1582	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI ,	07/2012	884.30 -	884.30	729.63	12/2015 -	-	-	0/0
1583	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI ,	06/2012	4,264.00 -	4,439.23	3,246.53	11/2019 -	11/2019	0(O) -	3/7
1584	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG NEW DELHI - [N28000087]CPWD,DELHI ,	06/2015	197.33 -	197.33	61.47	04/2019 -	11/2020	19(O) -	0/2
1585	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI ,	07/2016	2,694.00 -	2,694.00	.00	- -	-	-	0/0
1586	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS MINTO ROAD NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI ,	11/2017	238.56 -	238.56	63.45	05/2020 -	05/2020	0(O) -	1/2
1587	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]CPWD,DELHI ,	12/2017	188.00 -	188.00	146.45	06/2019 -	-	-	0/0
1588	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI ,	10/2016	422.00 -	422.00	14.20	- -	12/2020	- -	0/0

MoSPI OCMS

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1589	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR NEW DELHI-CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI ,	10/2016	392.00 -	392.00	12.56	- 08/2020	03/2021	- 0	0/0
1590	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI ,	10/2016	248.20 -	248.20	45.03	04/2018 02/2020	08/2020	28(O) 0	0/0
1591	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI ,	10/2017	271.90 -	271.90	61.81	11/2019 08/2020	08/2020	9(O) 0	0/0
1592	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI - [N28000123]CPWD,DELHI ,	07/2017	218.72 218.72	218.72	57.71	- -	-	-	0/2
1593	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128]CPWD,DELHI ,	10/2016	1,180.00 -	1,180.00	.00	07/2021 -	07/2021	0(O) -	0/0
1594	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]CPWD,DELHI ,	10/2016	1,128.00 -	1,128.00	.00	03/2022 -	03/2022	0(O) -	0/0
1595	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT - [N28000132]CPWD,DELHI ,	11/2018	361.60 -	361.60	.45	07/2021 -	07/2021	0(O) -	0/2
1596	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS - [N28000135]DMRC,DELHI ,	07/2019	24,948.65 -	24,948.65	1.74	03/2025 -	03/2025	0(O) -	0/0
1597	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]DMRC,DELHI ,	05/2017	565.00 -	565.00	321.05	12/2020 -	12/2020	0(O) -	0/0
1598	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR GUJARAT - [N12000106]HSCL,GUJARAT ,	01/2013	175.00 -	175.00	1.83	- -	-	-	0/0
1599	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT ,	11/2014	10,773.00 -	10,773.00	6,296.85	12/2018 -	07/2020	19(O) -	0/0
1600	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137]MEGA,GUJARAT ,	03/2019	5,384.17 -	5,384.17	4.35	03/2024 -	03/2024	0(O) -	0/0
1601	SURAT METRO RAIL PROJECT - [N28000138]MEGA,GUJARAT ,	03/2019	12,020.32 -	12,020.32	4.67	03/2024 -	03/2024	0(O) -	0/0
1602	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH ,	11/2012	270.83 -	270.83	199.91	11/2014 -	-	-	2/8
1603	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD,HIMACHAL PRADESH ,	12/2018	260.00 -	260.00	12.50	06/2021 -	06/2021	0(O) -	0/0
1604	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]CPWD,JAMMU AND KASHMIR ,	03/2019	329.00 -	329.00	.00	- -	-	-	0/0
1605	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]CPWD,JAMMU AND KASHMIR ,	01/2018	676.00 -	676.00	.00	- -	-	-	0/0
1606	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTEINANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND ,	12/2007	253.92 253.92	253.92	193.97	06/2016 -	-	-	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1607	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI KODERMA HAZARIBAG RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND ,	12/2007	200.00 -	200.00	131.15	03/2018 -	-	-	0/0
1608	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND ,	02/2014	787.29 -	787.29	285.30	12/2016 -	-	-	0/0
1609	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND ,	04/2013	170.00 -	170.00	88.91	04/2018 -	-	-	0/0
1610	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND ,	09/2012	171.86 -	171.86	89.53	03/2016 -	09/2020	54(O) -	1/6
1611	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA ,	05/2005	768.88 1,070.97	1,113.34	1,085.64	02/2014 -	-	-	0/0
1612	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA ,	07/2011	324.87 324.87	324.87	262.93	12/2015 -	-	-	0/0
1613	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA ,	02/2014	26,405.14 -	26,405.14	499.85	02/2019 -	03/2020	13(O) -	0/0
1614	RESIDENTIAL QUATERS FOR HAL BANGLORE - [N28000103]CPWD,KARNATAKA ,	12/2016	246.31 -	246.31	80.34	02/2020 -	09/2020	7(O) -	0/0
1615	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA ,	01/2010	165.23 -	165.23	94.62	10/2012 -	03/2020	89(O) -	1/7
1616	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA ,	07/2012	5,181.79 5,687.79	5,687.79	5,656.62	07/2017 -	03/2020	32(O) -	0/0
1617	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITIUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST - [N28000112]CPWD,KERALA ,	09/2017	150.29 -	150.29	21.82	03/2020 11/2020	03/2021	12(O) 12	2/7
1618	BHOPAL METRO RAIL - [N28000124]MPMRCL,MADHYA PRADESH ,	11/2018	6,941.40 -	6,941.40	41.94	02/2023 -	02/2023	0(O) -	0/0
1619	INDORE METRO RAIL - [N28000125]MPMRCL,MADHYA PRADESH ,	11/2018	7,500.80 -	7,500.80	45.70	02/2023 -	02/2023	0(O) -	0/0
1620	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA ,	06/2010	205.00 -	205.00	165.95	03/2012 -	12/2019	93(O) -	19/20
1621	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA ,	08/2014	8,680.00 -	8,680.00	6,405.74	03/2018 -	12/2019	21(O) -	0/0
1622	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA ,	07/2013	23,136.00 -	23,136.00	.00	01/2015 -	05/2020	64(O) -	0/0
1623	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY POWAI MUMBAI - [N28000117]CPWD,MAHARASHTRA ,	01/2018	223.37 -	223.37	42.19	07/2020 -	11/2020	4(O) -	3/14
1624	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA ,	12/2016	11,420.00 -	11,420.00	3,372.86	11/2021 03/2022	03/2022	4(O) 2	0/0
1625	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR , Central Sector Projects	02/2014	216.69 -	216.69	52.00	03/2015 -	10/2020	67(O) -	0/10
1626	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA ,	04/2014	151.33 -	151.33	7.15	09/2017 -	-	-	0/0
1627	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134]NCRTC,MULTI STATE ,	03/2019	30,274.00 -	30,274.00	613.92	06/2025 -	06/2025	0(O) -	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1628	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD,ODISHA ,	01/2019	790.79 -	800.00	11.01	03/2022 -	06/2022	3(O) -	0/0
1629	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR PUNJAB - [N28000088]CPWD,PUNJAB ,	02/2014	388.00 -	488.28	440.59	05/2017 -	12/2019	31(O) -	8/12
1630	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR PUNJAB - [N28000102]CPWD,PUNJAB ,	08/2016	294.00 -	294.00	208.99	04/2019 -	02/2020	10(O) -	6/8
1631	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR PUNJAB - [N28000120]CPWD,PUNJAB ,	01/2018	430.00 -	430.00	97.92	05/2020 -	01/2021	8(O) -	1/5
1632	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN ,	05/2015	189.00 -	189.00	.00	03/2017 -	-	-	0/0
1633	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN ,	12/2016	549.31 559.47	559.47	373.45	07/2019 12/2019	04/2020	9(O) 1	0/0
1634	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU ,	02/2009	14,600.00 -	19,058.00	16,352.87	12/2015 -	-	-	12/24
1635	C/O OF 152 NOS TYPE-II 304 NOS TYPE-III 76 NOS TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU ,	12/2015	209.00 -	209.00	150.71	10/2019 -	07/2020	9(O) -	1/6
1636	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU ,	06/2016	3,770.00 -	3,770.00	2,086.51	03/2018 06/2020	06/2020	27(O) 0	4/19
1637	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU ,	11/2017	348.77 -	348.77	31.97	- -	11/2021	- -	0/0
1638	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA ,	10/2016	209.84 -	209.84	58.75	03/2020 -	05/2021	14(O) -	1/5
1639	CONSTRUCTION AND MAINTEINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA ,	03/2007	149.73 173.00	175.94	176.65	12/2015 -	-	-	0/0
1640	CONSTRUCTION AND MAINTEINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA ,	12/2007	202.61 227.00	227.00	199.95	12/2016 -	-	-	0/0
1641	CONSTRUCTION AND MAINTEINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA ,	10/2011	175.49 206.71	206.71	141.28	12/2016 -	-	-	0/0
1642	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH ,	01/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	-	-	0/0
1643	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH ,	11/2017	171.72 -	171.72	32.00	03/2020 -	03/2020	0(O) -	0/0
1644	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND ,	12/2008	114.26 266.00	266.00	.00	12/2013 -	-	-	0/0
1645	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL , Central Sector Projects	08/2012	185.37 -	185.37	178.30	03/2016 -	-	-	0/0

MoSPI OCMS

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1646	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL ,	02/2014	156.57 -	156.57	159.35	08/2016 -	-	-	10/16
1647	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL , Central Sector Projects	10/2014	162.88 179.10	162.88	144.06	04/2018 06/2020	06/2020	26(O) 0	5/6
	Total		2,63,975.80 -	2,70,607.62	90,163.27				84/214
	WATER RESOURCES								
1648	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA,ANDHRA PRADESH , National Project	02/2009	10,151.04 -	55,548.87	16,417.99	03/2020 -	06/2021	15(O) -	0/19
1649	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]BUIDCO,BIHAR ,	03/2018	230.06 -	230.06	.00	07/2021 -	07/2021	0(O) -	0/0
1650	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO,BIHAR ,	10/2017	254.13 -	254.13	.00	09/2020 -	09/2020	0(O) -	0/0
1651	I AND D AND STP AT CHAPPRA - [N30000028]BUIDCO,BIHAR ,	11/2018	236.15 -	236.15	.00	12/2020 -	12/2020	0(O) -	0/0
1652	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO,BIHAR ,	03/2018	305.19 -	305.19	.00	08/2021 -	08/2021	0(O) -	0/0
1653	SEWER NETWORKS SPS AND STP MUNGER - [N30000036]BUIDCO,BIHAR ,	03/2018	294.02 -	294.02	.00	10/2021 -	10/2021	0(O) -	0/0
1654	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO,BIHAR ,	12/2014	225.77 -	225.77	.00	03/2020 -	03/2020	0(O) -	0/0
1655	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR - [N30000038]BUIDCO,BIHAR ,	04/2015	184.93 -	184.93	.00	04/2020 -	04/2020	0(O) -	0/0
1656	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO,BIHAR ,	04/2015	268.63 -	268.63	.00	01/2021 -	01/2021	0(O) -	0/0
1657	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]BUIDCO,BIHAR ,	05/2017	356.37 -	356.37	.00	04/2021 -	04/2021	0(O) -	0/0
1658	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA - [N30000041]BUIDCO,BIHAR ,	05/2017	184.86 -	184.86	.00	05/2021 -	05/2021	0(O) -	0/0
1659	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO,BIHAR ,	05/2017	191.62 -	191.62	.00	11/2020 -	11/2020	0(O) -	0/0
1660	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]BUIDCO,BIHAR ,	03/2017	277.42 -	277.42	.00	05/2021 -	05/2021	0(O) -	0/0
1661	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]BUIDCO,BIHAR ,	08/2017	578.89 -	578.89	.00	06/2022 -	06/2022	0(O) -	0/0
1662	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE PATNA - [N30000051]BUIDCO,BIHAR ,	08/2017	824.00 -	824.00	.00	06/2022 -	06/2022	0(O) -	0/0
1663	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]DJB,DELHI ,	03/2017	665.78 -	665.78	.00	12/2022 -	12/2022	0(O) -	0/0
1664	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB,DELHI ,	05/2016	211.79 -	211.79	.00	12/2021 -	12/2021	0(O) -	0/0
1665	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB,DELHI ,	05/2016	239.11 -	239.11	.00	02/2022 -	02/2022	0(O) -	0/0
1666	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O&M AT CORONATION PILLAR DELHI - [N30000017]DJB,DELHI ,	12/2018	515.07 -	515.07	.00	01/2021 -	01/2021	0(O) -	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1667	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB,DELHI ,	05/2017	344.81 -	344.81	.00	05/2020 -	05/2020	0(O) -	0/0
1668	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB,MAHARASHTRA ,	03/2017	233.57 -	233.57	32.20	12/2019 -	12/2019	0(O) -	0/0
1669	SEWERAGE WORKS IN SEWERAGE DISTRICT A OF ALLAHABAD - [N30000005]UPJalNigam,UTTAR PRADESH ,	02/2014	288.94 -	288.94	.00	09/2019 -	09/2019	-	0/0
1670	INTERCEPTION DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]UPJalNigam,UTTAR PRADESH ,	05/2017	767.59 -	767.59	.00	09/2021 -	09/2021	0(O) -	0/0
1671	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS - [N30000007]UPJalNigam,UTTAR PRADESH ,	03/2018	904.00 -	904.00	.00	09/2021 -	09/2021	0(O) -	0/0
1672	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]UPJalNigam,UTTAR PRADESH ,	10/2017	213.62 -	213.62	.00	03/2022 -	03/2022	0(O) -	0/0
1673	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR - [N30000009]UPJalNigam,UTTAR PRADESH ,	10/2016	370.40 -	370.40	.00	08/2020 -	08/2020	0(O) -	0/0
1674	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]UPJalNigam,UTTAR PRADESH ,	03/2018	967.23 -	967.23	.00	09/2021 -	09/2021	0(O) -	0/0
1675	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA - [N30000011]UPJalNigam,UTTAR PRADESH ,	02/2017	161.31 -	161.31	.00	11/2019 -	11/2019	0(O) -	0/0
1676	REHABILITATION RENOVATION OF AGRA SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS IN AGRA UTTAR PR - [N30000012]UPJalNigam,UTTAR PRADESH ,	12/2018	857.26 -	857.26	.00	08/2021 -	08/2021	0(O) -	0/0
1677	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY UTTAR PRADESH - [N30000013]UPJalNigam,UTTAR PRADESH ,	03/2019	271.39 -	271.39	.00	08/2021 -	08/2021	0(O) -	0/0
1678	MATHURA SEWERAGE SCHEME - [N30000019]UPJalNigam,UTTAR PRADESH ,	12/2017	460.45 -	460.45	.00	12/2020 -	12/2020	0(O) -	0/0
1679	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]UPJalNigam,UTTAR PRADESH ,	02/2011	279.91 -	279.91	.00	12/2019 -	12/2019	0(O) -	0/0
1680	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]UPJalNigam,UTTAR PRADESH ,	01/2019	231.79 -	231.79	.00	12/2021 -	12/2021	0(O) -	0/0
1681	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]UPJalNigam,UTTAR PRADESH ,	01/2019	206.05 -	206.05	.00	10/2021 -	10/2021	0(O) -	0/0
1682	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS AT AGRA - [N30000023]UPJalNigam,UTTAR PRADESH ,	02/2019	317.19 -	317.19	.00	08/2021 -	08/2021	0(O) -	0/0
1683	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]UPJalNigam,UTTAR PRADESH ,	02/2019	681.78 -	681.78	.00	06/2022 -	06/2022	0(O) -	0/0

Detail of ongoing Projects **Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Antici pated Cost	Cumulative Expenditure Cost	Original / Revised	Antici pated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1684	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UPJalNigam,UTTAR PRADESH ,	03/2019	298.12 -	298.12	.00	07/2021 -	07/2021	0(O) -	0/0
1685	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI - [N30000003]UKJalNigam,UTTARAKHAND ,	03/2017	273.37 -	273.37	.00	08/2019 -	08/2019	-	0/0
1686	INTERCEPTION AND DIVERSION (I&D)WITH STP AT RISHIKESH - [N30000004]UKJalNigam,UTTARAKHAND ,	03/2017	158.00 -	158.00	.00	11/2019 -	11/2019	0(O) -	0/0
1687	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]KMDA,WEST BENGAL ,	01/2019	384.96 -	384.96	.00	04/2022 -	04/2022	0(O) -	0/0
1688	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPURL - [N30000030]KMDA,WEST BENGAL ,	03/2019	287.53 -	287.53	.00	04/2022 -	04/2022	0(O) -	0/0
1689	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]KMDA,WEST BENGAL ,	12/2018	234.31 -	234.31	.00	04/2022 -	04/2022	0(O) -	0/0
1690	INTERCEPTION & DIVERSION WITH STP AT MAHESHTALA - [N30000032]KMDA,WEST BENGAL ,	05/2018	198.43 -	198.43	.00	02/2022 -	02/2022	0(O) -	0/0
1691	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]KMDA,WEST BENGAL ,	03/2018	165.16 -	165.16	.00	06/2022 -	06/2022	0(O) -	0/0
1692	INTERCEPTION DIVERSION AND TREATMENT WORKS AT TOLLY'S NULLAH ADI GANGA - [N30000034]KMDA,WEST BENGAL ,	08/2017	307.12 -	307.12	.00	09/2022 -	09/2022	0(O) -	0/0
1693	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH - [N30000042]KMDA,WEST BENGAL ,	05/2018	160.00 -	160.00	.00	02/2022 -	02/2022	0(O) -	0/0
1694	INTERCEPTION DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]KMDA,WEST BENGAL ,	08/2017	185.22 -	185.22	.00	12/2021 -	12/2021	0(O) -	0/0
1695	SEWERAGE SYSTEM & STP WORKS AT HALISHAHR - [N30000046]KMDA,WEST BENGAL ,	02/2014	274.76 -	274.76	.00	12/2019 -	12/2019	0(O) -	0/0
1696	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA,WEST BENGAL ,	12/2014	272.32 -	272.32	.00	04/2020 -	04/2020	0(O) -	0/0
1697	INTERCEPTION DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]KMDA,WEST BENGAL ,	01/2018	172.10 -	172.10	.00	12/2021 -	12/2021	0(O) -	0/0
1698	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]KMDA,WEST BENGAL ,	10/2017	164.93 -	164.93	.00	12/2021 -	12/2021	0(O) -	0/0
	Total		27,288.45 -	72,686.28	16,450.19				0/19
	Grand Total		20,41,114.88	24,41,837.32	10,50,331.59				2882/5620

Summary of projects in the Flash Report
for the month of November, 2019

Project Implementation - Current Status:

Number of Projects in Previous Month	**1636**
Number of Projects completed/dropped/frozen in Current Month	**5**
Number of Projects Felldown to the status of Major project during the current month	**2**
Number of Projects Added in Current Month	**69**
Number of Projects in Current Month	**1698**

Brief Analysis

Project Status with respect to Original Schedule: Out of 1698 projects, 18 projects are ahead of schedule, 374 projects are on schedule 578 projects are delayed. 565 projects do not have fixed dates of commissioning.163 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

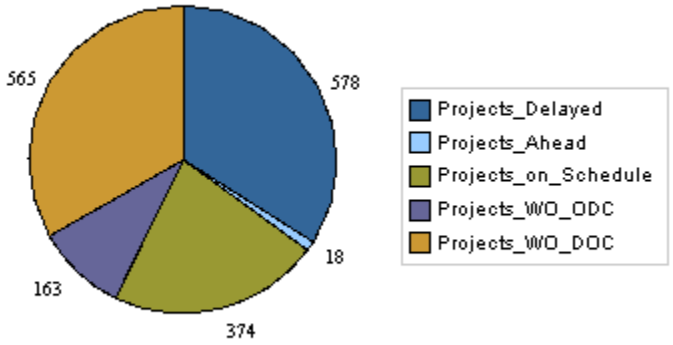

Total No Of Project's:- 1698

Investment Scenario

Total original cost of implementation of 1698 projects when sanctioned, was of the order of Rs. 2041114.88 crore but this was subsequently revised to Rs. 2441837.32 crore implying a cost overrun of 19.6%. The expenditure incurred on these projects till November, 2019 is Rs. 1050331.59 crore, which is 43% of the anticipated cost of the projects.

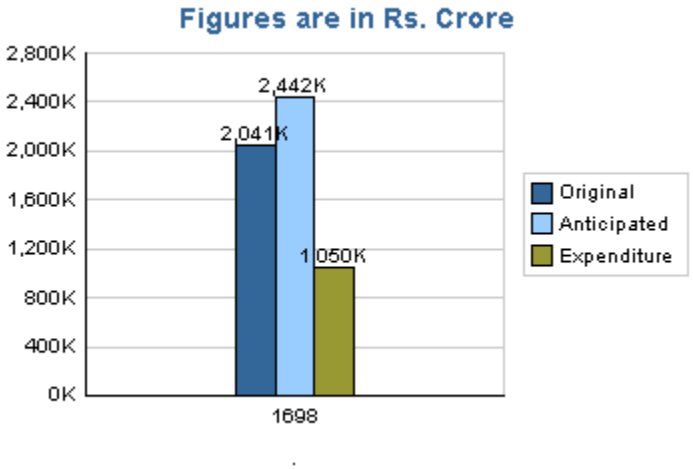

Sector wise current status of projects on the Flash Report

ATOMIC ENERGY

Current Status:

Number of Projects	**4**
Number of Projects Delayed	**4**

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.

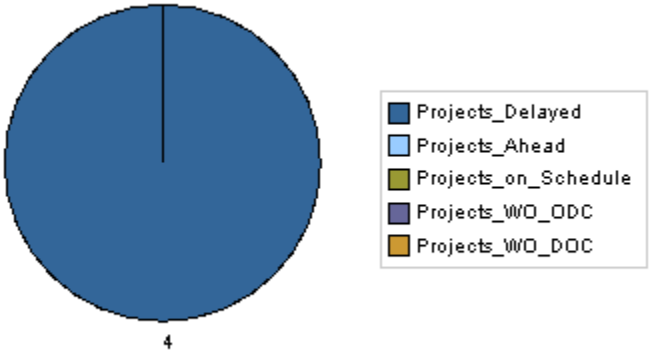

Total No Of Project's:- 4

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 67120 crore but this was subsequently anticipated to Rs. 80348 crore implying a cost overrun of 19.7%. The expenditure incurred on these projects till November, 2019 is Rs. 47067.84 crore, which is 58.6% of the anticipated cost of the projects.

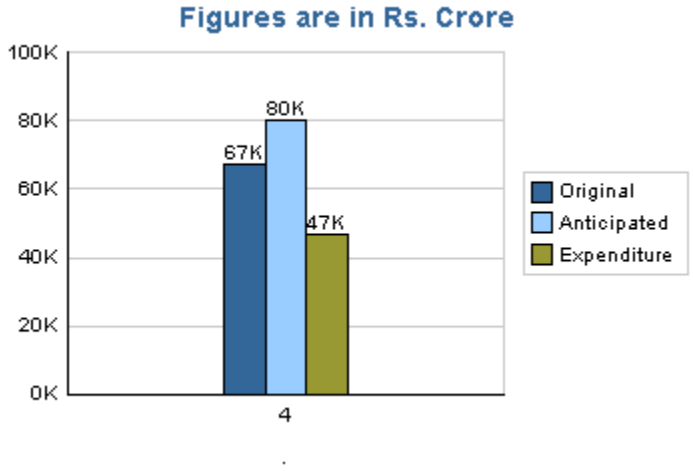

Sector wise current status of projects on the Flash Report

CIVIL AVIATION

Current Status:

Number of Projects	**13**
Number of Projects On Schedule	**8**
Number of Projects Delayed	**5**

Brief Analysis

Project Status with respect to Original Schedule: Out of 13 projects, 8 projects are on schedule 5 projects are delayed.

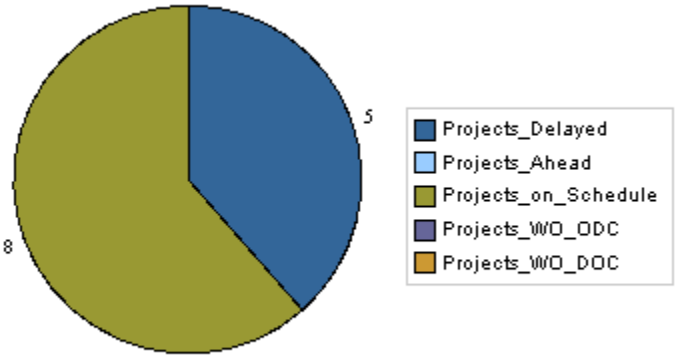

Total No Of Project's:- 13

Investment Scenario

Total original cost of implementation of 13 projects when sanctioned, was of the order of Rs. 8607.51 crore but this was subsequently anticipated to Rs. 8734.44 crore implying a cost overrun of 1.5%. The expenditure incurred on these projects till November, 2019 is Rs. 1357.47 crore, which is 15.5% of the anticipated cost of the projects.

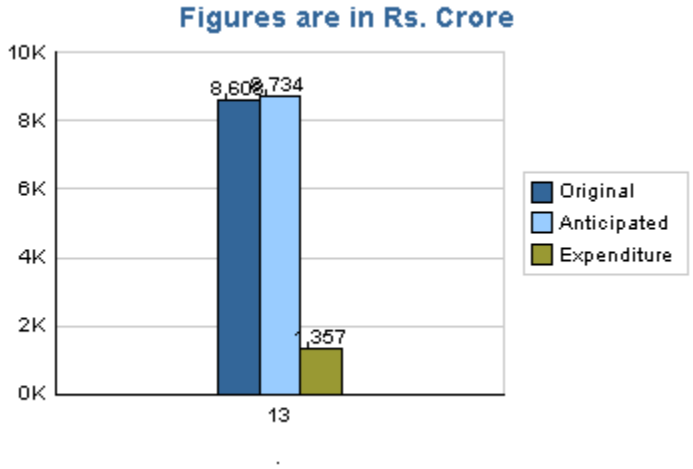

Sector wise current status of projects on the Flash Report

COAL

Current Status:

Number of Projects	**107**
Number of Projects On Schedule	**54**
Number of Projects Delayed	**39**
Number of Projects Ahead	**1**
Number of Projects Without Original Date of Commissioning	**3**
Number of Projects Without Date Of Commissioning	**10**

Brief Analysis

Project Status with respect to Original Schedule: Out of 107 projects, 1 project is ahead of schedule, 54 projects are on schedule 39 projects are delayed. 10 projects do not have fixed dates of commissioning.3 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

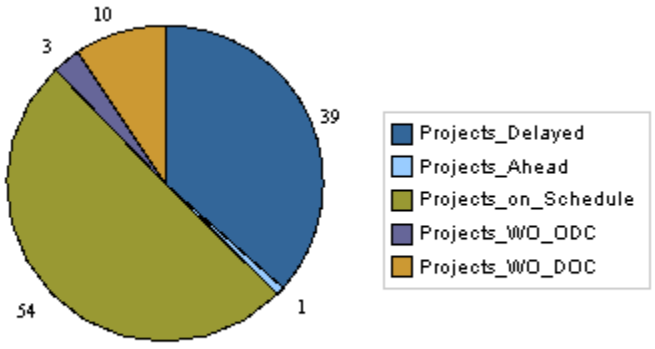

Total No Of Project's:- 107

Investment Scenario

Total original cost of implementation of 107 projects when sanctioned, was of the order of Rs. 104997.33 crore but this was subsequently anticipated to Rs. 107962.2 crore implying a cost overrun of 2.8%. The expenditure incurred on these projects till November, 2019 is Rs. 37121.19 crore, which is 34.4% of the anticipated cost of the projects.

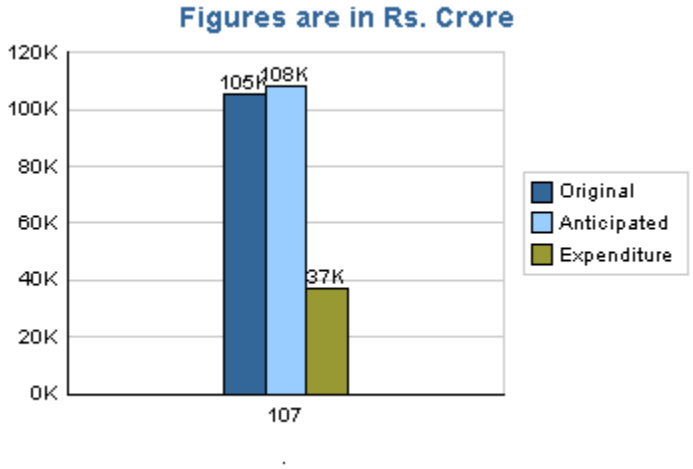

Sector wise current status of projects on the Flash Report

FERTILISERS

Current Status:

Number of Projects	**5**
Number of Projects On Schedule	**4**
Number of Projects Without Date Of Commissioning	**1**

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 4 projects are on schedule 1 project does not have fixed dates of commissioning.

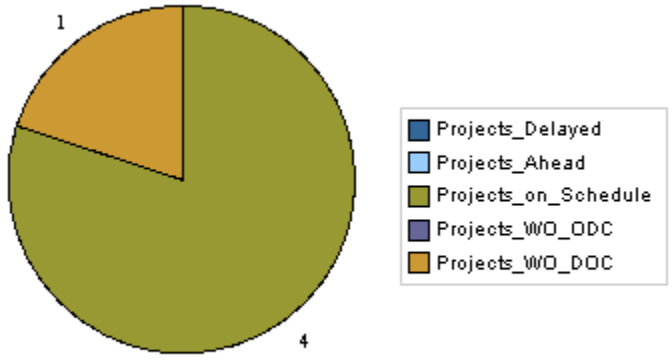

Total No Of Project's:- 5

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 1299.07 crore but this was subsequently anticipated to Rs. 1310.72 crore implying a cost overrun of .9%. The expenditure incurred on these projects till November, 2019 is Rs. 840.4 crore, which is 64.1% of the anticipated cost of the projects.

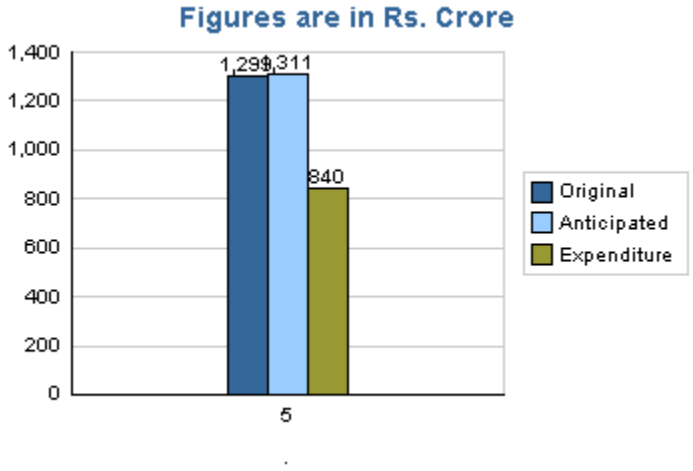

Sector wise current status of projects on the Flash Report

MINES

Current Status:

Number of Projects	**5**
Number of Projects On Schedule	**4**
Number of Projects Delayed	**1**

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 4 projects are on schedule 1 project is delayed.

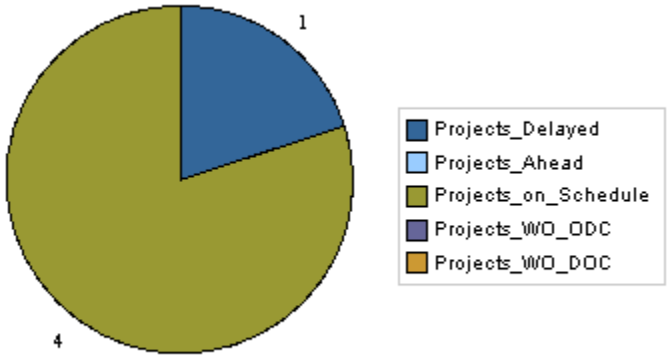

Total No Of Project's:- 5

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 7078.62 crore but this was subsequently anticipated to Rs. 7075.17 crore The expenditure incurred on these projects till November, 2019 is Rs. 653.4 crore, which is 9.2% of the anticipated cost of the projects.

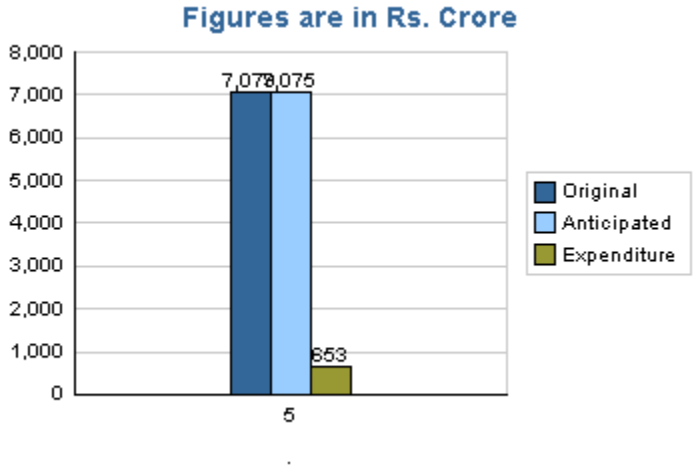

Sector wise current status of projects on the Flash Report

STEEL

Current Status:

Number of Projects	**9**
Number of Projects On Schedule	**1**
Number of Projects Delayed	**8**

Brief Analysis

Project Status with respect to Original Schedule: Out of 9 projects, 1 project is on schedule 8 projects are delayed.

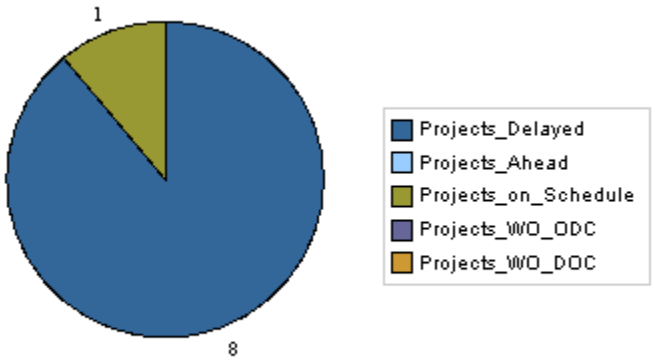

Total No Of Project's:- 9

Investment Scenario

Total original cost of implementation of 9 projects when sanctioned, was of the order of Rs. 26228.23 crore but this was subsequently anticipated to Rs. 33485.23 crore implying a cost overrun of 27.7%. The expenditure incurred on these projects till November, 2019 is Rs. 23942.27 crore, which is 71.5% of the anticipated cost of the projects.

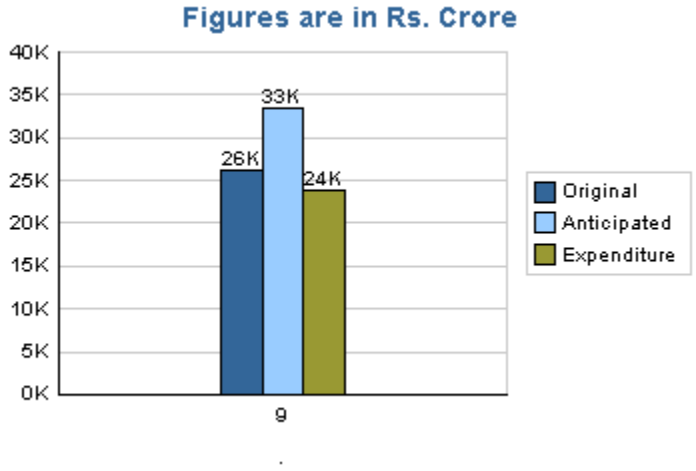

Sector wise current status of projects on the Flash Report

PETROLEUM

Current Status:

Number of Projects	**150**
Number of Projects On Schedule	**74**
Number of Projects Delayed	**55**
Number of Projects Ahead	**7**
Number of Projects Without Original Date of Commissioning	**2**
Number of Projects Without Date Of Commissioning	**12**

Brief Analysis

Project Status with respect to Original Schedule: Out of 150 projects, 7 projects are ahead of schedule, 74 projects are on schedule 55 projects are delayed. 12 projects do not have fixed dates of commissioning.2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

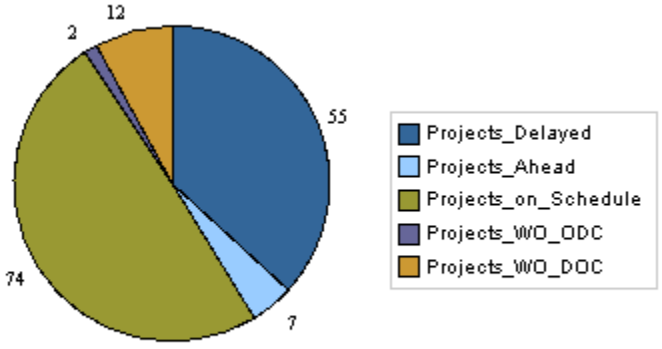

Total No Of Project's:- 150

Investment Scenario

Total original cost of implementation of 150 projects when sanctioned, was of the order of Rs. 249934.93 crore but this was subsequently anticipated to Rs. 265162.48 crore implying a cost overrun of 6.1%. The expenditure incurred on these projects till November, 2019 is Rs. 99549.9 crore, which is 37.5% of the anticipated cost of the projects.

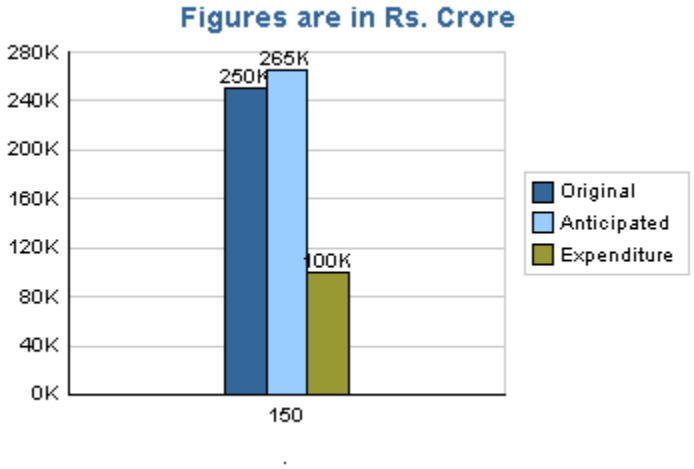

Sector wise current status of projects on the Flash Report

POWER

Current Status:

Number of Projects	**70**
Number of Projects On Schedule	**13**
Number of Projects Delayed	**50**
Number of Projects Without Date Of Commissioning	**7**

Brief Analysis

Project Status with respect to Original Schedule: Out of 70 projects, 13 projects are on schedule 50 projects are delayed. 7 projects do not have fixed dates of commissioning.

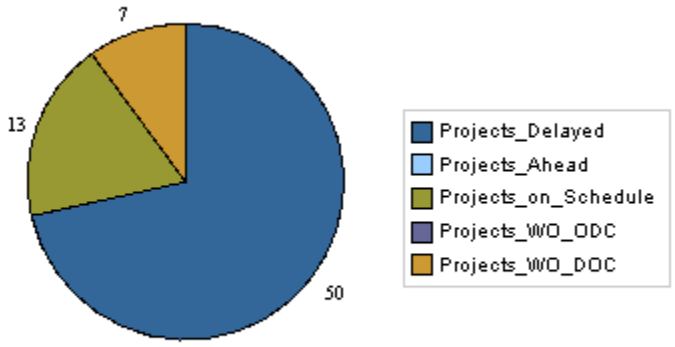

Total No Of Project's:- 70

Investment Scenario

Total original cost of implementation of 70 projects when sanctioned, was of the order of Rs. 279157.68 crore but this was subsequently anticipated to Rs. 353357.42 crore implying a cost overrun of 26.6%. The expenditure incurred on these projects till November, 2019 is Rs. 222975.18 crore, which is 63.1% of the anticipated cost of the projects.

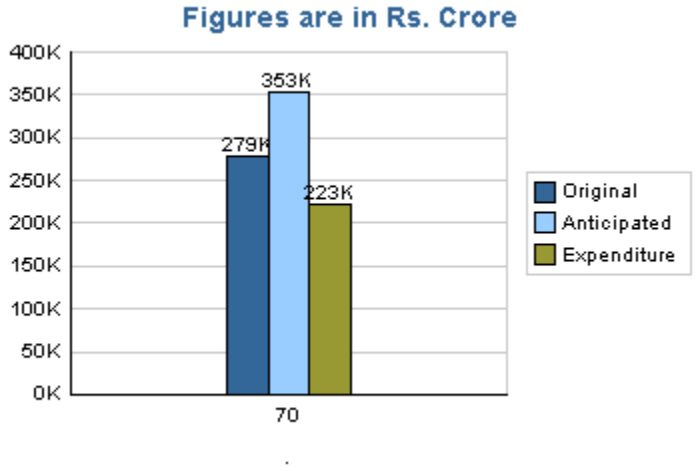

Sector wise current status of projects on the Flash Report

HEAVY INDUSTRY

Current Status:

Number of Projects	**1**
Number of Projects Delayed	**1**

Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project is delayed.

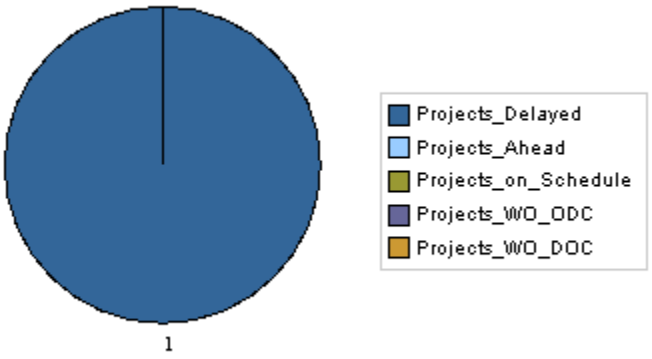

Total No Of Project's:- 1

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 1554 crore but this was subsequently anticipated to Rs. 1554 crore The expenditure incurred on these projects till November, 2019 is Rs. 665.35 crore, which is 42.8% of the anticipated cost of the projects.

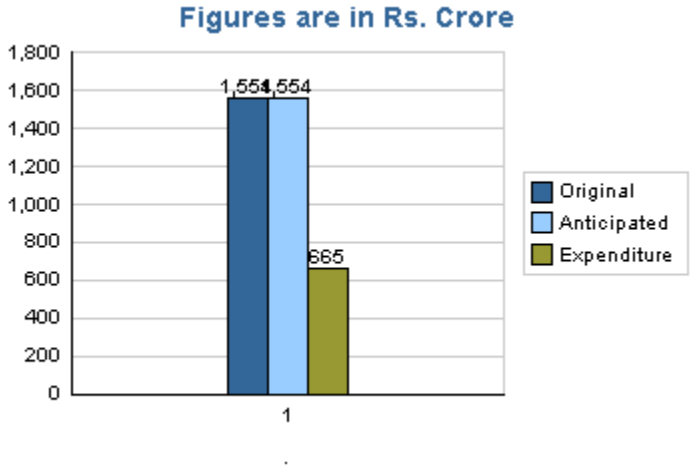

Sector wise current status of projects on the Flash Report

HEALTH AND FAMILY WELFARE

Current Status:

Number of Projects	**21**
Number of Projects On Schedule	**1**
Number of Projects Delayed	**11**
Number of Projects Without Original Date of Commissioning	**6**
Number of Projects Without Date Of Commissioning	**3**

Brief Analysis

Project Status with respect to Original Schedule: Out of 21 projects, 1 project is on schedule 11 projects are delayed. 3 projects do not have fixed dates of commissioning.6 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

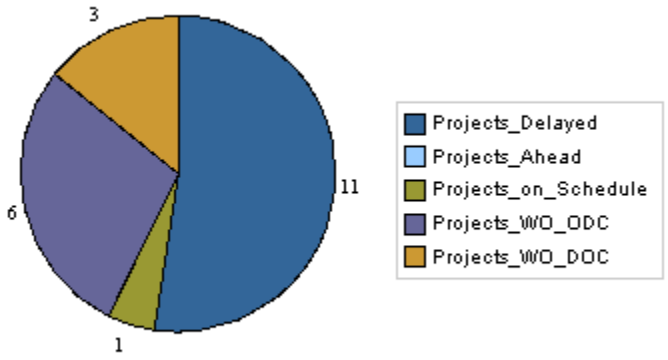

Total No Of Project's:- 21

Investment Scenario

Total original cost of implementation of 21 projects when sanctioned, was of the order of Rs. 9473.56 crore but this was subsequently anticipated to Rs. 9444.06 cr The expenditure incurred on these projects till November, 2019 is Rs. 4742.85 crore, which is 50.2% of the anticipated cost of the projects.

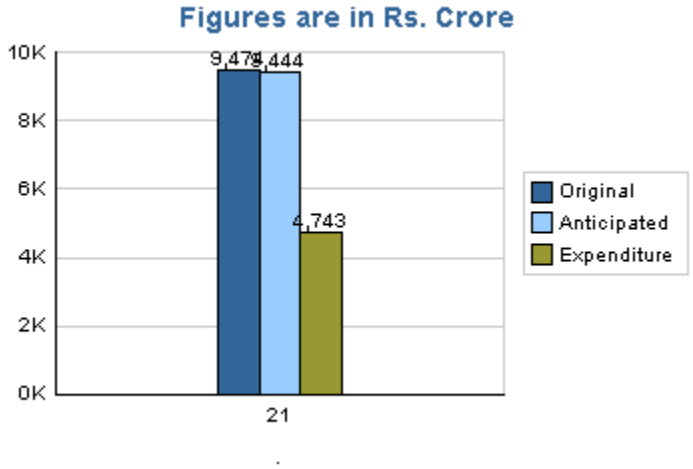

Sector wise current status of projects on the Flash Report

RAILWAYS

Current Status:

Number of Projects	**312**
Number of Projects On Schedule	**37**
Number of Projects Delayed	**150**
Number of Projects Ahead	**7**
Number of Projects Without Original Date of Commissioning	**48**
Number of Projects Without Date Of Commissioning	**70**

Brief Analysis

Project Status with respect to Original Schedule: Out of 312 projects, 7 projects are ahead of schedule, 37 projects are on schedule 150 projects are delayed. 70 projects do not have fixed dates of commissioning.48 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

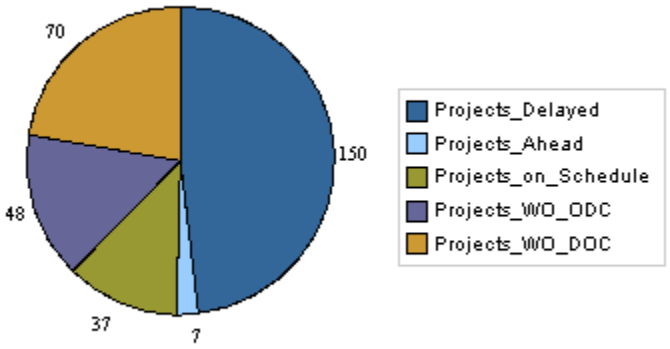

Total No Of Project's:- 312

Investment Scenario

Total original cost of implementation of 312 projects when sanctioned, was of the order of Rs. 459394.75 crore but this was subsequently anticipated to Rs. 667846.32 crore implying a cost overrun of 45.4%. The expenditure incurred on these projects till November, 2019 is Rs. 199661.27 crore, which is 29.9% of the anticipated cost of the projects.

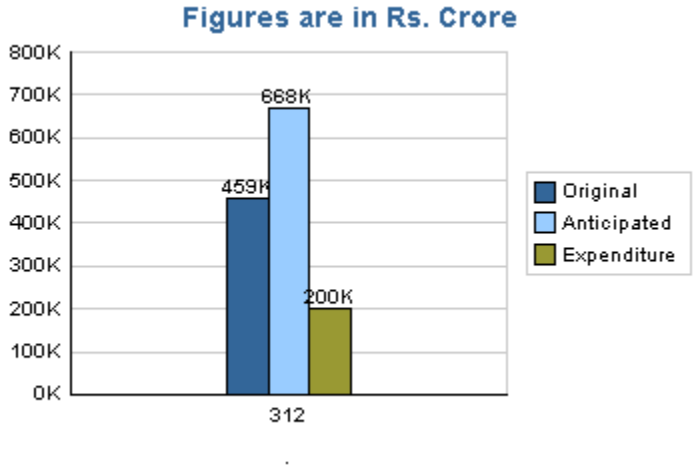

Sector wise current status of projects on the Flash Report

ROAD TRANSPORT AND HIGHWAYS

Current Status:

Number of Projects	**866**
Number of Projects On Schedule	**113**
Number of Projects Delayed	**221**
Number of Projects Ahead	**3**
Number of Projects Without Original Date of Commissioning	**101**
Number of Projects Without Date Of Commissioning	**428**

Brief Analysis

Project Status with respect to Original Schedule: Out of 866 projects, 3 projects are ahead of schedule, 113 projects are on schedule 221 projects are delayed. 428 projects do not have fixed dates of commissioning.101 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

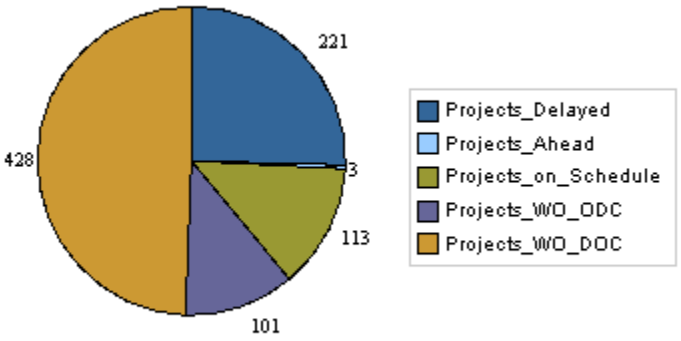

Total No Of Project's:- 866

Investment Scenario

Total original cost of implementation of 866 projects when sanctioned, was of the order of Rs. 513255.97 crore but this was subsequently anticipated to Rs. 527964.98 crore implying a cost overrun of 2.9%. The expenditure incurred on these projects till November, 2019 is Rs. 290564.48 crore, which is 55% of the anticipated cost of the projects.

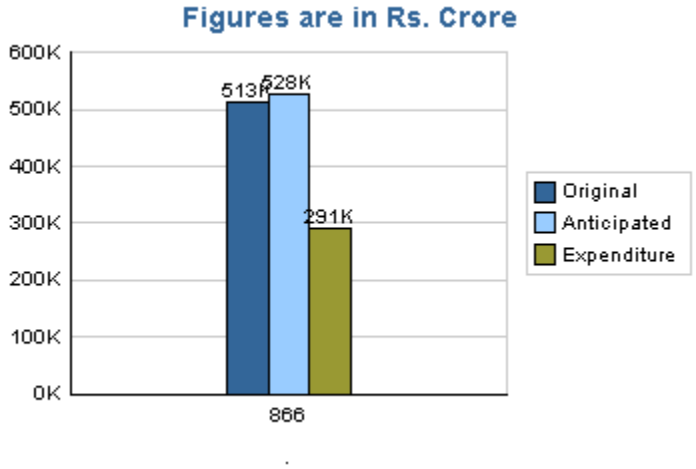

Sector wise current status of projects on the Flash Report

SHIPPING AND PORTS

Current Status:

Number of Projects	**1**
Number of Projects On Schedule	**1**

Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project is on schedule

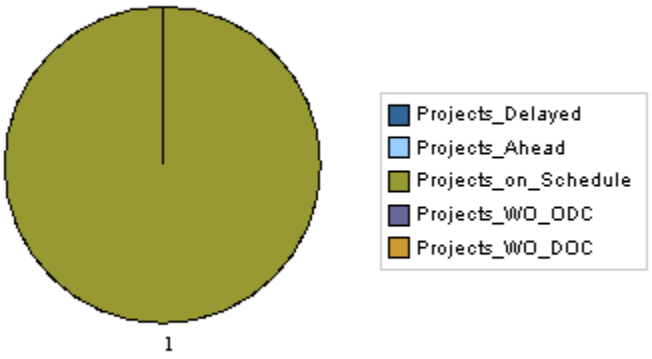

Total No Of Project's:- 1

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 4200 crore but this was subsequently anticipated to Rs. 5369.18 crore implying a cost overrun of 27.8%. The expenditure incurred on these projects till November, 2019 is Rs. 1662.16 crore, which is 31% of the anticipated cost of the projects.

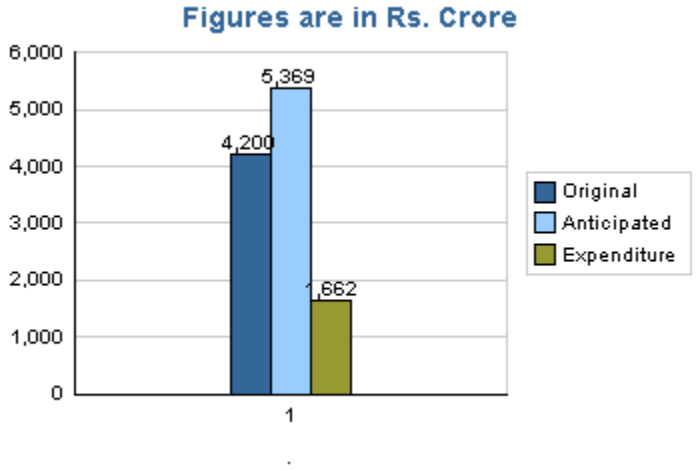

Sector wise current status of projects on the Flash Report

TELECOMMUNICATIONS

Current Status:

Number of Projects	**4**
Number of Projects Delayed	**2**
Number of Projects Without Date Of Commissioning	**2**

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are delayed. 2 projects do not have fixed dates of commissioning.

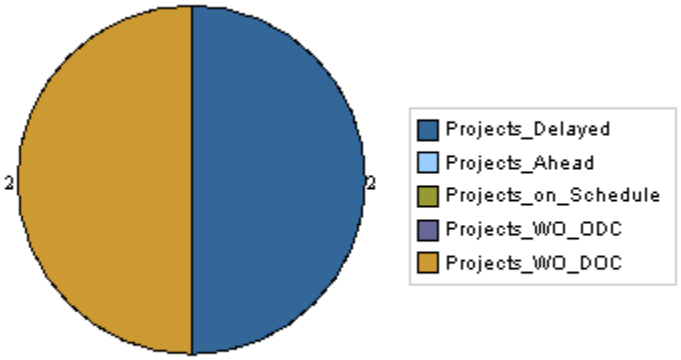

Total No Of Project's:- 4

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 16095.23 crore but this was subsequently anticipated to Rs. 27333.53 crore implying a cost overrun of 69.8%. The expenditure incurred on these projects till November, 2019 is Rs. 12884.57 crore, which is 47.1% of the anticipated cost of the projects.

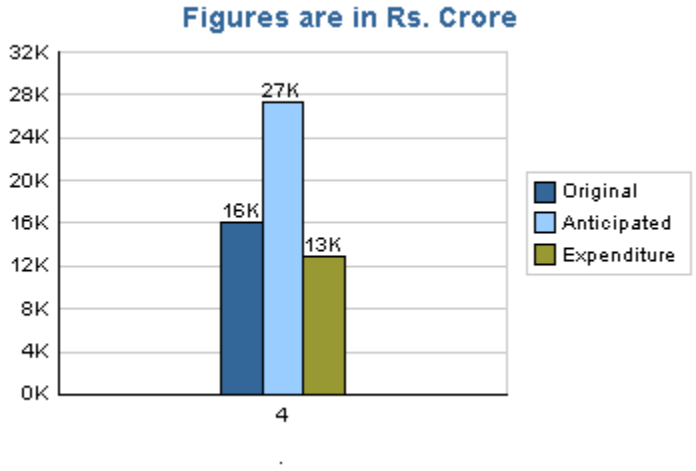

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT

Current Status:

Number of Projects	**75**
Number of Projects On Schedule	**15**
Number of Projects Delayed	**28**
Number of Projects Without Original Date of Commissioning	**3**
Number of Projects Without Date Of Commissioning	**29**

Brief Analysis

Project Status with respect to Original Schedule: Out of 75 projects, 15 projects are on schedule 28 projects are delayed. 29 projects do not have fixed dates of commissioning.3 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

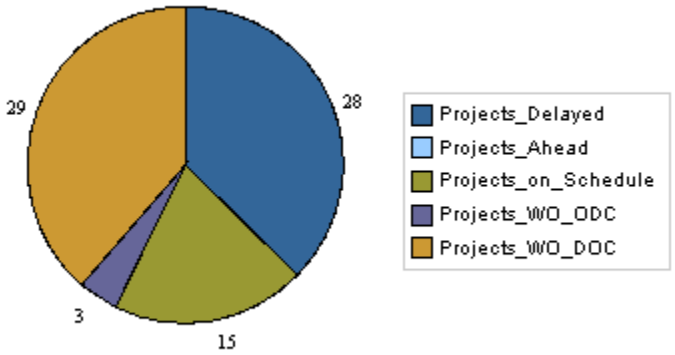

Total No Of Project's:- 75

Investment Scenario

Total original cost of implementation of 75 projects when sanctioned, was of the order of Rs. 263975.8 crore but this was subsequently anticipated to Rs. 270607.62 crore implying a cost overrun of 2.5%. The expenditure incurred on these projects till November, 2019 is Rs. 90163.27 crore, which is 33.3% of the anticipated cost of the projects.

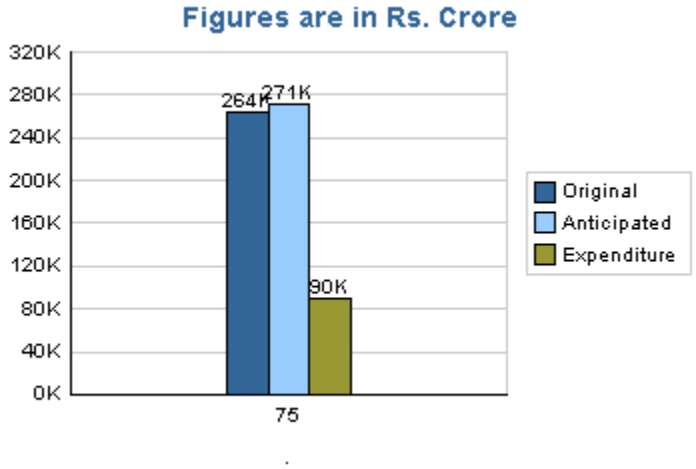

Annexure

Annexure - I

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE (NOVEMBER 2019)

(All Cost /Expenditure in Rs. crore

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	A & N ISLANDS	9	2,786.01	2,893.59	454.84
2	ANDHRA PRADESH	74	1,18,848.7	1,74,108.08	51,115.27
3	ARUNACHAL PRADESH	40	21,795.08	40,754.39	23,617.57
4	ASSAM	47	26,040.46	30,700.77	15,180.92
5	BIHAR	104	92,846.83	1,28,078.55	64,061.08
6	CHANDIGARH	2	349.15	570	0
7	CHHATISGARH	44	77,990.97	89,713.27	44,874.59
8	D & N HAVELI	1	6,086.08	5,842.31	4,784.88
9	DELHI	34	85,373.97	86,552.63	42,562.52
10	GOA	10	5,325.87	5,336.3	1,804.71
11	GUJARAT	58	82,316.29	88,517.56	47,765
12	HARYANA	42	34,417.9	37,813.53	17,329.74
13	HIMACHAL PRADESH	13	18,162.17	28,272.7	14,007.79
14	JAMMU AND KASHMIR	14	17,539.64	43,215.89	34,998.43
15	JHARKHAND	48	62,232.07	67,540.06	28,060.89
16	KARNATAKA	63	73,084.28	76,779.37	21,513.25
17	KERALA	20	36,309.6	39,755.52	15,165.41
18	MADHYA PRADESH	81	88,525.62	95,334.06	45,954.9
19	MAHARASHTRA	257	2,36,001.1	2,46,416.14	1,05,104.7
20	MANIPUR	5	6,002.36	14,012.39	9,822
21	MEGHALAYA	7	3,245.09	8,480.57	1,265.38
22	MIZORAM	13	7,757.62	11,189.69	4,820.39
23	MULTI STATE	126	3,45,904.63	4,57,316.12	1,46,694.53
24	NAGALAND	26	14,842.43	17,115.91	2,035.02
25	ODISHA	93	1,08,391.06	1,10,827.71	45,556.33
26	PUNJAB	27	13,539.35	15,616.61	9,606.15
27	RAJASTHAN	62	45,915.93	53,484.84	34,575.53
28	SIKKIM	9	3,476.73	6,368.17	1,169.06
29	TAMIL NADU	65	1,16,109.47	1,34,523.74	69,290.65
30	TELANGANA	55	39,236.69	41,643.9	14,632.52
31	TRIPURA	7	1,977.29	2,159.55	1,170.72
32	UTTAR PRADESH	133	1,51,214.21	1,57,530.32	74,058.76
33	UTTARAKHAND	33	36,092.7	44,984.12	15,572.3
34	WEST BENGAL	76	61,377.53	78,388.96	41,705.76
TOTAL		**1,698**	**20,41,114.88**	**24,41,837.32**	**10,50,331.59**

List of Projects in which Expenditure is More than Approved Cost

Annexure - II

Costing Rs. 150 Crore and above							(November 2019)
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	ATOMIC ENERGY						
	Bhavini Limited						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044	9/2003	3,492.00 -	6,840.00	5,837.84	09/2010 -	10/2021
	Nuclear Power Corporation Of India Limited						
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010	10/2009	11,459.00 -	16,580.00	14,137.00	12/2015 -	06/2020
	Total		14,951.00 -	23,420.00	19,974.84		
	COAL						
	Mahanadi Coal Fields Limited						
3	KANIHA OCP, MCL, (10.0 MTY) - [N06000035	12/2007	457.77 -	457.77	539.88	03/2013 -	03/2022
4	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067	8/2008	207.28 -	207.28	296.22	03/2012 -	03/2021
5	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034	12/2007	490.10 -	490.10	508.91	03/2017 -	03/2021
6	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044	12/2007	172.08 -	172.08	347.93	03/2010 -	03/2022
	Singareni Colliers Company Limitted						
7	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017	10/2006	249.03 -	448.86	296.17	03/2012 -	03/2024
	South-Eastern Coal Fields Limited						
8	JAGANNATHPOR OCP(3.00MTY) - [N06000075	9/2008	152.43 -	459.49	193.35	03/2015 -	03/2020
	Total		1,728.69 -	2,235.58	2,182.46		
	HEALTH AND FAMILY WELFARE						
	Hospital Services Consultancy Corporation Ltd						
9	AIIMS - MOTHER AND CHILD BLOCK - [N21000008	12/2013	204.44 -	270.00	204.70	05/2017 -	06/2020
10	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010	12/2014	168.90 -	191.20	169.51	05/2017 -	07/2019
11	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011	9/2014	505.58 -	585.00	586.96	03/2018 -	09/2019
12	AIIMS - OPD(NEW) - [N21000009	8/2014	293.65 -	325.00	297.16	05/2017 -	01/2020
	Total		1,172.57 -	1,371.20	1,258.33		
	PETROLEUM						

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning: Original/ Revised	Date of Commissioning: Anticipated
1	2	3	4	5	6	7	8
	Indian Strategic Petroleum Reserves Ltd						
13	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169	1/2006	993.00 -	1,693.00	1,549.85	01/2012 -	-
	Oil & Natural Gas Corporation Limited						
14	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128	3/2011	861.79 -	1,683.06	1,356.33	05/2013 12/2019	12/2019
15	DEVELOPMENT OF BSE-11 BLOCK - [N16000293	2/2017	511.30 -	511.30	523.88	11/2019 -	11/2019
	Total		2,366.09 -	3,887.36	3,430.06		
	POWER						
	National Hydro-Electric Power Corporation						
16	PARBATI HEP (4X200 MW) (NHPC) II - [180100210	9/2002	3,919.59 -	9,997.11	7,715.06	09/2009 -	12/2021
17	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221	9/2003	6,285.33 -	19,496.34	11,098.20	09/2010 -	-
	National Thermal Power Corporation						
18	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151	3/2013	11,638.55 -	12,865.92	12,361.29	01/2018 03/2020	03/2020
19	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193	4/2012	9,750.89 -	12,176.28	10,032.00	02/2017 06/2020	06/2020
20	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140	12/2012	11,846.00 -	12,739.82	12,839.84	10/2017 03/2020	03/2020
	Power Grid Corporation Of India Limited						
21	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	5/2005	1,779.29 -	2,187.32	2,237.45	11/2008 -	-
	Thdc India Limited						
22	DHUKWAN SMALL HYDRO PROJECT - [N18000189	5/2011	195.42 -	294.60	321.11	02/2014 -	12/2019
23	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	7/2006	1,657.00 -	5,024.35	3,118.00	02/2016 -	06/2022
	Total		47,072.07 -	74,781.74	59,722.95		
	RAILWAYS						
	Central Railways						
24	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247	4/2011	184.06 -	312.00	275.98	03/2019 12/2019	12/2019
25	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181	2/1997	2,271.50 -	3,712.50	2,434.24	03/2021 -	03/2022
	East Central Railways						
26	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222	3/1999	1,033.07 -	3,376.00	3,328.43	- -	03/2021

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning: Original/ Revised	Date of Commissioning: Anticipated
1	2	3	4	5	6	7	8
27	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476	4/1991	329.39 -	1,483.14	1,053.89	- -	12/2021
28	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182	4/2013	213.01 -	425.17	423.55	- -	01/2020
29	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240	4/1997	324.73 -	1,050.00	1,043.03	03/2012 -	03/2020
	East Coast Railway						
30	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319	3/2012	155.81 -	238.03	204.79	03/2020 -	03/2021
	Eastern Railways						
31	DEOGHAR - SULTANGANJ (INL), ER - [220100273	4/2000	607.09 -	1,425.44	637.54	02/2013 -	03/2024
32	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238	4/2011	175.80 -	251.18	251.18	- -	03/2021
33	MONIGRAM- NIMTITA - [N22000301	4/2012	250.93 -	310.70	275.20	- -	03/2024
34	BANDEL-BOINCHI 3RD LINE - [N22000221	4/2011	288.35 -	393.00	393.00	- -	03/2020
35	PIRPAINTI-BHAGALPUR - [N22000222	4/2011	261.38 -	478.08	478.08	- -	05/2019
	Metropolitan Rapid Transport Projects						
36	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	3/2000	1,049.69 -	3,404.92	3,837.57	12/2006 -	-
37	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135	3/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021
	North Central Railway						
38	ETAWAH-MAINPURI (NL),NCR - [220100318	4/1997	120.00 -	346.00	345.51	12/2008 -	-
	North East Frontier Railway						
39	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	4/2000	1,180.19 -	4,541.00	3,344.19	12/2008 -	03/2021
40	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207	4/2010	241.52 -	373.87	273.20	- -	06/2021
41	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499	2/1999	380.60 -	1,871.00	1,087.60	04/2010 -	-
42	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209	4/1999	819.23 -	1,871.00	1,082.01	- -	-
	North Eastern Railway						
43	HATHUA-BHATNI (N L) (NER) - [220100319	4/2005	230.03 -	230.03	277.14	12/2022 -	12/2022
44	CHHAPRA-BALLIA UP - [N22000134	3/2013	295.00 -	477.31	336.89	01/2019 -	01/2020
	North Western Railway						

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning: Original/ Revised	Date of Commissioning: Anticipated
1	2	3	4	5	6	7	8
45	AJMER-BANGURGRAM - [N22000155	4/2011	213.39 -	303.56	274.18	11/2019 -	05/2020
46	ALWAR-BANDIKUI DOUBLING - [N22000157	4/2013	242.09 -	410.00	362.96	02/2019 -	03/2020
	Northern Railway						
47	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492	3/2002	625.00 -	859.00	835.35	03/2016 -	03/2021
	Rail Vikas Nigam Ltd.						
48	HARIDASPUR-PARADEEP(NL) - [220100285	4/1996	1,185.64 -	1,844.47	1,829.53	12/2017 -	03/2020
49	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404	4/2011	927.01 -	1,200.00	1,178.67	03/2019 -	03/2020
50	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410	3/2006	948.04 -	1,500.00	1,374.96	03/2020 -	03/2021
51	BANASPANI- JAKHPURA - DOUBLING - [N22000412	3/2009	942.95 -	1,120.00	1,028.76	03/2019 -	06/2022
52	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407	3/2009	713.48 -	2,300.00	2,056.99	03/2020 -	03/2021
53	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213	4/2012	632.68 -	816.55	701.83	03/2016 -	12/2020
54	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	4/2000	133.41 207.00	385.00	387.92	03/2009 03/2009	06/2020
55	AHMEDABAD-BOTAD (GC) - [N22000140	4/2012	975.62 -	1,082.32	1,054.93	12/2021 -	12/2021
56	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313	3/2012	1,503.71 -	2,200.00	1,722.18	03/2020 -	03/2022
	South Central Railway						
57	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192	3/1996	164.36 -	1,050.00	999.64	02/2009 -	-
58	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432	4/2017	119.73 185.00	390.60	342.54	03/2022 -	03/2022
	South Eastern Railway						
59	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	4/2012	148.77 -	377.00	182.63	12/2016 08/2018	01/2020
	Southern Railway						
60	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079	9/2007	724.69 -	2,072.50	1,440.83	02/2019 -	02/2020
61	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187	4/1999	198.68 -	556.64	304.22	- -	-
62	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	9/1995	303.98 -	980.00	681.66	03/2020 -	03/2021
63	KURUPPANTHARA-CHINGAVANAM - [N22000190	4/2007	270.14 -	457.08	373.51	- -	-
64	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441	2/1996	268.87 -	950.00	927.86	03/2005 -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning: Original/ Revised	Date of Commissioning: Anticipated
1	2	3	4	5	6	7	8
65	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444	2/1999	257.00 257.00	257.00	268.31	03/2018 -	-
66	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215	4/2011	120.70 -	1,800.00	187.30	03/2019 -	12/2019
67	MADURAI-BODINAYAKKANUR - [N22000201	4/2008	164.41 -	450.00	167.49	- -	03/2020
	West Central Railway						
68	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	4/2001	424.60 -	2,909.99	1,975.34	03/2021 -	03/2023
	Western Railway						
69	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125	4/2006	117.36 196.95	202.35	809.40	03/2011 03/2017	03/2017
70	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121	4/2008	829.74 -	1,310.23	1,450.40	03/2020 03/2021	03/2021
	Total		28,442.01 -	62,929.63	50,195.13		
	ROAD TRANSPORT AND HIGHWAYS						
	Ministry Of Road Transport And Highways (State Pwds)						
71	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306	11/2010	624.41 -	992.67	853.82	03/2011 -	12/2019
72	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312	4/2013	151.59 -	151.59	196.76	08/2013 -	12/2019
73	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	8/2010	186.96 -	305.61	275.06	09/2014 -	12/2019
74	CITTORGARH-NEEMACH (4L) OF NH-79 AND NIMBAHARA PRATAPGARH (2L+PS) OF NH-113 UNDER PPP. - [N24000955	10/2012	511.21 -	511.21	814.79	10/2013 -	-
75	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523	12/2011	159.39 -	159.39	210.29	11/2017 -	-
76	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467	9/2012	511.00 -	511.00	2,323.04	10/2013 -	-
77	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415	8/2010	195.04 -	377.99	305.38	10/2010 -	06/2020
78	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411	11/2014	218.31 -	307.47	263.85	02/2018 -	-
79	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388	11/2013	497.05 -	881.05	544.84	05/2017 -	05/2020
80	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371	10/2013	445.89 -	653.29	464.05	03/2017 -	-
81	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314	1/2013	182.28 -	269.14	185.49	02/2013 -	12/2019

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning: Original/ Revised	Date of Commissioning: Anticipated
1	2	3	4	5	6	7	8
82	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308	8/2010	193.69 -	327.92	254.24	10/2010 -	12/2019
	National Highways And Infrastructure Development Corporation Ltd.						
83	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325	10/2015	179.82 -	179.82	197.77	01/2019 -	-
	National Highways Authority Of India						
84	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	525.00	492.41	02/2009 07/2019	07/2019
85	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049	12/2003	160.00 -	167.98	223.81	05/2008 -	06/2019
86	4 LANING OF NAGPUR-BETUL - [N24000155	2/2011	2,498.76 -	2,498.76	2,531.46	08/2014 -	-
87	INDORE-DEWAS(NH-3) - [N24000159	11/2010	325.00 -	475.00	469.54	05/2013 -	-
88	NALBARI T BIJNI (AS-7) - [N24000048	12/2003	208.00 -	230.00	339.22	04/2008 -	03/2020
89	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544	3/2016	676.73 -	676.73	945.17	04/2019 -	-
90	TRICHY - KARUR - [N24000528	3/2007	516.00 -	516.00	886.70	07/2008 -	-
91	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518	8/2015	399.54 -	297.27	509.75	04/2019 10/2017	10/2019
92	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517	12/2015	479.20 -	479.20	711.38	05/2018 03/2018	10/2019
93	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515	4/2014	1,665.00 -	1,665.00	4,357.89	- -	06/2019
94	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509	4/2010	1,170.52 -	1,170.52	2,051.36	06/2012 -	-
95	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508	7/2015	1,871.34 -	1,871.34	3,512.79	01/2018 12/2018	12/2019
96	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505	6/2015	1,583.79 -	1,583.79	1,648.90	01/2019 10/2019	10/2019
97	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	5/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	-
98	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	3/2017	988.34 -	1,043.28	1,034.00	03/2020 -	08/2020
99	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650	1/2017	244.90 -	244.90	251.87	05/2019 -	12/2019
100	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638	11/2012	605.84 -	722.46	723.95	07/2018 12/2019	02/2020
101	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624	9/2016	1,244.10 -	1,244.10	1,394.00	- -	02/2020

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning: Original/ Revised	Date of Commissioning: Anticipated
1	2	3	4	5	6	7	8
102	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622	9/2016	950.69 -	1,108.00	1,385.71	08/2019 -	12/2020
103	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621	9/2016	1,239.82 -	1,239.82	1,363.85	- -	05/2020
104	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477	2/2008	1,673.70 -	1,673.70	3,326.93	10/2011 -	-
105	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463	12/2015	1,083.00 -	1,083.00	1,487.87	06/2018 -	12/2019
106	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462	5/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020
107	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224	10/2012	1,928.22 -	2,945.00	2,467.00	04/2015 01/2017	06/2020
108	AHMEDABAD TO VADODARA SECTION - [N24000222	1/2013	2,125.24 -	2,125.24	4,669.71	12/2015 -	-
109	ETAWAH CHAKERI - [N24000219	3/2013	1,573.00 -	1,573.00	2,078.25	09/2015 -	-
110	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208	7/2012	291.36 -	291.36	459.07	01/2014 -	-
111	NASHRI- CHANANI - [N24000162	5/2011	2,159.00 -	2,519.00	4,706.90	06/2015 -	-
112	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161	7/2010	1,987.00 -	1,987.00	2,864.02	07/2015 12/2019	09/2020
113	INDORE-JHABUA-GUJRAT/MP - [N24000136	10/2010	1,175.00 -	1,175.00	1,509.96	04/2013 -	-
114	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232	11/2013	1,916.79 -	1,916.79	1,948.92	11/2016 -	-
115	NALBARI TO BIJNI (AS-6) - [N24000047	12/2003	225.00 -	225.00	328.47	06/2008 -	09/2019
116	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063	12/2003	217.61 -	360.84	453.70	04/2010 -	07/2019
117	PUNE-SATARA(NH-4) - [N24000156	10/2010	1,724.55 -	1,724.55	2,401.00	03/2013 -	12/2019
118	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149	2/2010	617.00 -	617.00	943.17	08/2012 -	12/2019
119	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230	5/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	-
120	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206	4/2012	1,396.18 -	1,396.18	2,894.94	09/2014 -	03/2020
121	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205	12/2011	1,047.00 -	1,047.00	1,874.43	06/2014 -	03/2019
122	4-LANING OF BRAHAMPORE-FARAKA - [N24000203	2/2011	998.79 -	998.79	1,807.21	08/2013 -	03/2021
123	4-LANING OF FARAKA-RAIGANJ - [N24000202	2/2011	1,078.84 -	1,078.84	2,181.00	08/2013 -	05/2020
124	MUZAFFARNAGAR-HARIDWAR - [N24000201	9/2011	754.00 -	754.00	1,364.18	03/2013 -	12/2019

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning: Original/ Revised	Date of Commissioning: Anticipated
1	2	3	4	5	6	7	8
125	PANIKHOLI-RIMOLI - [N24000197	3/2012	1,410.00 -	1,410.00	1,935.14	09/2014 -	-
126	SRINAGAR TO BANIHAL - [N24000189	6/2011	1,100.70 -	1,100.70	2,898.25	06/2014 09/2017	10/2020
127	4-LANNING OF CHAPRA-HAJIPUR - [N24000187	1/2011	575.00 -	575.00	850.24	07/2013 -	03/2020
128	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186	10/2011	375.09 -	375.09	494.33	04/2014 -	-
129	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460	12/2015	611.65 -	611.65	728.24	06/2016 -	-
130	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459	6/2015	845.24 -	941.00	847.81	- -	01/2020
131	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453	1/2015	972.50 -	972.50	3,512.79	07/2017 12/2019	03/2020
132	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452	7/2015	1,657.20 -	1,657.20	2,345.00	01/2019 -	-
133	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445	8/2014	822.90 -	822.90	844.08	04/2018 -	-
134	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432	9/2015	414.51 -	414.00	532.46	05/2018 05/2020	05/2020
135	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426	11/2012	530.07 -	530.07	556.02	08/2016 -	12/2019
136	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367	4/2014	495.78 -	495.78	633.24	01/2016 -	-
137	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360	4/2014	351.34 -	351.34	433.68	01/2016 -	-
138	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185	9/2011	574.00 -	574.00	768.73	03/2014 -	-
139	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183	11/2011	1,535.00 -	1,535.00	3,225.15	05/2014 12/2019	12/2019
140	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178	4/2011	571.00 -	571.00	582.53	10/2013 -	-
141	KANDLA - MUNDRA PORT - [N24000175	1/2011	953.88 -	953.88	976.79	07/2013 11/2020	11/2020
142	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172	9/2011	1,250.00 -	1,250.00	1,333.68	12/2013 -	06/2020
143	GHAZIABAD-ALIGARH NH-91 - [N24000170	2/2011	1,141.00 -	1,141.00	1,715.42	08/2013 -	-
144	PATNA-MUZZAFFARPUR - [N24000165	8/2010	671.30 -	671.30	1,132.48	02/2013 -	03/2020
145	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163	7/2010	1,813.76 -	1,813.76	2,393.99	07/2013 -	-
146	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	5/2009	1,108.00 -	2,967.50	3,990.72	11/2011 -	03/2020

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above							(November 2019)
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		68,973.62 -	75,218.24	1,09,274.45		
	URBAN DEVELOPMENT						
	Central Public Works Department						
147	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088	2/2014	388.00 -	488.28	440.59	05/2017 -	12/2019
148	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076	6/2014	157.84 -	169.16	163.98	03/2017 -	-
149	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062	2/2014	156.57 -	156.57	159.35	08/2016 -	-
	Chennai Metro Rail Ltd						
150	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084	2/2009	14,600.00 -	19,058.00	16,352.87	12/2015 -	-
	Hindustan Steelwork Construction Limited						
151	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101	5/2005	768.88 1,070.97	1,113.34	1,085.64	02/2014 -	-
152	CONSTRUCTION AND MAINTEINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098	3/2007	149.73 173.00	175.94	176.65	12/2015 -	-
	Total		16,221.02 -	21,161.29	18,379.08		
	WATER RESOURCES						
	Polavaram Project Authority						
153	POLAVARAM IRRIGATION PROJECT - [N30000002	2/2009	10,151.04 -	55,548.87	16,417.99	03/2020 -	06/2021
	Total		10,151.04 -	55,548.87	16,417.99		
	Grand Total		1,91,078.11	3,20,553.91	2,80,835.29		

MoSPI OCMS

Annexure - III

Details of Projects Ahead of Schedule w.r.t. Original Schedule

Costing Rs. 150 Crore and above							(November 2019)
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost (Rs. crore)	Antici pated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Antici pated
1	2	3	4	5	6	7	8
	COAL						
	South-Eastern Coal Fields Limited						
1	BATURA OCP (2.0 MTY) - [N06000049	8/2015	1,186.64 -	203.82	123.05	03/2023 -	03/2021
	Total		1,186.64 -	203.82	123.05		
	PETROLEUM						
	Indian Oil Corporation Limited						
2	PARADIP HYDERABAD PIPLEINE - [N16000194	1/2015	2,321.00 3,338.00	3,338.00	1,912.90	12/2020 -	08/2020
3	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254	9/2015	324.00 -	324.00	192.32	06/2020 -	03/2020
4	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302	8/2017	384.58	384.58	105.36	04/2021 -	09/2020
5	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252	5/2016	664.00 -	729.40	663.70	12/2020 -	02/2020
6	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308	8/2017	315.00 -	315.00	116.26	12/2021 -	12/2020
7	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332	3/2018	3,712.00 -	3,696.00	683.33	09/2022 -	06/2021
	Total		7,720.58 -	8,786.98	3,673.87		
	POWER						
	National Thermal Power Corporation						
8	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192	1/2013	12,964.60 17,304.00	17,304.00	14,229.00	05/2018 12/2021	06/2021
	Power Grid Corporation Of India Limited						
9	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164	5/2014	522.29 546.36	546.36	470.50	11/2016 06/2020	03/2020
10	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242	2/2017	322.30 -	322.30	164.09	02/2019 04/2020	03/2020
	Total		13,809.19 -	18,172.66	14,863.59		
	RAILWAYS						
	Central Railways						
11	PUNE-MIRAJ-LONDA (467 KM) - [N22000359	2/2015	3,627.47 -	3,627.47	761.03	03/2024 -	03/2023
	East Central Railways						

Costing Rs. 150 Crore and above							(November 2019)
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost (Rs. crore)	Antici pated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Antici pated
1	2	3	4	5	6	7	8
12	GARHWA ROAD-RAMNA - [N22000465	3/2015	348.23 -	348.23	187.91	03/2021 -	12/2020
	North East Frontier Railway						
13	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388	4/2015	2,232.32 -	2,182.00	756.32	03/2022 -	03/2020
14	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390	4/2016	602.27 -	612.00	336.17	12/2021 -	03/2020
	North Eastern Railway						
15	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347	3/2015	1,295.42 -	1,295.42	350.85	03/2022 -	12/2019
	Rail Vikas Nigam Ltd.						
16	BHANUPALI-BILASPUR BERI NL - [N22000273	4/2008	2,966.99 -	7,000.00	446.46	12/2026 -	12/2025
17	DIGHI PORT NEW LINE - [N22000408	4/2015	723.78 -	723.78	.19	12/2025 -	03/2025
	Total		11,796.48 -	15,788.90	2,838.93		
	ROAD TRANSPORT AND HIGHWAYS						
	Ministry Of Road Transport And Highways (State Pwds)						
18	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933	2/2017	429.43 -	429.43	209.09	11/2017 03/2020	11/2019
19	PARSHURAM GHAT TO ARAWALI - [N24001133	4/2016	983.14	983.14	655.15	12/2019 -	11/2019
20	REHABILITAITON AND UPGRADATION OF REPALLE TO EEPPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970	1/2017	576.48 -	576.48	228.31	01/2018 12/2020	01/2020
	National Highways Authority Of India						
21	GWALIOR-JHANSI, NH-75 - [N24000089	12/2003	604.00 364.59	364.59	215.58	12/2009 08/2020	03/2020
22	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655	3/2017	247.02 -	157.49	30.60	03/2020 02/2021	02/2020
23	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691	4/2017	894.00 -	929.32	750.00	04/2020 -	11/2019
24	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503	10/2015	447.29 746.43	746.43	613.57	12/2017 06/2020	12/2019
	Total		4,181.36 -	4,186.88	2,702.30		
	Grand Total		38,694.25	47,139.24	24,201.74		

Details of On Schedule Projects w.r.t. Original Schedule

Annexure - IV

Costing Rs. 150 Crore and above							(November 2019)
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Antici Pated
1	2	3	4	5	6	7	8
	CIVIL AVIATION						
	Airport Authority Of India Limited						
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083	12/2016	859.86 -	860.00	232.44	03/2021 -	03/2021
2	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085	7/2018	353.27 -	353.27	114.29	09/2020 -	09/2020
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT - [N04000079	3/2017	358.89 -	358.89	29.73	04/2021 -	04/2021
4	CONSTRUCTION OF TERMINAL BUILDING & ASSOCIATED WORKS AT LEH AIRPORT - [N04000078	7/2018	323.19 -	323.19	10.14	09/2021 -	09/2021
5	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075	8/2018	951.28 -	951.28	71.55	10/2021 -	10/2021
6	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082	5/2018	539.20 -	539.20	25.64	10/2022 -	10/2022
7	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081	1/2019	264.99 -	264.99	0.42	11/2021 -	11/2021
8	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077	6/2018	1,383.00 -	1,383.00	210.62	09/2021 -	09/2021
	Total		5,033.68 -	5,033.82	694.83		
	COAL						
	Bharat Coking Coal Limited						
9	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106	2/2014	555.52 -	555.52	5.24	03/2021 -	03/2021
	Central Coal Fields Limited						
10	NORTH URIMARI EXPANSION OCP - [N06000182	3/2019	1,553.06 -	1,553.06	203.46	03/2023 -	03/2023
11	AMRAPALI OC(12MTY) - [N06000103	2/2012	858.11 -	858.11	187.61	03/2020 -	03/2020
	Eastern Coal Fields Limited						
12	TILABONI UG MINE - [N06000172	2/2019	916.62 -	916.62	-	03/2027 -	03/2027
13	JHANJRA COMBINED PR(3.50 MTY) - [N06000020	11/2015	602.86 -	602.86	317.12	03/2022 -	03/2022
14	HURA - C OC (3 MTY) - [N06000143	10/2015	359.69 -	359.69	84.91	03/2022 -	03/2022
15	CHITRA EAST (RCE) OCP - [N06000169	8/2018	513.98 -	513.98	92.51	03/2024 -	03/2024
16	SIDULI MINE (OC AND UG) - [N06000165	5/2018	535.18 -	535.18	-	03/2026 -	03/2026

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated
1	2	3	4	5	6	7	8
17	NAKRAKONDA KUMARDIH B OCP - [N06000170	8/2018	502.68 -	502.68	-	03/2029 -	03/2029
	Mahanadi Coal Fields Limited						
18	GARJANBAHAL OCP - [N06000117	11/2014	1,375.38 -	1,375.38	445.39	03/2021 -	03/2021
19	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171	11/2018	2,838.87 -	2,838.87	1,157.99	03/2029 -	03/2029
20	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167	5/2018	2,434.75 -	2,434.75	123.99	03/2027 -	03/2027
21	SIARMAL OCP (40.00MTY) - [N06000113	5/2014	3,756.36 -	3,756.36	1,205.32	03/2026 -	03/2026
	Neyveli Lignite Corporation						
22	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152	7/2016	17,237.00 -	17,237.80	8,032.77	11/2021 -	11/2021
23	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145	3/2015	513.63 -	513.63	175.30	12/2019 -	12/2019
	Northern Coal Fields Limited						
24	SEMARIA OPENCAST PROJECT - [N06000176	5/2019	396.58 -	396.58	-	03/2026 -	03/2026
25	BLOCK-B EXPANSION OPENCAST PROJECT - [N06000184	7/2019	998.71 -	998.71	-	03/2023 -	03/2023
26	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159	5/2017	1,783.09 -	1,783.09	267.80	03/2021 -	03/2021
27	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162	11/2017	1,255.17 -	1,255.17	95.24	03/2022 -	03/2022
	Singareni Colliers Company Limitted						
28	KALYANIKHANI 6 INCLINE PROJECT - [N06000147	12/2015	477.65 -	477.65	2.11	03/2020 -	03/2020
	South-Eastern Coal Fields Limited						
29	AMADAND OPENCAST EXPANSION PROJECT - [N06000148	3/2016	869.44 -	869.44	116.75	03/2021 -	03/2021
30	DURGAPUR OPENCAST PROJECT - [N06000136	2/2015	916.24 -	916.24	4.11	03/2023 -	03/2023
31	JHIRIA WEST OPENCAST PROJECT - [N06000166	11/2018	389.97 -	389.97	-	03/2026 -	03/2026
32	BATURA HIGHWALL PROJECT - [N06000134	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
33	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093	6/2010	11,816.40 -	11,816.40	2,891.13	03/2023 -	03/2023
34	PELMA OCP(15.00MTY) - [N06000045	11/2014	1,624.59 -	1,624.59	6.50	03/2023 -	03/2023
35	BIJARI OC RCE (1.50 MTY) - [N06000111	5/2014	164.49 -	164.49	82.91	03/2020 -	03/2020
36	CHHAL OC SEAM -III (6.00 MTY) - [N06000104	12/2013	610.63 -	610.63	105.36	03/2022 -	03/2022
37	MADANNAGAR OPENCAST PROJECT - [N06000140	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
38	MAHAMAYA OPENCAST PROJECT - [N06000164	5/2018	410.26 -	410.26	9.53	03/2026 -	03/2026

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated
1	2	3	4	5	6	7	8
39	AMRITDHARA OC PROJECT - [N06000122	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
40	AMGAON OPENCAST PROJECT RCE - [N06000135	7/2015	316.10 -	316.10	86.43	03/2020 -	03/2020
41	VIJAY WEST OPENCAST PROJECT - [N06000158	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026
42	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008	8/2013	7,612.33 -	7,612.33	2,116.58	03/2023 -	03/2023
43	KANCHAN OC EXPANSION - [N06000125	12/2014	371.04 -	371.04	48.13	03/2021 -	03/2021
44	MALACHUA OPENCAST PROJECT - [N06000139	10/2015	488.33 -	488.33	27.33	03/2023 -	03/2023
45	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124	12/2014	357.80 -	357.80	104.66	03/2021 -	03/2021
	Western Coal Fields Limited						
46	VISHNUPURI UG TO OC MINE - [N06000178	7/2018	195.57 -	195.57	2.94	03/2025 -	03/2025
47	GANDHIGRAM UG MINE - [N06000183	8/2019	414.16 -	414.16	0.01	03/2026 -	03/2026
48	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154	8/2016	319.76 -	319.76	238.99	03/2022 -	03/2022
49	UKNI DEEP OC - [N06000179	11/2018	318.14 -	318.14	143.90	03/2021 -	03/2021
50	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157	2/2017	328.00 -	328.00	167.00	03/2021 -	03/2021
51	DINESH OCP - [N06000118	11/2014	611.16 -	611.16	413.02	03/2020 -	03/2020
52	BELLORA-NAIGAON DEEP OC - [N06000180	11/2018	252.71 -	252.71	45.09	03/2021 -	03/2021
53	SAONER I UG TO OC PHASE I - [N06000177	11/2016	162.10 -	162.10	50.64	03/2022 -	03/2022
54	KOLAR PIMPRI EXTENSION OC - [N06000160	3/2017	362.73 -	362.73	322.07	03/2020 -	03/2020
55	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153	7/2016	409.87 -	409.87	19.05	03/2022 -	03/2022
56	BHANEGAON OC - [N06000121	2/2015	187.94 -	409.68	127.70	03/2023 -	03/2023
57	AMALGAMATED PAUNI-II III OC MINE - [N06000131	6/2015	483.69 -	483.69	219.00	03/2021 -	03/2021
58	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142	11/2015	498.42 -	498.42	189.52	03/2020 -	03/2020
59	AMALGAMATED YEKONA-I YEKONA-II - [N06000132	8/2015	727.28 -	727.28	260.88	03/2025 -	03/2025
60	DHANKASA UG (1.00 MTY) - [N06000155	9/2016	458.07 -	458.07	20.86	03/2022 -	03/2022
61	SINGHORI OC MINE - [N06000130	6/2015	205.49 -	205.49	117.56	03/2020 -	03/2020
62	PENGANGA OCP(REVISED) - [N06000066	9/2014	441.82 -	441.82	215.48	03/2020 -	03/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated
1	2	3	4	5	6	7	8
	Total		75,355.21 -	75,577.75	20,625.85		
	FERTILISERS						
	National Fertiliser Limited						
63	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016	1/2018	239.81 -	239.81	145.72	11/2019 -	11/2019
64	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015	1/2018	218.83 -	218.83	131.34	11/2019 -	11/2019
65	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014	1/2018	215.92 -	215.92	128.60	11/2019 -	11/2019
	Rashtriya Chemical & Fertiliser Limited						
66	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018	4/2018	426.72 -	426.72	249.06	04/2020 -	04/2020
	Total		1,101.28 -	1,101.28	654.72		
	HEALTH AND FAMILY WELFARE						
	National Building Construcion Corporation Ltd						
67	AIIMS BILASPUR - [N21000028	4/2018	1,351.00 -	1,351.00	245.85	09/2021 -	09/2021
	Total		1,351.00 -	1,351.00	245.85		
	INFORMATION AND BROADCASTING						
68	NATIONAL CENTRE OF EXCELLENCE FOR ANIMATION VISUAL EFFECTS GAMING AND COMICS - [N09000003	12/2016	167.70 -	167.70	-	03/2020 -	03/2020
	Total		167.70 -	167.70	.00		
	MINES						
	National Aluminum Company Limited (Nalco)						
69	UTKAL D AND E COAL BLOCK - [N10000011	5/2016	534.00 -	534.00	320.18	01/2020 -	01/2020
70	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013	11/2017	483.00 -	483.00	1.20	04/2021 04/2021	04/2021
71	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012	12/2015	355.00 -	355.00	82.07	11/2020 -	11/2020
72	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010	12/2014	5,540.00 -	5,540.00	114.95	04/2021 04/2021	04/2021
	Total		6,912.00 -	6,912.00	518.40		

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above							(November 2019)
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Antici Pated
1	2	3	4	5	6	7	8
	PETROLEUM						
	Bharat Petroleum Corporation Limited						
73	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373	11/2018	248.55 -	248.55	23.38	06/2022 -	06/2022
74	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346	9/2018	11,130.00 -	11,130.00	54.40	03/2023 -	03/2023
75	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260	2/2016	554.00 -	554.00	375.80	02/2020 -	02/2020
76	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365	12/2017	1,524.06 -	1,524.06	20.02	12/2021 -	12/2021
77	2G ETHANOL BIO REFINERY AT BARGARH - [N16000341	8/2017	750.00 -	750.00	34.73	12/2020 -	12/2020
78	PUNE POL STORAGE DEPOT - [N16000313	8/2016	282.64 -	282.64	145.83	08/2020 -	08/2020
79	2ND GENERATION LIGNOCELLUOSIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA) - [N16000374	8/2019	1,607.00 -	1,607.00	37.49	08/2022 -	08/2022
80	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347	10/2018	206.26 -	206.26	2.84	03/2021 -	03/2021
81	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364	7/2017	580.20 -	580.20	47.41	02/2021 -	02/2021
	Chennai Petroleum Corporation Limited						
82	BS-VI PROJECTS - [N16000295	9/2017	1,858.00 -	1,858.00	1,119.38	12/2019 -	12/2019
83	RE-LIQUIFIED NATURAL GAS - [N16000301	8/2017	421.00 -	421.00	159.94	08/2020 -	08/2020
	Gas Authority Of India Limited						
84	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329	10/2017	226.45 -	226.45	56.99	10/2022 -	10/2022
85	BARAUNI-GUWAHATI PIPELINE - [N16000334	6/2018	3,308.00 -	3,308.00	1,349.36	12/2021 -	12/2021
86	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271	7/2015	2,881.40 -	2,000.00	1,293.26	12/2020 -	12/2020
87	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328	7/2017	182.20 -	182.20	32.85	07/2022 -	07/2022
88	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273	3/2017	2,433.00 -	2,433.00	1,496.03	12/2020 -	12/2020
89	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288	4/2017	287.49 -	287.49	133.40	04/2022 -	04/2022
90	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289	7/2017	243.53 -	243.53	55.03	07/2022 -	07/2022
91	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210	2/2015	749.00 -	842.00	606.89	02/2020 -	02/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated
1	2	3	4	5	6	7	8
92	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349	9/2018	225.54 -	225.54	2.35	02/2021 -	02/2021
93	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR - [N16000330	10/2017	221.45 -	221.45	51.10	10/2022 -	10/2022
94	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272	3/2017	1,933.00 -	1,933.00	1,055.91	12/2020 -	12/2020
95	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327	10/2017	359.25 -	359.25	75.57	10/2022 -	10/2022
96	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275	3/2017	1,740.00 -	1,740.00	462.88	12/2020 -	12/2020
97	BOKARO-ANGUL PIPELINE PROJECT - [N16000274	3/2017	3,437.00 -	3,437.00	1,309.83	12/2020 -	12/2020
	Hindustan Petroleum Corporation Limited						
98	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296	9/2017	2,677.00 -	2,677.00	971.81	03/2021 -	03/2021
99	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH - [N16000311	12/2016	300.00 -	300.00	1.09	04/2021 -	04/2021
100	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369	12/2018	854.00 -	854.00	38.34	12/2022 -	12/2022
101	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312	11/2017	255.00 -	255.00	94.33	11/2020 -	11/2020
102	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238	9/2016	1,879.00 -	1,879.00	1,536.16	06/2020 -	06/2020
103	REDEVELOPMENT/ EXPANSION OF MEERUT DEPOT FOR ENHANCING PRODUCT HANDLING CAPACITY - [N16000366	8/2016	154.84 -	154.84	128.71	11/2019 -	11/2019
104	MUMBAI REFINERY EXPANSION PROJECT - [N16000281	9/2015	4,199.00 -	5,060.00	3,071.60	03/2020 -	03/2020
105	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367	6/2019	2,166.38 -	2,166.38	15.61	06/2022 -	06/2022
	Indian Oil Corporation Limited						
106	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351	12/2018	611.00 -	611.00	13.11	04/2022 -	04/2022
107	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333	3/2018	676.00 -	676.00	251.64	12/2021 -	12/2021
108	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338	4/2018	5,654.00 -	5,654.00	467.39	10/2021 -	10/2021
109	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT - [N16000363	12/2018	278.60 -	278.60	-	06/2021 -	06/2021
110	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324	12/2017	199.36 -	199.36	9.39	10/2020 -	10/2020
111	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
112	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352	1/2019	909.00 -	909.00	22.76	01/2021 -	01/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated
1	2	3	4	5	6	7	8
113	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193	1/2015	1,823.00 -	3,027.90	955.36	12/2020 -	12/2020
114	R and D CAMPUS II AT FARIDABAD - [N16000375	6/2019	2,281.94 -	2,281.94	-	12/2022 -	12/2022
115	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249	5/2016	1,945.00 -	1,945.00	1,004.75	08/2021 -	08/2021
116	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362	5/2019	3,361.00 -	3,361.00	372.43	08/2021 -	08/2021
117	LPG BP PROJECT MOTIHARI - [N16000317	5/2018	206.50 -	206.50	21.62	03/2021 -	03/2021
118	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361	11/2018	462.30 -	462.30	-	09/2021 -	09/2021
119	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350	10/2018	316.20 -	316.20	14.78	10/2021 -	10/2021
120	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340	8/2018	1,636.00 -	1,636.00	152.56	08/2020 -	08/2020
121	INFRASTRUCTURE DEVLOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284	9/2016	208.35 -	208.35	126.98	07/2020 -	07/2020
122	LAB REVAMP AT GUJARAT REFINERY - [N16000377	10/2019	403.00 -	403.00	43.50	12/2021 -	12/2021
123	AUGMENTATION OF CTMPL - [N16000286	12/2016	228.00 -	228.00	24.50	06/2020 -	06/2020
124	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
125	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251	4/2016	1,021.00 -	1,021.00	4.45	12/2020 -	12/2020
126	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337	7/2018	189.00 -	189.00	23.10	01/2021 -	01/2021
127	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344	4/2018	522.00 -	522.00	158.65	03/2021 -	03/2021
128	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321	4/2018	206.63 -	206.63	19.25	02/2020 -	02/2020
129	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345	10/2018	1,297.50 -	1,297.50	18.30	10/2021 -	10/2021
130	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI - [N16000276	5/2016	261.00 -	261.00	52.11	01/2021 -	01/2021
131	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309	8/2017	1,342.00 -	1,342.00	6.30	08/2020 -	08/2020
132	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323	8/2017	255.40 -	255.40	4.07	08/2020 -	08/2020
133	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353	10/2018	598.00 -	598.00	17.37	02/2020 -	02/2020
134	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376	8/2019	1,255.00 -	1,255.00	99.93	10/2021 -	10/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated
1	2	3	4	5	6	7	8
135	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368	6/2019	371.00 -	371.00	-	09/2022 -	09/2022
136	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162	5/2013	711.00 -	711.00	11.12	06/2020 -	06/2020
	Oil & Natural Gas Corporation Limited						
137	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358	4/2019	3,228.80 -	3,228.80	497.01	03/2022 -	03/2022
138	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335	4/2018	766.37 -	766.37	465.86	12/2019 -	12/2019
139	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278	7/2016	249.85 250.00	265.49	180.20	05/2020 -	05/2020
140	REDEVELOPMENT OF SANTHAL FIELD - [N16000279	2/2017	1,162.56 -	1,162.56	412.79	03/2026 -	03/2026
141	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370	5/2019	763.92 -	763.92	116.82	12/2020 -	12/2020
142	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357	2/2019	2,292.46 -	2,292.46	402.18	05/2021 -	05/2021
143	DEVELOPMENT OF BSE-11 BLOCK - [N16000293	2/2017	511.30 -	511.30	523.88	11/2019 -	11/2019
144	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294	2/2017	968.61 -	1,033.95	968.11	11/2019 -	11/2019
	Oil India Limited						
145	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356	6/2016	224.75 -	224.75	69.99	08/2020 -	08/2020
146	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258	5/2016	406.00 -	406.00	91.19	10/2020 -	10/2020
	Total		90,266.64 -	91,625.12	23,483.77		
	POWER						
	National Thermal Power Corporation						
147	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273	12/2018	587.44 -	587.44	250.00	09/2020 -	09/2020
148	PATRATU STPP-I (3X800MW) - [N18000275	11/2017	18,668.00 -	18,668.00	2,078.50	03/2023 -	03/2023
149	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274	3/2019	349.00 -	349.00	125.00	11/2020 -	11/2020
150	TALAIPALLI COAL MINING PROJECT - [N18000266	9/2015	3,004.00 -	3,004.00	1,782.00	11/2019 -	11/2019
	Power Grid Corporation Of India Limited						
151	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247	2/2017	5,070.13 -	5,070.13	3,042.59	04/2020 -	04/2020
152	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264	8/2017	1,931.39 -	1,931.39	1,107.54	02/2020 -	02/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated
1	2	3	4	5	6	7	8
153	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258	3/2017	3,500.00 3,500.00	3,500.00	1,949.00	07/2020 -	07/2020
154	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268	11/2017	358.83 -	358.83	166.27	05/2020 -	05/2020
155	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238	3/2017	283.72 -	283.72	196.10	11/2019 -	11/2019
	Satluj Jal Vidyut Nigam Limited						
156	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194	3/2019	10,439.09 -	10,439.09	836.81	01/2024 -	01/2024
157	NAITWAR MORI HEP - [N18000265	10/2017	648.33 -	648.33	284.44	12/2021 -	12/2021
	Thdc India Limited						
158	KHURJA SUPER THERMAL POWER PROJECT - [N18000272	3/2019	11,089.42 -	11,089.42	672.81	09/2023 -	09/2023
159	AMELIA COAL MINE - [N18000252	1/2017	2,104.21 -	1,587.16	308.34	09/2020 -	09/2020
	Total		58,033.56 -	57,516.51	12,799.40		
	RAILWAYS						
	Central Railways						
160	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358	2/2015	2,449.91 -	2,449.91	180.76	03/2023 -	03/2023
161	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353	2/2016	9,968.00 -	9,968.00	-	03/2024 -	03/2024
162	DAUND - MANMAD (236 KM) - [N22000360	2/2016	1,876.00 -	2,081.27	187.09	03/2023 -	03/2023
163	PUNE-NASIK (265 KM) - [N22000354	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
164	WARDHA-NANDED MAHARASHTRA - [N22000231	4/2008	3,168.29 -	3,168.29	1,202.21	03/2023 -	03/2023
	Dedicated Freight Corridor Corporation Of India Ltd						
165	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	03/2020
	East Central Railways						
166	KOSI BRIDGE (NL), ECR - [220100304	4/2002	499.41 -	516.02	402.55	03/2020 -	03/2020
	East Coast Railway						
167	KOTTAVALSA - KORAPUT DOUBLING - [N22000377	4/2015	2,499.71 -	3,382.95	397.90	03/2022 -	03/2022
	North Central Railway						
168	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372	4/2015	668.70 668.00	680.00	330.00	03/2020 -	03/2020
169	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495	3/2018	4,329.53 -	4,329.53	3.90	03/2023 -	03/2023
170	JHANSI BINA DOUBLING - [N22000496	9/2016	2,001.00 -	2,001.00	416.59	03/2021 -	03/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated
1	2	3	4	5	6	7	8
	North East Frontier Railway						
171	DIGARU-HOJAI (102 KM) - [N22000389	4/2015	870.96 -	2,136.01	580.01	03/2021 -	03/2021
172	MURKONGSELEK-PASIGHAT NL - [N22000208	4/2011	414.84 -	661.00	122.93	03/2020 -	03/2020
173	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206	4/2010	242.22 -	471.00	69.09	03/2020 -	03/2020
174	DIMAPUR-TIZIT NL - [N22000196	4/2013	4,274.00 -	4,274.00	-	03/2020 -	03/2020
175	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205	4/2010	906.46 -	6,000.00	263.12	03/2021 -	03/2021
	North Eastern Railway						
176	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131	3/2007	243.78 -	895.00	106.55	12/2021 -	12/2021
177	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469	4/2016	600.00 -	600.00	31.72	01/2022 -	01/2022
178	HATHUA-BHATNI (N L) (NER) - [220100319	4/2005	230.03 -	230.03	277.14	12/2022 -	12/2022
179	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457	4/2016	1,900.00 -	1,277.06	-	01/2022 -	01/2022
	Northern Railway						
180	CHANDIGARH-BADDI - [N22000467	4/2007	328.14 -	1,540.00	234.79	03/2023 -	03/2023
	National High Speed Rail Corporation Limited						
181	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463	12/2015	1,08,000.00 -	1,08,000.00	5,969.41	12/2023 12/2023	12/2023
	Rail India Technical And Economic Service						
182	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498	2/2016	393.98 -	393.98	290.45	03/2020 -	03/2020
183	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394	3/2015	636.38 -	636.38	281.85	03/2021 -	03/2021
	Rail Vikas Nigam Ltd.						
184	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403	4/2015	773.94 -	773.94	475.85	12/2024 -	12/2024
185	VIJAYAWADA-GUDUR - [N22000369	4/2015	3,246.26 -	3,548.67	1,211.97	12/2023 -	12/2023
186	AHMEDABAD-BOTAD (GC) - [N22000140	4/2012	975.62 -	1,082.32	1,054.93	12/2021 -	12/2021
187	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409	1/1991	2,335.67 -	2,335.68	647.54	12/2024 -	12/2024
188	DHASA-JETALSAR (GC) - [N22000141	4/2012	644.38 -	644.38	418.93	03/2021 -	03/2021
	South Central Railway						
189	BHADRACHALAM ROAD-SATTUPALLI - [N22000287	4/2010	704.31 -	952.16	303.24	03/2020 03/2020	03/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated
1	2	3	4	5	6	7	8
190	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432	4/2017	119.73 185.00	390.60	342.54	03/2022 -	03/2022
	South East Central Railway						
191	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420	9/2016	1,908.51 -	2,686.63	515.29	03/2023 03/2023	03/2023
	South Western Railway						
192	ARSIKERE-TUMKUR - [N22000332	3/2015	578.00 -	578.00	525.85	03/2020 -	03/2020
193	YELAHANKA-PENUKONDA - [N22000328	5/2015	860.43 -	958.00	756.85	03/2020 -	03/2020
	Southern Railway						
194	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449	2/2015	1,700.00 -	1,003.00	252.02	03/2022 -	03/2022
	Western Railway						
195	CHOTTAUDEPUR-DHAR(NL) - [N22000138	4/2007	1,347.26 -	1,347.26	741.93	03/2022 03/2022	03/2022
196	SURENDRA NAGAR RAJKOT - [N22000392	4/2015	1,002.39 -	1,002.39	396.54	03/2021 03/2021	03/2021
	Total		1,81,714.84 -	2,29,437.14	41,476.54		
	ROAD TRANSPORT AND HIGHWAYS						
	Ministry Of Road Transport And Highways (State Pwds)						
197	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777	11/2017	283.51 -	283.51	126.38	11/2019 -	11/2019
198	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907	3/2018	293.10 -	293.10	63.14	08/2020 -	08/2020
199	PUNE TO MALE VILLAGE - [N24001078	3/2018	228.31 -	228.31	13.50	12/2019 -	12/2019
200	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 -	238.00	7.48	11/2019 -	11/2019
201	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197	3/2018	351.00 -	351.00	0.49	06/2021 -	06/2021
202	SHIVUR TO YEOLA - [N24001059	3/2018	181.08 -	181.08	7.50	12/2019 -	12/2019
203	REHABILITATION AND UPGRADATION OF ALLAHABAD - MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203	10/2016	218.90 -	218.90	62.69	03/2020 -	03/2020
204	DHANGIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064	3/2018	217.14 217.00	217.14	99.77	02/2020 -	02/2020
205	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174	10/2016	235.31 -	235.31	91.38	11/2020 -	11/2020
206	JALGAON TO NANDURA - [N24001088	3/2018	177.84 177.00	177.84	73.69	12/2019 -	12/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated
1	2	3	4	5	6	7	8
207	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994	3/2018	626.76 -	626.76	80.66	07/2020 -	07/2020
208	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781	5/2018	248.00 -	248.00	-	05/2020 -	05/2020
209	NALDURG TO AKKALKOT - [N24001051	2/2018	274.50 275.00	274.50	65.39	12/2019 -	12/2019
210	KALMATH TO ZARAP - [N24001137	9/2016	1,338.13 1,338.00	1,338.13	959.51	03/2020 -	03/2020
211	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883	3/2018	254.30 -	254.30	53.02	10/2020 -	10/2020
212	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139	10/2016	218.94 219.00	218.94	103.89	03/2020 -	03/2020
213	WADIGODRI TO DHANGRIPIMPRI - [N24001063	3/2018	194.23 194.00	194.23	86.23	02/2020 -	02/2020
214	PAHUR TO BODHWAD - [N24001084	1/2017	244.93 -	244.93	59.23	05/2020 -	05/2020
215	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141	3/2016	240.30 240.00	240.30	198.06	01/2020 -	01/2020
216	DEULGAON SAKARSHA TO MEHKAR - [N24001076	3/2018	219.91 -	219.91	126.76	12/2019 -	12/2019
217	TALGAON TO KALMATH - [N24001136	10/2016	904.70 905.00	904.70	604.05	03/2020 -	03/2020
218	KUNDRAL TO WAZAR - [N24001077	1/2018	225.25 225.00	225.25	148.75	12/2019 -	12/2019
219	TASGAON TO SHIRDHON - [N24001054	1/2017	195.64 196.00	195.64	169.73	11/2019 -	11/2019
220	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774	12/2017	248.22 -	248.22	57.20	12/2019 -	12/2019
221	SANGOLA TO JATH - [N24001052	1/2018	257.38 257.00	257.38	84.15	12/2019 -	12/2019
222	SALAIKHURD TO TIRORA - [N24001042	1/2018	415.25 415.25	415.25	96.22	12/2019 -	12/2019
223	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062	3/2018	336.21 336.00	336.21	71.66	12/2019 -	12/2019
224	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905	3/2018	322.48 -	322.48	120.18	07/2020 -	07/2020
225	MALEGAON TO RISOD - [N24001089	2/2018	303.24 303.00	303.24	131.97	12/2019 -	12/2019
226	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984	1/2017	283.00 -	283.00	166.22	12/2019 -	12/2019
227	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208	3/2018	288.30 -	288.30	0.34	08/2020 -	08/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated
1	2	3	4	5	6	7	8
228	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992	2/2018	426.52 -	426.52	225.51	04/2020 -	04/2020
229	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216	12/2016	196.00 -	196.00	-	09/2021 -	09/2021
230	PANCHARAL TO MANDANGHAR - [N24001107	7/2018	381.08 302.00	381.08	13.03	05/2020 -	05/2020
231	HIMAYATNAGAR TO PHULSAWANGI - [N24001081	3/2018	294.87 295.00	294.87	36.30	12/2019 -	12/2019
232	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080	3/2018	256.15 -	256.15	36.50	12/2019 -	12/2019
233	PATGAON KHOPOLI SECTION I - [N24001028	1/2018	170.00 -	170.00	56.57	12/2019 -	12/2019
234	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772	12/2017	257.34 -	257.34	62.79	12/2019 -	12/2019
235	KHAMGAON TO DEULGAON SAKARSHA - [N24001074	3/2018	249.29 -	249.29	97.20	12/2019 -	12/2019
236	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131	3/2018	212.99 -	212.99	93.80	06/2020 -	06/2020
237	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778	11/2017	266.52 -	266.52	144.27	11/2019 -	11/2019
238	JALKOT TO TOGRI - [N24001071	7/2018	299.92 300.00	299.92	19.20	08/2020 -	08/2020
239	KARAD TO VITA - [N24001049	1/2018	344.85 245.00	344.85	96.04	12/2019 -	12/2019
240	KANTE TO WAKED - [N24001134	3/2016	1,230.02 1,230.00	1,230.02	555.61	11/2019 -	11/2019
241	KHERDA TO NAGZARI - [N24001072	3/2018	181.30 -	181.30	72.50	12/2019 -	12/2019
242	PALPHATA TO PHULAMBARI - [N24001060	3/2018	227.19 227.00	227.19	74.23	12/2019 -	12/2019
243	WARDHA TO HINGAGHAT - [N24001098	1/2018	216.90 217.00	216.90	55.00	12/2019 -	12/2019
244	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198	1/2019	264.50 -	264.50	-	03/2021 -	03/2021
245	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993	3/2018	322.81 -	322.81	1.66	09/2020 -	09/2020
246	CHIKALI TO DHAD - [N24001061	3/2018	189.46 189.00	189.46	35.54	12/2019 -	12/2019
247	RISOD TO HINGOLI - [N24001149	2/2018	355.99 -	355.99	131.97	12/2019 -	12/2019
248	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991	2/2018	220.28 -	220.28	37.58	11/2019 -	11/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated
1	2	3	4	5	6	7	8
249	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180	3/2019	237.51 -	237.51	-	12/2022 -	12/2022
250	KARASWADA TO BAMBOLIM - [N24001005	3/2017	852.67 -	852.67	86.04	12/2019 -	12/2019
251	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990	2/2018	294.13 -	294.13	39.44	11/2019 -	11/2019
252	MANGRUPHIR TO MAHAN - [N24001087	3/2018	222.13 222.00	222.13	78.63	11/2019 -	11/2019
253	LATUR TO PANGAON - [N24001066	3/2018	336.47 336.00	336.47	123.48	12/2019 -	12/2019
254	PARBHANI TO GANGKHED - [N24001065	3/2018	238.19 238.00	238.19	45.85	12/2019 -	12/2019
255	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179	3/2017	217.35 -	217.35	35.10	11/2020 -	11/2020
256	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927	3/2018	293.64 -	293.64	28.24	08/2020 -	08/2020
257	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148	3/2016	599.34 -	599.34	485.53	01/2020 -	01/2020
258	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206	3/2018	263.89 -	242.05	139.38	04/2020 -	04/2020
259	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152	9/2018	160.00 -	160.00	0.50	09/2021 -	09/2021
260	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209	3/2016	296.50 -	296.50	40.27	09/2020 -	09/2020
261	WASHIM TO DASTAPUR - [N24001068	3/2018	165.51 -	165.51	34.45	12/2019 -	12/2019
262	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989	2/2018	206.13 -	206.13	127.86	06/2020 -	06/2020
263	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207	3/2018	185.18 -	185.18	65.66	02/2020 -	02/2020
264	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082	3/2018	223.46 -	223.46	21.42	12/2019 -	12/2019
265	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176	10/2016	172.63 -	172.63	45.02	12/2020 -	12/2020
266	CHIKLI TO TAKARKHED - [N24001083	3/2018	393.10 393.00	393.10	153.97	12/2019 -	12/2019
267	VITA TO NAGAJ - [N24001050	3/2018	304.58 305.00	304.58	24.16	12/2019 -	12/2019
268	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988	1/2018	230.03 -	230.03	127.98	12/2019 -	12/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated
1	2	3	4	5	6	7	8
269	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821	11/2017	257.34 -	238.00	41.09	11/2019 -	11/2019
270	BAMNI TO NAVAEGAON - [N24001110	9/2017	241.69 242.00	241.69	83.29	04/2020 -	04/2020
271	JALGAON TO BHADGAON - [N24001045	1/2018	307.54 308.00	307.54	124.59	11/2019 -	11/2019
272	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987	1/2018	283.15 -	283.15	42.22	05/2020 -	05/2020
273	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475	11/2015	628.45 -	628.45	259.33	01/2020 -	01/2020
274	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478	12/2015	957.54 -	957.54	503.38	02/2020 -	02/2020
275	ARNI TO NAIGAINBANDI - [N24001093	12/2017	309.94 310.00	309.94	51.32	12/2019 -	12/2019
276	DASTAPUR TO KARANJA - [N24001070	3/2018	182.63 -	182.63	82.40	12/2019 -	12/2019
277	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773	12/2017	200.34 -	200.34	31.00	12/2019 -	12/2019
278	SHAHPUR PATGAON SECTION I - [N24001027	1/2018	150.79 -	150.79	21.42	12/2019 -	12/2019
279	SELDOH TO PANVAR - [N24001097	7/2018	404.33 404.00	404.33	30.19	05/2020 -	05/2020
280	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175	10/2016	167.62 -	167.62	42.15	12/2020 -	12/2020
281	PATRADEVI TO KARASWADA 4L - [N24001004	3/2017	634.32 -	634.32	109.33	05/2020 -	05/2020
282	JAHIRABAD TO LATUR - [N24001040	1/2017	461.96 -	461.96	160.43	11/2019 -	11/2019
283	MANSAR TO SALAIKHURD - [N24001035	1/2018	418.36 -	418.36	125.13	12/2019 -	12/2019
284	WARDHA TO ARVI - [N24001150	2/2018	313.58 -	313.58	12.96	04/2020 -	04/2020
285	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091	3/2016	536.65 356.00	536.65	465.20	12/2019 -	12/2019
286	ARDHAPUR TO HIMAYATNAGAR - [N24001079	12/2017	426.06 426.00	426.06	66.97	06/2020 -	06/2020
287	MAHAD TO RAIGAD FORT - [N24001038	7/2018	237.40 -	237.40	8.34	05/2020 -	05/2020
288	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779	2/2018	418.88 -	418.88	88.00	02/2020 -	02/2020
289	KUSUMBA TO MALEGAON - [N24001109	3/2018	243.45 244.00	243.45	80.02	12/2019 -	12/2019
290	CHALISGAON TO NANDGAON - [N24001108	3/2018	206.97 207.00	206.97	92.89	12/2019 -	12/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated
1	2	3	4	5	6	7	8
291	BHOGAN KHURD TO KASHEDI - [N24001132	9/2017	743.21 743.00	743.21	52.87	06/2021 -	06/2021
292	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177	10/2016	171.90 -	171.90	14.77	08/2020 -	08/2020
293	BHADGAON TO CHALISGAON - [N24001047	1/2018	259.55 260.00	259.55	145.00	11/2019 -	11/2019
294	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941	3/2018	293.64 -	293.64	134.32	08/2020 -	08/2020
295	REHABILITATION AND UPGRADATION OF BARAICH - SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA - [N24001202	3/2016	388.83 -	388.83	304.47	12/2019 -	12/2019
296	KOTHARI TO DHANORA - [N24001073	9/2018	301.38 301.00	301.38	41.00	08/2020 -	08/2020
297	NILAJPHATA TO BHANDARA - [N24001043	1/2018	420.63 421.00	420.63	31.60	05/2020 -	05/2020
298	KARWANDI TO RAJURI - [N24001058	3/2018	276.95 277.00	276.95	87.47	12/2019 -	12/2019
299	OSMANNAGAR TO KUNDRAL - [N24001075	9/2017	344.25 344.00	344.25	61.02	08/2020 -	08/2020
300	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906	3/2018	173.24 -	173.24	56.66	06/2020 -	06/2020
301	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776	11/2017	232.81 -	232.81	59.44	11/2019 -	11/2019
302	OMREGA TO AUSA - [N24001067	3/2018	272.04 272.00	272.04	137.24	12/2019 -	12/2019
	National Highways Authority Of India						
303	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	3/2017	672.89 -	736.01	-	03/2020 -	03/2020
304	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602	8/2016	1,664.20 -	1,664.20	721.93	04/2020 -	04/2020
305	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	3/2017	744.64 -	982.00	-	03/2020 -	03/2020
306	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652	3/2017	848.45 -	848.45	87.01	03/2020 -	03/2020
307	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667	3/2017	648.32 -	512.72	501.52	03/2020 -	03/2020
308	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670	3/2017	239.68 -	235.90	91.24	03/2020 -	03/2020
309	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669	3/2017	165.50 -	172.16	117.09	03/2020 -	03/2020
	Total		39,371.18 -	39,497.96	12,643.82		

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated
1	2	3	4	5	6	7	8
	SHIPPING AND PORTS						
	Inland Waterways Authority Of India						
310	JAL MARG VIKAS PROJECT - [N25000072	1/2018	4,200.00 -	5,369.18	1,662.16	03/2023 03/2023	03/2023
	Total		4,200.00 -	5,369.18	1,662.16		
	STEEL						
	Steel Authority Of India Limited (Sail)						
311	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121	12/2018	263.36 -	263.36	15.67	09/2020 -	09/2020
	Total		263.36 -	263.36	15.67		
	URBAN DEVELOPMENT						
	Ahmedabad Metro Rail						
312	SURAT METRO RAIL PROJECT - [N28000138	3/2019	12,020.32 -	12,020.32	4.67	03/2024 -	03/2024
313	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137	3/2019	5,384.17 -	5,384.17	4.35	03/2024 -	03/2024
	Central Public Works Department						
314	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111	11/2017	171.72 -	171.72	32.00	03/2020 -	03/2020
315	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127	12/2018	260.00 -	260.00	12.50	06/2021 -	06/2021
316	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129	10/2016	1,128.00 -	1,128.00	-	03/2022 -	03/2022
317	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133	2/2019	186.00 199.00	186.00	-	09/2020 -	09/2020
318	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106	11/2017	238.56 -	238.56	63.45	05/2020 -	05/2020
319	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT - [N28000132	11/2018	361.60 -	361.60	0.45	07/2021 -	07/2021
320	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128	10/2016	1,180.00 -	1,180.00	-	07/2021 -	07/2021
	Delhi Metro Rail Corporation						
321	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136	5/2017	565.00 -	565.00	321.05	12/2020 -	12/2020
322	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS - [N28000135	7/2019	24,948.65 -	24,948.65	1.74	03/2025 -	03/2025
	Madhya Pradesh Metro Rail Co Limited						
323	BHOPAL METRO RAIL - [N28000124	11/2018	6,941.40 -	6,941.40	41.94	02/2023 -	02/2023

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated
1	2	3	4	5	6	7	8
324	INDORE METRO RAIL - [N28000125	11/2018	7,500.80 -	7,500.80	45.70	02/2023 -	02/2023
	National Building Construcion Corporation Ltd						
325	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	6/2012	4,264.00 -	4,439.23	3,246.53	11/2019 -	11/2019
	National Capital Region Transport Corp						
326	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134	3/2019	30,274.00 -	30,274.00	613.92	06/2025 -	06/2025
	Total		95,424.22 -	95,599.45	4,388.30		
	WATER RESOURCES						
	Brahmaputra Board						
327	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001	3/2017	233.57 -	233.57	32.20	12/2019 -	12/2019
	Bihar Urban Infrastructure Development Corporation Ltd						
328	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051	8/2017	824.00 -	824.00	-	06/2022 -	06/2022
329	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040	5/2017	356.37 -	356.37	-	04/2021 -	04/2021
330	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026	3/2018	230.06 -	230.06	-	07/2021 -	07/2021
331	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR - [N30000038	4/2015	184.93 -	184.93	-	04/2020 -	04/2020
332	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA - [N30000041	5/2017	184.86 -	184.86	-	05/2021 -	05/2021
333	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050	8/2017	578.89 -	578.89	-	06/2022 -	06/2022
334	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037	12/2014	225.77 -	225.77	-	03/2020 -	03/2020
335	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036	3/2018	294.02 -	294.02	-	10/2021 -	10/2021
336	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044	3/2017	277.42 -	277.42	-	05/2021 -	05/2021
337	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043	5/2017	191.62 -	191.62	-	11/2020 -	11/2020
338	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027	10/2017	254.13 -	254.13	-	09/2020 -	09/2020
339	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035	3/2018	305.19 -	305.19	-	08/2021 -	08/2021
340	SAIDPUR SEWER NETWORK PATNA - [N30000039	4/2015	268.63 -	268.63	-	01/2021 -	01/2021
341	I AND D AND STP AT CHAPPRA - [N30000028	11/2018	236.15 -	236.15	-	12/2020 -	12/2020
	Delhi Jal Board						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated
1	2	3	4	5	6	7	8
342	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014	3/2017	665.78 -	665.78	-	12/2022 -	12/2022
343	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015	5/2016	211.79 -	211.79	-	12/2021 -	12/2021
344	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O&M AT CORONATION PILLAR DELHI - [N30000017	12/2018	515.07 -	515.07	-	01/2021 -	01/2021
345	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016	5/2016	239.11 -	239.11	-	02/2022 -	02/2022
346	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018	5/2017	344.81 -	344.81	-	05/2020 -	05/2020
	Kolkata Metropolitan Development Authority						
347	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045	8/2017	185.22 -	185.22	-	12/2021 -	12/2021
348	INTERCEPTION DIVERSION AND TREATMENT WORKS AT TOLLY'S NULLAH ADI GANGA - [N30000034	8/2017	307.12 -	307.12	-	09/2022 -	09/2022
349	SEWERAGE SYSTEM & STP WORKS AT HALISHAHR - [N30000046	2/2014	274.76 -	274.76	-	12/2019 -	12/2019
350	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049	10/2017	164.93 -	164.93	-	12/2021 -	12/2021
351	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033	3/2018	165.16 -	165.16	-	06/2022 -	06/2022
352	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH - [N30000042	5/2018	160.00 -	160.00	-	02/2022 -	02/2022
353	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048	1/2018	172.10 -	172.10	-	12/2021 -	12/2021
354	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047	12/2014	272.32 -	272.32	-	04/2020 -	04/2020
355	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031	12/2018	234.31 -	234.31	-	04/2022 -	04/2022
356	INTERCEPTION & DIVERSION WITH STP AT MAHESHTALA - [N30000032	5/2018	198.43 -	198.43	-	02/2022 -	02/2022
357	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPURL - [N30000030	3/2019	287.53 -	287.53	-	04/2022 -	04/2022
358	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029	1/2019	384.96 -	384.96	-	04/2022 -	04/2022
	Uttar Pradesh Jal Nigam						
359	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS AT AGRA - [N30000023	2/2019	317.19 -	317.19	-	08/2021 -	08/2021
360	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020	2/2011	279.91 -	279.91	-	12/2019 -	12/2019
361	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025	3/2019	298.12 -	298.12	-	07/2021 -	07/2021
362	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021	1/2019	231.79 -	231.79	-	12/2021 -	12/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above							(November 2019)
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Antici Pated
1	2	3	4	5	6	7	8
363	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024	2/2019	681.78 -	681.78	-	06/2022 -	06/2022
364	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008	10/2017	213.62 -	213.62	-	03/2022 -	03/2022
365	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR - [N30000009	10/2016	370.40 -	370.40	-	08/2020 -	08/2020
366	MATHURA SEWERAGE SCHEME - [N30000019	12/2017	460.45 -	460.45	-	12/2020 -	12/2020
367	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS - [N30000007	3/2018	904.00 -	904.00	-	09/2021 -	09/2021
368	REHABILITATION RENOVATION OF AGRA SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS IN AGRA UTTAR PR - [N30000012	12/2018	857.26 -	857.26	-	08/2021 -	08/2021
369	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022	1/2019	206.05 -	206.05	-	10/2021 -	10/2021
370	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA - [N30000011	2/2017	161.31 -	161.31	-	11/2019 -	11/2019
371	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006	5/2017	767.59 -	767.59	-	09/2021 -	09/2021
372	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH - [N30000013	3/2019	271.39 -	271.39	-	08/2021 -	08/2021
373	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010	3/2018	967.23 -	967.23	-	09/2021 -	09/2021
	Uttarakhand Pey Jal Nigam						
374	INTERCEPTION AND DIVERSION (I&D)WITH STP AT RISHIKESH - [N30000004	3/2017	158.00 -	158.00	-	11/2019 -	11/2019
	Total		16,575.10 -	16,575.10	32.20		
	Grand Total		5,75,769.77	6,26,027.37	1,19,241.51		

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Annexure - V

(November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	ATOMIC ENERGY							
	Bhavini Limited							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044	09/2003	3,492.00 -	6,840.00	5,837.84	09/2010 -	10/2021	95.88
	Nuclear Power Corporation Of India Limited							
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010	10/2009	11,459.00 -	16,580.00	14,137.00	12/2015 -	06/2020	44.69
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027	10/2009	12,320.00 -	17,079.00	11,387.00	12/2016 -	12/2020	38.63
	Total		27,271.00 -	40,499.00	31,361.84			
	CIVIL AVIATION							
	Airport Authority Of India Limited							
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073	10/2013	314.61 -	441.33	85.79	09/2018 -	06/2020	40.28
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083	12/2016	859.86 -	860.00	232.44	03/2021 -	03/2021	.02
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084	09/2015	338.93 -	339.00	213.50	06/2019 -	12/2019	.02
	Total		1,513.40 -	1,640.33	31,893.57			
	COAL							
	Eastern Coal Fields Limited							
7	RANIGANJ MASTER PLAN - [N06000163	08/2009	2,661.73 -	5,173.26	336.63	08/2019 -	08/2024	94.36
	Neyveli Lignite Corporation							
8	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095	06/2011	5,907.11 -	7,080.41	6,867.42	12/2015 -	12/2019	19.86
9	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152	07/2016	17,237.00 -	17,237.80	8,032.77	11/2021 -	11/2021	.00
	Singareni Colliers Company Limitted							
10	RAMAGUNDAM OC-II EXTENSION - [N06000078	12/2009	418.97 -	489.62	353.10	03/2012 -	03/2023	16.86
11	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017	10/2006	249.03 -	448.86	296.17	03/2012 -	03/2024	80.24

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
12	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129	05/2015	397.09 -	442.42	99.42	03/2019 -	03/2020	11.42
13	JALAGAM VENGALA RAO OCP-II - [N06000094	07/2011	447.06 -	473.22	18.35	03/2015 -	03/2021	5.85
14	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093	07/2011	162.76 -	349.28	7.49	03/2015 -	03/2021	114.60
	South-Eastern Coal Fields Limited							
15	JAGANNATHPOR OCP(3.00MTY) - [N06000075	09/2008	152.43 -	459.49	193.35	03/2015 -	03/2020	201.44
	Western Coal Fields Limited							
16	KAMPTEE DEEP OC MINE - [N06000141	11/2015	277.65 -	313.34	117.85	03/2021 -	03/2024	12.85
17	BHANEGAON OC - [N06000121	02/2015	187.94 -	409.68	127.70	03/2023 -	03/2023	117.98
18	ADASA UG TO OC - [N06000133	08/2015	288.90 -	333.43	27.21	03/2023 -	03/2024	15.41
	Total		28,387.67 -	33,210.81	48,371.03			
	FERTILISERS							
	Rashtriya Chemical & Fertiliser Limited							
19	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009	10/2014	197.79 -	209.44	185.68	11/2016 -	09/2019	5.89
	Total		197.79 -	209.44	48,556.71			
	HEALTH AND FAMILY WELFARE							
	Hospital Services Consultancy Corporation Ltd							
20	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003	02/2013	414.11 -	499.23	302.02	11/2013 -	09/2020	20.55
21	AIIMS - MOTHER AND CHILD BLOCK - [N21000008	12/2013	204.44 -	270.00	204.70	05/2017 -	06/2020	32.07
22	AIIMS - OPD(NEW) - [N21000009	08/2014	293.65 -	325.00	297.16	05/2017 -	01/2020	10.68
23	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010	12/2014	168.90 -	191.20	169.51	05/2017 -	07/2019	13.20
24	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011	09/2014	505.58 -	585.00	586.96	03/2018 -	09/2019	15.71
25	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012	07/2016	152.95 -	177.92	139.70	02/2018 -	03/2020	16.33
26	CNCI KOLKATA WEST BENGAL - [N21000015	08/2016	244.00 -	248.00	224.92	09/2018 -	05/2019	1.64
27	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017	08/2017	272.19 -	272.54	191.86	03/2019 -	03/2020	.13

MoSPI OCMS

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
28	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019	12/2017	156.56 -	156.65	76.53	- -	05/2020	.06
	Total		2,412.38 -	2,725.54	50,750.07			
	HUMAN RESOURCE DEPARTMENT							
	Rail India Technical And Economic Service							
29	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001	09/2013	484.32 -	626.26	-	09/2014 -	12/2020	29.31
	Total		484.32 -	626.26	50,750.07			
	PETROLEUM							
	Bharat Petroleum Corporation Limited							
30	HALDIA LPG IMPORT FACILITY - [N16000223	03/2015	694.00 -	1,097.54	722.99	10/2018 -	12/2019	58.15
31	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227	11/2014	4,588.29 -	5,245.96	3,877.61	08/2018 -	12/2019	14.33
32	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314	12/2015	1,112.00 -	1,507.24	555.00	06/2019 -	02/2022	35.54
	Gas Authority Of India Limited							
33	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210	02/2015	749.00 -	842.00	606.89	02/2020 -	02/2020	12.42
34	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285	06/2009	2,915.00 2,915.00	4,915.00	2,742.24	12/2012 -	02/2022	68.61
	Hindustan Petroleum Corporation Limited							
35	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209	11/2011	310.00 -	370.00	17.84	03/2013 -	-	19.35
36	VISAKH REFINERY MODERNISATION PROJECT - [N16000235	07/2016	20,928.00 -	26,264.00	7,245.30	07/2020 -	07/2022	25.50
37	MUMBAI REFINERY EXPANSION PROJECT - [N16000281	09/2015	4,199.00 -	5,060.00	3,071.60	03/2020 -	03/2020	20.50
	Indian Oil Corporation Limited							
38	LPG TERMINAL AT KOCHI - [N16000171	10/2015	607.06 -	714.25	356.46	10/2017 -	-	17.66
39	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193	01/2015	1,823.00 -	3,027.90	955.36	12/2020 -	12/2020	66.09
40	PARADIP HYDERABAD PIPLEINE - [N16000194	01/2015	2,321.00 -	3,338.00	1,912.90	12/2020 -	08/2020	43.82

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
41	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252	05/2016	664.00 -	729.40	663.70	12/2020 -	02/2020	9.85
42	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253	05/2016	4,497.00 -	6,025.00	990.22	12/2018 -	02/2021	33.98
	Indian Strategic Petroleum Reserves Ltd							
43	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169	01/2006	993.00 -	1,693.00	1,549.85	01/2012 -	-	70.49
	Mangalore Refinery And Petrochemicals Limited							
44	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256	10/2015	135.00 171.00	170.70	156.65	03/2019 -	10/2019	26.44
45	SEA WATER DESALINATION PLANT - [N16000319	11/2017	581.00 -	621.00	102.99	03/2020 -	11/2020	6.88
	Oil & Natural Gas Corporation Limited							
46	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127	06/2010	202.94 -	345.92	155.61	01/2014 -	11/2019	70.45
47	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128	03/2011	861.79 -	1,683.06	1,356.33	05/2013 -	12/2019	95.30
48	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131	12/2011	2,059.63 -	2,665.65	1,932.09	03/2015 -	12/2019	29.42
49	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213	12/2015	3,190.69 -	3,247.19	2,298.77	04/2018 -	05/2020	1.77
50	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239	12/2015	823.27 -	910.23	403.18	03/2023 -	03/2022	10.56
51	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278	07/2016	249.85 250.00	265.49	180.20	05/2020 -	05/2020	6.26
52	DEVELOPMENT OF B-147 FIELD - [N16000292	02/2017	546.15 -	565.15	449.96	11/2019 -	03/2020	3.48
53	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294	02/2017	968.61 -	1,033.95	968.11	11/2019 -	11/2019	6.75
54	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297	02/2017	4,006.83 -	4,475.92	2,869.89	05/2021 -	12/2021	11.71
55	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359	02/2019	3,660.71 -	3,740.05	274.07	04/2021 -	05/2021	2.17
	Oil India Limited							
56	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167	07/2011	352.56 -	438.84	249.73	03/2017 -	06/2020	24.47
57	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148	09/2012	871.35 -	1,200.00	565.63	03/2015 -	-	37.72

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
58	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331	01/2018	543.91 -	682.90	71.46	02/2020 -	06/2020	25.55
	Total		65,454.64 -	82,875.34	88,052.70			
	POWER							
	National Hydro-Electric Power Corporation							
59	PARBATI HEP (4X200 MW) (NHPC) II - [180100210	09/2002	3,919.59 -	9,997.11	7,715.06	09/2009 -	12/2021	155.06
60	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221	09/2003	6,285.33 -	19,496.34	11,098.20	09/2010 -	-	210.19
	National Thermal Power Corporation							
61	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151	03/2013	11,638.55 -	12,865.92	12,361.29	01/2018 -	03/2020	10.55
62	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014	11/2006	2,978.48 -	5,867.38	4,264.84	03/2013 -	01/2021	96.99
63	TANDA TPP STAGE-II (2X660 MW) - [N18000175	09/2014	9,188.98 -	10,016.10	6,633.23	07/2019 -	07/2020	9.00
64	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176	02/2014	12,532.44 -	13,740.53	9,944.45	12/2018 -	09/2020	9.64
65	NORTH KARANPURA STPP (3X660 MW) - [N18000177	02/2014	14,366.58 -	15,164.05	9,861.12	06/2019 -	03/2022	5.55
66	RAMMAM-III HEPP (3X40 MW) - [N18000178	09/2014	1,381.84 -	1,592.34	502.87	09/2019 -	05/2024	15.23
67	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190	01/2007	5,353.00 -	9,583.00	7,981.46	07/2012 -	09/2020	79.02
68	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192	01/2013	12,964.60 -	17,304.00	14,229.00	05/2018 -	06/2021	33.47
69	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193	04/2012	9,750.89 -	12,176.28	10,032.00	02/2017 -	06/2020	24.87
70	BARH STPP(3X660MW) NTPC - [180100242	02/2005	8,692.97 -	21,312.11	16,756.64	10/2011 -	08/2021	145.16
71	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140	12/2012	11,846.00 -	12,739.82	12,839.84	10/2017 -	03/2020	7.55
72	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142	07/2012	1,527.00 -	1,801.07	148.93	08/2017 -	-	17.95
73	KHARGONE STPP STAGE I (1320 MW) - [N18000205	03/2015	9,870.51 -	11,148.86	9,055.78	01/2020 -	02/2020	12.95
74	PAKRI BARWADIH COAL MINING PROJECT - [N18000225	10/2004	4,237.96 4,238.00	4,552.00	3,293.00	10/2017 -	-	7.41
	North East Electric Power Corporation							
75	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239	12/2004	2,496.90 -	7,927.34	7,599.10	12/2009 06/2016	10/2019	217.49
	Power Grid Corporation Of India Limited							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
76	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061	10/2008	4,824.12 -	5,071.94	4,570.22	10/2012 -	03/2020	5.14
77	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066	02/2009	11,130.19 -	14,719.10	12,816.90	08/2013 -	03/2022	32.24
78	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155	10/2013	1,364.52 -	1,891.41	1,280.93	04/2016 -	12/2019	38.61
79	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164	05/2014	522.29 -	546.36	470.50	11/2016 -	03/2020	4.61
80	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182	01/2015	203.28 -	260.03	199.56	07/2017 -	11/2019	27.92
81	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109	10/2011	487.49 -	639.46	568.44	06/2014 -	12/2019	31.17
82	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	05/2005	1,779.29 -	2,187.32	2,237.45	11/2008 -	-	22.93
83	COMPREHENSIVE SCHEME FOR THE STRENGHTENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249	12/2014	4,754.42 -	9,072.36	1,352.46	12/2018 -	12/2020	90.82
84	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250	12/2014	5,111.33 -	6,880.36	1,779.00	12/2018 -	12/2020	34.61
	Thdc India Limited							
85	DHUKWAN SMALL HYDRO PROJECT - [N18000189	05/2011	195.42 -	294.60	321.11	02/2014 -	12/2019	50.75
86	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042	08/2008	2,491.58 -	4,397.80	1,823.10	06/2013 -	12/2022	76.51
87	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00 -	5,024.35	3,118.00	02/2016 -	06/2022	203.22
	Total		1,63,552.55 -	2,38,269.34	262,907.18			
	RAILWAYS							
	Central Railways							
88	KALYAN-KASARA 3RD LINE - [N22000233	04/2011	792.89 -	1,377.48	316.79	03/2021 -	03/2022	73.73
89	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247	04/2011	184.06 -	312.00	275.98	03/2019 -	12/2019	69.51
90	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181	02/1997	2,271.50 -	3,712.50	2,434.24	03/2021 -	03/2022	63.44
91	PUNE-NASIK (265 KM) - [N22000354	02/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024	120.28
92	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355	02/2016	2,750.00 -	3,438.51	-	03/2024 -	-	25.04
93	DAUND - MANMAD (236 KM) - [N22000360	02/2016	1,876.00 -	2,081.27	187.09	03/2023 -	03/2023	10.94
	Container Corporation Of India							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
94	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431	08/2016	234.50 -	235.00	10.88	03/2019 -	12/2020	.21
	Dedicated Freight Corridor Corporation Of India Ltd							
95	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346	10/2006	11,589.00 30,357.00	28,181.00	-	- -	-	143.17
96	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	03/2020	207.99
	East Central Railways							
97	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222	03/1999	1,033.07 -	3,376.00	3,328.43	- -	03/2021	226.79
98	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303	04/2003	528.65 -	2,066.78	1,441.80	- -	03/2023	290.95
99	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	477.88 283.95	751.55	674.58	03/2012 -	03/2020	57.27
100	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240	04/1997	324.73 -	1,050.00	1,043.03	03/2012 -	03/2020	223.35
101	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	162.87 -	614.45	309.76	- -	03/2022	277.26
102	KOSI BRIDGE (NL), ECR - [220100304	04/2002	499.41 -	516.02	402.55	03/2020 -	03/2020	3.33
103	SAMASTIPUR-DARBANGHA - [N22000329	05/2015	380.00 -	519.33	164.77	- -	02/2023	36.67
104	KODERMA-TILAIYA (NL), ECR - [220100305	04/2002	459.91 -	1,625.87	544.36	- -	03/2021	253.52
105	GAYA-CHATRA (NL) - [N22000169	04/2008	415.67 -	549.75	15.58	- -	-	32.26
106	BIHTA-AURANGABAD (NL) - [N22000170	04/2008	326.20 -	2,995.01	1.94	- -	03/2024	818.15
107	SAKRI-HASANPUR ROAD (NL) - [N22000171	04/1999	325.00 -	735.20	363.83	- -	03/2021	126.22
108	CHHAPRA-MUZAFFARPUR (NL) - [N22000172	04/2006	378.56 -	1,858.75	377.77	- -	03/2022	391.01
109	MOTIHARI-SITAMARHI (NL) - [N22000174	04/2006	211.00 -	1,006.00	24.16	- -	-	376.78
110	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180	04/2004	372.14 -	1,470.50	824.49	- -	03/2021	295.15
111	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181	04/2009	548.00 -	819.01	489.11	03/2020 -	03/2022	49.45
112	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182	04/2013	213.01 -	425.17	423.55	- -	01/2020	99.60
113	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374	01/1991	332.15 -	546.71	541.43	07/2014 -	-	64.60
114	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472	04/2016	744.04 -	1,215.54	79.18	03/2021 -	03/2022	63.37

MoSPI OCMS

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
115	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473	04/2016	731.64 -	1,185.73	35.74	03/2021 -	03/2022	62.06
116	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475	04/1998	180.82 -	726.31	510.91	- -	10/2019	301.68
117	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476	04/1991	329.39 -	1,483.14	1,053.89	- -	12/2021	350.27
	East Coast Railway							
118	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	810.78 -	1,928.07	770.82	06/2021 -	06/2024	137.80
119	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	2,923.13 -	3,791.66	1,243.45	03/2009 -	06/2024	29.71
120	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	1,111.99 -	1,539.28	937.49	02/2019 -	03/2022	38.43
121	KIRANDUL - JAGDALPUR DOUBLING - [N22000318	12/2012	1,160.00 -	1,160.83	699.40	03/2020 -	03/2023	.07
122	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319	03/2012	155.81 -	238.03	204.79	03/2020 -	03/2021	52.77
123	KOTTAVALSA - KORAPUT DOUBLING - [N22000377	04/2015	2,499.71 -	3,382.95	397.90	03/2022 -	03/2022	35.33
124	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380	04/2015	701.61 -	810.02	129.40	11/2018 -	03/2022	15.45
	Eastern Railways							
125	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	1,188.91 -	1,619.48	871.86	03/2019 12/2009	03/2025	36.22
126	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	607.09 -	1,425.44	637.54	02/2013 -	03/2024	134.80
127	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235	04/2010	365.17 -	527.54	1.76	- -	03/2025	44.46
128	HANSDIHA-GODDA NL - [N22000236	04/2011	542.18 -	693.80	458.91	03/2020 -	03/2021	27.96
129	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238	04/2011	175.80 -	251.18	251.18	- -	03/2021	42.88
130	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	12.02
131	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240	04/2010	494.54 -	494.59	32.00	03/2005 -	03/2025	.01
132	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241	04/2000	297.47 -	298.22	52.09	- -	03/2025	.25
133	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243	04/2009	499.96 -	680.68	159.45	02/2012 -	03/2025	36.15
134	MONIGRAM- NIMTITA - [N22000301	04/2012	250.93 -	310.70	275.20	- -	03/2024	23.82

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
135	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302	04/2012	255.64 -	272.20	177.61	- -	09/2021	6.48
136	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216	04/1987	406.99 -	545.70	148.48	03/2006 -	03/2025	34.08
137	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217	04/2007	450.00 -	1,261.34	-	- -	03/2025	180.30
138	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218	04/2010	172.03 -	260.10	10.73	- -	03/2025	51.19
139	PIRPAINTI-JASIDIH - [N22000219	04/2013	915.98 -	2,137.81	297.68	03/2022 -	03/2025	133.39
140	BANDEL-BOINCHI 3RD LINE - [N22000221	04/2011	288.35 -	393.00	393.00	- -	03/2020	36.29
141	PIRPAINTI-BHAGALPUR - [N22000222	04/2011	261.38 -	478.08	478.08	- -	05/2019	82.91
142	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224	04/2001	923.52 -	995.10	501.00	03/2016 -	03/2025	7.75
143	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225	04/2005	595.51 -	769.40	103.08	03/2017 -	03/2025	29.20
	Indian Railway Construction Company Limited							
144	GEVRA ROAD PENDRA ROAD - [N22000488	02/2014	2,288.00 -	4,970.11	628.61	03/2022 -	12/2022	117.23
	Metropolitan Rapid Transport Projects							
145	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,404.92	3,837.57	12/2006 -	-	224.37
146	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	2,980.41	1,431.38	03/2004 -	03/2021	501.57
147	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028	04/2006	495.74 -	734.01	445.91	06/2013 -	-	48.06
148	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	75.91
	North Central Railway							
149	ETAWAH-MAINPURI (NL),NCR - [220100318	04/1997	120.00 -	346.00	345.51	12/2008 -	-	188.33
150	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	04/2011	2,912.96 -	3,845.60	148.26	03/2022 -	12/2024	32.02
151	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372	04/2015	668.70 668.00	680.00	330.00	03/2020 -	03/2020	1.69
	North East Frontier Railway							
152	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135	04/1983	297.32 -	614.00	275.07	03/2019 -	03/2020	106.51

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
153	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	2,393.47 -	5,021.45	3,131.89	03/2014 -	03/2022	109.80
154	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	1,180.19 -	4,541.00	3,344.19	12/2008 -	03/2021	284.77
155	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	4,454.17 -	12,524.00	9,541.58	03/2011 -	03/2022	181.17
156	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	385.20 -	1,532.00	642.09	03/2019 -	03/2020	297.72
157	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087	09/2006	532.87 -	2,145.00	935.60	03/2019 -	03/2020	302.54
158	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124	04/2006	2,326.52 -	4,600.00	842.42	03/2015 -	10/2021	97.72
159	KISHANGANJ JALALGARH, NL, NEFR - [N22000101	04/2008	333.76 -	360.00	6.74	- -	03/2022	7.86
160	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	4,084.69	332.23	12/2015 -	-	204.95
161	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183	04/2013	1,798.00 -	2,496.67	-	03/2019 -	-	38.86
162	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193	04/2010	221.42 -	380.00	38.18	- -	03/2022	71.62
163	AGARTALA-AKHAURA NL - [N22000195	04/2012	569.63 -	670.00	107.83	03/2020 -	09/2021	17.62
164	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205	04/2010	906.46 -	6,000.00	263.12	03/2021 -	03/2021	561.92
165	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206	04/2010	242.22 -	471.00	69.09	03/2020 -	03/2020	94.45
166	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207	04/2010	241.52 -	373.87	273.20	- -	06/2021	54.80
167	MURKONGSELEK-PASIGHAT NL - [N22000208	04/2011	414.84 -	661.00	122.93	03/2020 -	03/2020	59.34
168	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209	04/1999	819.23 -	1,871.00	1,082.01	- -	-	128.39
169	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210	04/2011	314.00 -	728.00	727.55	03/2019 -	03/2020	131.85
170	DIGARU-HOJAI (102 KM) - [N22000389	04/2015	870.96 -	2,136.01	580.01	03/2021 -	03/2021	145.25
171	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390	04/2016	602.27 -	612.00	336.17	12/2021 -	03/2020	1.62
172	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499	02/1999	380.60 -	1,871.00	1,087.60	04/2010 -	-	391.59
	North Eastern Railway							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
173	KICHHA-KHATIMA (NL) - NER - [220100317	04/2003	142.45 -	228.40	0.15	- -	-	60.34
174	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321	04/2014	182.92 -	197.73	-	- -	-	8.10
175	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130	03/2013	307.00 -	1,409.09	-	- -	-	358.99
176	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131	03/2007	243.78 -	895.00	106.55	12/2021 -	12/2021	267.13
177	CHHAPRA-BALLIA UP - [N22000134	03/2013	295.00 -	477.31	336.89	01/2019 -	01/2020	61.80
178	KAPILVASTU-BASTI VIA BANSI SIDHARTHNAGAR BASTI NAUGARH UP - [N22000136	03/2013	643.00 -	644.00	-	- -	-	.16
179	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456	04/2016	213.00 -	213.35	9.62	04/2016 -	06/2020	.16
180	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460	04/2017	1,343.00 -	1,476.15	-	01/2018 -	-	9.91
181	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468	04/2016	602.50 -	714.34	18.40	- -	-	18.56
	North Western Railway							
182	DAUSA-GANGAPUR CITY(NL),NWR - [220100184	02/1997	410.08 -	886.41	559.84	02/2019 -	03/2021	116.16
183	PHULERA - DIGANA DOUBLING - [N22000326	05/2015	600.00 -	685.99	74.80	03/2020 -	04/2022	14.33
184	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330	05/2015	873.71 -	1,980.21	4.60	- -	-	126.64
185	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137	04/2012	246.08 -	348.55	229.00	12/2019 -	06/2020	41.64
186	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147	04/2011	2,082.75 -	4,079.15	185.30	- -	-	95.85
187	THIYAT HAMIRA-SANU - [N22000149	04/2013	236.93 -	294.90	226.61	10/2018 -	12/2019	24.47
188	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150	04/2013	822.00 -	1,099.54	-	- -	-	33.76
189	PUSHKAR-MERTA - [N22000151	04/2013	323.00 -	432.22	-	- -	-	33.81
190	AJMER-BANGURGRAM - [N22000155	04/2011	213.39 -	303.56	274.18	11/2019 -	05/2020	42.26
191	ALWAR-BANDIKUI DOUBLING - [N22000157	04/2013	242.09 -	410.00	362.96	02/2019 -	03/2020	69.36
	Northern Railway							
192	GRADE SEPERATOR AT DAYABASTI - [N22000269	04/1999	156.65 -	197.17	106.97	- -	03/2024	25.87
193	ROHTAK-MEHAM HANSI - [N22000272	04/2012	287.00 -	694.00	220.42	12/2011 -	03/2021	141.81

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
194	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274	04/2007	336.91 -	791.39	517.05	- -	03/2022	134.90
195	HARIDWAR-LAKSAR - [N22000289	04/2012	219.83 -	346.63	233.23	- -	06/2020	57.68
196	UNCHAHAR-AMETHI - [N22000294	04/2012	1,229.00 -	1,230.00	103.72	- -	03/2023	.08
197	QADIAN-BEAS - [N22000295	04/2011	205.22 -	841.90	1.73	- -	03/2024	310.24
198	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	450.00 -	2,200.00	666.00	07/2012 -	03/2024	388.89
199	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	27,949.00	19,767.15	11/2002 -	06/2022	1,017.96
200	CHANDIGARH-BADDI - [N22000467	04/2007	328.14 -	1,540.00	234.79	03/2023 -	03/2023	369.31
201	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492	03/2002	625.00 -	859.00	835.35	03/2016 -	03/2021	37.44
	Rail Vikas Nigam Ltd.							
202	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	1,185.64 -	1,844.47	1,829.53	12/2017 -	03/2020	55.57
203	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	385.00	387.92	03/2009 03/2009	06/2020	188.58
204	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111	04/2010	2,913.51 -	4,639.00	855.74	03/2016 -	03/2025	59.22
205	BHANUPALI-BILASPUR BERI NL - [N22000273	04/2008	2,966.99 -	7,000.00	446.46	12/2026 -	12/2025	135.93
206	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297	04/2010	2,127.00 -	2,900.00	1,737.30	03/2023 -	03/2024	36.34
207	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110	04/2010	3,951.98 -	4,724.30	2,278.26	03/2016 -	03/2025	19.54
208	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109	04/2010	2,298.42 -	2,733.86	40.13	03/2014 -	12/2025	18.95
209	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313	03/2012	1,503.71 -	2,200.00	1,722.18	03/2020 -	03/2022	46.30
210	AHMEDABAD-BOTAD (GC) - [N22000140	04/2012	975.62 -	1,082.32	1,054.93	12/2021 -	12/2021	10.94
211	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213	04/2012	632.68 -	816.55	701.83	03/2016 -	12/2020	29.06
212	VIJAYAWADA-GUDUR - [N22000369	04/2015	3,246.26 -	3,548.67	1,211.97	12/2023 -	12/2023	9.32
213	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404	04/2011	927.01 -	1,200.00	1,178.67	03/2019 -	03/2020	29.45
214	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407	03/2009	713.48 -	2,300.00	2,056.99	03/2020 -	03/2021	222.36

MoSPI OCMS

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
215	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409	01/1991	2,335.67 -	2,335.68	647.54	12/2024 -	12/2024	.00
216	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410	03/2006	948.04 -	1,500.00	1,374.96	03/2020 -	03/2021	58.22
217	BANASPANI- JAKHPURA - DOUBLING - [N22000412	03/2009	942.95 -	1,120.00	1,028.76	03/2019 -	06/2022	18.78
	Railway Electrification							
218	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094	02/2008	171.10 -	275.08	141.55	03/2012 -	-	60.77
	South Central Railway							
219	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	1,045.20 -	2,120.16	524.57	03/2009 -	03/2023	102.85
220	MANUGURU-RAMAGUNDAM - [N22000259	04/2013	1,112.00 -	2,911.84	0.92	- -	-	161.86
221	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261	04/2012	1,856.95 -	2,200.00	290.92	03/2023 -	03/2024	18.47
222	BHADRACHALAM-KOVVUR - [N22000264	04/2012	923.23 -	2,184.83	2.46	- -	-	136.65
223	NADIKUDE-SRI KALAHASTI - [N22000286	04/2011	2,288.70 -	2,643.25	810.35	03/2021 -	03/2024	15.49
224	BHADRACHALAM ROAD-SATTUPALLI - [N22000287	04/2010	704.31 -	952.16	303.24	03/2020 -	03/2020	35.19
225	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192	03/1996	164.36 -	1,050.00	999.64	02/2009 -	-	538.84
226	MUNEERABAD-MAHABOOBNAGAR(NL),SCR - [220100205	04/1997	1,723.00 1.00	1,780.09	1,478.40	03/2000 -	03/2021	3.31
227	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	458.25 -	458.26	3.83	- -	-	.00
228	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432	04/2017	119.73 185.00	390.60	342.54	03/2022 -	03/2022	226.23
	South East Central Railway							
229	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	1,413.76	1,351.73	- -	01/2020	268.37
230	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	511.86 -	1,756.00	1,668.96	04/2020 -	01/2021	243.06
231	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420	09/2016	1,908.51 -	2,686.63	515.29	03/2023 -	03/2023	40.77
232	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438	04/2010	585.93 -	1,268.32	669.57	02/2019 -	12/2020	116.46
233	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480	06/2018	229.00 -	852.50	39.69	12/2021 -	03/2023	272.27
234	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483	04/2008	872.00 -	1,226.51	1,062.76	12/2019 -	03/2020	40.65

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
235	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484	04/2015	1,973.00 -	1,973.64	174.40	03/2021 -	03/2023	.03
236	ANUPPUR-KATNI - [N22000485	04/2015	1,370.00 -	1,370.94	311.76	12/2021 -	11/2022	.07
	South Eastern Railway							
237	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00	182.49	03/2007 03/2007	-	160.76
238	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	04/2012	148.77 -	377.00	182.63	12/2016 -	01/2020	153.41
239	BOWAICHANDI-ARAMBAGH - [N22000159	04/2010	267.37 -	620.00	40.99	- -	03/2025	131.89
240	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	54.99
241	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162	04/2010	149.90 -	230.00	54.46	03/2015 -	-	53.44
242	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165	04/2012	258.20 -	358.68	265.54	12/2018 -	06/2020	38.92
243	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395	11/2015	969.83 -	1,312.96	562.50	03/2020 -	06/2020	35.38
244	BONDAMUNDA RANCHI DOUBLING - [N22000396	03/2016	1,724.20 -	1,993.24	411.64	03/2021 -	12/2021	15.60
245	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402	04/1998	1,027.40 -	2,373.00	485.04	03/2003 -	03/2030	130.97
	South Western Railway							
246	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276	04/2013	558.00 -	692.43	-	- -	12/2023	24.09
247	SRINIVASA-PURA-MADANAPALLI NL - [N22000277	04/2013	296.00 -	466.65	-	- -	12/2023	57.65
248	TORANAGALLU-RANJITPURA DL - [N22000298	04/2011	146.75 -	167.50	0.34	- -	12/2023	14.14
249	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300	04/2013	327.25 -	367.77	-	- -	12/2023	12.38
250	YELAHANKA-PENUKONDA - [N22000328	05/2015	860.43 -	958.00	756.85	03/2020 -	03/2020	11.34
251	HOTGI-KUDGI-GADAG - [N22000333	03/2015	1,614.59 -	1,870.41	885.55	03/2019 -	03/2021	15.84
252	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486	03/1996	644.78 -	890.00	443.52	03/2017 -	03/2020	38.03
	Southern Railway							
253	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079	09/2007	724.69 -	2,072.50	1,440.83	02/2019 -	02/2020	185.98
254	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084	09/2006	227.40 -	900.00	63.28	- -	-	295.78
255	TIDIVANAM-NAGARI (NL) - [N22000085	09/2006	582.83 -	2,300.00	241.58	- -	-	294.63

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
256	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	303.98 -	980.00	681.66	03/2020 -	03/2021	222.39
257	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	1,566.00 -	2,815.62	264.28	- -	-	79.80
258	ATTIPPATTU PUTTUR - [N22000184	04/2008	151.84 -	1,105.00	3.34	02/2019 -	-	627.74
259	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185	04/2008	523.52 -	2,300.00	2.28	- -	-	339.33
260	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186	04/2013	839.00 -	1,500.00	0.62	- -	-	78.78
261	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187	04/1999	198.68 -	556.64	304.22	- -	-	180.17
262	KURUPPANTHARA-CHINGAVANAM - [N22000190	04/2007	270.14 -	457.08	373.51	- -	-	69.20
263	ERODE-PALANI - [N22000199	04/2008	288.57 -	1,140.00	1.63	- -	-	295.05
264	MADURAI-BODINAYAKKANUR - [N22000201	04/2008	164.41 -	450.00	167.49	- -	03/2020	173.71
265	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202	04/2007	931.98 -	951.24	738.83	- -	03/2020	2.07
266	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215	04/2011	120.70 -	1,800.00	187.30	03/2019 -	12/2019	1,391.30
267	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373	10/2013	187.26 -	231.67	162.06	04/2014 -	03/2020	23.72
268	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441	02/1996	268.87 -	950.00	927.86	03/2005 -	-	253.33
269	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451	02/2015	760.00 -	1,182.31	446.00	03/2020 -	06/2021	55.57
	West Central Railway							
270	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	04/2001	424.60 -	2,909.99	1,975.34	03/2021 -	03/2023	585.35
271	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	8,248.50	1,986.78	05/2008 -	03/2023	3,230.57
272	KATNI GRADE SEPARATOR/BYE PASS - [N22000416	08/2016	582.13 -	1,247.64	152.01	03/2022 -	09/2022	114.32
	Western Railway							
273	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120	04/2008	3,503.69 -	3,975.22	1,758.23	03/2022 -	03/2023	13.46
274	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125	04/2006	117.36 196.95	202.35	809.40	03/2011 -	03/2017	72.42
275	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123	04/2008	318.24 -	321.62	125.76	03/2012 -	03/2022	1.06

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
276	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121	04/2008	829.74 -	1,310.23	1,450.40	03/2020 -	03/2021	57.91
277	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143	04/1994	320.66 -	858.96	534.00	03/2019 -	03/2022	167.87
278	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487	02/1991	551.51 -	809.07	641.51	03/2019 -	03/2020	46.70
	Total		1,87,179.52 -	4,06,704.48	421,342.27			
	ROAD TRANSPORT AND HIGHWAYS							
	Ministry Of Road Transport And Highways (State Pwds)							
279	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276	12/2011	156.26 227.00	247.95	175.00	- -	-	58.68
280	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306	11/2010	624.41 -	992.67	853.82	03/2011 -	12/2019	58.98
281	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307	12/2011	156.63 276.00	276.00	147.65	02/2012 -	-	76.21
282	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308	08/2010	193.69 -	327.92	254.24	10/2010 -	12/2019	69.30
283	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311	03/2012	207.03 -	389.45	291.55	05/2012 -	12/2019	88.11
284	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314	01/2013	182.28 -	269.14	185.49	02/2013 -	12/2019	47.65
285	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316	03/2015	258.97 -	268.92	-	08/2015 -	-	3.84
286	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317	03/2015	157.18 162.00	162.00	-	07/2015 -	-	3.07
287	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259	03/2015	280.16 -	290.59	219.47	- -	-	3.72
288	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	290.12	09/2017 -	12/2019	36.24
289	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371	10/2013	445.89 -	653.29	464.05	03/2017 -	-	46.51

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
290	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388	11/2013	497.05 -	881.05	544.84	05/2017 -	05/2020	77.26
291	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391	11/2015	889.24 -	904.82	739.41	- -	-	1.75
292	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396	11/2010	470.20 -	630.36	344.32	02/2011 -	-	34.06
293	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398	01/1991	282.41 -	322.01	278.45	08/2016 -	-	14.02
294	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402	01/1991	358.22 -	377.64	325.19	10/2016 -	-	5.42
295	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407	10/2015	333.21 -	353.89	256.11	11/2015 -	-	6.21
296	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411	11/2014	218.31 -	307.47	263.85	02/2018 -	-	40.84
297	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415	08/2010	195.04 -	377.99	305.38	10/2010 -	06/2020	93.80
298	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531	01/1991	319.68 -	369.77	113.67	- -	-	15.67
299	WIDENING AND STRENFTHENING OF EXISITNG SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639	03/2014	191.50 192.00	192.00	136.19	05/2016 -	12/2019	.26
300	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645	08/2013	171.96 172.00	172.00	88.30	06/2016 -	-	.02
301	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782	03/2018	460.73 -	461.00	-	- -	-	.06
302	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 -	238.00	7.48	11/2019 -	-	.08
303	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O - [N24000871	08/2014	600.87 720.97	720.97	652.08	11/2017 -	05/2019	19.99
304	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873	08/2014	823.20 937.76	937.76	751.19	11/2017 -	06/2019	13.92
305	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874	03/2016	271.17 291.20	291.20	89.25	11/2018 -	11/2019	7.39

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
306	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885	03/2016	160.27 -	213.97	20.11	08/2019 -	08/2021	33.51
307	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887	06/2016	236.78 -	263.26	59.92	08/2019 -	08/2021	11.18
308	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889	04/2014	279.70 398.22	398.52	322.75	08/2017 -	07/2019	42.48
309	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928	10/2015	333.21 -	355.89	265.48	12/2015 -	12/2020	6.81
310	NAGAUR-BIKANER OF NH-11 (2L+PS) UNDER PPP. - [N24000954	01/2012	378.07 -	478.73	188.98	01/2014 -	-	26.62
311	DEVELOPMENT AND OPERATION OF BIKANER-SURATGARH SECTION OF NH-15 BY 2L+PS IN THE STATE OF RAJASTHAN - [N24000956	03/2009	501.00 -	671.54	659.98	09/2013 -	-	34.04
312	BHOKAR TO SARSAM - [N24001128	02/2017	295.09 -	295.99	162.64	07/2019 -	-	.31
313	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144	10/2013	445.89 653.00	653.29	464.07	03/2017 -	10/2019	46.51
314	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	08/2010	186.96 -	305.61	275.06	09/2014 -	12/2019	63.46
315	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219	01/2016	476.20 544.00	544.00	-	09/2016 -	-	14.24
316	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221 - [N24001223	03/2010	179.89 271.00	271.00	-	03/2013 -	03/2013	50.65
317	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1 - [N24001225	12/2010	169.26 299.00	299.00	-	01/2019 -	01/2019	76.65
	National Highways And Infrastructure Development Corporation Ltd.							
318	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676	12/2016	138.93 155.00	155.00	75.99	01/2017 -	01/2020	11.57
319	RHENOK-RORAHTHANG-PAKYONG ON NH 717A - [N24000695	04/2017	388.00 -	447.37	142.95	10/2017 -	-	15.30
	National Highways Authority Of India							
320	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	525.00	492.41	02/2009 -	07/2019	87.50
321	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	340.14	319.96	04/2009 -	08/2019	70.23
322	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279	12/2003	167.64 -	408.77	395.78	11/2008 -	01/2014	143.84

MoSPI OCMS

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
323	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	255.23	251.39	11/2008 -	08/2013	64.62
324	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049	12/2003	160.00 -	167.98	223.81	05/2008 -	06/2019	4.99
325	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	655.17	655.17	07/2009 -	10/2018	234.27
326	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,967.50	3,990.72	11/2011 -	03/2020	167.82
327	INDORE-DEWAS(NH-3) - [N24000159	11/2010	325.00 -	475.00	469.54	05/2013 -	-	46.15
328	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063	12/2003	217.61 -	360.84	453.70	04/2010 -	07/2019	65.82
329	NALBARI T BIJNI (AS-7) - [N24000048	12/2003	208.00 -	230.00	339.22	04/2008 -	03/2020	10.58
330	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	04/2014	1,266.60 -	1,544.00	1,446.45	09/2016 -	09/2019	21.90
331	NASHRI- CHANANI - [N24000162	05/2011	2,159.00 -	2,519.00	4,706.90	06/2015 -	-	16.67
332	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188	05/2011	511.54 -	591.00	571.22	11/2013 -	03/2020	15.53
333	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224	10/2012	1,928.22 -	2,945.00	2,467.00	04/2015 -	06/2020	52.73
334	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347	08/2015	723.54 -	1,286.84	1,163.65	02/2018 -	-	77.85
335	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435	10/2015	531.13 -	727.00	509.85	05/2018 -	09/2020	36.88
336	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441	10/2015	593.26 -	636.24	461.85	05/2018 -	06/2020	7.24
337	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459	06/2015	845.24 -	941.00	847.81	- -	01/2020	11.33
338	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482	08/2015	814.04 -	825.17	646.72	- -	01/2020	1.37
339	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492	11/2015	867.66 -	1,464.24	1,255.55	05/2018 -	-	68.76
340	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	05/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	-	51.83
341	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503	10/2015	447.29 -	746.43	613.57	12/2017 -	12/2019	66.88
342	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506	01/1991	642.41 -	681.67	402.94	- -	10/2020	6.11
343	MEERUT-BULANDSHAHAR - [N24000539	01/2016	683.24 -	987.94	727.69	- -	02/2020	44.60
344	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551	03/2016	1,587.49 -	2,982.00	276.87	04/2019 -	-	87.84

MoSPI OCMS

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
345	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572	05/2016	364.56 -	392.00	260.72	- -	12/2019	7.53
346	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600	08/2016	1,388.34 -	2,587.50	1,449.00	09/2019 -	03/2020	86.37
347	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622	09/2016	950.69 -	1,108.00	1,385.71	08/2019 -	12/2020	16.55
348	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623	09/2016	1,100.19 -	1,145.31	967.00	- -	05/2020	4.10
349	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631	11/2016	290.73 -	315.00	234.43	- -	03/2019	8.35
350	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638	11/2012	605.84 -	722.46	723.95	07/2018 -	02/2020	19.25
351	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 -	1,310.00	563.15	03/2020 -	08/2020	10.58
352	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	03/2017	744.64 -	982.00	-	03/2020 -	03/2020	31.88
353	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	03/2017	1,030.44 -	1,065.51	1,005.76	03/2020 -	05/2020	3.40
354	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	03/2017	988.34 -	1,043.28	1,034.00	03/2020 -	08/2020	5.56
355	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659	03/2017	1,059.73 -	1,071.00	582.87	03/2017 -	11/2020	1.06
356	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	03/2017	1,098.06 -	1,160.64	1,056.76	03/2020 -	08/2020	5.70
357	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 -	756.27	181.12	03/2020 -	04/2020	.23
358	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 -	736.01	-	03/2020 -	03/2020	9.38
359	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 -	1,187.10	807.76	03/2020 -	05/2020	13.97
360	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669	03/2017	165.50 -	172.16	117.09	03/2020 -	03/2020	4.02
361	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	446.76	03/2020 -	03/2021	10.24
362	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 -	2,447.00	1,896.03	03/2020 -	06/2020	18.50

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
363	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	657.59	03/2020 -	07/2020	41.54
364	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	695.33	03/2020 -	06/2020	44.39
365	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691	04/2017	894.00 -	929.32	750.00	04/2020 -	11/2019	3.95
366	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704	09/2017	1,124.11 -	1,232.76	292.23	09/2017 -	06/2020	9.67
367	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713	12/2017	404.94 -	448.18	165.51	- -	10/2020	10.68
368	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784	02/2018	1,424.77 -	1,853.42	14.19	- -	-	30.09
369	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787	02/2018	1,995.34 -	2,400.00	1,558.83	- -	11/2021	20.28
370	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789	02/2018	2,177.80 -	2,450.00	898.52	- -	-	12.50
371	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793	03/2018	925.40 -	1,197.00	401.68	- -	-	29.35
372	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800	03/2018	1,120.57 -	1,332.00	183.54	- -	-	18.87
373	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801	02/2018	1,052.21 -	1,449.00	336.43	- -	01/2021	37.71
374	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807	03/2018	1,532.62 -	2,499.00	584.50	03/2021 -	04/2021	63.05
375	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814	03/2018	1,029.96 -	1,261.05	97.55	- -	03/2021	22.44
376	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829	03/2018	1,016.92 -	1,071.00	-	- -	04/2021	5.32
377	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830	03/2018	2,065.96 -	2,169.00	-	- -	-	4.99
378	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831	03/2018	1,294.47 -	1,296.00	-	- -	-	.12
379	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839	03/2018	634.70 -	931.21	125.31	- -	07/2021	46.72

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
380	SIX LANING AND STREGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841	03/2018	795.50 -	799.30	115.56	- -	07/2021	.48
381	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853	03/2018	642.13 -	807.00	341.71	- -	12/2020	25.68
	Total		69,830.87 -	90,339.87	476,771.06			
	SHIPPING AND PORTS							
	Inland Waterways Authority Of India							
382	JAL MARG VIKAS PROJECT - [N25000072	01/2018	4,200.00 -	5,369.18	1,662.16	03/2023 -	03/2023	27.84
	Total		4,200.00 -	5,369.18	478,433.22			
	STEEL							
	National Mineral Development Corporation (Nmdc)							
383	NMDC INTEGRATED STEEL PLANT - [N12000086	01/2010	15,525.00 -	23,140.00	16,244.05	05/2015 -	07/2020	49.05
	Total		15,525.00 -	23,140.00	494,677.27			
	TELECOMMUNICATIONS							
	Bharat Sanchar Nigam Limited							
384	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113	01/2018	231.80 -	240.10	117.63	10/2018 -	12/2019	3.58
	Department Of Telecommunication							
385	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 -	24,664.00	12,146.00	07/2015 -	05/2020	84.97
	Total		13,565.80 -	24,904.10	506,940.90			
	URBAN DEVELOPMENT							
	Central Public Works Department							
386	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088	02/2014	388.00 -	488.28	440.59	05/2017 -	12/2019	25.85
387	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	2,000.00	408.23	10/2019 -	03/2021	64.04
388	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076	06/2014	157.84 -	169.16	163.98	03/2017 -	-	7.17

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original/ Revised	Date of Commissioning (Month/Year) Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
389	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100	02/2016	496.18 496.00	498.99	97.67	06/2017 -	03/2021	.57
390	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101	12/2008	114.26 266.00	266.00	-	12/2013 -	-	132.80
391	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119	12/2016	549.31 -	559.47	373.45	07/2019 -	04/2020	1.85
392	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126	01/2019	790.79 -	800.00	11.01	03/2022 -	06/2022	1.16
	Chennai Metro Rail Ltd							
393	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084	02/2009	14,600.00 -	19,058.00	16,352.87	12/2015 -	-	30.53
	Hindustan Steelwork Construction Limited							
394	CONSTRUCTION AND MAINTEINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099	12/2007	202.61 227.00	227.00	199.95	12/2016 -	-	12.04
395	CONSTRUCTION AND MAINTEINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100	10/2011	175.49 206.71	206.71	141.28	12/2016 -	-	17.79
396	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101	05/2005	768.88 1,070.97	1,113.34	1,085.64	02/2014 -	-	44.80
397	CONSTRUCTION AND MAINTEINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098	03/2007	149.73 173.00	175.94	176.65	12/2015 -	-	17.50
	Kochi Metro Rail Corporation Ltd							
398	KOCHI METRO RAIL PROJECT - [N28000081	07/2012	5,181.79 -	5,687.79	5,656.62	07/2017 -	03/2020	9.77
	National Building Construcion Corporation Ltd							
399	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	06/2012	4,264.00 -	4,439.23	3,246.53	11/2019 -	-	4.11
	Total		29,058.09 -	35,689.91	535,295.37			
	WATER RESOURCES							
	Polavaram Project Authority							
400	POLAVARAM IRRIGATION PROJECT - [N30000002	02/2009	10,151.04 -	55,548.87	16,417.99	03/2020 -	06/2021	447.22
	Total		10,151.04 -	55,548.87	551,713.36			
	Grand Total		6,18,784.07	10,41,752.47	4,077,816.62			

Details of Delayed Projects w.r.t. Original Schedule

Annexure - VI

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	ATOMIC ENERGY									
	Bhavini Limited									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 -	6,840.00	5,837.84	09/2010 -	10/2021	133	95.88	
	Nuclear Power Corporation Of India Limited									
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	16,580.00	14,137.00	12/2015 -	06/2020	54	44.69	
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	17,079.00	11,387.00	12/2016 -	12/2020	48	38.63	
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU	03/2013	39,849.00 -	39,849.00	15,706.00	11/2020 -	11/2023	36	0	
	Total		67,120.00 -	80,348.00	47,067.84					
	CIVIL AVIATION									
	Airport Authority Of India Limited									
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI,TRIPURA	09/2015	338.93 -	339.00	213.50	06/2019 -	12/2019	6	.02	
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,A & N ISLANDS	10/2013	314.61 -	441.33	85.79	09/2018 -	06/2020	21	40.28	
7	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI	11/2016	233.38 -	233.38	84.73	04/2020 -	12/2020	8	0	
8	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA - [N04000080]AAI,WEST BENGAL	01/2016	219.91 -	219.91	65.45	03/2020 -	12/2020	9	0	
9	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI,TAMIL NADU	06/2018	2,467.00 -	2,467.00	213.17	02/2022 -	08/2022	6	0	
	Total		3,573.83 -	3,700.62	662.64					

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	COAL									
	Bharat Coking Coal Limited									
10	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	269.82	180.83	04/2014 -	01/2020	69	0	
11	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	289.45	260.10	05/2014 03/2020	03/2020	70	0	
12	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	401.81	04/2015 04/2022	04/2022	84	0	
	Central Coal Fields Limited									
13	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	106.41	03/2011 -	03/2021	120	0	
14	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	181.17	03/2012 -	03/2021	108	0	
15	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	365.62	03/2016 -	03/2021	60	0	
16	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	90.75	03/2014 -	03/2021	84	0	
17	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40 -	706.40	432.82	07/2012 -	03/2022	116	0	
	Eastern Coal Fields Limited									
18	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	528.96	03/2018 -	10/2020	31	0	1. Rehabilitation of PAFs: Progress of R&R activity delayed due to disputes among villagers for selection of rehab. site and resistance by villagers in shifting. 2.Expediting the work of tree felling for hand over of 32.65 Ha forest land.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
19	RANIGANJ MASTER PLAN - [N06000163]ECL,WEST BENGAL	08/2009	2,661.73 -	5,173.26	336.63	08/2019 -	08/2024	60	94.36	i). Publication of Demographic survey report for non-ECL households by ADDA. ii). Publication of valuation report by ADDA against immovable properties for LTH households to assess the financial impact for payment of cash compensation. As per decision taken by WB Govt. publication of survey report will be done as and when construction of bulk chunk of flats at rehabilitation sites are completed. iii). Identification of balance 74.55 Ha land in non- coal bearing measures for construction of balance 16000 flats. CMPDI,RI-1 has identified and submitted list of land areas both in non-coal bearing and deep-seated coal bearing areas to ADDA for utilization under rehabilitation purpose. WB Govt. is now examining the actual quantum of encumbrance free land areas available for utilization under construction. v).Delay in taking over permissive possession of 4.83 acres ECL land in connection with construction of rehabilitation townships. ADDA requested IC&E Deptt, Govt. of WB to accord permission for taking over permissive possession of ECL land, pending execution of deed conveyance. However, communication in this regard is yet to be received. vi). Consideration of WB Govt. vested land areas below 25 acres for construction purposes, where NOC was accorded on the basis of study and evaluation made by CMPDI, RI-1. Accordingly, ADDA requested IC& E Deptt. to take up the matter at appropriate level for

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	Mahanadi Coal Fields Limited									
20	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	272.73	03/2010 -	03/2020	120	0	
21	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA	05/2014	337.66 -	337.66	188.48	03/2019 -	03/2020	12	0	
22	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.10 -	490.10	508.91	03/2017 -	03/2021	48	0	
23	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	296.22	03/2012 -	03/2021	108	0	
24	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.53	389.52	03/2013 -	03/2021	96	0	
25	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA	06/2014	289.03 -	289.03	-	03/2018 -	03/2021	36	0	
26	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	539.88	03/2013 -	03/2022	108	0	
27	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	347.93	03/2010 -	03/2022	144	0	
28	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA	05/2014	479.15 -	479.15	211.71	03/2019 -	03/2024	60	0	
	Neyveli Lignite Corporation									
29	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 7,080.41	7,080.41	6,867.42	12/2015 -	12/2019	48	19.86	
	Singareni Colliers Company Limitted									
30	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	143.61	03/2015 -	03/2020	60	0	
31	RG OC -III EXTENSION (PHASE - II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	159.81	06/2015 -	03/2020	57	0	
32	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	384.32	112.52	07/2016 -	03/2020	44	-7.91	
33	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 -	415.37	187.89	03/2016 -	03/2020	48	-3.5	
34	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]SCCL,TELANGANA	05/2015	397.09 -	442.42	99.42	03/2019 -	03/2020	12	11.42	
35	KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL,TELANGANA	10/2015	426.79 -	426.79	.72	03/2018 -	03/2020	24	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
36	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	164.04	119.85	03/2015 -	03/2021	72	-32.3	
37	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	349.28	7.49	03/2015 -	03/2021	72	114.6	
38	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	473.22	18.35	03/2015 -	03/2021	72	5.85	
39	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA	03/2017	413.84 -	413.84	56.86	03/2019 -	03/2022	36	0	
40	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	489.62	353.10	03/2012 -	03/2023	132	16.86	
41	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	448.86	296.17	03/2012 -	03/2024	144	80.24	
	South-Eastern Coal Fields Limited									
42	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	459.49	193.35	03/2015 -	03/2020	60	201.44	
43	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	2.92	03/2014 -	03/2020	72	0	
44	BAROUD OC EXPANSION (RCE)-3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	181.44	03/2016 -	03/2020	48	0	
45	AMERA OC RCE - [N06000123]SECL,CHHATISGARH	02/2015	335.97 -	335.97	51.21	03/2018 -	03/2020	24	0	
46	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	197.28	03/2014 -	03/2021	84	0	
	Western Coal Fields Limited									
47	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA	08/2015	288.90 -	333.43	27.21	03/2023 -	03/2024	12	15.41	
48	KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA	11/2015	277.65 -	313.34	117.85	03/2021 -	03/2024	36	12.85	
	Total		22,430.74 -	26,905.00	14,834.95					
	INFORMATION AND BROADCASTING									
	Central Public Works Department									
49	FILM AND TELEVISION INSTITUTE ARUNACHAL PRADESH - [N09000002]CPWD,ANDHRA PRADESH	11/2016	204.32 -	204.32	-	02/2019 -	11/2019	9	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	Total		204.32 -	204.32	.00					
	MINES									
	National Aluminum Company Limited (Nalco)									
50	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO,TAMIL NADU	09/2017	166.62 163.17	163.17	135.00	06/2019 03/2020	03/2020	9	-2.07	
	Total		166.62 -	163.17	135.00					
	STEEL									
	National Mineral Development Corporation (Nmdc)									
51	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH	01/2010	15,525.00 23,140.00	23,140.00	16,244.05	05/2015 07/2020	07/2020	62	49.05	
	Rastriya Ispat Nigam Limited									
52	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH	04/2014	1,682.85 -	1,682.85	1,270.63	09/2018 12/2019	12/2019	15	0	No
53	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH	12/2011	2,858.00 -	2,500.00	1,482.76	12/2017 12/2019	12/2019	24	-12.53	No
54	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH	08/2015	320.66 -	320.66	253.54	08/2018 12/2019	12/2019	16	0	NO
	Steel Authority Of India Limited (Sail)									
55	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA	04/2015	3,127.30 -	3,127.30	3,119.34	04/2018 11/2019	01/2020	21	0	
56	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	1,154.18	978.83	12/2017 11/2019	01/2020	25	0	
57	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	447.34	10/2017 06/2020	06/2020	32	0	
58	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND	11/2016	262.87 -	262.87	130.11	06/2019 06/2020	06/2020	12	0	
	Total		25,964.87 -	33,221.87	23,926.60					

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	PETROLEUM									
	Bharat Petroleum Corporation Limited									
59	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL,WEST BENGAL	03/2015	694.00 1,097.54	1,097.54	722.99	10/2018 12/2019	12/2019	14	58.15	
60	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA	11/2014	4,588.29 5,245.96	5,245.96	3,877.61	08/2018 11/2019	12/2019	16	14.33	
61	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA	04/2013	449.58 -	449.58	192.13	12/2019 07/2020	07/2020	7	0	
62	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA	02/2016	3,313.00 3,288.96	3,288.96	1,349.99	02/2020 10/2020	10/2020	8	-.73	
63	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 -	678.00	7.28	02/2017 -	10/2021	56	0	
64	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 1,507.24	1,507.24	555.00	06/2019 02/2022	02/2022	32	35.54	
	Gas Authority Of India Limited									
65	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT	04/2016	327.78 -	200.00	150.72	04/2018 -	12/2019	20	-38.98	
66	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL,HARYANA	08/2018	286.42 -	286.42	1.92	08/2020 09/2020	09/2020	1	0	
67	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE	06/2009	2,915.00 4,915.00	4,915.00	2,742.24	12/2012 02/2022	02/2022	110	68.61	
	Hindustan Petroleum Corporation Limited									
68	180 TMTPA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA	06/2017	249.26 -	249.26	60.45	06/2020 -	09/2021	15	0	
69	120 TMTPA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND	06/2017	161.50 -	161.50	17.78	06/2020 -	09/2021	15	0	
70	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH	07/2016	20,928.00 26,264.00	26,264.00	7,245.30	07/2020 07/2022	07/2022	24	25.5	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	Indian Oil Corporation Limited									
71	JAIPUR-PANIPAT NAPTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE	02/2015	890.00 -	887.00	609.28	10/2019 -	12/2019	2	-.34	
72	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]IOCL,UTTAR PRADESH	01/2018	666.64 -	666.64	468.46	09/2019 -	01/2020	4	0	
73	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]IOCL,ASSAM	02/2016	2,582.00 -	2,582.00	1,613.96	11/2019 -	02/2020	3	0	
74	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]IOCL,HARYANA	12/2017	3,529.00 -	3,529.00	1,895.18	07/2019 -	02/2020	7	0	
75	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]IOCL,GUJARAT	03/2018	3,380.00 -	3,380.00	2,238.63	09/2019 -	03/2020	6	0	
76	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]IOCL,ASSAM	05/2018	1,222.00 -	1,222.00	606.24	09/2019 -	04/2020	7	0	
77	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]IOCL,WEST BENGAL	05/2018	2,934.40 -	2,934.40	1,780.52	09/2019 -	04/2020	7	0	
78	FUEL QUALITY UPGRADATION (NSU,NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY - [N16000348]IOCL,BIHAR	06/2017	951.64 -	951.64	490.98	10/2019 -	05/2020	7	0	
79	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]IOCL,ODISHA	05/2016	429.00 -	429.00	318.90	01/2019 -	06/2020	17	0	
80	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM	08/2018	557.00 -	557.00	249.46	02/2020 -	06/2020	4	0	
81	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00 -	236.00	30.20	06/2020 -	08/2020	2	0	
82	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	326.08	07/2018 -	10/2020	27	0	
83	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND	02/2017	160.10 -	160.10	51.57	02/2020 -	10/2020	8	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
84	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT	10/2017	906.00 -	906.00	98.97	02/2020 -	10/2020	8	0	
85	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM	06/2016	423.00 -	423.00	282.50	08/2019 -	12/2020	16	0	
86	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00 6,025.00	6,025.00	990.22	12/2018 -	02/2021	26	33.98	
87	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL,WEST BENGAL	04/2017	163.02 -	163.02	54.53	04/2020 -	03/2021	11	0	
88	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	212.00	46.99	01/2021 -	04/2021	3	0	
89	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA	12/2016	161.59 -	161.59	38.65	12/2019 -	07/2021	19	0	
90	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00 -	466.00	96.28	04/2021 -	07/2021	3	0	
91	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	466.43	35.01	10/2020 -	08/2021	10	0	
92	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	348.00	37.01	01/2021 -	10/2021	9	0	
93	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	318.80	52.67	08/2021 -	11/2021	3	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
94	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	355.00	14.89	04/2022 -	02/2023	10	0	
	Mangalore Refinery And Petrochemicals Limited									
95	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA	09/2016	1,810.00 1,810.00	1,810.00	940.45	12/2019 07/2020	07/2020	7	0	
96	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA	11/2017	581.00 -	621.00	102.99	03/2020 11/2020	11/2020	8	6.88	
	Oil & Natural Gas Corporation Limited									
97	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 345.92	345.92	155.61	01/2014 -	11/2019	70	70.45	
98	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.86	2,147.00	03/2013 12/2019	12/2019	81	-3.5	
99	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 -	1,683.06	1,356.33	05/2013 12/2019	12/2019	79	95.3	
100	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	1,932.09	03/2015 12/2019	12/2019	57	29.42	
101	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA	11/2014	6,068.80 -	5,296.93	4,767.31	04/2019 12/2019	12/2019	8	-12.72	
102	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA	01/2015	4,619.94 -	4,619.94	4,444.58	12/2017 03/2020	03/2020	27	0	
103	DEVELOPMENT OF B-147 FIELD - [N16000292]ONGC,MAHARASHTRA	02/2017	546.15 565.15	565.15	449.96	11/2019 03/2020	03/2020	4	3.48	
104	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA	08/2015	2,818.88 -	2,818.88	2,302.10	03/2019 05/2020	05/2020	14	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
105	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA	12/2015	3,190.69 -	3,247.19	2,298.77	04/2018 05/2020	05/2020	25	1.77	
106	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	650.82 -	650.82	415.38	03/2019 05/2020	05/2020	14	0	
107	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]ONGC,MAHARASHTRA	02/2019	3,660.71 3,740.05	3,740.05	274.07	04/2021 -	05/2021	1	2.17	
108	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH	03/2016	34,012.00 -	34,012.00	4,204.96	06/2020 -	08/2021	14	0	
109	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC,MAHARASHTRA	02/2017	4,006.83 -	4,475.92	2,869.89	05/2021 12/2021	12/2021	7	11.71	
110	HEERA REDEVELOPMENT - PHASE III - [N16000360]ONGC,MAHARASHTRA	05/2019	2,494.68 -	2,494.68	48.07	12/2021 -	03/2022	3	0	
	Oil India Limited									
111	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	438.84	249.73	03/2017 06/2020	06/2020	39	24.47	
112	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE	09/2016	571.66 -	571.66	297.66	12/2019 06/2020	06/2020	6	0	
113	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM	01/2018	543.91 -	682.90	71.46	02/2020 06/2020	06/2020	4	25.55	
	Total		1,33,765.59 -	1,45,532.53	58,679.00					
	POWER									
	National Hydro-Electric Power Corporation									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
114	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	9,997.11	7,715.06	09/2009 -	12/2021	147	155.05	
	National Thermal Power Corporation									
115	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH	03/2015	9,870.51 -	11,148.86	9,055.78	01/2020 -	02/2020	1	12.95	
116	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	12/2012	11,846.00 -	12,739.82	12,839.84	10/2017 03/2020	03/2020	29	7.55	
117	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	03/2013	11,638.55 -	12,865.92	12,361.29	01/2018 03/2020	03/2020	26	10.55	
118	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA	05/2016	1,885.13 -	1,885.13	527.90	12/2018 -	03/2020	15	0	
119	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL	12/2016	529.68 -	529.68	140.10	11/2018 -	03/2020	16	0	
120	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	12,176.28	10,032.00	02/2017 06/2020	06/2020	40	24.87	
121	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH	09/2014	9,188.98 -	10,016.10	6,633.23	07/2019 03/2020	07/2020	12	9	
122	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA	02/2014	12,532.44 -	13,740.53	9,944.45	12/2018 02/2020	09/2020	21	9.64	
123	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 7,998.00	9,583.00	7,981.46	07/2012 -	09/2020	98	79.02	
124	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 5,867.38	5,867.38	4,264.84	03/2013 12/2020	01/2021	94	96.99	
125	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 17,304.00	17,304.00	14,229.00	05/2018 12/2021	06/2021	37	33.47	
126	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA	01/2016	10,598.98 -	10,598.98	5,851.67	11/2020 06/2021	06/2021	7	0	
127	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 21,312.11	21,312.11	16,756.64	10/2011 08/2021	08/2021	118	145.16	
128	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	15,164.05	9,861.12	06/2019 09/2019	03/2022	33	5.55	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
129	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL	09/2014	1,381.84 -	1,592.34	502.87	09/2019 05/2024	05/2024	56	15.23	
	Power Grid Corporation Of India Limited									
130	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 -	871.62	584.94	10/2017 09/2019	11/2019	25	0	
131	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 260.03	260.03	199.56	07/2017 06/2019	11/2019	28	27.92	
132	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA	04/2016	844.64 -	844.64	435.25	04/2019 04/2019	11/2019	7	0	
133	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 639.46	639.46	568.44	06/2014 09/2019	12/2019	66	31.17	
134	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 1,891.41	1,891.41	1,280.93	04/2016 08/2019	12/2019	44	38.61	Severe ROW problem at Rajarhat area due to protest by political groups.
135	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 374.63	374.63	214.62	04/2016 12/2017	12/2019	44	0	
136	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 5,151.37	5,151.37	3,216.41	03/2018 12/2019	12/2019	21	0	
137	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 197.40	197.40	83.94	03/2018 -	12/2019	21	0	
138	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	431.80	05/2017 06/2019	12/2019	31	0	
139	GREEN ENERGY CORRIDORS - INTER STATE TRANSSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	3,519.59	2,534.01	05/2019 -	12/2019	7	0	
140	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE	09/2016	562.25 -	562.25	420.20	03/2019 -	12/2019	9	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
141	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE	10/2016	608.24 -	608.24	416.24	04/2019 -	12/2019	8	0	
142	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE	03/2017	337.75 -	337.75	99.94	06/2019 -	12/2019	6	0	
143	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE	12/2015	3,654.00 -	3,654.00	3,485.19	04/2019 -	12/2019	8	0	
144	EASTERN REGION STRENGTHENNING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL	04/2016	454.11 -	454.11	297.16	04/2018 01/2020	01/2020	21	0	
145	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 -	408.46	311.82	01/2019 09/2019	01/2020	12	0	
146	TRANSMISSION SYSTEM FOR EVACUTION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 -	186.17	110.60	07/2019 -	01/2020	6	0	
147	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE	05/2016	14,733.37 -	14,733.37	9,317.26	11/2019 -	02/2020	3	0	
148	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE	09/2017	198.49 -	198.49	119.50	09/2019 02/2020	02/2020	5	0	
149	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 5,071.94	5,071.94	4,570.22	10/2012 12/2019	03/2020	89	5.14	
150	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 546.36	546.36	470.50	11/2016 06/2020	03/2020	40	4.61	
151	TRANSMISSION SYSTEM STRENTHENNING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	808.63	534.82	01/2018 03/2020	03/2020	26	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Antici Pated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
152	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	322.30	164.09	02/2019 04/2020	03/2020	13	0	
153	EASTERN REGION STRENTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	235.53	130.55	06/2019 -	03/2020	9	0	
154	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 -	379.95	93.48	12/2019 -	03/2020	3	0	
155	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT	05/2017	175.64 -	175.64	101.85	09/2018 03/2020	03/2020	18	0	
156	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA	05/2017	445.89 -	445.89	295.78	02/2019 12/2019	03/2020	13	0	
157	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT	12/2017	193.14 -	193.14	100.18	06/2019 03/2020	03/2020	9	0	
158	COMPREHENSIVE SCHEME FOR THE STRENGHTENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	9,072.36	1,352.46	12/2018 -	12/2020	24	90.82	
159	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	6,880.36	1,779.00	12/2018 -	12/2020	24	34.61	
160	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 14,719.10	14,719.10	12,816.90	08/2013 03/2022	03/2022	103	32.24	
	Thdc India Limited									
161	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 -	294.60	321.11	02/2014 -	12/2019	70	50.75	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
162	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 -	5,024.35	3,118.00	02/2016 -	06/2022	76	203.22	Renewal of lease for 3.0 Ha land at Asena Quarry and Transfer of additional 05 Ha. Forest land and permission for mining are pending. It needs to be expedited.
163	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	4,397.80	1,823.10	06/2013 -	12/2022	114	76.51	1) There have been frequent hindrances by local villagers since mobilization of works in Jan 2014. Local hindrances have minimized in VPHEP with the strong intervention of MoP and support of District Administration. Still regular support of Distt. Administration is required for smooth and unobstructed execution of the project works. 2) Approval of Gadi quarry and crusher plant is pending with District Administration/ GoUK.
	Total		1,96,297.55 -	2,51,376.75	1,80,497.10					
	HEAVY INDUSTRY									
	Bharat Heavy Electricals Limited									
164	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI	08/2016	1,554.00 -	1,554.00	665.35	09/2019 -	03/2020	6	0	
	Total		1,554.00 -	1,554.00	665.35					
	HEALTH AND FAMILY WELFARE									
	HII Infra Tech Services Limited									
165	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	715.06	345.41	04/2020 06/2020	10/2020	6	-8.91	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
166	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	557.48	283.12	06/2020 08/2020	10/2020	4	-20.7	
167	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 -	747.80	110.70	05/2021 10/2021	10/2021	5	-14.54	
	Hospital Services Consultancy Corporation Ltd									
168	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	325.00	297.16	05/2017 -	01/2020	32	10.68	
169	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	177.92	139.70	02/2018 -	03/2020	25	16.33	
170	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	274.19	241.58	03/2019 -	03/2020	12	0	
171	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	272.54	191.86	03/2019 -	03/2020	12	.13	
172	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	270.00	204.70	05/2017 -	06/2020	37	32.07	
173	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	363.99	208.29	05/2018 -	07/2020	26	0	
174	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL	08/2017	355.15 -	355.15	217.00	03/2019 -	07/2020	16	0	
175	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	499.23	302.02	11/2013 -	09/2020	82	20.55	
	Total		4,693.67 -	4,558.36	2,541.54					
	RAILWAYS									
	Central Railways									
176	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 199.12	312.00	275.98	03/2019 12/2019	12/2019	9	69.51	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
177	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	3,712.50	2,434.24	03/2021 -	03/2022	12	63.44	
178	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 -	1,377.48	316.79	03/2021 -	03/2022	12	73.73	
179	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	1,272.19	319.94	03/2022 -	03/2023	12	0	
180	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	540.02	252.82	03/2022 -	03/2024	24	0	
181	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	1,035.16	117.02	03/2022 -	03/2024	24	0	
182	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	637.95	73.16	03/2023 -	03/2024	12	0	
	Container Corporation Of India									
183	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	305.00	261.28	03/2019 -	12/2019	9	0	
184	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	343.00	222.83	03/2019 -	12/2019	9	0	
185	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	174.00	152.48	03/2019 -	02/2020	11	0	
186	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	493.17	441.09	03/2018 -	03/2020	24	0	
187	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	346.32	288.65	03/2019 -	03/2020	12	0	
188	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	235.00	10.88	03/2019 -	12/2020	21	.21	
	East Central Railways									
189	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	118.49	03/2019 -	12/2019	9	0	
190	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 898.53	1,050.00	1,043.03	03/2012 -	03/2020	96	223.35	

MoSPI OCMS

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
191	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88 751.55	751.55	674.58	03/2012 -	03/2020	96	57.27	
192	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	678.54 678.54	678.54	495.04	03/2019 -	02/2021	23	0	
193	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	597.94	03/2020 -	03/2021	12	0	
194	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR	12/2015	1,200.20 1,200.20	1,200.20	397.15	03/2020 -	10/2021	19	0	
195	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 819.01	819.01	489.11	03/2020 -	03/2022	24	49.45	
196	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 1,215.54	1,215.54	79.18	03/2021 -	03/2022	12	63.37	
197	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 1,185.73	1,185.73	35.74	03/2021 -	03/2022	12	62.06	
198	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR	12/2015	1,491.47 -	1,491.47	443.64	03/2020 -	12/2022	33	0	
	East Coast Railway									
199	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	238.03	204.79	03/2020 -	03/2021	12	52.77	
200	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 1,539.28	1,539.28	937.49	02/2019 -	03/2022	37	38.43	
201	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 701.61	810.02	129.40	11/2018 -	03/2022	40	15.45	
202	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 1,172.92	1,172.92	546.12	12/2018 03/2022	03/2022	39	0	
203	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 843.04	843.04	141.96	10/2020 03/2023	03/2023	29	0	
204	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	1,160.00 1,160.83	1,160.83	699.40	03/2020 -	03/2023	36	.07	
205	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 1,547.38	1,547.38	366.66	03/2022 -	03/2023	12	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
206	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 3,791.66	3,791.66	1,243.45	03/2009 -	06/2024	183	29.71	
207	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 198.07	1,928.07	770.82	06/2021 -	06/2024	36	137.8	
208	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	2,361.74	208.19	03/2022 -	03/2025	36	0	
	Eastern Railways									
209	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	157.94	51.75	11/2018 -	03/2021	28	0	
210	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	542.18 -	693.80	458.91	03/2020 -	03/2021	12	27.96	State Govt. is requested to deposit their balance share of cost for the project. But still deposition is awaited.
211	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	1,425.44	637.54	02/2013 -	03/2024	133	134.8	
212	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	1,619.48	871.86	03/2019 12/2009	03/2025	72	36.22	1. Acquisition of land in stretch of 3.126 KM between Kamarpukur and Mayanapur and pending over of 5.679 KM stretch possession to Railway. 2. Villegers of Vill.Bhadadighi, Hooghly District,are not allowing to work over a pond namely .Bhabadighi between Goghat and Kamarpukur . 3. Tarakeshwar to Dhaniakhali (19 Km) New line, Arambagh – Irphala (18.3 Km) New line , Irphala – Ghatal (11.2 Km) New line and Arambagh – Champadanga (23.30 Km) New line -- Work could not be started due to non availability of land

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
213	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62 -	1,091.59	860.08	12/2010 12/2017	03/2025	171	-1.36	Govt. of West Bengal to deposit Rs. 238.68 Cr. for their balance share towards project Katwa- BWN G.C.
214	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	545.70	148.48	03/2006 -	03/2025	228	34.08	Land is required for execution of the MM projects
215	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	2,137.81	297.68	03/2022 -	03/2025	36	133.39	1. Jharkhand & Bihar Government to expedite land acquisition. Milestones may be set only after physical possession of land. 2. Jharkhand Govt. is to deposit Rs. 158.50Crs. as share of expenditure incurred in this project..
216	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	995.10	501.00	03/2016 -	03/2025	108	7.75	1 Krishnanagar City (Dhubulia) – Charatala (13.00KM) New line, Krishnanagar – Chapra (19.2 KM) New line Work could not be started due to non – availability of land. 2 For Krishnanagar – Nabadwipghat (12.2 KM) Gauge Conversion— (Section Krishnanagar – Amghata) could not be commissioned due to religious structures in alignment and Amghata to Nabadwipghat work is held up due to 41 nos. of un authorized crossings.
217	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51 -	769.40	103.08	03/2017 -	03/2025	96	29.2	Suri – Prantik New Line (33.90 km). The land acquisition details for 250.627 Hectares,submitted to Govt. of West Bengal.
218	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	266.32	162.57	03/2016 -	03/2025	108	-3.95	For Bira - Chakla (11.50) New line- The work will start after acquisition and handing over of land by State Government.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
219	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	296.43	248.70	03/2017 -	03/2025	96	-18.82	Baruipara – Furfura (12.30 km) New line - Work could not be started due to non availability of land.
220	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	494.59	32.00	03/2005 -	03/2025	240	.01	Budge Budge to Pujali (11.00 km) New Line, Pujali – Uluberia (Birshivpur) (10.25 Km) New Line and Pujali – Bakrahat (9.75 Km) New line-- Work could not be started due to non availability of land
221	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	680.68	159.45	02/2012 -	03/2025	157	36.15	Sangrampur – Krishanchandpur (25 Km) New Line, Diamond Harbour (Gurudasnagar) – Bahrahat (21 Km) New Line and Daimond Harbour (Gurudasnagar) - Kulpi (17.25 Km) New Line: Work could not be started due to non availability of land.
222	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	257.42	107.49	03/2014 -	03/2025	132	0	226.542 acres of land required to be acquired for the MM work.
223	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108	12.02	
	Indian Railway Construction Company Limited									
224	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH	04/2013	3,055.00 -	3,055.00	1,951.07	09/2018 -	12/2020	27	0	
225	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH	02/2014	2,288.00 -	4,970.11	628.61	03/2022 -	12/2022	9	117.23	
226	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA	04/2016	5,200.00 -	1,700.43	48.00	03/2020 -	06/2023	39	-67.3	
	Metropolitan Rapid Transport Projects									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
227	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	2,980.41	1,431.38	03/2004 -	03/2021	204	501.57	
228	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 -	918.53	284.75	03/2014 -	03/2021	84	-82.67	
229	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	63	75.91	
	North Central Railway									
230	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	2,912.96 -	3,845.60	148.26	03/2022 -	12/2024	33	32.02	
	North East Frontier Railway									
231	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	297.32 -	614.00	275.07	03/2019 -	03/2020	12	106.51	
232	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 1,532.00	1,532.00	642.09	03/2019 -	03/2020	12	297.72	
233	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 2,145.00	2,145.00	935.60	03/2019 -	03/2020	12	302.54	
234	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	314.00 728.00	728.00	727.55	03/2019 -	03/2020	12	131.85	
235	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	1,180.19 3,300.00	4,541.00	3,344.19	12/2008 -	03/2021	147	284.77	
236	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	569.63 670.00	670.00	107.83	03/2020 09/2021	09/2021	18	17.62	
237	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 -	4,600.00	842.42	03/2015 -	10/2021	79	97.72	
238	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 13,809.00	12,524.00	9,541.58	03/2011 -	03/2022	132	181.17	
239	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	2,393.47 4,968.00	5,021.45	3,131.89	03/2014 03/2022	03/2022	96	109.8	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	North Eastern Railway									
240	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	477.31	336.89	01/2019 -	01/2020	12	61.8	
241	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	426.74	195.35	04/2017 -	01/2020	33	-31.45	
242	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	213.35	9.62	04/2016 -	06/2020	50	.16	
243	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	1,028.95	26.06	12/2019 -	04/2021	16	-12.65	
244	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	0	
245	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	150.00	-	04/2017 -	10/2022	66	0	
	North Western Railway									
246	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	294.90	226.61	10/2018 -	12/2019	14	24.47	
247	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 281.03	410.00	362.96	02/2019 -	03/2020	13	69.36	
248	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	303.56	274.18	11/2019 -	05/2020	6	42.26	
249	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	348.55	229.00	12/2019 -	06/2020	6	41.64	
250	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 -	420.18	184.64	03/2020 -	06/2020	3	0	
251	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 780.98	886.41	559.84	02/2019 -	03/2021	25	116.16	
252	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	685.99	74.80	03/2020 -	04/2022	25	14.33	
253	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	808.85	60.28	08/2022 -	09/2022	1	0	
	Northern Railway									
254	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	694.00	220.42	12/2011 -	03/2021	111	141.81	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
255	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 781.00	859.00	835.35	03/2016 -	03/2021	60	37.44	
256	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	27,949.00	19,767.15	11/2002 -	06/2022	235	1017.96	
257	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 2,010.00	2,200.00	666.00	07/2012 -	03/2024	140	388.89	
	Rail Vikas Nigam Ltd.									
258	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64 -	1,844.47	1,829.53	12/2017 -	03/2020	27	55.57	
259	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	1,200.00	1,178.67	03/2019 -	03/2020	12	29.45	
260	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	385.00	387.92	03/2009 03/2009	06/2020	135	188.58	
261	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02 -	1,100.00	1,088.23	03/2020 -	06/2020	3	-21.54	
262	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	816.55	701.83	03/2016 -	12/2020	57	29.06	
263	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48 -	2,300.00	2,056.99	03/2020 -	03/2021	12	222.36	
264	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	1,500.00	1,374.96	03/2020 -	03/2021	12	58.22	
265	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.85 -	1,485.85	1,158.89	12/2020 -	03/2021	3	0	
266	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 -	1,202.70	947.96	02/2015 -	12/2021	82	0	
267	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,548.66 -	1,548.66	1,339.35	12/2021 -	03/2022	3	0	
268	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	2,200.00	1,722.18	03/2020 -	03/2022	24	46.3	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
269	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	1,120.00	1,028.76	03/2019 -	06/2022	39	18.78	
270	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	1,183.25	1,136.44	12/2020 -	12/2022	24	0	
271	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA	04/2010	2,127.00 -	2,900.00	1,737.30	03/2023 -	03/2024	12	36.34	
272	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	750.56	409.09	03/2022 -	12/2024	33	-20.46	
273	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	650.11	03/2023 -	12/2024	21	0	
274	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	4,724.30	2,278.26	03/2016 -	03/2025	108	19.54	
275	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	4,639.00	855.74	03/2016 -	03/2025	108	59.22	
276	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	16,216.00	1,790.80	12/2024 -	03/2025	3	0	
277	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	2,733.86	40.13	03/2014 -	12/2025	141	18.95	
	South Central Railway									
278	MUNEERABAD-MAHABOOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1,780.29	1,780.09	1,478.40	03/2000 -	03/2021	252	3.31	
279	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 2,120.16	2,120.16	524.57	03/2009 -	03/2023	168	102.85	
280	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	1,160.48 1,160.48	1,160.48	323.09	03/2010 -	03/2023	156	0	
281	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 2,063.03	2,063.03	792.70	03/2021 -	03/2023	24	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
282	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 3,631.00	3,631.00	617.19	03/2022 -	03/2023	12	0	
283	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 2,200.00	2,200.00	290.92	03/2023 -	03/2024	12	18.47	
284	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	2,288.70 2,643.25	2,643.25	810.35	03/2021 -	03/2024	36	15.49	
285	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,132.77 2,132.77	2,132.77	331.15	03/2014 -	03/2024	120	0	
	South East Central Railway									
286	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH	04/2008	872.00 1,226.51	1,226.51	1,062.76	12/2019 03/2020	03/2020	3	40.65	
287	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH	04/2010	585.93 1,268.32	1,268.32	669.57	02/2019 12/2020	12/2020	22	116.46	
288	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	511.86 1,756.00	1,756.00	1,668.96	04/2020 01/2021	01/2021	9	243.06	
289	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00 1,370.94	1,370.94	311.76	12/2021 11/2022	11/2022	11	.07	
290	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA	06/2018	229.00 852.50	852.50	39.69	12/2021 03/2023	03/2023	15	272.27	
291	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH	04/2015	1,973.00 1,973.64	1,973.64	174.40	03/2021 03/2023	03/2023	24	.03	
	South Eastern Railway									
292	RAJKHARSWAN-CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	377.00	182.63	12/2016 08/2018	01/2020	37	153.41	
293	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 358.68	358.68	265.54	12/2018 -	06/2020	18	38.92	
294	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 1,312.96	1,312.96	562.50	03/2020 03/2020	06/2020	3	35.38	
295	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	1,993.24	411.64	03/2021 03/2021	12/2021	9	15.6	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
296	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	1,009.00	7.96	03/2015 03/2025	03/2025	120	54.99	
297	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 1,966.70	2,373.00	485.04	03/2003 03/2030	03/2030	324	130.97	
	South Western Railway									
298	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 644.78	890.00	443.52	03/2017 -	03/2020	36	38.03	
299	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,156.94 1,140.94	1,140.94	773.28	03/2020 -	03/2021	12	-1.38	
300	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 1,870.41	1,870.41	885.55	03/2019 -	03/2021	24	15.84	
301	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	986.30 986.30	986.30	302.38	03/2016 -	12/2023	93	0	Land acquisition.
302	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 279.54	279.54	30.34	03/2016 -	12/2023	93	0	
303	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 1,382.78	1,382.78	7.35	03/2002 -	03/2024	264	0	
304	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 832.47	832.47	.94	03/2016 -	03/2024	96	0	GoK has not released any funds to DCs concerned for land acquisition.
305	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 2,841.84	2,841.84	169.45	12/2018 -	12/2024	72	0	land acquisition.
	Southern Railway									
306	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	1,800.00	187.30	03/2019 -	12/2019	9	1391.3	
307	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	2,072.50	1,440.83	02/2019 -	02/2020	12	185.98	
308	OMALUR-METTURDAM-DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	231.67	162.06	04/2014 -	03/2020	71	23.72	
309	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	980.00	681.66	03/2020 -	03/2021	12	222.39	
310	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	1,182.31	446.00	03/2020 -	06/2021	15	55.57	
311	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	West Central Railway									
312	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH	08/2016	582.13 -	1,247.64	152.01	03/2022 09/2022	09/2022	6	114.32	
313	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 6,672.85	8,248.50	1,986.78	05/2008 03/2022	03/2023	178	3230.57	
314	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	424.60 -	2,909.99	1,975.34	03/2021 -	03/2023	24	585.35	
315	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93 -	1,762.94	847.47	03/2020 03/2023	03/2023	36	-.06	
316	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH	06/2016	2,478.23 -	2,478.23	477.93	03/2022 -	03/2023	12	0	
	Western Railway									
317	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT	02/1991	551.51 809.07	809.07	641.51	03/2019 03/2020	03/2020	12	46.7	
318	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	829.74 1,215.34	1,310.23	1,450.40	03/2020 03/2021	03/2021	12	57.91	
319	DABHOI-CHANDOD (17.07KM) - GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT	04/2017	691.84 663.29	663.29	180.20	03/2020 03/2021	03/2021	12	-4.13	
320	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH	04/2016	700.00 603.69	603.69	113.47	06/2020 06/2021	06/2021	12	-13.76	
321	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 321.62	321.62	125.76	03/2012 03/2022	03/2022	120	1.06	
322	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 858.56	858.96	534.00	03/2019 03/2022	03/2022	36	167.87	
323	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	1,037.15 1,037.15	1,037.15	1,017.75	03/2021 03/2022	03/2022	12	0	
324	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 3,975.22	3,975.22	1,758.23	03/2022 03/2023	03/2023	12	13.46	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
325	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 1,640.04	1,640.04	739.31	03/2022 03/2023	03/2023	12	0	
	Total		1,84,312.90 -	2,77,298.11	1,25,647.99					
	ROAD TRANSPORT AND HIGHWAYS									
	Ministry Of Road Transport And Highways (State Pwds)									
326	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA	08/2013	171.96 172.00	172.00	88.30	06/2016 -	11/2019	41	.02	
327	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]MoRTH,WEST BENGAL	03/2016	271.17 291.20	291.20	89.25	11/2018 11/2019	11/2019	12	7.39	
328	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MoRTH,ANDHRA PRADESH	02/2017	429.43 -	429.43	209.09	11/2017 03/2020	11/2019	24	0	
329	SAKOLI TO BHANDARA - [N24001118]MoRTH,MAHARASHTRA	01/2017	362.96 362.96	362.96	37.83	06/2019 -	11/2019	5	0	
330	NASHIK TO PETH - [N24001121]MoRTH,MAHARASHTRA	12/2015	289.60 -	289.60	118.81	11/2018 -	11/2019	12	0	
331	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH,KERALA	01/2014	255.75 348.00	348.43	290.12	09/2017 -	12/2019	27	36.24	
332	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM	11/2010	624.41 -	992.67	853.82	03/2011 -	12/2019	105	58.98	
333	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM	08/2010	193.69 -	327.92	254.24	10/2010 -	12/2019	110	69.3	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
334	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]MoRTH,ARUNACHAL PRADESH	03/2012	207.03 389.45	389.45	291.55	05/2012 05/2015	12/2019	91	88.11	
335	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]MoRTH,SIKKIM	04/2013	151.59 -	151.59	196.76	08/2013 -	12/2019	76	0	
336	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]MoRTH,SIKKIM	01/2013	182.28 -	269.14	185.49	02/2013 -	12/2019	82	47.65	
337	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH	05/2013	164.54 -	164.54	126.41	08/2015 -	12/2019	52	0	
338	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA	12/2011	191.08 -	191.08	99.98	08/2015 -	12/2019	52	0	
339	WIDENING AND STRENFTHENING OF EXISITNG SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA	03/2014	191.50 192.00	192.00	136.19	05/2016 -	12/2019	43	.26	
340	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND	06/2017	282.08 -	282.08	77.05	06/2019 -	12/2019	6	0	
341	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]MoRTH,MADHYA PRADESH	09/2016	287.34 -	287.34	148.65	01/2019 -	12/2019	11	0	
342	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]MoRTH,ANDHRA PRADESH	09/2016	372.68 -	372.68	185.04	02/2017 12/2019	12/2019	34	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
343	REHABILITATION AND UPGRADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942]MoRTH,UTTAR PRADESH	03/2016	208.50 -	208.50	139.97	11/2019 -	12/2019	1	0	
344	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MoRTH,ANDHRA PRADESH	01/2016	386.09 -	386.09	183.00	05/2016 12/2019	12/2019	43	0	
345	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA	01/2017	244.54 -	244.54	138.52	05/2019 09/2019	12/2019	7	0	
346	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA	01/2017	196.52 -	196.52	103.22	10/2019 -	12/2019	2	0	
347	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA	01/2017	359.27 -	359.27	237.90	05/2019 -	12/2019	7	0	
348	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA	03/2018	192.67 -	192.67	107.37	07/2019 -	12/2019	5	0	
349	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA	02/2017	203.21 203.00	203.21	109.79	05/2019 -	12/2019	7	0	
350	SHEGAON TO DEORI PHATA - [N24001010]MoRTH,MAHARASHTRA	02/2017	373.10 373.00	373.10	143.43	05/2019 -	12/2019	7	0	
351	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA	01/2017	385.87 386.00	385.87	203.75	06/2019 -	12/2019	6	0	
352	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA	01/2017	341.16 341.00	341.16	156.29	06/2019 -	12/2019	6	0	
353	NAGAJ TO VAIJAPUR - [N24001023]MoRTH,MAHARASHTRA	01/2017	376.72 377.00	376.72	183.81	06/2019 -	12/2019	6	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
354	INDAPAUR TO AGARDANDA - [N24001025]MoRTH,MAHARASHTRA	01/2017	355.17 -	355.17	164.87	07/2019 -	12/2019	5	0	
355	TAKARKHED TO JALNA - [N24001085]MoRTH,MAHARASHTRA	09/2017	417.90 418.00	417.90	119.26	06/2019 -	12/2019	6	0	
356	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA	12/2017	244.04 244.00	244.04	40.94	03/2019 -	12/2019	9	0	
357	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA	01/2018	264.41 264.00	264.41	36.71	03/2019 -	12/2019	9	0	
358	PEN TO KHOPOLI - [N24001106]MoRTH,MAHARASHTRA	03/2018	301.39 302.00	301.39	-	03/2018 -	12/2019	21	0	
359	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND	08/2016	234.88 -	208.89	118.26	12/2017 -	12/2019	24	-11.07	
360	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]MoRTH,ASSAM	11/2010	197.37 -	197.37	88.86	02/2014 -	12/2019	70	0	
361	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM	08/2010	186.96 -	305.61	275.06	09/2014 -	12/2019	63	63.46	
362	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH	07/2016	208.88 -	208.88	88.62	10/2019 -	12/2019	2	0	
363	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]MoRTH,ANDHRA PRADESH	03/2015	271.45 -	271.45	159.15	10/2015 01/2020	01/2020	51	0	
364	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO - [N24000930]MoRTH,ANDHRA PRADESH	11/2016	378.24 -	378.24	287.63	01/2018 01/2020	01/2020	24	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
365	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938]MoRTH,ANDHRA PRADESH	03/2018	297.12 294.00	294.12	291.57	07/2018 01/2020	01/2020	18	-1.01	
366	REHABILITAITON AND UPGRADATION OF REPALLE TO EEPPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MoRTH,ANDHRA PRADESH	01/2017	576.48 -	576.48	228.31	01/2018 12/2020	01/2020	24	0	
367	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH	03/2015	511.83 -	511.83	261.31	08/2017 -	02/2020	30	0	
368	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH	01/2016	809.16 -	809.16	236.96	07/2018 -	02/2020	19	0	
369	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU - [N24000936]MoRTH,ANDHRA PRADESH	03/2018	244.95 245.00	244.95	126.99	08/2018 02/2020	02/2020	18	0	
370	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MoRTH,ANDHRA PRADESH	03/2018	289.67 290.00	289.67	103.90	08/2018 02/2020	02/2020	18	0	
371	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MoRTH,ANDHRA PRADESH	11/2016	376.25 -	376.25	201.42	08/2017 02/2020	02/2020	30	0	
372	AKKALKOT TO DHUDHNI - [N24001120]MoRTH,MAHARASHTRA	04/2016	211.42 -	211.42	131.85	02/2019 -	02/2020	12	0	
373	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]MoRTH,MADHYA PRADESH	11/2011	954.43 -	954.43	235.61	09/2015 -	03/2020	54	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
374	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH	03/2018	162.56 -	162.56	88.47	03/2018 -	03/2020	24	0	
375	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]MoRTH,MADHYA PRADESH	11/2017	235.91 -	235.91	144.76	02/2018 -	03/2020	25	0	
376	UPGRADATION OF PACHORE-SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH	11/2017	184.62 -	184.62	65.06	02/2018 -	03/2020	25	0	
377	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH	03/2018	233.04 -	233.04	109.26	03/2018 -	03/2020	24	0	
378	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH	11/2017	249.05 -	249.05	127.30	07/2018 -	03/2020	20	0	
379	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH	11/2017	254.17 -	254.17	152.81	02/2018 -	03/2020	25	0	
380	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA	01/2017	247.25 -	247.25	144.71	03/2019 03/2020	03/2020	12	0	
381	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]MoRTH,ANDHRA PRADESH	11/2016	290.15 -	290.15	70.35	05/2017 03/2020	03/2020	34	0	
382	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MoRTH,ANDHRA PRADESH	01/2017	319.28 -	319.28	108.34	08/2017 03/2020	03/2020	31	0	
383	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MoRTH,ANDHRA PRADESH	03/2018	228.32 -	228.32	47.96	08/2018 03/2020	03/2020	19	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
384	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]MoRTH,ANDHRA PRADESH	01/2016	348.95 -	348.95	161.26	08/2016 03/2020	03/2020	43	0	
385	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MoRTH,ANDHRA PRADESH	03/2016	444.84 -	444.84	251.28	09/2016 03/2020	03/2020	42	0	
386	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA	10/2016	248.83 -	248.83	91.52	03/2019 -	03/2020	12	0	
387	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA	01/2017	300.00 -	300.00	100.33	05/2019 -	03/2020	10	0	
388	INDAPUR TO VADPALE - [N24001114]MoRTH,MAHARASHTRA	01/2017	1,202.52 1,202.52	1,202.52	635.90	12/2019 -	03/2020	3	0	
389	VADPALE TO BHOGAN KHURD - [N24001115]MoRTH,MAHARASHTRA	01/2017	1,598.47 1,560.00	1,598.47	751.91	11/2019 -	03/2020	4	0	
390	REHABILITATION AND UPGRADATION OF TULSIPUR - BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH	03/2016	249.50 -	249.50	156.70	05/2019 -	03/2020	10	0	
391	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH	02/2018	279.44 -	279.44	76.00	03/2018 -	04/2020	25	0	
392	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MoRTH,ANDHRA PRADESH	08/2016	350.61 -	350.61	310.25	01/2017 04/2020	04/2020	39	0	
393	KOLHA TO NASRATPUR - [N24001111]MoRTH,MAHARASHTRA	04/2016	281.78 282.00	281.78	47.73	04/2019 -	04/2020	12	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
394	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 - [N24001205]MoRTH,UTTAR PRADESH	12/2016	209.10 -	209.10	159.51	10/2019 04/2020	04/2020	6	0	
395	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]MoRTH,MADHYA PRADESH	11/2013	497.05 -	881.05	544.84	05/2017 -	05/2020	36	77.26	
396	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH	01/2017	373.82 -	373.82	116.34	09/2019 -	05/2020	8	0	
397	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MoRTH,ANDHRA PRADESH	03/2018	504.19 504.00	504.19	226.14	11/2018 05/2020	05/2020	18	0	
398	WAKAN PALI KHOPOLI - [N24001026]MoRTH,MAHARASHTRA	01/2017	376.19 376.19	376.19	34.03	05/2019 -	05/2020	12	0	
399	DEORI TO AMGAON - [N24001032]MoRTH,MAHARASHTRA	01/2017	409.62 410.00	409.62	181.78	05/2019 -	05/2020	12	0	
400	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA	05/2018	171.60 -	171.60	.86	05/2018 -	05/2020	24	0	
401	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM	08/2010	195.04 -	377.99	305.38	10/2010 -	06/2020	116	93.8	
402	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH	03/2018	166.21 -	166.21	40.28	08/2018 -	06/2020	22	0	
403	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]MoRTH,MADHYA PRADESH	03/2018	191.21 -	191.21	72.02	11/2019 -	06/2020	7	0	

MoSPI OCMS

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
404	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH	01/2017	205.05 -	205.05	79.65	03/2017 -	06/2020	39	0	
405	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH	03/2018	214.69 -	214.69	25.88	03/2018 -	06/2020	27	0	
406	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH	03/2018	217.22 -	217.22	45.76	08/2018 -	06/2020	22	0	
407	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA	10/2016	298.32 -	298.32	83.57	02/2019 -	06/2020	16	0	
408	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA	01/2017	391.06 391.00	391.06	107.00	06/2019 -	06/2020	12	0	
409	KARAD TO TAGAON - [N24001053]MoRTH,MAHARASHTRA	01/2017	537.81 538.00	537.81	89.97	06/2019 -	06/2020	12	0	
410	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MoRTH,MAHARASHTRA	02/2017	407.19 407.00	407.19	25.00	06/2019 -	06/2020	12	0	
411	MALEWADA TO CHIMUR - [N24001104]MoRTH,MAHARASHTRA	10/2016	322.55 -	322.55	156.91	06/2019 -	06/2020	12	0	
412	PARLI PIMPLA DAHIGUDA - [N24001138]MoRTH,MAHARASHTRA	02/2017	205.72 205.72	205.72	30.42	06/2019 -	06/2020	12	0	
413	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH	11/2017	392.33 -	392.33	242.88	03/2018 -	06/2020	27	0	
414	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH	02/2018	169.63 -	169.63	11.39	03/2018 -	07/2020	28	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
415	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]MoRTH,ANDHRA PRADESH	03/2016	995.09 995.00	995.09	410.28	05/2016 07/2020	07/2020	50	0	
416	MANGAON TO DIGHI PORT - [N24001024]MoRTH,MAHARASHTRA	01/2017	457.52 457.52	457.52	277.98	07/2019 -	07/2020	12	0	
417	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALAT JUNCTION) TO KM 420.800(P - [N24000963]MoRTH,ANDHRA PRADESH	01/2018	418.03 -	418.03	170.05	08/2018 08/2020	08/2020	24	0	
418	WADI TO ASOLA - [N24001022]MoRTH,MAHARASHTRA	01/2017	363.82 363.82	363.82	41.10	09/2019 -	09/2020	12	0	
419	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH	03/2016	877.79 -	877.79	436.12	06/2019 -	12/2020	18	0	
420	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB	10/2017	1,069.59 -	1,069.59	663.50	10/2019 12/2020	12/2020	14	0	
421	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MoRTH,ANDHRA PRADESH	10/2015	333.21 -	355.89	265.48	12/2015 01/2020	12/2020	60	6.81	
422	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]MoRTH,ANDHRA PRADESH	01/2017	263.45 -	263.45	59.79	09/2017 12/2020	12/2020	39	0	
423	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]MoRTH,BIHAR	05/2014	199.98 -	199.98	153.43	08/2016 -	12/2020	52	0	
424	BARASGAON TO RAHATEE - [N24001113]MoRTH,MAHARASHTRA	07/2016	289.11 290.00	289.11	23.82	09/2018 -	04/2021	31	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
425	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB	03/2018	170.57 192.48	170.57	46.23	11/2020 -	05/2021	6	0	
426	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA	02/2017	157.32 188.00	157.32	-	05/2019 -	05/2021	24	0	
427	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH,WEST BENGAL	03/2016	160.27 213.97	213.97	20.11	08/2019 -	08/2021	24	33.51	
428	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH,WEST BENGAL	06/2016	236.78 263.26	263.26	59.92	08/2019 -	08/2021	24	11.18	
	National Highways And Infrastructure Development Corporation Ltd.									
429	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 - [N24001184]NHIDCL,DELHI	07/2017	269.69 -	269.69	-	09/2019 -	12/2019	3	0	
430	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	155.00	75.99	01/2017 -	01/2020	36	11.57	
431	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH	03/2015	394.00 -	394.00	272.92	06/2018 -	03/2020	21	0	
432	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 339.55	396.52	235.52	08/2016 -	06/2020	46	0	
433	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM	05/2015	454.89 -	454.89	123.20	05/2018 05/2020	12/2020	31	0	

MoSPI OCMS

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
434	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH	02/2017	168.32 168.32	168.32	34.87	04/2017 02/2018	02/2021	46	0	
435	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 180.57	180.57	14.27	04/2017 02/2018	02/2021	46	0	
436	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH	02/2017	216.71 216.71	216.71	19.67	04/2017 02/2018	02/2021	46	0	
437	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 167.28	167.28	19.83	04/2017 02/2018	02/2021	46	0	
438	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH	03/2017	284.09 284.09	284.09	77.42	04/2017 03/2018	03/2021	47	0	
439	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM	01/2016	294.17 -	294.17	63.00	01/2016 02/2019	04/2021	63	0	
440	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL,MANIPUR	08/2017	517.57 -	457.77	137.04	10/2018 -	10/2021	36	-11.55	
441	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM	06/2015	437.39 -	437.39	9.30	06/2018 12/2020	12/2021	42	0	
442	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM	06/2015	463.49 -	463.49	22.32	06/2018 01/2021	12/2021	42	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
443	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM	01/2016	252.00 -	252.00	4.74	01/2016 12/2021	12/2021	71	0	
444	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH	01/2017	1,253.10 -	1,253.10	158.90	03/2017 -	03/2022	60	0	
	National Highways Authority Of India									
445	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 537.16	537.16	503.20	07/2018 -	11/2019	16	-6.46	
446	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	763.23	439.88	06/2019 -	11/2019	5	0	
447	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	2,016.00	1,996.00	04/2019 -	11/2019	7	0	
448	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	232.49	-	10/2017 -	11/2019	25	0	
449	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 3,787.21	1,509.10	3,684.44	09/2012 12/2019	12/2019	87	0	
450	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	946.00	818.53	06/2018 -	12/2019	18	0	
451	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	943.17	08/2012 -	12/2019	88	0	
452	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,401.00	03/2013 -	12/2019	81	0	
453	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	3,225.15	05/2014 12/2019	12/2019	67	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
454	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	1,364.18	03/2013 -	12/2019	81	0	
455	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	530.07	556.02	08/2016 -	12/2019	40	0	
456	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 -	1,083.00	1,487.87	06/2018 -	12/2019	18	0	
457	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 746.43	746.43	613.57	12/2017 06/2020	12/2019	24	66.88	
458	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 67.34	1,871.34	3,512.79	01/2018 12/2018	12/2019	23	0	
459	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	227.49	129.93	01/2019 -	12/2019	11	0	
460	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	244.90	251.87	05/2019 -	12/2019	7	0	
461	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	323.72	232.58	08/2018 -	01/2020	17	0	
462	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	248.97	236.19	05/2019 -	01/2020	8	0	TBRL Issue: 23.4875 Acres land is not available due to transfer of TBRL land in favour of NHAI. Letter written by NHAI HQ in Apr 2019 to MoRTH to take-up the case with MoD for waiver of land compensation of Rs 31 Cr and to hand over the possession of land. The proposal is pending with MoRTH/MOD.
463	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	639.97	331.84	10/2017 -	01/2020	27	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
464	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	478.00	315.11	10/2013 -	02/2020	76	-.11	
465	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	722.46	723.95	07/2018 12/2019	02/2020	19	19.25	
466	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	230.00	339.22	04/2008 -	03/2020	143	10.58	
467	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 364.59	364.59	215.58	12/2009 08/2020	03/2020	123	-39.64	
468	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	470.01	05/2010 -	03/2020	118	0	
469	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 2,967.50	2,967.50	3,990.72	11/2011 -	03/2020	100	167.82	
470	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	1,132.48	02/2013 -	03/2020	85	0	
471	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	850.24	07/2013 -	03/2020	80	0	
472	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 585.00	591.00	571.22	11/2013 12/2019	03/2020	76	15.53	
473	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	1,396.18	2,894.94	09/2014 -	03/2020	66	0	
474	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	597.00	587.64	10/2017 04/2018	03/2020	29	0	
475	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	972.50	3,512.79	07/2017 12/2019	03/2020	32	0	
476	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 1,302.98	934.46	531.34	03/2018 -	03/2020	24	0	
477	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 897.03	897.03	757.88	11/2018 07/2019	03/2020	16	-37	
478	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	1,388.00	1,185.00	08/2018 -	03/2020	19	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
479	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 598.13	598.13	414.73	04/2018 03/2020	03/2020	23	-17.69	The CALA, Raipur had submitted Proposal of additional 3A area for 12.6814 Ha (missing Khasra/plot no.) . 3A notification was published in Gazette on 04.07.2018 but CALA, Raipur did not provide revenue/ Khasra map to NHAI inspite of repeated request. In 680m length work was held up due to non-payment of land compensation to land owners, so NHAI has processed the 3D notification for 2.561Ha private land considering urgency at project site without revenue khasra map plan and balance 3D for area 10.1204 Ha was kept in hold due to non-receipt of Revenue Khasra map plan from CALA, Raipur. 3D of 2.561 Ha. land was published on 24.08.2018 . Inspite of repeated request to CALA, Raipur has not submitted revenue Khasra map plan showing 12.6814Ha land so the 3A notification dated 04.07.2018 balance area 10.1204Ha has lapsed on 03.07.2019. Some land owners (which land 3A was published on 04.07.2018 but 3D not published due to want of revenue Khasra map plan) have filed writ petition in Bilaspur High Court and Court passed order that land compensation should be paid to land owners within 09 months from the date of order after duly verification of land proposed in the acquisition. The land acquisition map showing RoW width for 25 villages are still not submitted by SDM Raipur & SDM Simga due to which 3A for balance 10.1204Ha of land could not be processed.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
480	CONSTRUCTION OF ROB – FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL	03/2016	229.37 -	229.37	110.52	11/2018 03/2020	03/2020	16	0	
481	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	707.82	375.47	08/2018 -	03/2020	19	0	
482	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 2,541.32	2,587.50	1,449.00	09/2019 03/2020	03/2020	6	86.37	
483	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 2,257.49	667.00	464.05	07/2018 -	04/2020	21	0	
484	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 3,007.86	667.00	549.07	06/2018 -	04/2020	22	0	
485	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	804.97	456.79	06/2018 -	04/2020	22	0	
486	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	756.27	181.12	03/2020 -	04/2020	1	.23	
487	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	244.27	168.40	09/2017 -	04/2020	31	0	
488	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,181.00	08/2013 -	05/2020	81	0	
489	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 414.00	414.00	532.46	05/2018 05/2020	05/2020	24	-.12	
490	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	923.04	764.07	11/2016 -	05/2020	42	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
491	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	641.17	369.23	07/2018 -	05/2020	22	0	
492	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 911.07	904.16	854.25	02/2020 11/2017	05/2020	3	0	
493	4-LANNING OF WARDHA-BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	1,065.51	1,005.76	03/2020 -	05/2020	2	3.4	
494	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 2,602.09	1,989.00	882.41	03/2020 11/2017	05/2020	2	0	
495	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	1,187.10	807.76	03/2020 -	05/2020	2	13.97	
496	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	641.17	369.23	07/2016 -	05/2020	46	0	
497	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,333.68	12/2013 -	06/2020	78	0	
498	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,159.10	03/2014 04/2017	06/2020	75	0	
499	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	2,945.00	2,467.00	04/2015 01/2017	06/2020	62	52.73	
500	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 41.54	636.24	461.85	05/2018 06/2020	06/2020	25	7.24	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
501	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 2,182.03	815.28	520.89	06/2018 -	06/2020	24	0	
502	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 2,433.38	1,027.53	601.13	06/2018 -	06/2020	24	0	
503	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	2,447.00	1,896.03	03/2020 06/2020	06/2020	3	18.5	
504	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	1,434.00	695.33	03/2020 -	06/2020	3	44.39	
505	4-LANNING OF THALSERRY - MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	1,232.76	292.23	09/2017 -	06/2020	33	9.67	
506	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	2,136.97	1,214.48	12/2018 -	07/2020	19	0	
507	FOUR LANNING OF RAMPUR-KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	899.00	561.27	04/2019 07/2020	07/2020	15	0	
508	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	1,177.00	657.59	03/2020 -	07/2020	4	41.54	
509	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	306.00	152.56	06/2017 -	07/2020	37	-52.8	
510	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	174.34	225.34	03/2008 -	08/2020	149	-28.84	
511	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	329.92	06/2013 01/2019	08/2020	86	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
512	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 870.00	870.00	265.48	03/2019 03/2017	08/2020	17	-25.48	Nil
513	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	1,310.00	563.15	03/2020 -	08/2020	5	10.58	
514	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 988.00	1,043.28	1,034.00	03/2020 -	08/2020	5	5.56	
515	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	1,160.64	1,056.76	03/2020 -	08/2020	5	5.7	
516	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	1,227.87	330.29	09/2017 -	08/2020	35	0	
517	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	2,864.02	07/2015 12/2019	09/2020	62	0	
518	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	727.00	509.85	05/2018 -	09/2020	28	36.88	
519	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	504.00	235.19	05/2018 04/2019	09/2020	28	-.2	
520	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	1,176.37	193.39	08/2017 -	09/2020	37	0	
521	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	2,898.25	06/2014 09/2017	10/2020	76	0	
522	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	976.79	07/2013 11/2020	11/2020	88	0	
523	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	701.40	29.48	03/2019 -	11/2020	20	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
524	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	870.00	36.30	03/2019 -	11/2020	20	0	
525	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	1,373.28	571.96	03/2020 -	11/2020	8	0	
526	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	1,071.00	582.87	03/2017 05/2018	11/2020	44	1.06	
527	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	964.17	390.91	10/2017 -	11/2020	37	0	
528	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020	52	0	
529	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	2,168.66	684.57	06/2019 -	12/2020	18	0	The Funds disbursement by the state government is very slow. 1040 trees are to be cut from the forest/state land.
530	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 247.00	322.09	77.53	04/2018 -	12/2020	32	0	
531	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	546.00	269.67	07/2019 12/2020	12/2020	17	0	
532	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	591.66	310.56	07/2019 12/2020	12/2020	17	0	
533	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 1,008.00	1,108.00	1,385.71	08/2019 -	12/2020	16	16.55	
534	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	990.61	397.89	09/2017 -	01/2021	40	0	Administrative assistance required for removal of Encroachments.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
535	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	400.25	64.89	03/2019 -	02/2021	23	0	
536	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	1,958.88	1,116.85	06/2020 02/2018	02/2021	8	0	
537	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,807.21	08/2013 -	03/2021	91	0	
538	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	2,510.04	313.18	08/2019 -	03/2021	19	0	
539	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	446.17	38.97	03/2019 -	03/2021	24	0	
540	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	1,420.00	446.76	03/2020 -	03/2021	12	10.24	
541	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	649.50	137.85	03/2019 04/2021	04/2021	25	0	
542	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH	03/2018	1,532.62 2,499.00	2,499.00	584.50	03/2021 -	04/2021	1	63.05	
543	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	227.77	11.00	03/2020 -	05/2021	14	-3.27	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
544	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	476.56	-	07/2017 11/2020	06/2021	47	0	
545	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 2,946.82	2,485.93	359.79	06/2020 -	09/2021	15	0	
546	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	950.64	102.51	08/2017 -	02/2022	54	0	
	Total		1,40,429.64 -	1,48,178.67	1,06,236.91					
	TELECOMMUNICATIONS									
	Bharat Sanchar Nigam Limited									
547	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]BSNL,MAHARASHTRA	01/2018	231.80 240.10	240.10	117.63	10/2018 12/2019	12/2019	14	3.58	
	Department Of Telecommunication									
548	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	24,664.00	12,146.00	07/2015 -	05/2020	58	84.97	
	Total		13,565.80 -	24,904.10	12,263.63					
	URBAN DEVELOPMENT									
	Ahmedabad Metro Rail									
549	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	10,773.00	6,296.85	12/2018 -	07/2020	19	0	
	Bangalore Metro Rail Corporation Limited									
550	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	26,405.14	499.85	02/2019 -	03/2020	13	0	
	Central Public Works Department									
551	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	205.00	165.95	03/2012 -	12/2019	93	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
552	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB	02/2014	388.00 -	488.28	440.59	05/2017 -	12/2019	31	25.85	
553	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD,PUNJAB	08/2016	294.00 -	294.00	208.99	04/2019 -	02/2020	10	0	
554	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	94.62	10/2012 -	03/2020	89	0	
555	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN	12/2016	549.31 559.47	559.47	373.45	07/2019 12/2019	04/2020	9	1.85	
556	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL	10/2014	162.88 179.10	162.88	144.06	04/2018 06/2020	06/2020	26	0	
557	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	209.00	150.71	10/2019 -	07/2020	9	0	
558	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2016	248.20 -	248.20	45.03	04/2018 02/2020	08/2020	28	0	
559	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI	10/2017	271.90 -	271.90	61.81	11/2019 08/2020	08/2020	9	0	
560	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	89.53	03/2016 -	09/2020	54	0	
561	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]CPWD,KARNATAKA	12/2016	246.31 -	246.31	80.34	02/2020 -	09/2020	7	0	
562	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR	02/2014	216.69 -	216.69	52.00	03/2015 -	10/2020	67	0	
563	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 -	197.33	61.47	04/2019 -	11/2020	19	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
564	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD,MAHARASHTRA	01/2018	223.37 -	223.37	42.19	07/2020 -	11/2020	4	0	
565	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]CPWD,PUNJAB	01/2018	430.00 -	430.00	97.92	05/2020 -	01/2021	8	0	
566	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	2,000.00	408.23	10/2019 -	03/2021	17	64.04	
567	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	498.99	97.67	06/2017 -	03/2021	45	.57	
568	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITIUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST - [N28000112]CPWD,KERALA	09/2017	150.29 -	150.29	21.82	03/2020 11/2020	03/2021	12	0	
569	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA	10/2016	209.84 -	209.84	58.75	03/2020 -	05/2021	14	0	
570	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD,ODISHA	01/2019	790.79 -	800.00	11.01	03/2022 -	06/2022	3	1.16	
	Chennai Metro Rail Ltd									
571	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	3,770.00	2,086.51	03/2018 06/2020	06/2020	27	0	
	Hindustan Steelwork Construction Limited									
572	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72	0	
	Kochi Metro Rail Corporation Ltd									
573	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 5,687.79	5,687.79	5,656.62	07/2017 -	03/2020	32	9.76	
	Maharastra Metro Rail Corporation Ltd.									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
574	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA	12/2016	11,420.00 -	11,420.00	3,372.86	11/2021 03/2022	03/2022	4	0	
	Mumbai Metro Rail Corporation Ltd									
575	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	05/2020	64	0	
	Nagpur Metro Rail Corporation Ltd									
576	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	8,680.00	6,405.74	03/2018 -	12/2019	21	0	
	Total		97,167.32 -	98,576.57	27,675.78					
	WATER RESOURCES									
	Polavaram Project Authority									
577	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA,ANDHRA PRADESH	02/2009	10,151.04 -	55,548.87	16,417.99	03/2020 -	06/2021	15	447.22	
	Total		10,151.04 -	55,548.87	16,417.99					
	HUMAN RESOURCE DEPARTMENT									
	Rail India Technical And Economic Service									
578	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES,MEGHALAYA	09/2013	484.32 -	626.26	-	09/2014 -	12/2020	75	29.31	
	Total		484.32 -	626.26	.00					
	Grand Total		9,01,882.21	11,52,697.20	6,17,252.32					

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Annexure - VII

(November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	ATOMIC ENERGY								
	Bhavini Limited								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044	09/2003	3,492.00 -	6,840.00	5,837.84	09/2010 -	10/2021	95.88	133
	Nuclear Power Corporation Of India Limited								
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010	10/2009	11,459.00 -	16,580.00	14,137.00	12/2015 -	06/2020	44.69	54
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027	10/2009	12,320.00 -	17,079.00	11,387.00	12/2016 -	12/2020	38.63	48
	Total		27,271.00 -	40,499.00	31,361.84				
	CIVIL AVIATION								
	Airport Authority Of India Limited								
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084	09/2015	338.93 -	339.00	213.50	06/2019 -	12/2019	.02	6
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073	10/2013	314.61 -	441.33	85.79	09/2018 -	06/2020	40.28	21
	Total		653.54 -	780.33	31,661.13				
	COAL								
	Eastern Coal Fields Limited								
6	RANIGANJ MASTER PLAN - [N06000163	08/2009	2,661.73 -	5,173.26	336.63	08/2019 -	08/2024	94.36	60
	Neyveli Lignite Corporation								
7	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095	06/2011	5,907.11 -	7,080.41	6,867.42	12/2015 -	12/2019	19.86	48
	Singareni Colliers Company Limitted								
8	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093	07/2011	162.76 -	349.28	7.49	03/2015 -	03/2021	114.60	72
9	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129	05/2015	397.09 -	442.42	99.42	03/2019 -	03/2020	11.42	12
10	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017	10/2006	249.03 -	448.86	296.17	03/2012 -	03/2024	80.24	144
11	JALAGAM VENGALA RAO OCP-II - [N06000094	07/2011	447.06 -	473.22	18.35	03/2015 -	03/2021	5.85	72
12	RAMAGUNDAM OC-II EXTENSION - [N06000078	12/2009	418.97 -	489.62	353.10	03/2012 -	03/2023	16.86	132

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	South-Eastern Coal Fields Limited								
13	JAGANNATHPOR OCP(3.00MTY) - [N06000075	09/2008	152.43 -	459.49	193.35	03/2015 -	03/2020	201.44	60
	Western Coal Fields Limited								
14	KAMPTEE DEEP OC MINE - [N06000141	11/2015	277.65 -	313.34	117.85	03/2021 -	03/2024	12.85	36
15	ADASA UG TO OC - [N06000133	08/2015	288.90 -	333.43	27.21	03/2023 -	03/2024	15.41	12
	Total		10,962.73 -	15,563.33	39,978.12				
	HEALTH AND FAMILY WELFARE								
	Hospital Services Consultancy Corporation Ltd								
16	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012	07/2016	152.95 -	177.92	139.70	02/2018 -	03/2020	16.33	25
17	AIIMS - MOTHER AND CHILD BLOCK - [N21000008	12/2013	204.44 -	270.00	204.70	05/2017 -	06/2020	32.07	37
18	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017	08/2017	272.19 -	272.54	191.86	03/2019 -	03/2020	.13	12
19	AIIMS - OPD(NEW) - [N21000009	08/2014	293.65 -	325.00	297.16	05/2017 -	01/2020	10.68	32
20	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003	02/2013	414.11 -	499.23	302.02	11/2013 -	09/2020	20.55	82
	Total		1,337.34 -	1,544.69	41,113.56				
	HUMAN RESOURCE DEPARTMENT								
	Rail India Technical And Economic Service								
21	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001	09/2013	484.32 -	626.26	-	09/2014 -	12/2020	29.31	75
	Total		484.32 -	626.26	41,113.56				
	PETROLEUM								
	Bharat Petroleum Corporation Limited								
22	HALDIA LPG IMPORT FACILITY - [N16000223	03/2015	694.00 -	1,097.54	722.99	10/2018 -	12/2019	58.15	14
23	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314	12/2015	1,112.00 -	1,507.24	555.00	06/2019 -	02/2022	35.54	32
24	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227	11/2014	4,588.29 -	5,245.96	3,877.61	08/2018 -	12/2019	14.33	16
	Gas Authority Of India Limited								

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
25	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285	06/2009	2,915.00 2,915.00	4,915.00	2,742.24	12/2012 -	02/2022	68.61	110
	Hindustan Petroleum Corporation Limited								
26	VISAKH REFINERY MODERNISATION PROJECT - [N16000235	07/2016	20,928.00 -	26,264.00	7,245.30	07/2020 -	07/2022	25.50	24
	Indian Oil Corporation Limited								
27	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253	05/2016	4,497.00 -	6,025.00	990.22	12/2018 -	02/2021	33.98	26
	Mangalore Refinery And Petrochemicals Limited								
28	SEA WATER DESALINATION PLANT - [N16000319	11/2017	581.00 -	621.00	102.99	03/2020 -	11/2020	6.88	8
	Oil & Natural Gas Corporation Limited								
29	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127	06/2010	202.94 -	345.92	155.61	01/2014 -	11/2019	70.45	70
30	DEVELOPMENT OF B-147 FIELD - [N16000292	02/2017	546.15 -	565.15	449.96	11/2019 -	03/2020	3.48	4
31	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128	03/2011	861.79 -	1,683.06	1,356.33	05/2013 -	12/2019	95.30	79
32	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131	12/2011	2,059.63 -	2,665.65	1,932.09	03/2015 -	12/2019	29.42	57
33	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213	12/2015	3,190.69 -	3,247.19	2,298.77	04/2018 -	05/2020	1.77	25
34	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359	02/2019	3,660.71 -	3,740.05	274.07	04/2021 -	05/2021	2.17	1
35	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297	02/2017	4,006.83 -	4,475.92	2,869.89	05/2021 -	12/2021	11.71	7
	Oil India Limited								
36	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167	07/2011	352.56 -	438.84	249.73	03/2017 -	06/2020	24.47	39
37	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331	01/2018	543.91 -	682.90	71.46	02/2020 -	06/2020	25.55	4
	Total		50,740.50 -	63,520.42	67,007.82				
	POWER								
	National Hydro-Electric Power Corporation								
38	PARBATI HEP (4X200 MW) (NHPC) II - [180100210	09/2002	3,919.59 -	9,997.11	7,715.06	09/2009 -	12/2021	155.06	147
	National Thermal Power Corporation								

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
39	RAMMAM-III HEPP (3X40 MW) - [N18000178	09/2014	1,381.84 -	1,592.34	502.87	09/2019 -	05/2024	15.23	56
40	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014	11/2006	2,978.48 -	5,867.38	4,264.84	03/2013 -	01/2021	96.99	94
41	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190	01/2007	5,353.00 -	9,583.00	7,981.46	07/2012 -	09/2020	79.02	98
42	TANDA TPP STAGE-II (2X660 MW) - [N18000175	09/2014	9,188.98 -	10,016.10	6,633.23	07/2019 -	07/2020	9.00	12
43	KHARGONE STPP STAGE I (1320 MW) - [N18000205	03/2015	9,870.51 -	11,148.86	9,055.78	01/2020 -	02/2020	12.95	1
44	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193	04/2012	9,750.89 -	12,176.28	10,032.00	02/2017 -	06/2020	24.87	40
45	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140	12/2012	11,846.00 -	12,739.82	12,839.84	10/2017 -	03/2020	7.55	29
46	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151	03/2013	11,638.55 -	12,865.92	12,361.29	01/2018 -	03/2020	10.55	26
47	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176	02/2014	12,532.44 -	13,740.53	9,944.45	12/2018 -	09/2020	9.64	21
48	NORTH KARANPURA STPP (3X660 MW) - [N18000177	02/2014	14,366.58 -	15,164.05	9,861.12	06/2019 -	03/2022	5.55	33
49	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192	01/2013	12,964.60 -	17,304.00	14,229.00	05/2018 -	06/2021	33.47	37
50	BARH STPP(3X660MW) NTPC - [180100242	02/2005	8,692.97 -	21,312.11	16,756.64	10/2011 -	08/2021	145.16	118
	Power Grid Corporation Of India Limited								
51	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182	01/2015	203.28 -	260.03	199.56	07/2017 -	11/2019	27.92	28
52	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164	05/2014	522.29 -	546.36	470.50	11/2016 -	03/2020	4.61	40
53	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109	10/2011	487.49 -	639.46	568.44	06/2014 -	12/2019	31.17	66
54	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155	10/2013	1,364.52 -	1,891.41	1,280.93	04/2016 -	12/2019	38.61	44
55	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061	10/2008	4,824.12 -	5,071.94	4,570.22	10/2012 -	03/2020	5.14	89
56	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250	12/2014	5,111.33 -	6,880.36	1,779.00	12/2018 -	12/2020	34.61	24
57	COMPREHENSIVE SCHEME FOR THE STRENGHTENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249	12/2014	4,754.42 -	9,072.36	1,352.46	12/2018 -	12/2020	90.82	24
58	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066	02/2009	11,130.19 -	14,719.10	12,816.90	08/2013 -	03/2022	32.24	103
	Thdc India Limited								

MoSPI OCMS

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(November 2019)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Antici Pated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
59	DHUKWAN SMALL HYDRO PROJECT - [N18000189	05/2011	195.42 -	294.60	321.11	02/2014 -	12/2019	50.75	70
60	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042	08/2008	2,491.58 -	4,397.80	1,823.10	06/2013 -	12/2022	76.51	114
61	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00 -	5,024.35	3,118.00	02/2016 -	06/2022	203.22	76
	Total		1,47,226.07 -	2,02,305.27	217,485.62				
	RAILWAYS								
	Central Railways								
62	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247	04/2011	184.06 -	312.00	275.98	03/2019 -	12/2019	69.51	9
63	KALYAN-KASARA 3RD LINE - [N22000233	04/2011	792.89 -	1,377.48	316.79	03/2021 -	03/2022	73.73	12
64	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181	02/1997	2,271.50 -	3,712.50	2,434.24	03/2021 -	03/2022	63.44	12
	Container Corporation Of India								
65	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431	08/2016	234.50 -	235.00	10.88	03/2019 -	12/2020	.21	21
	East Central Railways								
66	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	477.88 283.95	751.55	674.58	03/2012 -	03/2020	57.27	96
67	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181	04/2009	548.00 -	819.01	489.11	03/2020 -	03/2022	49.45	24
68	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240	04/1997	324.73 -	1,050.00	1,043.03	03/2012 -	03/2020	223.35	96
69	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473	04/2016	731.64 -	1,185.73	35.74	03/2021 -	03/2022	62.06	12
70	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472	04/2016	744.04 -	1,215.54	79.18	03/2021 -	03/2022	63.37	12
	East Coast Railway								
71	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319	03/2012	155.81 -	238.03	204.79	03/2020 -	03/2021	52.77	12
72	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380	04/2015	701.61 -	810.02	129.40	11/2018 -	03/2022	15.45	40
73	KIRANDUL - JAGDALPUR DOUBLING - [N22000318	12/2012	1,160.00 -	1,160.83	699.40	03/2020 -	03/2023	.07	36
74	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	1,111.99 -	1,539.28	937.49	02/2019 -	03/2022	38.43	37
75	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	810.78 -	1,928.07	770.82	06/2021 -	06/2024	137.80	36

MoSPI OCMS

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
76	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	2,923.13 -	3,791.66	1,243.45	03/2009 -	06/2024	29.71	183
	Eastern Railways								
77	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	12.02	108
78	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240	04/2010	494.54 -	494.59	32.00	03/2005 -	03/2025	.01	240
79	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216	04/1987	406.99 -	545.70	148.48	03/2006 -	03/2025	34.08	228
80	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243	04/2009	499.96 -	680.68	159.45	02/2012 -	03/2025	36.15	157
81	HANSDIHA-GODDA NL - [N22000236	04/2011	542.18 -	693.80	458.91	03/2020 -	03/2021	27.96	12
82	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225	04/2005	595.51 -	769.40	103.08	03/2017 -	03/2025	29.20	96
83	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224	04/2001	923.52 -	995.10	501.00	03/2016 -	03/2025	7.75	108
84	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	607.09 -	1,425.44	637.54	02/2013 -	03/2024	134.80	133
85	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	1,188.91 -	1,619.48	871.86	03/2019 12/2009	03/2025	36.22	72
86	PIRPAINTI-JASIDIH - [N22000219	04/2013	915.98 -	2,137.81	297.68	03/2022 -	03/2025	133.39	36
	Indian Railway Construction Company Limited								
87	GEVRA ROAD PENDRA ROAD - [N22000488	02/2014	2,288.00 -	4,970.11	628.61	03/2022 -	12/2022	117.23	9
	Metropolitan Rapid Transport Projects								
88	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	2,980.41	1,431.38	03/2004 -	03/2021	501.57	204
89	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	75.91	63
	North Central Railway								
90	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	04/2011	2,912.96 -	3,845.60	148.26	03/2022 -	12/2024	32.02	33
	North East Frontier Railway								
91	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135	04/1983	297.32 -	614.00	275.07	03/2019 -	03/2020	106.51	12
92	AGARTALA-AKHAURA NL - [N22000195	04/2012	569.63 -	670.00	107.83	03/2020 -	09/2021	17.62	18

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
93	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210	04/2011	314.00 -	728.00	727.55	03/2019 -	03/2020	131.85	12
94	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	385.20 -	1,532.00	642.09	03/2019 -	03/2020	297.72	12
95	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087	09/2006	532.87 -	2,145.00	935.60	03/2019 -	03/2020	302.54	12
96	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	1,180.19 -	4,541.00	3,344.19	12/2008 -	03/2021	284.77	147
97	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124	04/2006	2,326.52 -	4,600.00	842.42	03/2015 -	10/2021	97.72	79
98	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	2,393.47 -	5,021.45	3,131.89	03/2014 -	03/2022	109.80	96
99	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	4,454.17 -	12,524.00	9,541.58	03/2011 -	03/2022	181.17	132
	North Eastern Railway								
100	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456	04/2016	213.00 -	213.35	9.62	04/2016 -	06/2020	.16	50
101	CHHAPRA-BALLIA UP - [N22000134	03/2013	295.00 -	477.31	336.89	01/2019 -	01/2020	61.80	12
	North Western Railway								
102	THIYAT HAMIRA-SANU - [N22000149	04/2013	236.93 -	294.90	226.61	10/2018 -	12/2019	24.47	14
103	AJMER-BANGURGRAM - [N22000155	04/2011	213.39 -	303.56	274.18	11/2019 -	05/2020	42.26	6
104	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137	04/2012	246.08 -	348.55	229.00	12/2019 -	06/2020	41.64	6
105	ALWAR-BANDIKUI DOUBLING - [N22000157	04/2013	242.09 -	410.00	362.96	02/2019 -	03/2020	69.36	13
106	PHULERA - DIGANA DOUBLING - [N22000326	05/2015	600.00 -	685.99	74.80	03/2020 -	04/2022	14.33	25
107	DAUSA-GANGAPUR CITY(NL),NWR - [220100184	02/1997	410.08 -	886.41	559.84	02/2019 -	03/2021	116.16	25
	Northern Railway								
108	ROHTAK-MEHAM HANSI - [N22000272	04/2012	287.00 -	694.00	220.42	12/2011 -	03/2021	141.81	111
109	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492	03/2002	625.00 -	859.00	835.35	03/2016 -	03/2021	37.44	60
110	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	450.00 -	2,200.00	666.00	07/2012 -	03/2024	388.89	140
111	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	27,949.00	19,767.15	11/2002 -	06/2022	1,017.96	235
	Rail Vikas Nigam Ltd.								

MoSPI OCMS

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(November 2019)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Antici Pated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
112	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	385.00	387.92	03/2009 03/2009	06/2020	188.58	135
113	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213	04/2012	632.68 -	816.55	701.83	03/2016 -	12/2020	29.06	57
114	BANASPANI- JAKHPURA - DOUBLING - [N22000412	03/2009	942.95 -	1,120.00	1,028.76	03/2019 -	06/2022	18.78	39
115	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404	04/2011	927.01 -	1,200.00	1,178.67	03/2019 -	03/2020	29.45	12
116	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410	03/2006	948.04 -	1,500.00	1,374.96	03/2020 -	03/2021	58.22	12
117	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	1,185.64 -	1,844.47	1,829.53	12/2017 -	03/2020	55.57	27
118	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313	03/2012	1,503.71 -	2,200.00	1,722.18	03/2020 -	03/2022	46.30	24
119	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407	03/2009	713.48 -	2,300.00	2,056.99	03/2020 -	03/2021	222.36	12
120	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109	04/2010	2,298.42 -	2,733.86	40.13	03/2014 -	12/2025	18.95	141
121	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297	04/2010	2,127.00 -	2,900.00	1,737.30	03/2023 -	03/2024	36.34	12
122	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111	04/2010	2,913.51 -	4,639.00	855.74	03/2016 -	03/2025	59.22	108
123	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110	04/2010	3,951.98 -	4,724.30	2,278.26	03/2016 -	03/2025	19.54	108
	South Central Railway								
124	MUNEERABAD-MAHABOOBNAGAR(NL),SCR - [220100205	04/1997	1,723.00 1.00	1,780.09	1,478.40	03/2000 -	03/2021	3.31	252
125	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	1,045.20 -	2,120.16	524.57	03/2009 -	03/2023	102.85	168
126	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261	04/2012	1,856.95 -	2,200.00	290.92	03/2023 -	03/2024	18.47	12
127	NADIKUDE-SRI KALAHASTI - [N22000286	04/2011	2,288.70 -	2,643.25	810.35	03/2021 -	03/2024	15.49	36
	South East Central Railway								
128	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480	06/2018	229.00 -	852.50	39.69	12/2021 -	03/2023	272.27	15
129	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483	04/2008	872.00 -	1,226.51	1,062.76	12/2019 -	03/2020	40.65	3
130	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438	04/2010	585.93 -	1,268.32	669.57	02/2019 -	12/2020	116.46	22

MoSPI OCMS

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
131	ANUPPUR-KATNI - [N22000485	04/2015	1,370.00 -	1,370.94	311.76	12/2021 -	11/2022	.07	11
132	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	511.86 -	1,756.00	1,668.96	04/2020 -	01/2021	243.06	9
133	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484	04/2015	1,973.00 -	1,973.64	174.40	03/2021 -	03/2023	.03	24
	South Eastern Railway								
134	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165	04/2012	258.20 -	358.68	265.54	12/2018 -	06/2020	38.92	18
135	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	04/2012	148.77 -	377.00	182.63	12/2016 -	01/2020	153.41	37
136	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	54.99	120
137	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395	11/2015	969.83 -	1,312.96	562.50	03/2020 -	06/2020	35.38	3
138	BONDAMUNDA RANCHI DOUBLING - [N22000396	03/2016	1,724.20 -	1,993.24	411.64	03/2021 -	12/2021	15.60	9
139	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402	04/1998	1,027.40 -	2,373.00	485.04	03/2003 -	03/2030	130.97	324
	South Western Railway								
140	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486	03/1996	644.78 -	890.00	443.52	03/2017 -	03/2020	38.03	36
141	HOTGI-KUDGI-GADAG - [N22000333	03/2015	1,614.59 -	1,870.41	885.55	03/2019 -	03/2021	15.84	24
	Southern Railway								
142	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373	10/2013	187.26 -	231.67	162.06	04/2014 -	03/2020	23.72	71
143	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	303.98 -	980.00	681.66	03/2020 -	03/2021	222.39	12
144	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451	02/2015	760.00 -	1,182.31	446.00	03/2020 -	06/2021	55.57	15
145	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215	04/2011	120.70 -	1,800.00	187.30	03/2019 -	12/2019	1,391.30	9
146	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079	09/2007	724.69 -	2,072.50	1,440.83	02/2019 -	02/2020	185.98	12
	West Central Railway								
147	KATNI GRADE SEPARATOR/BYE PASS - [N22000416	08/2016	582.13 -	1,247.64	152.01	03/2022 -	09/2022	114.32	6
148	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	04/2001	424.60 -	2,909.99	1,975.34	03/2021 -	03/2023	585.35	24
149	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	8,248.50	1,986.78	05/2008 -	03/2023	3,230.57	178

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	Western Railway								
150	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123	04/2008	318.24 -	321.62	125.76	03/2012 -	03/2022	1.06	120
151	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487	02/1991	551.51 -	809.07	641.51	03/2019 -	03/2020	46.70	12
152	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143	04/1994	320.66 -	858.96	534.00	03/2019 -	03/2022	167.87	36
153	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121	04/2008	829.74 -	1,310.23	1,450.40	03/2020 -	03/2021	57.91	12
154	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120	04/2008	3,503.69 -	3,975.22	1,758.23	03/2022 -	03/2023	13.46	12
	Total		95,636.86 -	1,97,579.52	318,263.54				
	ROAD TRANSPORT AND HIGHWAYS								
	Ministry Of Road Transport And Highways (State Pwds)								
155	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645	08/2013	171.96 172.00	172.00	88.30	06/2016 -	-	.02	41
156	WIDENING AND STRENFTHENING OF EXISITNG SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639	03/2014	191.50 192.00	192.00	136.19	05/2016 -	12/2019	.26	43
157	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885	03/2016	160.27 -	213.97	20.11	08/2019 -	08/2021	33.51	24
158	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887	06/2016	236.78 -	263.26	59.92	08/2019 -	08/2021	11.18	24
159	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314	01/2013	182.28 -	269.14	185.49	02/2013 -	12/2019	47.65	82
160	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874	03/2016	271.17 291.20	291.20	89.25	11/2018 -	11/2019	7.39	12
161	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	08/2010	186.96 -	305.61	275.06	09/2014 -	12/2019	63.46	63
162	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308	08/2010	193.69 -	327.92	254.24	10/2010 -	12/2019	69.30	110
163	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	290.12	09/2017 -	12/2019	36.24	27

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
164	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928	10/2015	333.21 -	355.89	265.48	12/2015 -	12/2020	6.81	60
165	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415	08/2010	195.04 -	377.99	305.38	10/2010 -	06/2020	93.80	116
166	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311	03/2012	207.03 -	389.45	291.55	05/2012 -	12/2019	88.11	91
167	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388	11/2013	497.05 -	881.05	544.84	05/2017 -	05/2020	77.26	36
168	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306	11/2010	624.41 -	992.67	853.82	03/2011 -	12/2019	58.98	105
	National Highways And Infrastructure Development Corporation Ltd.								
169	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676	12/2016	138.93 155.00	155.00	75.99	01/2017 -	01/2020	11.57	36
	National Highways Authority Of India								
170	NALBARI T BIJNI (AS-7) - [N24000048	12/2003	208.00 -	230.00	339.22	04/2008 -	03/2020	10.58	143
171	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188	05/2011	511.54 -	591.00	571.22	11/2013 -	03/2020	15.53	76
172	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441	10/2015	593.26 -	636.24	461.85	05/2018 -	06/2020	7.24	25
173	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638	11/2012	605.84 -	722.46	723.95	07/2018 -	02/2020	19.25	19
174	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435	10/2015	531.13 -	727.00	509.85	05/2018 -	09/2020	36.88	28
175	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503	10/2015	447.29 -	746.43	613.57	12/2017 -	12/2019	66.88	24
176	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 -	756.27	181.12	03/2020 -	04/2020	.23	1
177	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	03/2017	988.34 -	1,043.28	1,034.00	03/2020 -	08/2020	5.56	5
178	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	03/2017	1,030.44 -	1,065.51	1,005.76	03/2020 -	05/2020	3.40	2
179	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659	03/2017	1,059.73 -	1,071.00	582.87	03/2017 -	11/2020	1.06	44

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
180	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622	09/2016	950.69 -	1,108.00	1,385.71	08/2019 -	12/2020	16.55	16
181	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	03/2017	1,098.06 -	1,160.64	1,056.76	03/2020 -	08/2020	5.70	5
182	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	657.59	03/2020 -	07/2020	41.54	4
183	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 -	1,187.10	807.76	03/2020 -	05/2020	13.97	2
184	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704	09/2017	1,124.11 -	1,232.76	292.23	09/2017 -	06/2020	9.67	33
185	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 -	1,310.00	563.15	03/2020 -	08/2020	10.58	5
186	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	446.76	03/2020 -	03/2021	10.24	12
187	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	695.33	03/2020 -	06/2020	44.39	3
188	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 -	2,447.00	1,896.03	03/2020 -	06/2020	18.50	3
189	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807	03/2018	1,532.62 -	2,499.00	584.50	03/2021 -	04/2021	63.05	1
190	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600	08/2016	1,388.34 -	2,587.50	1,449.00	09/2019 -	03/2020	86.37	6
191	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224	10/2012	1,928.22 -	2,945.00	2,467.00	04/2015 -	06/2020	52.73	62
192	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,967.50	3,990.72	11/2011 -	03/2020	167.82	100
	Total		27,110.31 -	36,600.27	344,315.23				
	STEEL								
	National Mineral Development Corporation (Nmdc)								
193	NMDC INTEGRATED STEEL PLANT - [N12000086	01/2010	15,525.00 -	23,140.00	16,244.05	05/2015 -	07/2020	49.05	62
	Total		15,525.00 -	23,140.00	360,559.28				
	TELECOMMUNICATIONS								
	Bharat Sanchar Nigam Limited								

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
194	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113	01/2018	231.80 -	240.10	117.63	10/2018 -	12/2019	3.58	14
	Department Of Telecommunication								
195	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 -	24,664.00	12,146.00	07/2015 -	05/2020	84.97	58
	Total		13,565.80 -	24,904.10	372,822.91				
	URBAN DEVELOPMENT								
	Central Public Works Department								
196	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088	02/2014	388.00 -	488.28	440.59	05/2017 -	12/2019	25.85	31
197	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100	02/2016	496.18 496.00	498.99	97.67	06/2017 -	03/2021	.57	45
198	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119	12/2016	549.31 -	559.47	373.45	07/2019 -	04/2020	1.85	9
199	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126	01/2019	790.79 -	800.00	11.01	03/2022 -	06/2022	1.16	3
200	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	2,000.00	408.23	10/2019 -	03/2021	64.04	17
	Kochi Metro Rail Corporation Ltd								
201	KOCHI METRO RAIL PROJECT - [N28000081	07/2012	5,181.79 -	5,687.79	5,656.62	07/2017 -	03/2020	9.77	32
	Total		8,625.28 -	10,034.53	379,810.48				
	WATER RESOURCES								
	Polavaram Project Authority								
202	POLAVARAM IRRIGATION PROJECT - [N30000002	02/2009	10,151.04 -	55,548.87	16,417.99	03/2020 -	06/2021	447.22	15
	Total		10,151.04 -	55,548.87	396,228.47				
	Grand Total		4,09,289.79	6,72,646.59	396,228.47				

MoSPI OCMS

Details of Projects Without Date of Commissioning

Annexure - VIII

Costing Rs. 150 Crore and above					(November 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	COAL				
	Bharat Coking Coal Limited				
1	MURAIDIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	04/2014 -	-
2	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND	08/2011	988.35 -	04/2017 -	-
	Neyveli Lignite Corporation				
3	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN	03/2015	522.45 -	09/2019 -	-
4	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU	04/2013	1,458.17 709.06	06/2015 -	-
	Singareni Colliers Company Limitted				
5	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	12/2012 -	-
6	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	03/2012 -	-
	Western Coal Fields Limited				
7	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA	05/2015	295.56 -	03/2019 -	-
8	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA	02/2016	198.68 -	03/2019 -	-
9	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA	02/2016	304.52 -	03/2019 -	-
10	GAURI DEEP OC - [N06000181]WCL,MAHARASHTRA	10/2016	164.96 -	03/2019 -	-
	Total		4,907.39 -		
	FERTILISERS				
	Rashtriya Chemical & Fertiliser Limited				
11	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 -	11/2016 -	09/2019
	Total		197.79 -		
	INFORMATION AND BROADCASTING				
	National Film Archive Of India				
12	NATIONAL FILM HERITAGE MISSION - [N09000001]NFAI,MAHARASHTRA	11/2014	597.41 -	- -	-
	Total		597.41 -		

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Anticipated
1	2	3	4	5	6
	PETROLEUM				
	Chennai Petroleum Corporation Limited				
13	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	03/2013	3,110.36 -	11/2015 -	-
	Hindustan Petroleum Corporation Limited				
14	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN	11/2011	310.00 -	03/2013 -	-
	Indian Oil Corporation Limited				
15	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 -	10/2017 -	-
16	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	09/2017 -	-
17	120 TMTPA LPG BOTTLING PLANT AT GORAKHPUR UP - [N16000354]IOCL,UTTAR PRADESH	03/2014	204.00 -	09/2019 -	-
	Indian Strategic Petroleum Reserves Ltd				
18	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KARNATAKA	01/2006	993.00 -	01/2012 -	-
	Mangalore Refinery And Petrochemicals Limited				
19	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]MANGALORE REFIN,KARNATAKA	10/2015	135.00 170.70	03/2019 10/2019	10/2019
20	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]MANGALORE REFIN,KARNATAKA	05/2015	224.00 207.00	04/2019 -	-
	Oil & Natural Gas Corporation Limited				
21	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 5,842.31	05/2019 10/2019	10/2019
	Oil India Limited				
22	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE	11/2015	500.00 -	06/2017 -	-
23	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM	07/2011	350.00 -	01/2019 -	-
24	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	03/2015 -	-
	Total		16,540.85 -		
	POWER				
	National Hydro-Electric Power Corporation				
25	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR	12/1999	578.62 -	06/2006 -	-
26	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-
	National Thermal Power Corporation				
27	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	09/2016 -	-
28	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Anticipated
1	2	3	4	5	6
29	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 -	-
	North East Electric Power Corporation				
30	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 7,927.34	12/2009 10/2019	10/2019
	Power Grid Corporation Of India Limited				
31	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 -	11/2008 -	-
	Total		24,826.57 -		
	HEALTH AND FAMILY WELFARE				
	Hospital Services Consultancy Corporation Ltd				
32	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00 -	09/2018 -	05/2019
33	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL	12/2014	168.90 -	05/2017 -	07/2019
34	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA	09/2014	505.58 -	03/2018 -	09/2019
	Total		918.48 -		
	RAILWAYS				
	Central Railways				
35	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	03/2024 -	-
	Container Corporation Of India				
36	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	-
37	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00 -	03/2018 -	-
	Dedicated Freight Corridor Corporation Of India Ltd				
38	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 30,357.00	- -	-
	East Central Railways				
39	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR	04/1998	180.82 726.31	- -	10/2019
40	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-
41	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 546.71	07/2014 -	-
42	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR	04/2008	633.87 -	- -	-
43	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-
44	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR	04/2008	445.25 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Anticipated
1	2	3	4	5	6
45	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE	04/2008	415.67 -	- -	-
46	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-
47	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
48	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
49	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
50	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
	Eastern Railways				
51	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	05/2019
	Kolkata Metro Rail Corporation Limited				
52	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL,WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-
	Metropolitan Rapid Transport Projects				
53	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-
54	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	06/2013 -	-
55	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	04/2016 -	-
	North Central Railway				
56	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-
57	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	2,030.50 -	- -	-
	North East Frontier Railway				
58	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	12/2015 -	-
59	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 -	03/2019 -	-
60	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE	04/1999	819.23 -	- -	-
61	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]NFR,WEST BENGAL	02/1999	380.60 -	04/2010 -	-
	North Eastern Railway				
62	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-
63	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-

MoSPI OCMS

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Anticipated
1	2	3	4	5	6
64	KAPILVASTU-BASTI VIA BANSI SIDHARTHNAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
65	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
66	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-
67	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50 -	- -	-
	North Western Railway				
68	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
69	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
70	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
71	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
	Rail India Technical And Economic Service				
72	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-
	Railway Electrification				
73	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-
	South Central Railway				
74	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	164.36 -	02/2009 -	-
75	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	458.25 458.25	- -	-
76	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 2,911.84	- -	-
77	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 2,184.83	- -	-
78	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	761.37 761.37	- -	-
79	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 829.00	- -	-
80	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 3,873.07	- -	-
	South Eastern Railway				
81	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-
82	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-
	Southern Railway				
83	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 -	- -	-
84	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40 -	- -	-

MoSPI OCMS

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Anticipated
1	2	3	4	5	6
85	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	- -	-
86	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	151.84 -	02/2019 -	-
87	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-
88	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
89	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-
90	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-
91	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
92	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
93	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
94	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 -	- -	-
95	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-
96	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	03/2005 -	-
97	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-
98	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU	02/1999	257.00 257.00	03/2018 -	-
	Western Railway				
99	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 03/2017	03/2017
100	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-
101	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-
102	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-
103	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-
104	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-
	Total		57,582.58 -		
	ROAD TRANSPORT AND HIGHWAYS				

MoSPI OCMS

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Anticipated
1	2	3	4	5	6
	Ministry Of Road Transport And Highways (State Pwds)				
105	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224]MoRTH,CHHATISGARH	03/2017	423.79 -	01/2018 -	01/2018
106	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226]MoRTH,CHHATISGARH	12/2014	496.02 -	03/2015 -	03/2015
107	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATISGARH	11/2015	335.32 -	06/2017 -	06/2017
108	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH,CHHATISGARH	03/2016	452.94 -	07/2016 -	07/2016
109	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH,CHHATISGARH	01/2016	497.14 -	08/2016 -	08/2016
110	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]MoRTH,CHHATISGARH	01/2016	476.20 544.00	09/2016 -	09/2016
111	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 127.500 TO 178.944 DARRIGHAT TO BANARI SECTION - [N24001220]MoRTH,CHHATISGARH	03/2016	491.52 -	09/2016 -	09/2016
112	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA	03/2015	153.21 -	01/2017 -	09/2019
113	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND	11/2016	336.25 -	09/2019 -	09/2019
114	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATISGARH	01/2016	624.98 -	10/2016 -	10/2016
115	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH,TELANGANA	01/2017	605.08 -	10/2019 -	10/2019
116	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221 - [N24001223]MoRTH,CHANDIGARH	03/2010	179.89 271.00	03/2013 -	03/2013
117	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229]MoRTH,CHHATISGARH	12/2014	379.16 -	11/2017 -	11/2017
118	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1 - [N24001225]MoRTH,CHANDIGARH	12/2010	169.26 299.00	01/2019 -	01/2019
119	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O - [N24000871]MoRTH,WEST BENGAL	08/2014	600.87 720.97	11/2017 05/2019	05/2019
120	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH,CHHATISGARH	11/2017	188.80 -	05/2019 -	05/2019
121	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873]MoRTH,WEST BENGAL	08/2014	823.20 937.76	11/2017 06/2019	06/2019

MoSPI OCMS

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)	
				Original / Revised	Anticipated
1	2	3	4	5	6
122	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH,WEST BENGAL	04/2014	279.70 398.52	08/2017 07/2019	07/2019
123	AJANTHA TO BULDHANA - [N24001008]MoRTH,A & N ISLANDS	02/2017	401.00 401.00	07/2019 -	07/2019
124	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]MoRTH,MAHARASHTRA	01/2017	486.19 486.19	07/2019 -	07/2019
125	PARTUR TO MAJALGAON - [N24001034]MoRTH,MAHARASHTRA	01/2017	420.57 420.57	07/2019 -	07/2019
126	MAJALGAON TO KAIJ - [N24001036]MoRTH,MAHARASHTRA	01/2017	413.99 -	07/2019 -	07/2019
127	KAIJ TO KUSALAM - [N24001037]MoRTH,MAHARASHTRA	01/2017	554.78 554.78	07/2019 -	07/2019
128	SHIROD SHAHPURER TO NANDED - [N24001041]MoRTH,MAHARASHTRA	01/2017	211.34 211.34	07/2019 -	07/2019
129	MUL TO CHANDRAPUR - [N24001117]MoRTH,MAHARASHTRA	12/2016	162.34 -	07/2019 -	07/2019
130	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2- - [N24001147]MoRTH,UTTAR PRADESH	10/2016	239.63 -	02/2019 -	07/2019
131	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]MoRTH,MADHYA PRADESH	09/2016	178.23 -	09/2018 -	08/2019
132	KATOL TO WARUD - [N24001019]MoRTH,MAHARASHTRA	01/2017	463.62 664.00	06/2019 -	08/2019
133	AMDI TO SAONER - [N24001021]MoRTH,MAHARASHTRA	01/2017	396.91 396.91	06/2019 -	08/2019
134	AHMADPUR TO PIMPLA - [N24001029]MoRTH,MAHARASHTRA	01/2017	422.38 422.38	08/2019 -	08/2019
135	PIMPLA TO MANJARSUMBHA - [N24001030]MoRTH,MAHARASHTRA	01/2017	595.77 595.77	08/2019 -	08/2019
136	MANJUSUMBA TO CHUMBALI - [N24001031]MoRTH,MAHARASHTRA	01/2017	228.54 228.54	08/2019 -	08/2019
137	AHMEDNAGAR TO BARAMATI - [N24001100]MoRTH,MAHARASHTRA	01/2017	955.40 -	08/2019 -	08/2019
138	NANDED TO JALKOT - [N24001069]MoRTH,MAHARASHTRA	12/2017	456.93 457.00	09/2019 -	09/2019
139	NASRATPUR TO BARASGAON - [N24001112]MoRTH,MAHARASHTRA	07/2016	406.54 406.54	09/2019 -	09/2019
140	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]MoRTH,UTTAR PRADESH	10/2016	176.94 177.00	10/2018 -	09/2019
141	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH	01/2012	410.72 -	04/2015 -	10/2019
142	CHIKALI TO KHAMGAON - [N24001012]MoRTH,MAHARASHTRA	02/2017	548.03 548.00	06/2019 -	10/2019
143	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]MoRTH,UTTAR PRADESH	11/2016	215.16 215.00	09/2019 -	10/2019

MoSPI OCMS

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)	
				Original / Revised	Anticipated
1	2	3	4	5	6
144	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MoRTH,UTTAR PRADESH	10/2013	445.89 653.00	03/2017 -	10/2019
145	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]MoRTH,TELANGANA	01/2014	270.00 -	03/2016 -	-
146	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDEAPAR BRIDGE - [N24000251]MoRTH,GOA	03/2015	297.00 -	04/2018 -	-
147	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]MoRTH,MAHARASHTRA	03/2015	168.30 -	- -	-
148	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]MoRTH,MAHARASHTRA	08/2014	187.79 -	07/2016 -	-
149	REHABILATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]MoRTH,MAHARASHTRA	01/2014	446.77 -	- -	-
150	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]MoRTH,GOA	03/2015	298.33 -	- -	-
151	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]MoRTH,GOA	03/2015	184.05 -	- -	-
152	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]MoRTH,GOA	03/2015	280.16 -	- -	-
153	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]MoRTH,ANDHRA PRADESH	07/2015	333.21 333.21	12/2015 -	-
154	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MoRTH,MAHARASHTRA	10/2015	289.60 -	- -	-
155	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MoRTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-
156	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]MoRTH,CHHATISGARH	12/2015	291.05 -	- -	-
157	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]MoRTH,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	-
158	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]MoRTH,CHHATISGARH	11/2015	485.44 -	12/2015 -	-
159	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MoRTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-
160	WIDENING AND STRENGHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MoRTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-
161	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MoRTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Anticipated
1	2	3	4	5	6
162	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MoRTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-
163	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MoRTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-
164	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]MoRTH,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	-
165	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]MoRTH,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-
166	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]MoRTH,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-
167	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]MoRTH,SIKKIM	04/2013	166.27 -	08/2013 -	-
168	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]MoRTH,NAGALAND	12/2010	1,296.00 -	02/2011 -	-
169	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MoRTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-
170	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MoRTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-
171	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- - [N24000318]MoRTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-
172	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-
173	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA	01/2015	225.81 -	- -	-
174	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MoRTH,RAJASTHAN	12/2015	621.43 -	06/2018 -	-
175	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-
176	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MoRTH,KARNATAKA	03/2015	159.12 -	11/2015 -	-
177	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]MoRTH,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	-
178	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]MoRTH,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	-
179	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]MoRTH,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)	
				Original / Revised	Anticipated
1	2	3	4	5	6
180	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MoRTH,KARNATAKA	01/1991	219.40 -	01/2018 -	-
181	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MoRTH,ODISHA	01/1991	218.63 -	10/2017 -	-
182	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR	01/1991	675.00 -	- -	-
183	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]MoRTH,PUNJAB	12/2015	766.36 -	- 09/2019	-
184	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]MoRTH,PUNJAB	11/2015	847.02 -	- 09/2019	-
185	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM	11/2010	268.08 -	05/2017 -	-
186	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]MoRTH,MADHYA PRADESH	08/2015	257.80 -	- -	-
187	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]MoRTH,ASSAM	11/2010	470.20 -	02/2011 -	-
188	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MoRTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	-
189	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MoRTH,BIHAR	01/1991	282.41 -	08/2016 -	-
190	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MoRTH,BIHAR	01/1991	358.22 -	10/2016 -	-
191	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]MoRTH,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-
192	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]MoRTH,ASSAM	11/2014	218.31 -	02/2018 -	-
193	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MoRTH,ODISHA	01/1991	229.41 -	05/2018 -	-
194	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]MoRTH,ODISHA	07/2014	342.05 -	01/2017 -	-
195	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA	10/2015	936.40 -	- -	-
196	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]MoRTH,RAJASTHAN	09/2012	511.00 -	10/2013 -	-
197	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]MoRTH,RAJASTHAN	09/2012	511.00 -	10/2013 -	-

MoSPI OCMS

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)	
				Original / Revised	Anticipated
1	2	3	4	5	6
198	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA	12/2015	773.98 -	- -	-
199	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH,GOA	12/2015	819.95 -	- -	-
200	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MoRTH,BIHAR	01/1991	478.35 -	- -	-
201	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]MoRTH,ODISHA	12/2011	159.39 -	11/2017 -	-
202	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]MoRTH,PUNJAB	06/2015	892.17 -	- -	-
203	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]MoRTH,BIHAR	01/1991	154.62 -	- -	-
204	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH,BIHAR	01/1991	319.68 -	- -	-
205	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MoRTH,BIHAR	10/2013	278.39 -	08/2014 -	-
206	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH,BIHAR	11/2013	683.83 -	07/2016 -	-
207	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MoRTH,BIHAR	02/2014	665.50 -	07/2016 -	-
208	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH,BIHAR	02/2016	178.85 -	05/2016 -	-
209	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MoRTH,BIHAR	02/2016	369.77 -	06/2016 -	-
210	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH,BIHAR	02/2016	553.30 -	05/2016 -	-
211	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-
212	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPR - [N24000580]MoRTH,BIHAR	03/2015	206.80 -	07/2016 -	-
213	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MoRTH,BIHAR	08/2015	288.24 -	11/2015 -	-
214	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA	03/2016	1,142.62 -	- -	-

MoSPI OCMS

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Anticipated
1	2	3	4	5	6
215	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA	03/2016	1,101.58 -	- -	-
216	REHABILIATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-
217	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MoRTH,ODISHA	01/2015	326.63 327.00	04/2018 -	-
218	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MoRTH,ODISHA	02/2015	239.91 240.00	10/2017 -	-
219	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MoRTH,ODISHA	07/2014	342.05 342.00	01/2017 -	-
220	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MoRTH,ODISHA	06/2016	157.30 157.00	06/2018 -	-
221	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH,UTTARAKHAND	02/2018	293.68 -	- -	-
222	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND	03/2018	460.73 -	- -	-
223	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH,WEST BENGAL	01/2017	396.86 396.86	09/2019 -	-
224	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH	11/2016	326.99 327.00	- -	-
225	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]MoRTH,WEST BENGAL	03/2017	202.69 202.69	11/2019 -	-
226	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH,WEST BENGAL	02/2018	426.18 426.18	09/2020 -	-
227	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH,WEST BENGAL	02/2018	218.70 218.70	11/2020 -	-
228	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]MoRTH,HARYANA	01/2017	276.01 -	03/2019 07/2019	-
229	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. - [N24000911]MoRTH,ODISHA	03/2016	165.06 -	12/2016 -	-
230	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA	08/2016	287.70 -	02/2017 -	-
231	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA	09/2016	295.67 -	02/2017 -	-
232	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA	12/2016	223.50 -	08/2018 -	-

MoSPI OCMS

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Anticipated
1	2	3	4	5	6
233	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA	12/2016	206.88 -	04/2018 -	-
234	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA	03/2018	214.23 -	08/2018 -	-
235	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA	03/2018	199.16 -	08/2018 -	-
236	WIDENING FROM TWO LANE TO FOUR LANE WITH PAVED SHOULDER AND STRENGTHNING OF EXISTING PAVEMENT BETWEE - [N24000920]MoRTH,GUJARAT	03/2016	223.67 -	02/2017 -	-
237	UPGRADATION TO 2 LANE WITH PAVED SHOULDER WITH RIGID PAVEMETS FROM 37/400 TO KM 66/700 ON NH 848 ON - [N24000921]MoRTH,GUJARAT	03/2016	208.34 -	02/2016 -	-
238	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]MoRTH,GUJARAT	12/2017	867.97 -	11/2018 -	-
239	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEE - [N24000923]MoRTH,GUJARAT	03/2018	464.07 -	11/2018 -	-
240	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPIR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]MoRTH,GUJARAT	10/2018	400.76 -	05/2019 -	-
241	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]MoRTH,GUJARAT	08/2017	962.43 -	03/2018 -	-
242	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR	09/2018	1,478.40 -	- -	-
243	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552-EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]MoRTH,RAJASTHAN	11/2017	187.82 -	04/2018 -	-
244	NETRA VILLAGE TO MANDORE SECTION OF NH-65 KM 267+500 TO 296+070 (4L) UNDER EPC. - [N24000951]MoRTH,RAJASTHAN	10/2014	382.81 -	01/2015 -	-
245	UP-GRADATION TO TWO LANE WITH PAVED SHOULDER FOR SECTION FROM KM 58.000 TO KM 91.600 (BALOTRA TO SAN - [N24000952]MoRTH,RAJASTHAN	01/2017	179.32 -	11/2017 -	-
246	CONSTRUCTION OF NAGAUR BYPASS FROM EXISTING KM 166/260 TO KM 180/500 OF NH-65 ON EPC MODE. - [N24000953]MoRTH,RAJASTHAN	03/2016	155.77 -	09/2016 -	-
247	NAGAUR-BIKANER OF NH-11 (2L+PS) UNDER PPP. - [N24000954]MoRTH,RAJASTHAN	01/2012	378.07 478.73	01/2014 -	-
248	CITTORGARH-NEEMACH (4L) OF NH-79 AND NIMBAHARA PRATAPGARH (2L+PS) OF NH-113 UNDER PPP. - [N24000955]MoRTH,RAJASTHAN	10/2012	511.21 -	10/2013 -	-
249	DEVELOPMENT AND OPERATION OF BIKANER- SURATGARH SECTION OF NH-15 BY 2L+PS IN THE STATE OF RAJASTHAN - [N24000956]MoRTH,RAJASTHAN	03/2009	501.00 671.54	09/2013 -	-
250	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]MoRTH,RAJASTHAN	11/2017	163.95 -	04/2018 -	-

MoSPI OCMS

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)	
				Original / Revised	Anticipated
1	2	3	4	5	6
251	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]MoRTH,RAJASTHAN	02/2018	370.30 -	06/2018 -	-
252	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]MoRTH,RAJASTHAN	02/2018	341.79 -	05/2018 -	-
253	CONSTRUCTION OF 4 LANING BY CC PAVEMENT ON KOTA-DARAH OF NH-12 FROM 256/550 TO 289/550 UNDER EPC. - [N24000960]MoRTH,RAJASTHAN	12/2015	621.43 -	10/2016 -	-
254	UP-GRADATION TO 2 LANE WITH PAVED SHOULDER FOR SECTION FROM KM 118.900 TO KM 156.955 BALOTRA TOSANDE - [N24000961]MoRTH,RAJASTHAN	01/2017	163.54 -	07/2017 -	-
255	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH,TELANGANA	01/2019	193.19 -	- -	-
256	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999]MoRTH,BIHAR	11/2016	230.34 -	10/2019 -	-
257	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR	03/2018	153.24 -	- -	-
258	SARSAM TO KOTHARI - [N24001002]MoRTH,MAHARASHTRA	02/2016	545.64 -	07/2019 -	-
259	AKOLA TO AKOT - [N24001003]MoRTH,MAHARASHTRA	01/2017	313.95 -	06/2019 -	-
260	AKOT TO ANJANGAON - [N24001006]MoRTH,MAHARASHTRA	01/2017	245.77 246.00	06/2019 -	-
261	ANJANGAON TO MAH/MP BORDER - [N24001007]MoRTH,MADHYA PRADESH	01/2017	359.00 359.00	06/2019 -	-
262	MEHKAR TO CHIKALI - [N24001011]MoRTH,MAHARASHTRA	02/2017	322.48 322.00	05/2019 -	-
263	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	-
264	DAHEGAON TO KUHI - [N24001017]MoRTH,MAHARASHTRA	01/2017	228.89 228.89	06/2019 -	-
265	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	-
266	JINTUR TO PARBHANI - [N24001039]MoRTH,MAHARASHTRA	01/2017	356.66 356.66	- -	-
267	KALMAB TO RALEGAON - [N24001044]MoRTH,MAHARASHTRA	01/2017	467.78 -	06/2019 -	-
268	RALEGAON TO RAMTIRTH - [N24001046]MoRTH,MAHARASHTRA	01/2017	210.81 -	07/2019 -	-
269	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	-
270	HELWAK TO KARAD - [N24001055]MoRTH,MAHARASHTRA	02/2017	416.99 -	07/2019 -	-
271	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA	02/2017	422.02 422.00	07/2019 -	-
272	BODHWAD TO STATE BORDER - [N24001086]MoRTH,MAHARASHTRA	01/2017	178.26 -	07/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)	
				Original / Revised	Anticipated
1	2	3	4	5	6
273	KOLDE TO KHETIYA - [N24001090]MoRTH,MAHARASHTRA	01/2017	509.18 -	07/2019 -	-
274	SATARA TO MHASWAD - [N24001092]MoRTH,MAHARASHTRA	01/2017	653.46 -	07/2019 -	-
275	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA	01/2017	388.44 -	- -	-
276	MHASWAD TO TEMBHURNI - [N24001099]MoRTH,MAHARASHTRA	01/2017	488.60 -	07/2019 -	-
277	KURUDWADI TO PANDHARPUR - [N24001101]MoRTH,MAHARASHTRA	01/2017	307.63 -	07/2019 -	-
278	PANDHARPUR TO SANGOLA - [N24001102]MoRTH,MAHARASHTRA	07/2017	218.38 -	07/2019 -	-
279	SARAD VANI PIMPALGAON - [N24001103]MoRTH,MAHARASHTRA	01/2017	250.46 -	07/2019 -	-
280	CHIMUR TO WARORA - [N24001105]MoRTH,MAHARASHTRA	11/2016	467.70 -	03/2019 -	-
281	GADCHIROLI TO MUL - [N24001116]MoRTH,MAHARASHTRA	12/2016	484.15 -	06/2019 -	-
282	NAGBHID TO ARMORI - [N24001119]MoRTH,MAHARASHTRA	09/2016	269.05 -	07/2019 -	-
283	PAITHAN TO SHIRUR - [N24001122]MoRTH,MAHARASHTRA	03/2017	341.80 -	06/2019 -	-
284	SHIRUR TO KHARDA - [N24001123]MoRTH,MAHARASHTRA	02/2017	381.77 -	06/2019 -	-
285	AURANGABAD TO SILLOD - [N24001124]MoRTH,MAHARASHTRA	02/2017	456.32 -	06/2019 -	-
286	SILLOD TO FARDAPUR - [N24001125]MoRTH,MAHARASHTRA	02/2017	337.46 -	06/2019 -	-
287	FARDAPUR TO JALGAON - [N24001126]MoRTH,MAHARASHTRA	02/2017	456.45 -	06/2019 -	-
288	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	-
289	BHOKAR TO SARSAM - [N24001128]MoRTH,MAHARASHTRA	02/2017	295.09 -	07/2019 -	-
290	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	-
291	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]MoRTH,UTTAR PRADESH	05/2013	164.54 165.00	08/2015 -	-
292	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT - [N24001154]MoRTH,KARNATAKA	08/2016	367.44 -	01/2017 -	-
293	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT - [N24001155]MoRTH,KARNATAKA	08/2016	175.20 -	01/2017 -	-
294	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA - [N24001156]MoRTH,KARNATAKA	01/2017	166.67 -	09/2017 -	-

MoSPI OCMS

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Anticipated
1	2	3	4	5	6
295	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA	08/2016	175.50 -	02/2017 -	-
296	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA	03/2018	159.97 -	06/2019 -	-
297	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]MoRTH,KARNATAKA	01/2018	159.70 -	07/2018 -	-
298	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA	09/2017	191.60 -	10/2018 -	-
299	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]MoRTH,KARNATAKA	12/2017	297.30 -	01/2019 -	-
300	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA	03/2018	325.86 -	10/2018 -	-
301	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA	08/2016	329.01 -	02/2017 -	-
302	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA	10/2016	396.96 -	03/2017 -	-
303	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA	11/2016	314.90 -	03/2017 -	-
304	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA	03/2015	159.12 -	01/2016 -	-
305	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776) - [N24001167]MoRTH,KARNATAKA	03/2015	165.67 -	01/2016 -	-
306	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM. - [N24001170]MoRTH,KARNATAKA	01/2014	471.16 -	08/2014 -	-
307	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA	01/2017	291.49 -	08/2017 -	-
308	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S - [N24001183]MoRTH,ANDHRA PRADESH	07/2014	251.55 -	02/2015 -	-
309	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MoRTH,RAJASTHAN	03/2019	178.13 -	- -	-
310	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR	02/2019	2,926.42 -	- -	-
311	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH	03/2018	306.59 -	- -	-

MoSPI OCMS

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Anticipated
1	2	3	4	5	6
312	IMPROVEMENT AND UP-GRADATION OF EXISITING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH	11/2018	281.45 -	- -	-
	National Highways And Infrastructure Development Corporation Ltd.				
313	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH	07/2015	197.16 197.16	10/2018 09/2015	09/2018
314	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH	10/2015	210.50 210.50	- 01/2016	01/2019
315	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH	03/2015	194.11 -	05/2018 -	08/2019
316	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 387.00	08/2016 -	08/2019
317	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 340.00	08/2016 -	08/2019
318	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM	04/2017	519.09 -	09/2019 -	09/2019
319	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM	04/2017	640.07 -	09/2019 -	09/2019
320	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM	04/2017	642.96 -	09/2019 -	09/2019
321	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM	04/2017	473.18 -	09/2019 -	09/2019
322	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM	04/2017	537.82 -	09/2019 -	09/2019
323	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM	04/2017	518.53 -	09/2019 -	09/2019
324	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM	04/2017	404.29 -	09/2019 -	09/2019
325	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM	04/2017	428.11 -	09/2019 -	09/2019
326	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH	04/2016	198.00 -	10/2016 -	10/2019
327	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM	06/2016	829.00 -	01/2019 -	-
328	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM	03/2015	168.39 -	11/2018 -	-

MoSPI OCMS

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)	
				Original / Revised	Anticipated
1	2	3	4	5	6
329	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM	10/2014	588.95 -	11/2018 -	-
330	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL,ARUNACHAL PRADESH	10/2015	179.82 -	01/2019 -	-
331	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA	10/2014	369.00 -	03/2018 12/2019	-
332	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM	12/2015	225.02 -	12/2018 -	-
333	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM	12/2015	223.30 -	06/2018 -	-
334	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-
335	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM	12/2015	289.99 -	12/2018 -	-
336	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROMKM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH	01/2016	183.65 -	11/2016 -	-
337	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-
338	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-
339	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-
340	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND	02/2017	507.68 -	04/2017 -	-
341	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-
342	RHENOK-RORAHTHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	-
343	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND	03/2018	274.31 -	05/2018 -	-
344	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND	03/2018	403.36 -	06/2018 -	-
345	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND	03/2018	417.24 -	05/2018 -	-
346	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS	03/2015	262.97 -	10/2018 -	-

MoSPI OCMS

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Anticipated
1	2	3	4	5	6
347	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS	03/2017	409.85 -	12/2017 -	-
348	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS	03/2015	277.17 -	04/2017 -	-
349	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS	02/2018	391.00 -	10/2018 -	-
350	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS	03/2018	234.27 -	10/2018 -	-
351	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND	02/2017	387.00 -	09/2018 -	-
352	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 -	09/2018 -	-
353	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND	03/2018	339.57 233.35	09/2018 07/2019	-
354	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND	03/2018	239.30 -	09/2018 05/2019	-
355	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND	03/2018	285.68 -	09/2018 -	-
356	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND	03/2018	315.03 -	09/2018 -	-
357	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND	03/2018	240.64 -	09/2018 -	-
358	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND	03/2018	237.72 136.73	09/2018 11/2018	-
359	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND	03/2018	251.97 160.10	09/2018 11/2018	-
360	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND	03/2018	282.98 -	09/2018 11/2018	-
361	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND	03/2018	215.12 -	09/2018 -	-
362	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND	03/2018	215.79 -	09/2018 -	-
363	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND	03/2018	272.89 -	09/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Anticipated
1	2	3	4	5	6
364	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND	03/2018	323.98 -	09/2018 -	-
365	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM	04/2017	318.42 -	11/2017 -	-
366	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM	03/2017	375.80 -	- -	-
367	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM	11/2017	290.05 -	11/2017 -	-
368	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM	03/2018	264.84 -	06/2018 -	-
369	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I - [N24000770]NHIDCL,WEST BENGAL	03/2017	158.65 -	06/2018 -	-
370	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM	03/2015	829.00 -	01/2016 -	-
371	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND	03/2018	1,383.78 -	07/2018 -	-
372	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR	03/2018	404.17 -	08/2018 -	-
373	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR	03/2018	216.00 -	11/2018 -	-
374	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR	03/2018	253.44 -	07/2019 -	-
375	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA	03/2019	306.28 -	05/2019 -	-
376	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH	12/2016	200.44 -	- -	-
377	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH	03/2017	1,718.59 -	- -	-
378	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM - [N24000947]NHIDCL,ARUNACHAL PRADESH	05/2016	259.52 -	- -	-
379	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92 -	- -	-
380	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH	12/2016	188.78 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Anticipated
1	2	3	4	5	6
381	BORDUMSA NAMCHIK (BURIDEHING - JAIRAMPUR) ROAD ON NH-52B (NEW NH-215) FROM KM. 0.15 (STARTING CHAIN - [N24000977]NHIDCL,ARUNACHAL PRADESH	07/2015	189.91 -	- -	-
382	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN - [N24000978]NHIDCL,ARUNACHAL PRADESH	03/2015	172.75 -	- -	-
383	TWO-LANING OF HAYULIANG– HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI - [N24000979]NHIDCL,ARUNACHAL PRADESH	01/2017	256.66 -	- -	-
384	OUR LANNNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM	03/2017	1,049.51 -	- -	-
	National Highways Authority Of India				
385	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 255.23	11/2008 01/2011	08/2013
386	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 408.77	11/2008 07/2011	01/2014
387	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- 06/2015	06/2015
388	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- 06/2015	06/2015
389	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	10/2017
390	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 03/2018	03/2018
391	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 08/2018	08/2018
392	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 655.17	07/2009 10/2018	10/2018
393	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	05/2019 -	02/2019
394	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	03/2019
395	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 315.00	- 03/2020	03/2019
396	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 04/2019	04/2019
397	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 -	06/2019
398	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	- -	06/2019
399	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 725.87	02/2019 -	06/2019
400	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 490.00	02/2009 07/2019	07/2019
401	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	04/2010 -	07/2019

MoSPI OCMS

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Anticipated
1	2	3	4	5	6
402	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	07/2019
403	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 340.14	04/2009 03/2011	08/2019
404	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 -	09/2019
405	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 1,544.00	09/2016 -	09/2019
406	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 -	06/2019 12/2016	09/2019
407	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	06/2019 -	09/2019
408	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	06/2019 -	09/2019
409	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 767.03	08/2018 -	09/2019
410	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT	12/2016	417.19 -	- -	09/2019
411	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	09/2019
412	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA	03/2017	296.19 -	03/2020 -	09/2019
413	TWO LANING WITH PAVED SHOULDER OF KARAUII - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 09/2014	10/2019
414	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 507.70	06/2016 -	10/2019
415	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	05/2018 10/2019	10/2019
416	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH	06/2015	1,583.79 -	01/2019 10/2019	10/2019
417	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	05/2018 03/2018	10/2019
418	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	04/2019 10/2017	10/2019
419	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	- 02/2016	10/2019
420	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN	08/2016	320.30 -	01/2019 -	10/2019
421	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 2,848.49	08/2011 -	-
422	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-
423	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-

MoSPI OCMS

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)	
				Original / Revised	Anticipated
1	2	3	4	5	6
424	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
425	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-
426	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-
427	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-
428	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	-
429	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	-
430	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-
431	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-
432	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-
433	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-
434	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	-
435	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	-
436	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHTH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	-
437	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	06/2015 -	-
438	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-
439	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 2,125.24	12/2015 -	-
440	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	02/2014 -	-
441	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-
442	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA	08/2015	723.54 1,286.84	02/2018 10/2017	-
443	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-
444	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	-
445	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	01/2016 -	-
446	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	-
447	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	05/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Anticipated
1	2	3	4	5	6
448	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	05/2019 -	-
449	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	04/2018 -	-
450	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	04/2019 -	-
451	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	01/2019 -	-
452	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-
453	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-
454	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	-
455	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	04/2019 -	-
456	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA	11/2015	867.66 1,464.24	05/2018 02/2018	-
457	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-
458	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-
459	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-
460	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- -	-
461	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	04/2018 -	-
462	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-
463	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 151.11	07/2018 -	-
464	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	04/2019 -	-
465	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	11/2018 -	-
466	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 3,267.94	- 03/2017	-
467	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	03/2019 -	-
468	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPU - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-
469	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	-

MoSPI OCMS

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Anticipated
1	2	3	4	5	6
470	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	- -	-
471	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	- -	-
472	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	- -	-
473	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	- -	-
474	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 241.41	- -	-
475	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	10/2018 -	-
476	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-
477	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-
478	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA	03/2017	639.79 -	03/2020 -	-
479	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 218.85	09/2017 -	-
480	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	- -	-
481	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-
482	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-
483	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-
484	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-
485	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-
486	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-
487	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 999.00	- 06/2019	-
488	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH	01/2018	960.24 -	- -	-

MoSPI OCMS

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Anticipated
1	2	3	4	5	6
489	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-
490	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	- -	-
491	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 929.89	- -	-
492	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-
493	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-
494	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-
495	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-
496	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 2,283.50	- 10/2019	-
497	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 1,065.70	- -	-
498	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 1,197.00	- -	-
499	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 -	- -	-
500	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN	02/2018	716.76 -	- -	-
501	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-
502	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 1,332.00	- -	-
503	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-
504	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-
505	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-
506	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-
507	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-

MoSPI OCMS

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Anticipated
1	2	3	4	5	6
508	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA	03/2018	950.63 -	- -	-
509	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA	03/2018	857.62 -	- -	-
510	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU	03/2018	633.55 -	- -	-
511	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96 -	- -	-
512	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	- -	-
513	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	-
514	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN	03/2018	874.25 -	- -	-
515	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN	03/2018	1,158.35 -	- -	-
516	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB	03/2018	199.90 149.90	- -	-
517	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH – 14 - [N24001185]NHAI,UTTAR PRADESH	11/2017	2,159.00 -	01/2019 -	-
518	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA	01/2019	1,051.91 -	- -	-
519	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA	01/2019	1,120.06 -	- -	-
520	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA	01/2019	1,137.42 -	- -	-
521	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA	01/2019	1,033.19 -	- -	-
522	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA	01/2019	1,243.45 -	- -	-
523	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA	01/2019	889.36 -	- -	-
524	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA	01/2019	1,018.79 -	- -	-
525	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA	01/2019	996.65 -	- -	-
526	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH	10/2019	743.88 -	- -	-

MoSPI OCMS

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Anticipated
1	2	3	4	5	6
527	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]NHAI,MADHYA PRADESH	12/2017	656.98 -	- -	-
528	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213]NHAI,MADHYA PRADESH	12/2017	1,094.97 -	- -	-
529	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]NHAI,MADHYA PRADESH	12/2017	217.96 -	- -	-
530	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 275.00	05/2017 -	-
531	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	-
532	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 1,444.25	- 02/2019	-
	Total		2,45,532.22 -		
	TELECOMMUNICATIONS				
	Indian Telephone Industry				
533	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE	09/2014	2,111.17 -	09/2014 -	-
	Mahanagar Telephone Nigam Limited				
534	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI	06/2016	418.26 -	06/2017 -	-
	Total		2,529.43 -		
	URBAN DEVELOPMENT				
	Central Public Works Department				
535	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	08/2016 -	-
536	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	11/2014 -	-
537	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84 -	03/2017 -	-
538	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	12/2015 -	-
539	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	12/2013 -	-
540	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]CPWD,DELHI	12/2017	188.00 -	06/2019 -	-
541	CONSTRACTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108]CPWD,ANDHRA PRADESH	01/2018	206.58 -	03/2019 -	-

MoSPI OCMS

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Anticipated
1	2	3	4	5	6
542	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI - [N28000123]CPWD,DELHI	07/2017	218.72 218.72	- -	-
543	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]CPWD,JAMMU AND KASHMIR	03/2019	329.00 -	- -	-
544	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]CPWD,JAMMU AND KASHMIR	01/2018	676.00 -	- -	-
	Chennai Metro Rail Ltd				
545	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 -	12/2015 -	-
	Delhi Metro Rail Corporation				
546	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	03/2016 -	-
	Hindustan Steelwork Construction Limited				
547	CONSTRUCTION AND MAINTEINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	-
548	CONSTRUCTION AND MAINTEINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016 -	-
549	CONSTRUCTION AND MAINTEINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	12/2016 -	-
550	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 -	-
551	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	-
552	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	09/2017 -	-
553	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	- -	-
554	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT	01/2013	175.00 -	- -	-
555	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	03/2017 -	-
556	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTEINANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	06/2016 -	-
557	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND	12/2007	200.00 -	03/2018 -	-
558	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	12/2016 -	-
559	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND	04/2013	170.00 -	04/2018 -	-
560	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL	08/2012	185.37 -	03/2016 -	-
	Jawahar Lal Nehru National Urban Renewal Mission				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Anticipated
1	2	3	4	5	6
561	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-
	Lucknow Metro Rail Corporation Limited				
562	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	-
	National Building Construcion Corporation Ltd				
563	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI	07/2016	2,694.00 -	- -	-
	Total		70,221.49 -		
	WATER RESOURCES				
	Uttar Pradesh Jal Nigam				
564	SEWERAGE WORKS IN SEWERAGE DISTRICT A OF ALLAHABAD - [N30000005]UPJalNigam,UTTAR PRADESH	02/2014	288.94 -	09/2019 -	09/2019
	Uttarakhand Pey Jal Nigam				
565	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI - [N30000003]UKJalNigam,UTTARAKHAND	03/2017	273.37 -	08/2019 -	08/2019
	Total		562.31 -		
	Grand Total		4,24,416.52		

MoSPI OCMS

Details of Projects Without Original Date of Commissioning

Annexure - IX

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	COAL								
	Singareni Colliers Company Limitted								
1	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL,TELANGANA	11/2016	272.73 -	272.73	162.62	- 04/2017	03/2020	35(R3)	1/6
2	RAMPURAM SHAFT BLOCK - [N06000174]SCCL,TELANGANA	08/2016	431.92 -	431.92	-	- 03/2023	-	-	0/9
3	SRAVANAPALLI OPENCAST PROJECT - [N06000175]SCCL,TELANGANA	02/2018	412.70 -	412.70	.11	- 03/2023	-	-	0/7
	Total		1,117.35 -	1,117.35	162.73				1/22
	PETROLEUM								
	Indian Oil Corporation Limited								
4	LPG BP PROJECT JODHPUR - [N16000318]IOCL,RAJASTHAN	03/2018	229.80 -	229.80	74.26	- -	03/2021	-	11/26
5	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT - [N16000336]IOCL,GUJARAT	03/2018	588.20 -	588.20	1.24	- -	08/2022	-	8/17
	Total		818.00 -	818.00	75.50				19/43
	HEALTH AND FAMILY WELFARE								
	Hospital Services Consultancy Corporation Ltd								
6	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84 -	268.84	157.76	- -	04/2020	-	0/0
7	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI	12/2017	156.56 -	156.65	76.53	- -	05/2020	-	0/0
8	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01 -	249.01	126.78	- -	05/2020	-	0/0
9	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA	03/2018	582.99 -	582.99	211.20	- -	06/2020	-	0/0
10	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH	03/2018	601.02 -	601.02	169.38	- -	07/2020	-	0/0
11	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL	04/2018	651.99 -	651.99	232.42	- -	07/2020	-	0/0
	Total		2,510.41 -	2,510.50	974.07				0/0
	RAILWAYS								
	East Central Railways								

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
12	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 367.17	425.17	423.55	- -	01/2020	-	0/1
13	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	1,033.07 3,020.95	3,376.00	3,328.43	- -	03/2021	-	0/0
14	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 1,625.87	1,625.87	544.36	- -	03/2021	-	0/0
15	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR	04/1999	325.00 735.20	735.20	363.83	- -	03/2021	-	0/0
16	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 1,470.50	1,470.50	824.49	- -	03/2021	-	0/0
17	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]ECR,BIHAR	04/1991	329.39 803.11	1,483.14	1,053.89	- -	12/2021	-	0/0
18	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 614.45	614.45	309.76	- -	03/2022	-	0/0
19	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR	04/2006	378.56 -	1,858.75	377.77	- -	03/2022	-	0/0
20	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 519.33	519.33	164.77	- -	02/2023	-	0/0
21	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 2,066.78	2,066.78	1,441.80	- -	03/2023	-	0/0
22	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17 1,605.17	1,605.17	23.49	- 03/2023	03/2023	0(R3)	0/0
23	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR	04/2008	326.20 -	2,995.01	1.94	- -	03/2024	-	0/0
24	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	228.05	1.53	- -	03/2024	-	0/0
	Eastern Railways								
25	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	393.00	393.00	- -	03/2020	-	0/0
26	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	251.18	251.18	- -	03/2021	-	0/0
27	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	272.20	177.61	- -	09/2021	-	0/0
28	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	310.70	275.20	- -	03/2024	-	0/0
29	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	1,261.34	-	- -	03/2025	-	0/0
30	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	260.10	10.73	- -	03/2025	-	0/0
31	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	174.56	71.42	- -	03/2025	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
32	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	250.55	20.12	- -	03/2025	-	0/0
33	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	527.54	1.76	- -	03/2025	-	0/0
34	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	298.22	52.09	- -	03/2025	-	0/0
35	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	336.96	70.20	- -	03/2025	-	0/0
36	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	166.89	.02	- -	03/2025	-	0/0
	Metropolitan Rapid Transport Projects								
37	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSHPUR - [N22000212]MRTP,WEST BENGAL	04/2009	573.78 -	268.52	.03	- -	03/2025	-	0/0
	North East Frontier Railway								
38	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	373.87	273.20	- -	06/2021	-	0/0
39	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	333.76 -	360.00	6.74	- 03/2022	03/2022	0(R3)	0/0
40	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 -	380.00	38.18	- 03/2022	03/2022	0(R3)	0/0
	Northern Railway								
41	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 346.63	346.63	233.23	- -	06/2020	-	0/0
42	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 791.39	791.39	517.05	- 03/2022	03/2022	0(R3)	0/0
43	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	295.68	92.91	- -	03/2023	-	0/0
44	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00 -	1,230.00	103.72	- -	03/2023	-	0/0
45	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	197.17	106.97	- 03/2024	03/2024	0(R3)	0/0
46	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	841.90	1.73	- -	03/2024	-	0/0
	Rail Vikas Nigam Ltd.								
47	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE	04/2007	2,062.30 2,062.30	2,062.30	903.96	- -	03/2025	-	2/2
	South East Central Railway								
48	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 1,473.76	1,413.76	1,351.73	- 01/2020	01/2020	0(R3)	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above									(November 2019)
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Antici Pated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	South Eastern Railway								
49	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	620.00	40.99	- 03/2025	03/2025	0(R3)	0/0
	South Western Railway								
50	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 1,801.01	1,801.01	48.41	- -	12/2023	-	0/0
51	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 692.43	692.43	-	- -	12/2023	-	0/0
52	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 466.65	466.65	-	- -	12/2023	-	0/0
53	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.85 348.85	348.85	.36	- -	12/2023	-	0/0
54	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 146.75	167.50	.34	- -	12/2023	-	0/0
55	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 367.77	367.77	-	- -	12/2023	-	0/0
56	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 -	2,315.00	149.76	- -	12/2024	-	0/0
	Southern Railway								
57	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	450.00	167.49	- -	03/2020	-	0/0
58	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	931.98 -	951.24	738.83	- -	03/2020	-	0/0
	Western Railway								
59	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10 844.10	844.10	107.52	- 03/2021	03/2021	0(R3)	0/0
	Total		23,987.95 -	41,092.43	15,066.09				2/3
	ROAD TRANSPORT AND HIGHWAYS								
	Ministry Of Road Transport And Highways (State Pwds)								
60	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH	06/2015	390.51 -	390.51	198.91	- -	03/2020	-	0/0
61	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH	11/2016	243.89 -	243.89	121.47	- -	09/2020	-	0/0
62	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB	11/2015	889.24 -	904.82	739.41	- 12/2019	-	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
63	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH	09/2011	1,979.00 -	1,979.00	1,143.00	- 03/2020	-	-	0/0
	National Highways And Infrastructure Development Corporation Ltd.								
64	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL,ASSAM	10/2017	818.00 -	818.00	62.91	- -	06/2020	-	0/4
65	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH	04/2016	245.79 -	245.79	105.26	- -	09/2020	-	2/4
66	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH	11/2015	434.06 -	434.06	133.38	- -	12/2020	-	2/4
67	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D - [N24000974]NHIDCL,ARUNACHAL PRADESH	02/2017	199.02 199.02	199.02	11.87	- 02/2018	02/2021	36(R3)	0/0
68	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D - [N24000975]NHIDCL,ARUNACHAL PRADESH	02/2017	184.88 184.88	184.88	97.50	- 02/2018	02/2021	36(R3)	0/0
69	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA	04/2017	553.51 -	553.51	32.78	- -	09/2021	-	0/4
70	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH	02/2017	175.06 175.06	175.06	14.08	- 04/2019	04/2022	36(R3)	0/0
71	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH	02/2017	176.12 176.12	176.12	14.79	- 04/2019	04/2022	36(R3)	0/0
	National Highways Authority Of India								
72	FOUR LANING WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	752.28	76.78	- -	11/2019	-	0/1
73	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 881.00	688.70	701.76	- 05/2017	11/2019	30(R3)	0/0
74	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 1,238.21	447.75	1,028.99	- -	11/2019	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
75	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	328.67	176.29	- -	11/2019	-	0/0
76	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 622.00	622.00	638.13	- -	12/2019	-	0/0
77	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 622.00	622.00	592.72	- -	12/2019	-	0/0
78	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	1,167.45	113.26	- -	12/2019	-	0/0
79	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	392.00	260.72	- -	12/2019	-	0/0
80	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	458.03	325.89	- 12/2017	12/2019	24(R3)	0/0
81	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL	10/2015	361.15 -	361.15	186.64	- -	01/2020	-	0/0
82	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	941.00	847.81	- -	01/2020	-	0/0
83	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	825.17	646.72	- 07/2017	01/2020	30(R3)	2/3
84	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	1,668.00	946.08	- -	01/2020	-	0/0
85	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	829.97	192.41	- -	01/2020	-	0/0
86	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB	03/2018	196.05 149.90	196.05	143.03	- -	01/2020	-	0/0
87	MEERUT-BULANDSHAHAR - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 868.77	987.94	727.69	- 10/2019	02/2020	4(R3)	0/1
88	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	1,443.00	1,246.85	- -	02/2020	-	0/0
89	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	1,244.10	1,394.00	- -	02/2020	-	0/0
90	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	479.00	453.80	- -	03/2020	-	0/0
91	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	1,069.65	526.12	- -	03/2020	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
92	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	379.90	112.41	- -	03/2020	-	0/0
93	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	557.30	208.96	- -	03/2020	-	0/0
94	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA	03/2018	275.12 -	275.12	129.75	- -	03/2020	-	0/0
95	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROMEXISTI - [N24000837]NHAI,HARYANA	03/2018	307.79 -	307.79	147.50	- -	03/2020	-	0/0
96	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	198.05	98.90	- -	03/2020	-	0/0
97	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA	03/2018	551.58 -	551.58	305.46	- -	03/2020	-	0/0
98	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	1,737.00	1,159.07	- -	04/2020	-	0/0
99	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 1,367.00	1,169.61	1,151.18	- -	04/2020	-	0/0
100	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	1,239.82	1,363.85	- -	05/2020	-	3/4
101	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	1,145.31	967.00	- -	05/2020	-	0/0
102	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 3,207.63	1,087.00	502.12	- 02/2018	05/2020	27(R3)	0/0
103	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	181.78	66.03	- -	06/2020	-	0/0
104	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	1,408.00	442.70	- -	07/2020	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
105	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 1,464.12	1,273.71	573.04	- -	07/2020	-	0/0
106	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	1,031.95	367.00	- -	08/2020	-	0/0
107	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 2,170.44	1,583.18	271.06	- -	09/2020	-	0/0
108	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN	02/2018	1,103.88 -	1,103.88	344.06	- -	09/2020	-	0/0
109	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	681.67	402.94	- 04/2018	10/2020	30(R3)	1/2
110	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	720.00	322.19	- 10/2020	10/2020	0(R3)	0/0
111	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 448.18	448.18	165.51	- -	10/2020	-	0/0
112	FOUR LANINIG OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	505.35	36.14	- -	11/2020	-	0/0
113	FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	628.71	106.92	- -	11/2020	-	0/0
114	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	291.53	46.60	- 11/2020	11/2020	0(R3)	0/0
115	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	289.21	27.87	- -	11/2020	-	0/0
116	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAUR ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	1,308.73	99.68	- -	12/2020	-	0/0
117	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	207.00	34.77	- 03/2020	12/2020	9(R3)	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
118	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	314.43	24.90	- -	12/2020	-	0/0
119	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA	03/2018	1,484.30 -	1,484.30	111.66	- -	12/2020	-	0/0
120	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	807.00	341.71	- -	12/2020	-	0/0
121	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	1,251.11	1,084.26	- -	01/2021	-	0/0
122	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR	12/2017	1,471.75 1,339.00	1,339.00	399.89	- -	01/2021	-	1/3
123	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76 -	207.00	92.25	- -	01/2021	-	0/0
124	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT	02/2018	1,052.21 1,449.00	1,449.00	336.43	- -	01/2021	-	0/0
125	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	2,043.00	-	- 05/2018	01/2021	32(R3)	0/0
126	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	1,166.26	163.29	- -	02/2021	-	0/0
127	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	565.09	167.77	- -	02/2021	-	0/0
128	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	1,282.94	255.43	- -	03/2021	-	0/0
129	REHABILITAITON AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	1,008.96	506.49	- -	03/2021	-	0/0
130	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 -	1,261.05	97.55	- 03/2021	03/2021	0(R3)	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
131	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 1,073.10	1,005.08	-	- 03/2019	03/2021	24(R3)	0/0
132	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00 565.02	621.00	327.15	- 10/2018	04/2021	30(R3)	2/3
133	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92 -	1,071.00	-	- -	04/2021	-	0/0
134	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 -	806.11	21.39	- -	04/2021	-	0/0
135	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 1,071.75	478.74	15.06	- -	05/2021	-	0/0
136	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	686.65	91.47	- 07/2020	06/2021	11(R3)	0/0
137	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	417.51	35.52	- -	06/2021	-	0/0
138	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	953.09	126.71	- 05/2020	06/2021	13(R3)	0/0
139	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	668.86	134.42	- 05/2020	06/2021	13(R3)	0/0
140	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	686.65	89.80	- 03/2020	06/2021	15(R3)	0/0
141	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	1,522.00	132.24	- 06/2021	06/2021	0(R3)	0/0
142	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	999.00	-	- -	06/2021	-	0/0
143	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	503.88	3.98	- -	06/2021	-	0/0
144	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	1,071.61	404.89	- -	07/2021	-	1/4

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
145	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	1,064.88	-	- -	07/2021	-	0/4
146	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	1,323.15	403.93	- -	07/2021	-	0/0
147	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 -	1,261.98	793.49	- -	07/2021	-	0/0
148	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	1,959.00	657.85	- -	07/2021	-	0/0
149	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	1,550.98	673.04	- -	07/2021	-	0/0
150	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 1,687.00	1,437.64	564.11	- 12/2018	07/2021	31(R3)	0/0
151	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 931.21	931.21	125.31	- -	07/2021	-	0/0
152	SIX LANING AND STREGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 -	799.30	115.56	- -	07/2021	-	0/0
153	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 -	1,162.92	14.76	- -	07/2021	-	0/0
154	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00 512.99	607.00	163.98	- 02/2019	08/2021	30(R3)	0/1
155	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	614.48	52.00	- -	08/2021	-	0/0
156	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	564.66	46.76	- -	08/2021	-	0/0
157	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 2,190.00	2,400.00	1,558.83	- 05/2019	11/2021	30(R3)	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above									(November 2019)
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Antici Pated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
158	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	1,117.84	-	- -	12/2021	-	0/0
159	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA	03/2018	828.29 998.89	828.29	-	- 11/2019	-	-	0/0
160	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT	03/2018	1,161.39 1,404.00	1,161.39	-	- 11/2021	-	-	0/0
	Total		85,798.77 -	86,594.97	33,487.64				14/42
	URBAN DEVELOPMENT								
	Central Public Works Department								
161	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 -	422.00	14.20	- -	12/2020	-	0/0
162	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 -	392.00	12.56	- 08/2020	03/2021	7(R3)	0/0
163	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU	11/2017	348.77 -	348.77	31.97	- -	11/2021	-	0/0
	Total		1,162.77 -	1,162.77	58.73				0/0
	Grand Total		1,15,395.25	1,33,296.02	49,824.76				36/110

Details of Projects Without Milestones w.r.t. Original Schedule

Annexure - X

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	CIVIL AVIATION					
	Airport Authority Of India Limited					
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI,TRIPURA	09/2015	338.93 -	06/2019 -	12/2019	0/0
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,A & N ISLANDS	10/2013	314.61 -	09/2018 -	06/2020	0/0
3	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085]AAI,UTTARAKHAND	07/2018	353.27 -	09/2020 -	09/2020	0/0
4	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI	11/2016	233.38 -	04/2020 -	12/2020	0/0
5	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA - [N04000080]AAI,WEST BENGAL	01/2016	219.91 -	03/2020 -	12/2020	0/0
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM	12/2016	859.86 -	03/2021 -	03/2021	0/0
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT - [N04000079]AAI,MAHARASHTRA	03/2017	358.89 -	04/2021 -	04/2021	0/0
8	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]AAI,UTTAR PRADESH	06/2018	1,383.00 -	09/2021 -	09/2021	0/0
9	CONSTRUCTION OF TERMINAL BUILDING & ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]AAI,JAMMU AND KASHMIR	07/2018	323.19 -	09/2021 -	09/2021	0/0
10	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI,TAMIL NADU	08/2018	951.28 -	10/2021 -	10/2021	0/0
11	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081]AAI,WEST BENGAL	01/2019	264.99 -	11/2021 -	11/2021	0/0
12	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI,TAMIL NADU	06/2018	2,467.00 -	02/2022 -	08/2022	0/0
13	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]AAI,BIHAR	05/2018	539.20 -	10/2022 -	10/2022	0/0
	COAL					
	Neyveli Lignite Corporation					
14	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN	03/2015	513.63 -	12/2019 -	12/2019	0/0
15	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH	07/2016	17,237.00 -	11/2021 -	11/2021	0/0
16	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN	03/2015	522.45 -	09/2019 -	-	0/0
	Western Coal Fields Limited					
17	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA	03/2017	362.73 -	03/2020 -	03/2020	0/0
18	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH	07/2016	409.87 -	03/2022 -	03/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	INFORMATION AND BROADCASTING					
	Central Public Works Department					
19	FILM AND TELEVISION INSTITUTE ARUNACHAL PRADESH - [N09000002]CPWD,ANDHRA PRADESH	11/2016	204.32 -	02/2019 -	11/2019	0/0
	National Building Construcion Corporation Ltd					
20	NATIONAL CENTRE OF EXCELLENCE FOR ANIMATION VISUAL EFFECTS GAMING AND COMICS - [N09000003]NBCC,MAHARASHTRA	12/2016	167.70 -	03/2020 -	03/2020	0/0
	National Film Archive Of India					
21	NATIONAL FILM HERITAGE MISSION - [N09000001]NFAI,MAHARASHTRA	11/2014	597.41 -	- -	-	0/0
	PETROLEUM					
	Bharat Petroleum Corporation Limited					
22	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 -	02/2017 -	10/2021	0/0
23	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 1,507.24	06/2019 02/2022	02/2022	0/0
24	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]BPCL,JHARKHAND	11/2018	248.55 -	06/2022 -	06/2022	0/0
25	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]BPCL,KERALA	09/2018	11,130.00 -	03/2023 -	03/2023	0/0
	Chennai Petroleum Corporation Limited					
26	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU	09/2017	1,858.00 -	12/2019 -	12/2019	0/0
27	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU	08/2017	421.00 -	08/2020 -	08/2020	0/0
	Gas Authority Of India Limited					
28	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA	02/2015	749.00 -	02/2020 -	02/2020	0/0
29	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA	07/2017	243.53 -	07/2022 -	07/2022	0/0
30	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]GAIL,ODISHA	07/2017	182.20 -	07/2022 -	07/2022	0/0
31	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL,BIHAR	10/2017	359.25 -	10/2022 -	10/2022	0/0
32	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR - [N16000330]GAIL,JHARKHAND	10/2017	221.45 -	10/2022 -	10/2022	0/0
	Hindustan Petroleum Corporation Limited					
33	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR-CHAMPA IN STATE OF CHHATTISGARH - [N16000311]HPCL,CHHATISGARH	12/2016	300.00 -	04/2021 -	04/2021	0/0
	Indian Oil Corporation Limited					
34	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	06/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
35	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00 -	06/2020 -	08/2020	0/0
36	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]IOCL,ANDHRA PRADESH	08/2017	384.58 -	04/2021 -	09/2020	0/0
37	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL,WEST BENGAL	04/2016	1,021.00 -	12/2020 -	12/2020	0/0
38	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI - [N16000276]IOCL,MAHARASHTRA	05/2016	261.00 -	01/2021 -	01/2021	0/0
39	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]IOCL,HARYANA	01/2019	909.00 -	01/2021 -	01/2021	0/0
40	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL,ANDHRA PRADESH	01/2015	342.00 -	03/2021 -	03/2021	0/0
41	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL,ANDHRA PRADESH	07/2014	247.00 -	03/2021 -	03/2021	0/0
42	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]IOCL,BIHAR	04/2018	522.00 -	03/2021 -	03/2021	0/0
43	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	01/2021 -	04/2021	0/0
44	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00 -	04/2021 -	07/2021	0/0
45	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	10/2020 -	08/2021	0/0
46	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]IOCL,ODISHA	11/2018	462.30 -	09/2021 -	09/2021	0/0
47	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	01/2021 -	10/2021	0/0
48	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL,ANDHRA PRADESH	10/2018	316.20 -	10/2021 -	10/2021	0/0
49	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]IOCL,HARYANA	08/2019	1,255.00 -	10/2021 -	10/2021	0/0
50	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	08/2021 -	11/2021	0/0
51	LAB REVAMP AT GUJARAT REFINERY - [N16000377]IOCL,GUJARAT	10/2019	403.00 -	12/2021 -	12/2021	0/0
52	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00 -	04/2022 -	04/2022	0/0
53	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]IOCL,ODISHA	06/2019	371.00 -	09/2022 -	09/2022	0/0
54	R and D CAMPUS II AT FARIDABAD - [N16000375]IOCL,HARYANA	06/2019	2,281.94 -	12/2022 -	12/2022	0/0
55	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	04/2022 -	02/2023	0/0
	Indian Strategic Petroleum Reserves Ltd					
56	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KARNATAKA	01/2006	993.00 -	01/2012 -	-	0/0
	Oil India Limited					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
57	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]OIL,ASSAM	06/2016	224.75 -	08/2020 -	08/2020	0/0
58	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE	11/2015	500.00 -	06/2017 -	-	0/0
59	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM	07/2011	350.00 -	01/2019 -	-	0/0
	POWER					
	National Hydro-Electric Power Corporation					
60	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR	12/1999	578.62 -	06/2006 -	-	0/0
61	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-	0/0
	National Thermal Power Corporation					
62	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH	09/2015	3,004.00 -	11/2019 -	11/2019	0/0
63	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA	05/2016	1,885.13 -	12/2018 -	03/2020	0/0
64	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL	12/2016	529.68 -	11/2018 -	03/2020	0/0
65	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]NTPC,UTTAR PRADESH	12/2018	587.44 -	09/2020 -	09/2020	0/0
66	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]NTPC,UTTAR PRADESH	03/2019	349.00 -	11/2020 -	11/2020	0/0
67	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 -	-	0/0
	Power Grid Corporation Of India Limited					
68	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA	04/2016	844.64 -	04/2019 04/2019	11/2019	0/0
69	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE	03/2017	283.72 -	11/2019 -	11/2019	0/0
70	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 374.63	04/2016 12/2017	12/2019	0/0
71	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 197.40	03/2018 -	12/2019	0/0
72	GREEN ENERGY CORRIDORS - INTER STATE TRANSSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	05/2019 -	12/2019	0/0
73	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE	09/2016	562.25 -	03/2019 -	12/2019	0/0
74	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE	10/2016	608.24 -	04/2019 -	12/2019	0/0
75	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE	03/2017	337.75 -	06/2019 -	12/2019	0/0
76	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE	12/2015	3,654.00 -	04/2019 -	12/2019	0/0
77	EASTERN REGION STRENGTHENNING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL	04/2016	454.11 -	04/2018 01/2020	01/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
78	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 -	01/2019 09/2019	01/2020	0/0
79	TRANSMISSION SYSTEM FOR EVACUTION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 -	07/2019 -	01/2020	0/0
80	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE	05/2016	14,733.37 -	11/2019 -	02/2020	0/0
81	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	02/2020 -	02/2020	0/0
82	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE	09/2017	198.49 -	09/2019 02/2020	02/2020	0/0
83	TRANSMISSION SYSTEM STRENTHENNING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	01/2018 03/2020	03/2020	0/0
84	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	02/2019 04/2020	03/2020	0/0
85	EASTERN REGION STRENTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	06/2019 -	03/2020	0/0
86	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 -	12/2019 -	03/2020	0/0
87	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT	05/2017	175.64 -	09/2018 03/2020	03/2020	0/0
88	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA	05/2017	445.89 -	02/2019 12/2019	03/2020	0/0
89	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT	12/2017	193.14 -	06/2019 03/2020	03/2020	0/0
90	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE	02/2017	5,070.13 -	04/2020 -	04/2020	0/0
91	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE	11/2017	358.83 -	05/2020 -	05/2020	0/0
92	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE	03/2017	3,500.00 3,500.00	07/2020 -	07/2020	0/0
93	COMPREHENSIVE SCHEME FOR THE STRENGHTENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	12/2018 -	12/2020	0/0
94	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	12/2018 -	12/2020	0/0
	Thdc India Limited					
95	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH	03/2019	11,089.42 -	09/2023 -	09/2023	0/0
	HEAVY INDUSTRY					
	Bharat Heavy Electricals Limited					
96	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI	08/2016	1,554.00 -	09/2019 -	03/2020	0/0
	HEALTH AND FAMILY WELFARE					
	HII Infra Tech Services Limited					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
97	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	04/2020 06/2020	10/2020	0/0
98	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	06/2020 08/2020	10/2020	0/0
99	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 -	05/2021 10/2021	10/2021	0/0
	Hospital Services Consultancy Corporation Ltd					
100	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00 -	09/2018 -	05/2019	0/0
101	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	03/2019 -	03/2020	0/0
102	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	03/2019 -	03/2020	0/0
103	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84 -	- -	04/2020	0/0
104	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI	12/2017	156.56 -	- -	05/2020	0/0
105	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01 -	- -	05/2020	0/0
106	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA	03/2018	582.99 -	- -	06/2020	0/0
107	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	05/2018 -	07/2020	0/0
108	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL	08/2017	355.15 -	03/2019 -	07/2020	0/0
109	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH	03/2018	601.02 -	- -	07/2020	0/0
110	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL	04/2018	651.99 -	- -	07/2020	0/0
111	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	09/2020	0/0
	National Building Construcion Corporation Ltd					
112	AIIMS BILASPUR - [N21000028]NBCC,HIMACHAL PRADESH	04/2018	1,351.00 1,471.00	09/2021 -	09/2021	0/0
	RAILWAYS					
	Central Railways					
113	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 199.12	03/2019 12/2019	12/2019	0/0
114	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	03/2021 -	03/2022	0/0
115	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 -	03/2021 -	03/2022	0/0
116	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	3,168.29 -	03/2023 -	03/2023	0/0
117	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	03/2022 -	03/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
118	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,449.91 -	03/2023 -	03/2023	0/0
119	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA	02/2015	3,627.47 3,627.00	03/2024 -	03/2023	0/0
120	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 -	03/2023 -	03/2023	0/0
121	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	03/2022 -	03/2024	0/0
122	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA	02/2016	9,968.00 -	03/2024 -	03/2024	0/0
123	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA	02/2016	2,425.00 -	03/2024 -	03/2024	0/0
124	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	03/2022 -	03/2024	0/0
125	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	03/2023 -	03/2024	0/0
126	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	03/2024 -	-	0/0
	Container Corporation Of India					
127	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	03/2019 -	12/2019	0/0
128	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	03/2019 -	12/2019	0/0
129	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	03/2019 -	02/2020	0/0
130	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	03/2018 -	03/2020	0/0
131	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	03/2019 -	03/2020	0/0
132	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	12/2020	0/0
133	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	-	0/0
134	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00 -	03/2018 -	-	0/0
	Dedicated Freight Corridor Corporation Of India Ltd					
135	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	03/2020	0/0
136	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 30,357.00	- -	-	0/0
	East Central Railways					
137	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR	04/1998	180.82 726.31	- -	10/2019	0/0
138	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	03/2019 -	12/2019	0/0
139	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 898.53	03/2012 -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
140	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	499.41 516.02	03/2020 -	03/2020	0/0
141	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88 751.55	03/2012 -	03/2020	0/0
142	GARHWA ROAD-RAMNA - [N22000465]ECR,JHARKHAND	03/2015	348.23 -	03/2021 -	12/2020	0/0
143	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	1,033.07 3,020.95	- -	03/2021	0/0
144	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 1,625.87	- -	03/2021	0/0
145	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR	04/1999	325.00 735.20	- -	03/2021	0/0
146	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 1,470.50	- -	03/2021	0/0
147	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	03/2020 -	03/2021	0/0
148	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]ECR,BIHAR	04/1991	329.39 803.11	- -	12/2021	0/0
149	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 614.45	- -	03/2022	0/0
150	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR	04/2006	378.56 -	- -	03/2022	0/0
151	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 819.01	03/2020 -	03/2022	0/0
152	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 1,215.54	03/2021 -	03/2022	0/0
153	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 1,185.73	03/2021 -	03/2022	0/0
154	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 519.33	- -	02/2023	0/0
155	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 2,066.78	- -	03/2023	0/0
156	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17 1,605.17	- 03/2023	03/2023	0/0
157	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR	04/2008	326.20 -	- -	03/2024	0/0
158	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	03/2024	0/0
159	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-	0/0
160	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 546.71	07/2014 -	-	0/0
161	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR	04/2008	633.87 -	- -	-	0/0
162	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-	0/0
163	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR	04/2008	445.25 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
164	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE	04/2008	415.67 -	- -	-	0/0
165	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-	0/0
166	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-	0/0
167	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-	0/0
168	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-	0/0
169	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-	0/0
	East Coast Railway					
170	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	03/2020 -	03/2021	0/0
171	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 1,539.28	02/2019 -	03/2022	0/0
172	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 2,499.71	03/2022 -	03/2022	0/0
173	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 701.61	11/2018 -	03/2022	0/0
174	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 1,172.92	12/2018 03/2022	03/2022	0/0
175	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 843.04	10/2020 03/2023	03/2023	0/0
176	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 1,547.38	03/2022 -	03/2023	0/0
177	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 3,791.66	03/2009 -	06/2024	0/0
178	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 198.07	06/2021 -	06/2024	0/0
179	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	03/2022 -	03/2025	0/0
	Eastern Railways					
180	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	05/2019	0/0
181	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	03/2020	0/0
182	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	11/2018 -	03/2021	0/0
183	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	542.18 -	03/2020 -	03/2021	0/0
184	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	03/2021	0/0
185	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	09/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
186	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	02/2013 -	03/2024	0/0
187	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	03/2024	0/0
188	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	03/2019 12/2009	03/2025	0/0
189	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	03/2006 -	03/2025	0/0
190	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	03/2025	0/0
191	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	03/2025	0/0
192	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	03/2022 -	03/2025	0/0
193	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	03/2016 -	03/2025	0/0
194	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51 -	03/2017 -	03/2025	0/0
195	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	03/2025	0/0
196	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	03/2016 -	03/2025	0/0
197	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	03/2017 -	03/2025	0/0
198	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	03/2025	0/0
199	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	03/2025	0/0
200	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	03/2005 -	03/2025	0/0
201	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	03/2025	0/0
202	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	03/2025	0/0
203	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	02/2012 -	03/2025	0/0
204	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2025	0/0
205	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	03/2025	0/0
206	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	03/2026	0/0
	Indian Railway Construction Company Limited					
207	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA	04/2016	5,200.00 -	03/2020 -	06/2023	0/0
	Kolkata Metro Rail Corporation Limited					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
208	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL,WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-	0/0
	Metropolitan Rapid Transport Projects					
209	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	03/2004 -	03/2021	0/0
210	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 -	03/2014 -	03/2021	0/0
211	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	03/2016 -	06/2021	0/0
212	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSHPUR - [N22000212]MRTP,WEST BENGAL	04/2009	573.78 -	- -	03/2025	0/0
213	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-	0/0
214	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	04/2016 -	-	0/0
	North Central Railway					
215	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH	03/2018	4,329.53 -	03/2023 -	03/2023	0/0
216	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-	0/0
217	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	2,030.50 -	- -	-	0/0
	North East Frontier Railway					
218	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	297.32 -	03/2019 -	03/2020	0/0
219	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 1,532.00	03/2019 -	03/2020	0/0
220	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 2,145.00	03/2019 -	03/2020	0/0
221	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	03/2020 -	03/2020	0/0
222	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 -	03/2020 -	03/2020	0/0
223	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	414.84 -	03/2020 -	03/2020	0/0
224	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	314.00 728.00	03/2019 -	03/2020	0/0
225	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	03/2022 -	03/2020	0/0
226	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR,WEST BENGAL	04/2016	602.27 -	12/2021 -	03/2020	0/0
227	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	1,180.19 3,300.00	12/2008 -	03/2021	0/0
228	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	906.46 -	03/2021 -	03/2021	0/0
229	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM	04/2015	870.96 -	03/2021 -	03/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
230	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	- -	06/2021	0/0
231	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 -	03/2015 -	10/2021	0/0
232	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 13,809.00	03/2011 -	03/2022	0/0
233	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	2,393.47 4,968.00	03/2014 03/2022	03/2022	0/0
234	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	333.76 -	- 03/2022	03/2022	0/0
235	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 -	- 03/2022	03/2022	0/0
236	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	12/2015 -	-	0/0
237	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 -	03/2019 -	-	0/0
238	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE	04/1999	819.23 -	- -	-	0/0
239	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]NFR,WEST BENGAL	02/1999	380.60 -	04/2010 -	-	0/0
	North Eastern Railway					
240	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH	03/2015	1,295.42 -	03/2022 -	12/2019	0/0
241	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	01/2019 -	01/2020	0/0
242	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	04/2017 -	01/2020	0/0
243	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	04/2016 -	06/2020	0/0
244	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	12/2019 -	04/2021	0/0
245	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	12/2021 -	12/2021	0/0
246	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH	04/2016	1,900.00 -	01/2022 -	01/2022	0/0
247	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH	04/2016	600.00 -	01/2022 -	01/2022	0/0
248	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	04/2017 -	04/2022	0/0
249	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	04/2017 -	10/2022	0/0
250	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	12/2022 -	12/2022	0/0
251	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-	0/0
252	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
253	KAPILVASTU-BASTI VIA BANSI SIDHARTHNAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
254	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-	0/0
255	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-	0/0
256	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50 -	- -	-	0/0
	North Western Railway					
257	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	10/2018 -	12/2019	0/0
258	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 281.03	02/2019 -	03/2020	0/0
259	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	11/2019 -	05/2020	0/0
260	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	12/2019 -	06/2020	0/0
261	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 -	03/2020 -	06/2020	0/0
262	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 780.98	02/2019 -	03/2021	0/0
263	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	03/2020 -	04/2022	0/0
264	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	08/2022 -	09/2022	0/0
265	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
266	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-	0/0
	Northern Railway					
267	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 346.63	- -	06/2020	0/0
268	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	12/2011 -	03/2021	0/0
269	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 781.00	03/2016 -	03/2021	0/0
270	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 791.39	- 03/2022	03/2022	0/0
271	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	11/2002 -	06/2022	0/0
272	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	03/2023	0/0
273	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00 -	- -	03/2023	0/0
274	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE	04/2007	328.14 -	03/2023 -	03/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
275	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 2,010.00	07/2012 -	03/2024	0/0
276	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- 03/2024	03/2024	0/0
277	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	03/2024	0/0
	National High Speed Rail Corporation Limited					
278	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE	12/2015	1,08,000.00 -	12/2023 12/2023	12/2023	0/0
	Rail India Technical And Economic Service					
279	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-	0/0
	Rail Vikas Nigam Ltd.					
280	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64 -	12/2017 -	03/2020	0/0
281	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	03/2019 -	03/2020	0/0
282	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02 -	03/2020 -	06/2020	0/0
283	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	03/2016 -	12/2020	0/0
284	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	644.38 -	03/2021 -	03/2021	0/0
285	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48 -	03/2020 -	03/2021	0/0
286	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	03/2020 -	03/2021	0/0
287	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.85 -	12/2020 -	03/2021	0/0
288	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 -	02/2015 -	12/2021	0/0
289	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT	04/2012	975.62 -	12/2021 -	12/2021	0/0
290	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,548.66 -	12/2021 -	03/2022	0/0
291	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	03/2020 -	03/2022	0/0
292	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	03/2019 -	06/2022	0/0
293	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	12/2020 -	12/2022	0/0
294	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH	04/2015	3,246.26 -	12/2023 -	12/2023	0/0
295	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	03/2022 -	12/2024	0/0
296	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA	04/2015	773.94 -	12/2024 -	12/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
297	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	03/2023 -	12/2024	0/0
298	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67 -	12/2024 -	12/2024	0/0
299	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	03/2016 -	03/2025	0/0
300	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	03/2016 -	03/2025	0/0
301	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	12/2024 -	03/2025	0/0
302	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA	04/2015	723.78 -	12/2025 -	03/2025	0/0
303	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	03/2014 -	12/2025	0/0
304	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH	04/2008	2,966.99 -	12/2026 -	12/2025	0/0
	Railway Electrification					
305	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-	0/0
	South Central Railway					
306	MUNEERABAD-MAHABOOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1,780.29	03/2000 -	03/2021	0/0
307	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA	04/2017	119.73 185.00	03/2022 -	03/2022	0/0
308	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 2,120.16	03/2009 -	03/2023	0/0
309	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 2,063.03	03/2021 -	03/2023	0/0
310	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 3,631.00	03/2022 -	03/2023	0/0
311	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 2,200.00	03/2023 -	03/2024	0/0
312	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	164.36 -	02/2009 -	-	0/0
313	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	458.25 458.25	- -	-	0/0
314	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	761.37 761.37	- -	-	0/0
315	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 3,873.07	- -	-	0/0
	South East Central Railway					
316	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 1,473.76	- 01/2020	01/2020	0/0
317	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH	04/2008	872.00 1,226.51	12/2019 03/2020	03/2020	0/0
318	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00 1,370.94	12/2021 11/2022	11/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	South Eastern Railway					
319	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	12/2016 08/2018	01/2020	0/0
320	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 358.68	12/2018 -	06/2020	0/0
321	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 1,312.96	03/2020 03/2020	06/2020	0/0
322	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	03/2021 03/2021	12/2021	0/0
323	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- 03/2025	03/2025	0/0
324	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	03/2015 03/2025	03/2025	0/0
325	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 1,966.70	03/2003 03/2030	03/2030	0/0
326	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-	0/0
327	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-	0/0
	South Western Railway					
328	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	03/2020 -	03/2020	0/0
329	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 644.78	03/2017 -	03/2020	0/0
330	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 1,870.41	03/2019 -	03/2021	0/0
331	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 1,801.01	- -	12/2023	0/0
332	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 692.43	- -	12/2023	0/0
333	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 466.65	- -	12/2023	0/0
334	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.85 348.85	- -	12/2023	0/0
335	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 146.75	- -	12/2023	0/0
336	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 367.77	- -	12/2023	0/0
337	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 279.54	03/2016 -	12/2023	0/0
338	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 1,382.78	03/2002 -	03/2024	0/0
339	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 832.47	03/2016 -	03/2024	0/0
340	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 -	- -	12/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
341	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 2,841.84	12/2018 -	12/2024	0/0
	Southern Railway					
342	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	03/2019 -	12/2019	0/0
343	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	02/2019 -	02/2020	0/0
344	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	03/2020	0/0
345	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	931.98 -	- -	03/2020	0/0
346	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	04/2014 -	03/2020	0/0
347	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	03/2020 -	03/2021	0/0
348	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	03/2020 -	06/2021	0/0
349	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU	02/2015	1,700.00 -	03/2022 -	03/2022	0/0
350	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	03/2024 -	03/2026	0/0
351	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 -	- -	-	0/0
352	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40 -	- -	-	0/0
353	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	- -	-	0/0
354	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	151.84 -	02/2019 -	-	0/0
355	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-	0/0
356	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
357	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-	0/0
358	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-	0/0
359	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
360	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
361	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-	0/0
362	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 -	- -	-	0/0
363	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
364	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	03/2005 -	-	0/0
365	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-	0/0
366	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU	02/1999	257.00 257.00	03/2018 -	-	0/0
	Western Railway					
367	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 03/2017	03/2017	0/0
368	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT	02/1991	551.51 809.07	03/2019 03/2020	03/2020	0/0
369	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	829.74 1,215.34	03/2020 03/2021	03/2021	0/0
370	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10 844.10	- 03/2021	03/2021	0/0
371	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 1,002.39	03/2021 03/2021	03/2021	0/0
372	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT	04/2017	691.84 663.29	03/2020 03/2021	03/2021	0/0
373	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH	04/2016	700.00 603.69	06/2020 06/2021	06/2021	0/0
374	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 321.62	03/2012 03/2022	03/2022	0/0
375	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 1,347.26	03/2022 03/2022	03/2022	0/0
376	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 858.56	03/2019 03/2022	03/2022	0/0
377	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	1,037.15 1,037.15	03/2021 03/2022	03/2022	0/0
378	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 3,975.22	03/2022 03/2023	03/2023	0/0
379	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 1,640.04	03/2022 03/2023	03/2023	0/0
380	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-	0/0
381	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-	0/0
382	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-	0/0
383	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-	0/0
384	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-	0/0
	ROAD TRANSPORT AND HIGHWAYS					
	Ministry Of Road Transport And Highways (State Pwds)					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
385	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224]MoRTH,CHHATISGARH	03/2017	423.79 -	01/2018 -	01/2018	0/0
386	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226]MoRTH,CHHATISGARH	12/2014	496.02 -	03/2015 -	03/2015	0/0
387	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATISGARH	11/2015	335.32 -	06/2017 -	06/2017	0/0
388	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH,CHHATISGARH	03/2016	452.94 -	07/2016 -	07/2016	0/0
389	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH,CHHATISGARH	01/2016	497.14 -	08/2016 -	08/2016	0/0
390	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]MoRTH,CHHATISGARH	01/2016	476.20 544.00	09/2016 -	09/2016	0/0
391	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 127.500 TO 178.944 DARRIGHAT TO BANARI SECTION - [N24001220]MoRTH,CHHATISGARH	03/2016	491.52 -	09/2016 -	09/2016	0/0
392	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA	03/2015	153.21 -	01/2017 -	09/2019	0/0
393	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND	11/2016	336.25 -	09/2019 -	09/2019	0/0
394	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATISGARH	01/2016	624.98 -	10/2016 -	10/2016	0/0
395	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH,TELANGANA	01/2017	605.08 -	10/2019 -	10/2019	0/0
396	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA	08/2013	171.96 172.00	06/2016 -	11/2019	0/0
397	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2-LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND	11/2017	232.81 -	11/2019 -	11/2019	0/0
398	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND	11/2017	283.51 -	11/2019 -	11/2019	0/0
399	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND	11/2017	266.52 -	11/2019 -	11/2019	0/0
400	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS	11/2017	237.80 -	11/2019 -	11/2019	0/0
401	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH,TELANGANA	02/2018	294.13 -	11/2019 -	11/2019	0/0
402	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH,TELANGANA	02/2018	220.28 -	11/2019 -	11/2019	0/0
403	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221 - [N24001223]MoRTH,CHANDIGARH	03/2010	179.89 271.00	03/2013 -	03/2013	0/0
404	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229]MoRTH,CHHATISGARH	12/2014	379.16 -	11/2017 -	11/2017	0/0
405	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1 - [N24001225]MoRTH,CHANDIGARH	12/2010	169.26 299.00	01/2019 -	01/2019	0/0
406	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O - [N24000871]MoRTH,WEST BENGAL	08/2014	600.87 720.97	11/2017 05/2019	05/2019	0/0
407	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH,CHHATISGARH	11/2017	188.80 -	05/2019 -	05/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
408	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873]MoRTH,WEST BENGAL	08/2014	823.20 937.76	11/2017 06/2019	06/2019	0/0
409	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH,WEST BENGAL	04/2014	279.70 398.52	08/2017 07/2019	07/2019	0/0
410	MAJALGAON TO KAIJ - [N24001036]MoRTH,MAHARASHTRA	01/2017	413.99 -	07/2019 -	07/2019	0/0
411	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2- - [N24001147]MoRTH,UTTAR PRADESH	10/2016	239.63 -	02/2019 -	07/2019	0/0
412	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]MoRTH,MADHYA PRADESH	09/2016	178.23 -	09/2018 -	08/2019	0/0
413	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]MoRTH,UTTAR PRADESH	10/2016	176.94 177.00	10/2018 -	09/2019	0/0
414	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH	01/2012	410.72 -	04/2015 -	10/2019	0/0
415	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]MoRTH,UTTAR PRADESH	11/2016	215.16 215.00	09/2019 -	10/2019	0/0
416	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MoRTH,UTTAR PRADESH	10/2013	445.89 653.00	03/2017 -	10/2019	0/0
417	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS	11/2017	257.34 -	11/2019 -	11/2019	0/0
418	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]MoRTH,WEST BENGAL	03/2016	271.17 291.20	11/2018 11/2019	11/2019	0/0
419	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA	01/2018	259.55 260.00	11/2019 -	11/2019	0/0
420	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH,KERALA	01/2014	255.75 348.00	09/2017 -	12/2019	0/0
421	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM	11/2010	624.41 -	03/2011 -	12/2019	0/0
422	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM	08/2010	193.69 -	10/2010 -	12/2019	0/0
423	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]MoRTH,ARUNACHAL PRADESH	03/2012	207.03 389.45	05/2012 05/2015	12/2019	0/0
424	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]MoRTH,SIKKIM	04/2013	151.59 -	08/2013 -	12/2019	0/0
425	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]MoRTH,SIKKIM	01/2013	182.28 -	02/2013 -	12/2019	0/0
426	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	12/2019	0/0
427	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA	12/2011	191.08 -	08/2015 -	12/2019	0/0
428	WIDENING AND STRENFTHENING OF EXISITNG SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA	03/2014	191.50 192.00	05/2016 -	12/2019	0/0
429	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH,UTTARAKHAND	12/2017	257.34 -	12/2019 -	12/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
430	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH,UTTARAKHAND	12/2017	200.34 -	12/2019 -	12/2019	0/0
431	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH,UTTARAKHAND	12/2017	248.22 -	12/2019 -	12/2019	0/0
432	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND	06/2017	282.08 -	06/2019 -	12/2019	0/0
433	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]MoRTH,MADHYA PRADESH	09/2016	287.34 -	01/2019 -	12/2019	0/0
434	REHABILITATION AND UPGRADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942]MoRTH,UTTAR PRADESH	03/2016	208.50 -	11/2019 -	12/2019	0/0
435	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA	01/2017	244.54 -	05/2019 09/2019	12/2019	0/0
436	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA	01/2017	196.52 -	10/2019 -	12/2019	0/0
437	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH,TELANGANA	01/2017	283.00 -	12/2019 -	12/2019	0/0
438	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA	01/2017	359.27 -	05/2019 -	12/2019	0/0
439	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH,TELANGANA	01/2018	230.03 -	12/2019 -	12/2019	0/0
440	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA	03/2018	192.67 -	07/2019 -	12/2019	0/0
441	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA	02/2017	203.21 203.00	05/2019 -	12/2019	0/0
442	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA	01/2017	385.87 386.00	06/2019 -	12/2019	0/0
443	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA	01/2017	341.16 341.00	06/2019 -	12/2019	0/0
444	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA	03/2018	249.29 -	12/2019 -	12/2019	0/0
445	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	12/2019	0/0
446	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA	03/2018	228.31 -	12/2019 -	12/2019	0/0
447	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA	03/2018	256.15 -	12/2019 -	12/2019	0/0
448	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA	03/2018	223.46 -	12/2019 -	12/2019	0/0
449	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA	03/2018	177.84 177.00	12/2019 -	12/2019	0/0
450	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]MoRTH,MAHARASHTRA	03/2016	536.65 356.00	12/2019 -	12/2019	0/0
451	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA	12/2017	309.94 310.00	12/2019 -	12/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
452	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA	12/2017	244.04 244.00	03/2019 -	12/2019	0/0
453	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA	01/2018	264.41 264.00	03/2019 -	12/2019	0/0
454	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND	08/2016	234.88 -	12/2017 -	12/2019	0/0
455	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA	02/2018	355.99 355.99	12/2019 -	12/2019	0/0
456	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]MoRTH,ASSAM	11/2010	197.37 -	02/2014 -	12/2019	0/0
457	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM	08/2010	186.96 -	09/2014 -	12/2019	0/0
458	REHABILITATION AND UPGRADATION OF BARAICH -SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA - [N24001202]MoRTH,UTTAR PRADESH	03/2016	388.83 -	12/2019 -	12/2019	0/0
459	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH	07/2016	208.88 -	10/2019 -	12/2019	0/0
460	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH	11/2015	628.45 -	01/2020 -	01/2020	0/0
461	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH	03/2016	240.30 240.00	01/2020 -	01/2020	0/0
462	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148]MoRTH,UTTAR PRADESH	03/2016	599.34 -	01/2020 -	01/2020	0/0
463	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH	12/2015	957.54 -	02/2020 -	02/2020	0/0
464	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH	03/2015	511.83 -	08/2017 -	02/2020	0/0
465	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH,UTTARAKHAND	02/2018	418.88 -	02/2020 -	02/2020	0/0
466	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH	01/2016	809.16 -	07/2018 -	02/2020	0/0
467	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH	03/2018	185.18 -	02/2020 -	02/2020	0/0
468	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH	06/2015	390.51 -	- -	03/2020	0/0
469	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]MoRTH,MADHYA PRADESH	11/2011	954.43 -	09/2015 -	03/2020	0/0
470	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH	03/2018	162.56 -	03/2018 -	03/2020	0/0
471	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]MoRTH,MADHYA PRADESH	11/2017	235.91 -	02/2018 -	03/2020	0/0
472	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH	11/2017	184.62 -	02/2018 -	03/2020	0/0
473	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH	03/2018	233.04 -	03/2018 -	03/2020	0/0
474	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH	11/2017	249.05 -	07/2018 -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
475	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH	11/2017	254.17 -	02/2018 -	03/2020	0/0
476	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA	01/2017	247.25 -	03/2019 03/2020	03/2020	0/0
477	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA	10/2016	248.83 -	03/2019 -	03/2020	0/0
478	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA	01/2017	300.00 -	05/2019 -	03/2020	0/0
479	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139]MoRTH,UTTAR PRADESH	10/2016	218.94 219.00	03/2020 -	03/2020	0/0
480	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH	03/2016	249.50 -	05/2019 -	03/2020	0/0
481	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]MoRTH,UTTAR PRADESH	10/2016	218.90 -	03/2020 -	03/2020	0/0
482	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH	02/2018	279.44 -	03/2018 -	04/2020	0/0
483	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH,TELANGANA	02/2018	426.52 -	04/2020 -	04/2020	0/0
484	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 - [N24001205]MoRTH,UTTAR PRADESH	12/2016	209.10 -	10/2019 04/2020	04/2020	0/0
485	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH	03/2018	263.89 242.05	04/2020 -	04/2020	0/0
486	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]MoRTH,MADHYA PRADESH	11/2013	497.05 -	05/2017 -	05/2020	0/0
487	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH,UTTARAKHAND	05/2018	248.00 -	05/2020 -	05/2020	0/0
488	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH	01/2017	373.82 -	09/2019 -	05/2020	0/0
489	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH,TELANGANA	01/2018	283.15 -	05/2020 -	05/2020	0/0
490	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA	05/2018	171.60 -	05/2018 -	05/2020	0/0
491	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM	08/2010	195.04 -	10/2010 -	06/2020	0/0
492	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH	03/2018	166.21 -	08/2018 -	06/2020	0/0
493	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]MoRTH,MADHYA PRADESH	03/2018	191.21 -	11/2019 -	06/2020	0/0
494	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH	01/2017	205.05 -	03/2017 -	06/2020	0/0
495	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH	03/2018	214.69 -	03/2018 -	06/2020	0/0
496	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH	03/2018	217.22 -	08/2018 -	06/2020	0/0
497	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]MoRTH,PUNJAB	03/2018	173.24 -	06/2020 -	06/2020	0/0
498	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA	10/2016	298.32 -	02/2019 -	06/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
499	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH,TELANGANA	02/2018	206.13 -	06/2020 -	06/2020	0/0
500	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA	01/2017	391.06 391.00	06/2019 -	06/2020	0/0
501	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131]MoRTH,JHARKHAND	03/2018	212.99 -	06/2020 -	06/2020	0/0
502	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH	11/2017	392.33 -	03/2018 -	06/2020	0/0
503	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH	02/2018	169.63 -	03/2018 -	07/2020	0/0
504	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905]MoRTH,PUNJAB	03/2018	322.48 -	07/2020 -	07/2020	0/0
505	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH,TELANGANA	03/2018	626.76 -	07/2020 -	07/2020	0/0
506	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB	03/2018	293.10 -	08/2020 -	08/2020	0/0
507	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	08/2020	0/0
508	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	08/2020	0/0
509	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA	09/2018	301.38 301.00	08/2020 -	08/2020	0/0
510	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH,TRIPURA	10/2016	171.90 -	08/2020 -	08/2020	0/0
511	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208]MoRTH,UTTAR PRADESH	03/2018	288.30 -	08/2020 -	08/2020	0/0
512	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH,TELANGANA	03/2018	322.81 -	09/2020 -	09/2020	0/0
513	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH	11/2016	243.89 -	- -	09/2020	0/0
514	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH	03/2016	296.50 -	09/2020 -	09/2020	0/0
515	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]MoRTH,WEST BENGAL	03/2018	254.30 254.30	10/2020 -	10/2020	0/0
516	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174]MoRTH,MANIPUR	10/2016	235.31 -	11/2020 -	11/2020	0/0
517	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND	03/2017	217.35 -	11/2020 -	11/2020	0/0
518	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH	03/2016	877.79 -	06/2019 -	12/2020	0/0
519	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB	10/2017	1,069.59 -	10/2019 12/2020	12/2020	0/0
520	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]MoRTH,BIHAR	05/2014	199.98 -	08/2016 -	12/2020	0/0
521	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND	10/2016	167.62 -	12/2020 -	12/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
522	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND	10/2016	172.63 -	12/2020 -	12/2020	0/0
523	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MoRTH,MADHYA PRADESH	01/2019	264.50 -	03/2021 -	03/2021	0/0
524	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB	03/2018	170.57 192.48	11/2020 -	05/2021	0/0
525	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA	02/2017	157.32 188.00	05/2019 -	05/2021	0/0
526	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197]MoRTH,GUJARAT	03/2018	351.00 -	06/2021 -	06/2021	0/0
527	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH,WEST BENGAL	03/2016	160.27 213.97	08/2019 -	08/2021	0/0
528	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH,WEST BENGAL	06/2016	236.78 263.26	08/2019 -	08/2021	0/0
529	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152]MoRTH,ASSAM	09/2018	160.00 -	09/2021 -	09/2021	0/0
530	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216]MoRTH,JHARKHAND	12/2016	196.00 -	09/2021 -	09/2021	0/0
531	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180]MoRTH,NAGALAND	03/2019	237.51 -	12/2022 -	12/2022	0/0
532	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MoRTH,MAHARASHTRA	10/2015	289.60 -	- -	-	0/0
533	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MoRTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-	0/0
534	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]MoRTH,CHHATISGARH	12/2015	291.05 -	- -	-	0/0
535	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]MoRTH,CHHATISGARH	11/2015	485.44 -	12/2015 -	-	0/0
536	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MoRTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-	0/0
537	WIDENING AND STRENGHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MoRTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-	0/0
538	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MoRTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-	0/0
539	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MoRTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-	0/0
540	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MoRTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-	0/0
541	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]MoRTH,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-	0/0
542	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]MoRTH,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-	0/0
543	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]MoRTH,SIKKIM	04/2013	166.27 -	08/2013 -	-	0/0
544	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]MoRTH,NAGALAND	12/2010	1,296.00 -	02/2011 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
545	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MoRTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-	0/0
546	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MoRTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-	0/0
547	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- - [N24000318]MoRTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-	0/0
548	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-	0/0
549	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA	01/2015	225.81 -	- -	-	0/0
550	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-	0/0
551	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MoRTH,KARNATAKA	03/2015	159.12 -	11/2015 -	-	0/0
552	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]MoRTH,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	-	0/0
553	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]MoRTH,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	-	0/0
554	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]MoRTH,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	-	0/0
555	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MoRTH,KARNATAKA	01/1991	219.40 -	01/2018 -	-	0/0
556	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MoRTH,ODISHA	01/1991	218.63 -	10/2017 -	-	0/0
557	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR	01/1991	675.00 -	- -	-	0/0
558	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]MoRTH,PUNJAB	12/2015	766.36 -	- 09/2019	-	0/0
559	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]MoRTH,PUNJAB	11/2015	847.02 -	- 09/2019	-	0/0
560	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB	11/2015	889.24 -	- 12/2019	-	0/0
561	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM	11/2010	268.08 -	05/2017 -	-	0/0
562	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]MoRTH,MADHYA PRADESH	08/2015	257.80 -	- -	-	0/0
563	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]MoRTH,ASSAM	11/2010	470.20 -	02/2011 -	-	0/0
564	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MoRTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	-	0/0
565	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MoRTH,BIHAR	01/1991	282.41 -	08/2016 -	-	0/0
566	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MoRTH,BIHAR	01/1991	358.22 -	10/2016 -	-	0/0
567	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]MoRTH,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
568	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]MoRTH,ASSAM	11/2014	218.31 -	02/2018 -	-	0/0
569	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MoRTH,ODISHA	01/1991	229.41 -	05/2018 -	-	0/0
570	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]MoRTH,ODISHA	07/2014	342.05 -	01/2017 -	-	0/0
571	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA	10/2015	936.40 -	- -	-	0/0
572	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]MoRTH,RAJASTHAN	09/2012	511.00 -	10/2013 -	-	0/0
573	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA	12/2015	773.98 -	- -	-	0/0
574	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH,GOA	12/2015	819.95 -	- -	-	0/0
575	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MoRTH,BIHAR	01/1991	478.35 -	- -	-	0/0
576	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]MoRTH,ODISHA	12/2011	159.39 -	11/2017 -	-	0/0
577	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]MoRTH,PUNJAB	06/2015	892.17 -	- -	-	0/0
578	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]MoRTH,BIHAR	01/1991	154.62 -	- -	-	0/0
579	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH,BIHAR	01/1991	319.68 -	- -	-	0/0
580	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MoRTH,BIHAR	10/2013	278.39 -	08/2014 -	-	0/0
581	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH,BIHAR	11/2013	683.83 -	07/2016 -	-	0/0
582	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MoRTH,BIHAR	02/2014	665.50 -	07/2016 -	-	0/0
583	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH,BIHAR	02/2016	178.85 -	05/2016 -	-	0/0
584	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MoRTH,BIHAR	02/2016	369.77 -	06/2016 -	-	0/0
585	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH,BIHAR	02/2016	553.30 -	05/2016 -	-	0/0
586	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-	0/0
587	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPR - [N24000580]MoRTH,BIHAR	03/2015	206.80 -	07/2016 -	-	0/0
588	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MoRTH,BIHAR	08/2015	288.24 -	11/2015 -	-	0/0
589	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA	03/2016	1,142.62 -	- -	-	0/0
590	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA	03/2016	1,101.58 -	- -	-	0/0
591	REHABILIATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
592	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MoRTH,ODISHA	01/2015	326.63 327.00	04/2018 -	-	0/0
593	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MoRTH,ODISHA	02/2015	239.91 240.00	10/2017 -	-	0/0
594	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MoRTH,ODISHA	07/2014	342.05 342.00	01/2017 -	-	0/0
595	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MoRTH,ODISHA	06/2016	157.30 157.00	06/2018 -	-	0/0
596	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH,UTTARAKHAND	02/2018	293.68 -	- -	-	0/0
597	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND	03/2018	460.73 -	- -	-	0/0
598	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH,WEST BENGAL	01/2017	396.86 396.86	09/2019 -	-	0/0
599	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH	11/2016	326.99 327.00	- -	-	0/0
600	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]MoRTH,WEST BENGAL	03/2017	202.69 202.69	11/2019 -	-	0/0
601	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH,WEST BENGAL	02/2018	426.18 426.18	09/2020 -	-	0/0
602	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH,WEST BENGAL	02/2018	218.70 218.70	11/2020 -	-	0/0
603	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]MoRTH,HARYANA	01/2017	276.01 -	03/2019 07/2019	-	0/0
604	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. - [N24000911]MoRTH,ODISHA	03/2016	165.06 -	12/2016 -	-	0/0
605	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA	08/2016	287.70 -	02/2017 -	-	0/0
606	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA	09/2016	295.67 -	02/2017 -	-	0/0
607	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA	12/2016	223.50 -	08/2018 -	-	0/0
608	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA	12/2016	206.88 -	04/2018 -	-	0/0
609	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA	03/2018	214.23 -	08/2018 -	-	0/0
610	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA	03/2018	199.16 -	08/2018 -	-	0/0
611	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPIR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]MoRTH,GUJARAT	10/2018	400.76 -	05/2019 -	-	0/0
612	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR	09/2018	1,478.40 -	- -	-	0/0
613	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH,TELANGANA	01/2019	193.19 -	- -	-	0/0
614	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999]MoRTH,BIHAR	11/2016	230.34 -	10/2019 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
615	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR	03/2018	153.24 -	- -	-	0/0
616	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	-	0/0
617	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	-	0/0
618	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	-	0/0
619	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA	02/2017	422.02 422.00	07/2019 -	-	0/0
620	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA	01/2017	388.44 -	- -	-	0/0
621	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	-	0/0
622	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	-	0/0
623	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]MoRTH,UTTAR PRADESH	05/2013	164.54 165.00	08/2015 -	-	0/0
624	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT - [N24001154]MoRTH,KARNATAKA	08/2016	367.44 -	01/2017 -	-	0/0
625	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT - [N24001155]MoRTH,KARNATAKA	08/2016	175.20 -	01/2017 -	-	0/0
626	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA - [N24001156]MoRTH,KARNATAKA	01/2017	166.67 -	09/2017 -	-	0/0
627	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA	08/2016	175.50 -	02/2017 -	-	0/0
628	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA	03/2018	159.97 -	06/2019 -	-	0/0
629	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]MoRTH,KARNATAKA	01/2018	159.70 -	07/2018 -	-	0/0
630	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA	09/2017	191.60 -	10/2018 -	-	0/0
631	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]MoRTH,KARNATAKA	12/2017	297.30 -	01/2019 -	-	0/0
632	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA	03/2018	325.86 -	10/2018 -	-	0/0
633	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA	08/2016	329.01 -	02/2017 -	-	0/0
634	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA	10/2016	396.96 -	03/2017 -	-	0/0
635	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA	11/2016	314.90 -	03/2017 -	-	0/0
636	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA	03/2015	159.12 -	01/2016 -	-	0/0
637	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776) - [N24001167]MoRTH,KARNATAKA	03/2015	165.67 -	01/2016 -	-	0/0
638	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM. - [N24001170]MoRTH,KARNATAKA	01/2014	471.16 -	08/2014 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
639	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA	01/2017	291.49 -	08/2017 -	-	0/0
640	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S - [N24001183]MoRTH,ANDHRA PRADESH	07/2014	251.55 -	02/2015 -	-	0/0
641	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH	09/2011	1,979.00 -	- 03/2020	-	0/0
642	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MoRTH,RAJASTHAN	03/2019	178.13 -	- -	-	0/0
643	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR	02/2019	2,926.42 -	- -	-	0/0
644	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH	03/2018	306.59 -	- -	-	0/0
645	IMPROVEMENT AND UP-GRADATION OF EXISITING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH	11/2018	281.45 -	- -	-	0/0
	National Highways And Infrastructure Development Corporation Ltd.					
646	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH	10/2015	210.50 210.50	- 01/2016	01/2019	0/0
647	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM	04/2017	519.09 -	09/2019 -	09/2019	0/0
648	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM	04/2017	640.07 -	09/2019 -	09/2019	0/0
649	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM	04/2017	642.96 -	09/2019 -	09/2019	0/0
650	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM	04/2017	473.18 -	09/2019 -	09/2019	0/0
651	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM	04/2017	537.82 -	09/2019 -	09/2019	0/0
652	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM	04/2017	518.53 -	09/2019 -	09/2019	0/0
653	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM	04/2017	404.29 -	09/2019 -	09/2019	0/0
654	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM	04/2017	428.11 -	09/2019 -	09/2019	0/0
655	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 - [N24001184]NHIDCL,DELHI	07/2017	269.69 -	09/2019 -	12/2019	0/0
656	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D - [N24000974]NHIDCL,ARUNACHAL PRADESH	02/2017	199.02 199.02	- 02/2018	02/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
657	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D - [N24000975]NHIDCL,ARUNACHAL PRADESH	02/2017	184.88 184.88	- 02/2018	02/2021	0/0
658	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH	02/2017	175.06 175.06	- 04/2019	04/2022	0/0
659	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH	02/2017	176.12 176.12	- 04/2019	04/2022	0/0
660	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 -	09/2018 -	-	0/0
661	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND	03/2018	339.57 233.35	09/2018 07/2019	-	0/0
662	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM	03/2017	375.80 -	- -	-	0/0
663	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I - [N24000770]NHIDCL,WEST BENGAL	03/2017	158.65 -	06/2018 -	-	0/0
664	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR	03/2018	253.44 -	07/2019 -	-	0/0
665	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH	12/2016	200.44 -	- -	-	0/0
666	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH	03/2017	1,718.59 -	- -	-	0/0
667	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM - [N24000947]NHIDCL,ARUNACHAL PRADESH	05/2016	259.52 -	- -	-	0/0
668	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92 -	- -	-	0/0
669	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH	12/2016	188.78 -	- -	-	0/0
670	OUR LANNNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM	03/2017	1,049.51 -	- -	-	0/0
	National Highways Authority Of India					
671	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 255.23	11/2008 01/2011	08/2013	0/0
672	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 408.77	11/2008 07/2011	01/2014	0/0
673	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- 06/2015	06/2015	0/0
674	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- 06/2015	06/2015	0/0
675	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	10/2017	0/0
676	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 03/2018	03/2018	0/0
677	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 08/2018	08/2018	0/0
678	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 655.17	07/2009 10/2018	10/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
679	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	05/2019 -	02/2019	0/0
680	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	03/2019	0/0
681	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 315.00	- 03/2020	03/2019	0/0
682	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 04/2019	04/2019	0/0
683	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 -	06/2019	0/0
684	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	- -	06/2019	0/0
685	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 725.87	02/2019 -	06/2019	0/0
686	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 490.00	02/2009 07/2019	07/2019	0/0
687	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	04/2010 -	07/2019	0/0
688	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	07/2019	0/0
689	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 340.14	04/2009 03/2011	08/2019	0/0
690	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 -	09/2019	0/0
691	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 1,544.00	09/2016 -	09/2019	0/0
692	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 -	06/2019 12/2016	09/2019	0/0
693	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	06/2019 -	09/2019	0/0
694	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	06/2019 -	09/2019	0/0
695	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 767.03	08/2018 -	09/2019	0/0
696	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	09/2019	0/0
697	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA	03/2017	296.19 -	03/2020 -	09/2019	0/0
698	TWO LANING WITH PAVED SHOULDER OF KARAUII - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 09/2014	10/2019	0/0
699	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 507.70	06/2016 -	10/2019	0/0
700	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	05/2018 10/2019	10/2019	0/0
701	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	05/2018 03/2018	10/2019	0/0
702	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	- 02/2016	10/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
703	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 537.16	07/2018 -	11/2019	0/0
704	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 881.00	- 05/2017	11/2019	0/0
705	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	04/2019 -	11/2019	0/0
706	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 1,238.21	- -	11/2019	0/0
707	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00 -	04/2020 -	11/2019	0/0
708	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	11/2019	0/0
709	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	11/2019	0/0
710	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	12/2019	0/0
711	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	12/2019	0/0
712	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 12/2019	12/2019	0/0
713	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	12/2019	0/0
714	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	12/2019	0/0
715	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 -	06/2018 -	12/2019	0/0
716	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 622.00	- -	12/2019	0/0
717	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 622.00	- -	12/2019	0/0
718	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 746.43	12/2017 06/2020	12/2019	0/0
719	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	12/2019	0/0
720	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 67.34	01/2018 12/2018	12/2019	0/0
721	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	- -	12/2019	0/0
722	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- 12/2017	12/2019	0/0
723	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	05/2019 -	12/2019	0/0
724	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL	10/2015	361.15 -	- -	01/2020	0/0
725	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- -	01/2020	0/0
726	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	01/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
727	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	01/2020	0/0
728	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	08/2018 -	01/2020	0/0
729	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	05/2019 -	01/2020	0/0
730	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB	03/2018	196.05 149.90	- -	01/2020	0/0
731	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	02/2020	0/0
732	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	02/2020	0/0
733	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	- -	02/2020	0/0
734	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	07/2018 12/2019	02/2020	0/0
735	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	03/2020 02/2021	02/2020	0/0
736	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	04/2008 -	03/2020	0/0
737	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 364.59	12/2009 08/2020	03/2020	0/0
738	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	03/2020	0/0
739	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 2,967.50	11/2011 -	03/2020	0/0
740	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 585.00	11/2013 12/2019	03/2020	0/0
741	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	03/2020	0/0
742	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 12/2019	03/2020	0/0
743	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 1,302.98	03/2018 -	03/2020	0/0
744	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	- -	03/2020	0/0
745	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 897.03	11/2018 07/2019	03/2020	0/0
746	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	08/2018 -	03/2020	0/0
747	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 598.13	04/2018 03/2020	03/2020	0/0
748	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	03/2020	0/0
749	CONSTRUCTION OF ROB –FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL	03/2016	229.37 -	11/2018 03/2020	03/2020	0/0
750	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	08/2018 -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
751	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 2,541.32	09/2019 03/2020	03/2020	0/0
752	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 -	03/2020 -	03/2020	0/0
753	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	03/2020 -	03/2020	0/0
754	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 -	03/2020 -	03/2020	0/0
755	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI,ANDHRA PRADESH	03/2017	648.32 -	03/2020 -	03/2020	0/0
756	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI,JHARKHAND	03/2017	165.50 -	03/2020 -	03/2020	0/0
757	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND	03/2017	239.68 -	03/2020 -	03/2020	0/0
758	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	- -	03/2020	0/0
759	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	03/2020	0/0
760	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA	03/2018	275.12 -	- -	03/2020	0/0
761	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROMEXISTI - [N24000837]NHAI,HARYANA	03/2018	307.79 -	- -	03/2020	0/0
762	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	- -	03/2020	0/0
763	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA	03/2018	551.58 -	- -	03/2020	0/0
764	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 2,257.49	07/2018 -	04/2020	0/0
765	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 3,007.86	06/2018 -	04/2020	0/0
766	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	04/2020	0/0
767	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	06/2018 -	04/2020	0/0
768	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 1,367.00	- -	04/2020	0/0
769	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	04/2020 -	04/2020	0/0
770	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	03/2020 -	04/2020	0/0
771	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	04/2020	0/0
772	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	05/2020	0/0
773	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	07/2018 -	05/2020	0/0
774	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	- -	05/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
775	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 911.07	02/2020 11/2017	05/2020	0/0
776	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 2,602.09	03/2020 11/2017	05/2020	0/0
777	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	05/2020	0/0
778	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	07/2016 -	05/2020	0/0
779	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 3,207.63	- 02/2018	05/2020	0/0
780	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	06/2020	0/0
781	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 04/2017	06/2020	0/0
782	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 2,182.03	06/2018 -	06/2020	0/0
783	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 2,433.38	06/2018 -	06/2020	0/0
784	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 06/2020	06/2020	0/0
785	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	06/2020	0/0
786	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	09/2017 -	06/2020	0/0
787	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	- -	06/2020	0/0
788	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	07/2020	0/0
789	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	04/2019 07/2020	07/2020	0/0
790	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	07/2020	0/0
791	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 1,464.12	- -	07/2020	0/0
792	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	07/2020	0/0
793	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	06/2017 -	07/2020	0/0
794	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 -	08/2020	0/0
795	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 01/2019	08/2020	0/0
796	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 870.00	03/2019 03/2017	08/2020	0/0
797	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	- -	08/2020	0/0
798	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	09/2017 -	08/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
799	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 12/2019	09/2020	0/0
800	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	05/2018 -	09/2020	0/0
801	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 2,170.44	- -	09/2020	0/0
802	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	08/2017 -	09/2020	0/0
803	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN	02/2018	1,103.88 -	- -	09/2020	0/0
804	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 09/2017	10/2020	0/0
805	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- 10/2020	10/2020	0/0
806	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 448.18	- -	10/2020	0/0
807	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 11/2020	11/2020	0/0
808	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	03/2019 -	11/2020	0/0
809	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	03/2019 -	11/2020	0/0
810	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 05/2018	11/2020	0/0
811	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	11/2020	0/0
812	FOUR LANINIG OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	- -	11/2020	0/0
813	FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	- -	11/2020	0/0
814	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	- 11/2020	11/2020	0/0
815	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	- -	11/2020	0/0
816	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	08/2016 -	12/2020	0/0
817	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	12/2020	0/0
818	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 247.00	04/2018 -	12/2020	0/0
819	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	07/2019 12/2020	12/2020	0/0
820	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	07/2019 12/2020	12/2020	0/0
821	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 1,008.00	08/2019 -	12/2020	0/0
822	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAUR ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	12/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
823	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- 03/2020	12/2020	0/0
824	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	- -	12/2020	0/0
825	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA	03/2018	1,484.30 -	- -	12/2020	0/0
826	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	- -	12/2020	0/0
827	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	- -	01/2021	0/0
828	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76 -	- -	01/2021	0/0
829	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT	02/2018	1,052.21 1,449.00	- -	01/2021	0/0
830	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	- 05/2018	01/2021	0/0
831	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	03/2019 -	02/2021	0/0
832	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	- -	02/2021	0/0
833	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	- -	02/2021	0/0
834	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	03/2021	0/0
835	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	08/2019 -	03/2021	0/0
836	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	03/2019 -	03/2021	0/0
837	REHABILITAITON AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	03/2021	0/0
838	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	03/2020 -	03/2021	0/0
839	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 -	- 03/2021	03/2021	0/0
840	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 1,073.10	- 03/2019	03/2021	0/0
841	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	03/2019 04/2021	04/2021	0/0
842	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92 -	- -	04/2021	0/0
843	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 -	- -	04/2021	0/0
844	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	03/2020 -	05/2021	0/0
845	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 1,071.75	- -	05/2021	0/0
846	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	07/2017 11/2020	06/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
847	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	- 07/2020	06/2021	0/0
848	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	- -	06/2021	0/0
849	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	- 05/2020	06/2021	0/0
850	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	- 05/2020	06/2021	0/0
851	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	- 03/2020	06/2021	0/0
852	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- 06/2021	06/2021	0/0
853	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	- -	06/2021	0/0
854	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	- -	06/2021	0/0
855	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	07/2021	0/0
856	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 -	- -	07/2021	0/0
857	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	- -	07/2021	0/0
858	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	- -	07/2021	0/0
859	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 1,687.00	- 12/2018	07/2021	0/0
860	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 931.21	- -	07/2021	0/0
861	SIX LANING AND STREGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 -	- -	07/2021	0/0
862	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 -	- -	07/2021	0/0
863	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	- -	08/2021	0/0
864	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	- -	08/2021	0/0
865	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 2,946.82	06/2020 -	09/2021	0/0
866	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 2,190.00	- 05/2019	11/2021	0/0
867	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	- -	12/2021	0/0
868	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	08/2017 -	02/2022	0/0
869	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-	0/0
870	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
871	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-	0/0
872	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-	0/0
873	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	-	0/0
874	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	-	0/0
875	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-	0/0
876	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-	0/0
877	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-	0/0
878	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-	0/0
879	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	-	0/0
880	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	-	0/0
881	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHTH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	-	0/0
882	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	06/2015 -	-	0/0
883	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-	0/0
884	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-	0/0
885	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA	08/2015	723.54 1,286.84	02/2018 10/2017	-	0/0
886	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-	0/0
887	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	-	0/0
888	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	01/2016 -	-	0/0
889	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	-	0/0
890	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	05/2019 -	-	0/0
891	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	05/2019 -	-	0/0
892	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	04/2018 -	-	0/0
893	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	04/2019 -	-	0/0
894	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	01/2019 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
895	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-	0/0
896	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-	0/0
897	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	-	0/0
898	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	04/2019 -	-	0/0
899	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA	11/2015	867.66 1,464.24	05/2018 02/2018	-	0/0
900	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-	0/0
901	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-	0/0
902	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-	0/0
903	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-	0/0
904	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 151.11	07/2018 -	-	0/0
905	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	04/2019 -	-	0/0
906	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	11/2018 -	-	0/0
907	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 3,267.94	- 03/2017	-	0/0
908	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	03/2019 -	-	0/0
909	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPU - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-	0/0
910	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	-	0/0
911	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 241.41	- -	-	0/0
912	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	10/2018 -	-	0/0
913	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-	0/0
914	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-	0/0
915	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA	03/2017	639.79 -	03/2020 -	-	0/0
916	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-	0/0
917	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
918	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-	0/0
919	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-	0/0
920	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-	0/0
921	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-	0/0
922	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 999.00	- 06/2019	-	0/0
923	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH	01/2018	960.24 -	- -	-	0/0
924	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-	0/0
925	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	- -	-	0/0
926	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 929.89	- -	-	0/0
927	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-	0/0
928	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-	0/0
929	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-	0/0
930	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-	0/0
931	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 2,283.50	- 10/2019	-	0/0
932	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 1,065.70	- -	-	0/0
933	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 1,197.00	- -	-	0/0
934	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 -	- -	-	0/0
935	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN	02/2018	716.76 -	- -	-	0/0
936	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-	0/0
937	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 1,332.00	- -	-	0/0
938	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-	0/0
939	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-	0/0
940	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-	0/0
941	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
942	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-	0/0
943	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA	03/2018	950.63 -	- -	-	0/0
944	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA	03/2018	857.62 -	- -	-	0/0
945	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA	03/2018	828.29 998.89	- 11/2019	-	0/0
946	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU	03/2018	633.55 -	- -	-	0/0
947	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96 -	- -	-	0/0
948	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	- -	-	0/0
949	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	-	0/0
950	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT	03/2018	1,161.39 1,404.00	- 11/2021	-	0/0
951	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN	03/2018	874.25 -	- -	-	0/0
952	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN	03/2018	1,158.35 -	- -	-	0/0
953	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB	03/2018	199.90 149.90	- -	-	0/0
954	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH – 14 - [N24001185]NHAI,UTTAR PRADESH	11/2017	2,159.00 -	01/2019 -	-	0/0
955	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA	01/2019	1,051.91 -	- -	-	0/0
956	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA	01/2019	1,120.06 -	- -	-	0/0
957	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA	01/2019	1,137.42 -	- -	-	0/0
958	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA	01/2019	1,033.19 -	- -	-	0/0
959	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA	01/2019	1,243.45 -	- -	-	0/0
960	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA	01/2019	889.36 -	- -	-	0/0
961	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA	01/2019	1,018.79 -	- -	-	0/0
962	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA	01/2019	996.65 -	- -	-	0/0
963	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH	10/2019	743.88 -	- -	-	0/0
964	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]NHAI,MADHYA PRADESH	12/2017	656.98 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
965	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213]NHAI,MADHYA PRADESH	12/2017	1,094.97 -	- -	-	0/0
966	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]NHAI,MADHYA PRADESH	12/2017	217.96 -	- -	-	0/0
967	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 275.00	05/2017 -	-	0/0
968	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	-	0/0
969	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 1,444.25	- 02/2019	-	0/0
	SHIPPING AND PORTS					
	Inland Waterways Authority Of India					
970	JAL MARG VIKAS PROJECT - [N25000072]IWAI,MULTI STATE	01/2018	4,200.00 5,369.18	03/2023 03/2023	03/2023	0/0
	TELECOMMUNICATIONS					
	Bharat Sanchar Nigam Limited					
971	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]BSNL,MAHARASHTRA	01/2018	231.80 240.10	10/2018 12/2019	12/2019	0/0
	Department Of Telecommunication					
972	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	07/2015 -	05/2020	0/0
	Mahanagar Telephone Nigam Limited					
973	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI	06/2016	418.26 -	06/2017 -	-	0/0
	URBAN DEVELOPMENT					
	Ahmedabad Metro Rail					
974	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	12/2018 -	07/2020	0/0
975	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137]MEGA,GUJARAT	03/2019	5,384.17 -	03/2024 -	03/2024	0/0
976	SURAT METRO RAIL PROJECT - [N28000138]MEGA,GUJARAT	03/2019	12,020.32 -	03/2024 -	03/2024	0/0
	Bangalore Metro Rail Corporation Limited					
977	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	02/2019 -	03/2020	0/0
	Central Public Works Department					
978	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH	11/2017	171.72 -	03/2020 -	03/2020	0/0
979	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN	12/2016	549.31 559.47	07/2019 12/2019	04/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
980	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2016	248.20 -	04/2018 02/2020	08/2020	0/0
981	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI	10/2017	271.90 -	11/2019 08/2020	08/2020	0/0
982	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]CPWD,KARNATAKA	12/2016	246.31 -	02/2020 -	09/2020	0/0
983	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 -	- -	12/2020	0/0
984	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	06/2017 -	03/2021	0/0
985	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 -	- 08/2020	03/2021	0/0
986	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD,HIMACHAL PRADESH	12/2018	260.00 -	06/2021 -	06/2021	0/0
987	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128]CPWD,DELHI	10/2016	1,180.00 -	07/2021 -	07/2021	0/0
988	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU	11/2017	348.77 -	- -	11/2021	0/0
989	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]CPWD,DELHI	10/2016	1,128.00 -	03/2022 -	03/2022	0/0
990	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD,ODISHA	01/2019	790.79 -	03/2022 -	06/2022	0/0
991	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	12/2015 -	-	0/0
992	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	12/2013 -	-	0/0
993	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]CPWD,DELHI	12/2017	188.00 -	06/2019 -	-	0/0
994	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]CPWD,JAMMU AND KASHMIR	03/2019	329.00 -	- -	-	0/0
995	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]CPWD,JAMMU AND KASHMIR	01/2018	676.00 -	- -	-	0/0
	Delhi Metro Rail Corporation					
996	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]DMRC,DELHI	05/2017	565.00 -	12/2020 -	12/2020	0/0
997	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS - [N28000135]DMRC,DELHI	07/2019	24,948.65 -	03/2025 -	03/2025	0/0
998	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	03/2016 -	-	0/0
	Hindustan Steelwork Construction Limited					
999	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	03/2015 -	03/2021	0/0
1000	CONSTRUCTION AND MAINTEINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	-	0/0
1001	CONSTRUCTION AND MAINTEINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
1002	CONSTRUCTION AND MAINTEINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	12/2016 -	-	0/0
1003	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 -	-	0/0
1004	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	-	0/0
1005	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	09/2017 -	-	0/0
1006	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	- -	-	0/0
1007	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT	01/2013	175.00 -	- -	-	0/0
1008	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	03/2017 -	-	0/0
1009	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTEINANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	06/2016 -	-	0/0
1010	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND	12/2007	200.00 -	03/2018 -	-	0/0
1011	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	12/2016 -	-	0/0
1012	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND	04/2013	170.00 -	04/2018 -	-	0/0
1013	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL	08/2012	185.37 -	03/2016 -	-	0/0
	Jawahar Lal Nehru National Urban Renewal Mission					
1014	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-	0/0
	Kochi Metro Rail Corporation Ltd					
1015	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 5,687.79	07/2017 -	03/2020	0/0
	Lucknow Metro Rail Corporation Limited					
1016	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	-	0/0
	Maharastra Metro Rail Corporation Ltd.					
1017	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA	12/2016	11,420.00 -	11/2021 03/2022	03/2022	0/0
	Mumbai Metro Rail Corporation Ltd					
1018	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	05/2020	0/0
	Madhya Pradesh Metro Rail Co Limited					
1019	BHOPAL METRO RAIL - [N28000124]MPMRCL,MADHYA PRADESH	11/2018	6,941.40 -	02/2023 -	02/2023	0/0
1020	INDORE METRO RAIL - [N28000125]MPMRCL,MADHYA PRADESH	11/2018	7,500.80 -	02/2023 -	02/2023	0/0
	Nagpur Metro Rail Corporation Ltd					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
1021	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	12/2019	0/0
	National Building Construcion Corporation Ltd					
1022	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI	07/2016	2,694.00 -	- -	-	0/0
	National Capital Region Transport Corp					
1023	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134]NCRTC,MULTI STATE	03/2019	30,274.00 -	06/2025 -	06/2025	0/0
	WATER RESOURCES					
	Brahmaputra Board					
1024	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB,MAHARASHTRA	03/2017	233.57 -	12/2019 -	12/2019	0/0
	Bihar Urban Infrastructure Development Corporation Ltd					
1025	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO,BIHAR	12/2014	225.77 -	03/2020 -	03/2020	0/0
1026	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR - [N30000038]BUIDCO,BIHAR	04/2015	184.93 -	04/2020 -	04/2020	0/0
1027	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO,BIHAR	10/2017	254.13 -	09/2020 -	09/2020	0/0
1028	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO,BIHAR	05/2017	191.62 -	11/2020 -	11/2020	0/0
1029	I AND D AND STP AT CHAPPRA - [N30000028]BUIDCO,BIHAR	11/2018	236.15 -	12/2020 -	12/2020	0/0
1030	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO,BIHAR	04/2015	268.63 -	01/2021 -	01/2021	0/0
1031	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]BUIDCO,BIHAR	05/2017	356.37 -	04/2021 -	04/2021	0/0
1032	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA - [N30000041]BUIDCO,BIHAR	05/2017	184.86 -	05/2021 -	05/2021	0/0
1033	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]BUIDCO,BIHAR	03/2017	277.42 -	05/2021 -	05/2021	0/0
1034	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]BUIDCO,BIHAR	03/2018	230.06 -	07/2021 -	07/2021	0/0
1035	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO,BIHAR	03/2018	305.19 -	08/2021 -	08/2021	0/0
1036	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036]BUIDCO,BIHAR	03/2018	294.02 -	10/2021 -	10/2021	0/0
1037	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]BUIDCO,BIHAR	08/2017	578.89 -	06/2022 -	06/2022	0/0
1038	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051]BUIDCO,BIHAR	08/2017	824.00 -	06/2022 -	06/2022	0/0
	Delhi Jal Board					
1039	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB,DELHI	05/2017	344.81 -	05/2020 -	05/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
1040	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O&M AT CORONATION PILLAR DELHI - [N30000017]DJB,DELHI	12/2018	515.07 -	01/2021 -	01/2021	0/0
1041	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB,DELHI	05/2016	211.79 -	12/2021 -	12/2021	0/0
1042	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB,DELHI	05/2016	239.11 -	02/2022 -	02/2022	0/0
1043	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]DJB,DELHI	03/2017	665.78 -	12/2022 -	12/2022	0/0
	Kolkata Metropolitan Development Authority					
1044	SEWERAGE SYSTEM & STP WORKS AT HALISHAHR - [N30000046]KMDA,WEST BENGAL	02/2014	274.76 -	12/2019 -	12/2019	0/0
1045	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA,WEST BENGAL	12/2014	272.32 -	04/2020 -	04/2020	0/0
1046	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]KMDA,WEST BENGAL	08/2017	185.22 -	12/2021 -	12/2021	0/0
1047	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]KMDA,WEST BENGAL	01/2018	172.10 -	12/2021 -	12/2021	0/0
1048	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]KMDA,WEST BENGAL	10/2017	164.93 -	12/2021 -	12/2021	0/0
1049	INTERCEPTION & DIVERSION WITH STP AT MAHESHTALA - [N30000032]KMDA,WEST BENGAL	05/2018	198.43 -	02/2022 -	02/2022	0/0
1050	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH - [N30000042]KMDA,WEST BENGAL	05/2018	160.00 -	02/2022 -	02/2022	0/0
1051	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]KMDA,WEST BENGAL	01/2019	384.96 -	04/2022 -	04/2022	0/0
1052	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPURL - [N30000030]KMDA,WEST BENGAL	03/2019	287.53 -	04/2022 -	04/2022	0/0
1053	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]KMDA,WEST BENGAL	12/2018	234.31 -	04/2022 -	04/2022	0/0
1054	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]KMDA,WEST BENGAL	03/2018	165.16 -	06/2022 -	06/2022	0/0
1055	INTERCEPTION DIVERSION AND TREATMENT WORKS AT TOLLY'S NULLAH ADI GANGA - [N30000034]KMDA,WEST BENGAL	08/2017	307.12 -	09/2022 -	09/2022	0/0
	Uttar Pradesh Jal Nigam					
1056	SEWERAGE WORKS IN SEWERAGE DISTRICT A OF ALLAHABAD - [N30000005]UPJalNigam,UTTAR PRADESH	02/2014	288.94 -	09/2019 -	09/2019	0/0
1057	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA - [N30000011]UPJalNigam,UTTAR PRADESH	02/2017	161.31 -	11/2019 -	11/2019	0/0
1058	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]UPJalNigam,UTTAR PRADESH	02/2011	279.91 -	12/2019 -	12/2019	0/0
1059	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR - [N30000009]UPJalNigam,UTTAR PRADESH	10/2016	370.40 -	08/2020 -	08/2020	0/0
1060	MATHURA SEWERAGE SCHEME - [N30000019]UPJalNigam,UTTAR PRADESH	12/2017	460.45 -	12/2020 -	12/2020	0/0
1061	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UPJalNigam,UTTAR PRADESH	03/2019	298.12 -	07/2021 -	07/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
1062	REHABILITATION RENOVATION OF AGRA SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS IN AGRA UTTAR PR - [N30000012]UPJalNigam,UTTAR PRADESH	12/2018	857.26 -	08/2021 -	08/2021	0/0
1063	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH - [N30000013]UPJalNigam,UTTAR PRADESH	03/2019	271.39 -	08/2021 -	08/2021	0/0
1064	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS AT AGRA - [N30000023]UPJalNigam,UTTAR PRADESH	02/2019	317.19 -	08/2021 -	08/2021	0/0
1065	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]UPJalNigam,UTTAR PRADESH	05/2017	767.59 -	09/2021 -	09/2021	0/0
1066	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS - [N30000007]UPJalNigam,UTTAR PRADESH	03/2018	904.00 -	09/2021 -	09/2021	0/0
1067	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]UPJalNigam,UTTAR PRADESH	03/2018	967.23 -	09/2021 -	09/2021	0/0
1068	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]UPJalNigam,UTTAR PRADESH	01/2019	206.05 -	10/2021 -	10/2021	0/0
1069	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]UPJalNigam,UTTAR PRADESH	01/2019	231.79 -	12/2021 -	12/2021	0/0
1070	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]UPJalNigam,UTTAR PRADESH	10/2017	213.62 -	03/2022 -	03/2022	0/0
1071	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]UPJalNigam,UTTAR PRADESH	02/2019	681.78 -	06/2022 -	06/2022	0/0
	Uttarakhand Pey Jal Nigam					
1072	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI - [N30000003]UKJalNigam,UTTARAKHAND	03/2017	273.37 -	08/2019 -	08/2019	0/0
1073	INTERCEPTION AND DIVERSION (I&D)WITH STP AT RISHIKESH - [N30000004]UKJalNigam,UTTARAKHAND	03/2017	158.00 -	11/2019 -	11/2019	0/0
	HUMAN RESOURCE DEPARTMENT					
	Rail India Technical And Economic Service					
1074	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES,MEGHALAYA	09/2013	484.32 -	09/2014 -	12/2020	0/0
	Total		12,10,054.85 -			0/0
	Grand Total		12,10,054.85			0/0

MoSPI OCMS

Annexure - XI

List of Projects Ahead of Schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above							(November 2019)
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	COAL						
	South-Eastern Coal Fields Limited						
1	BATURA OCP (2.0 MTY) - [N06000049	8/2015	1,186.64 -	203.82	123.05	03/2023 -	03/2021
	Total		1,186.64 -	203.82	123.05		
	PETROLEUM						
	Indian Oil Corporation Limited						
2	PARADIP HYDERABAD PIPLEINE - [N16000194	1/2015	2,321.00 3,338.00	3,338.00	1,912.90	12/2020 -	08/2020
3	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254	9/2015	324.00 -	324.00	192.32	06/2020 -	03/2020
4	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302	8/2017	384.58	384.58	105.36	04/2021 -	09/2020
5	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252	5/2016	664.00 -	729.40	663.70	12/2020 -	02/2020
6	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308	8/2017	315.00 -	315.00	116.26	12/2021 -	12/2020
7	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332	3/2018	3,712.00 -	3,696.00	683.33	09/2022 -	06/2021
	Total		7,720.58 -	8,786.98	3,673.87		
	POWER						
	National Thermal Power Corporation						
8	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192	1/2013	12,964.60 17,304.00	17,304.00	14,229.00	05/2018 12/2021	06/2021
	Power Grid Corporation Of India Limited						
9	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164	5/2014	522.29 546.36	546.36	470.50	11/2016 06/2020	03/2020
10	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242	2/2017	322.30 -	322.30	164.09	02/2019 04/2020	03/2020
	Total		13,809.19 -	18,172.66	14,863.59		
	RAILWAYS						
	Central Railways						

Costing Rs. 150 Crore and above							(November 2019)
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
11	PUNE-MIRAJ-LONDA (467 KM) - [N22000359	2/2015	3,627.47 -	3,627.47	761.03	03/2024 -	03/2023
	East Central Railways						
12	GARHWA ROAD-RAMNA - [N22000465	3/2015	348.23 -	348.23	187.91	03/2021 -	12/2020
	North East Frontier Railway						
13	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388	4/2015	2,232.32 -	2,182.00	756.32	03/2022 -	03/2020
14	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390	4/2016	602.27 -	612.00	336.17	12/2021 -	03/2020
	North Eastern Railway						
15	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347	3/2015	1,295.42 -	1,295.42	350.85	03/2022 -	12/2019
	Rail Vikas Nigam Ltd.						
16	BHANUPALI-BILASPUR BERI NL - [N22000273	4/2008	2,966.99 -	7,000.00	446.46	12/2026 -	12/2025
17	DIGHI PORT NEW LINE - [N22000408	4/2015	723.78 -	723.78	0.19	12/2025 -	03/2025
	Total		11,796.48 -	15,788.90	2,838.93		
	ROAD TRANSPORT AND HIGHWAYS						
	Ministry Of Road Transport And Highways (State Pwds)						
18	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933	2/2017	429.43 -	429.43	209.09	11/2017 03/2020	11/2019
19	PARSHURAM GHAT TO ARAWALI - [N24001133	4/2016	983.14	983.14	655.15	12/2019 -	11/2019
20	REHABILITAITON AND UPGRADATION OF REPALLE TO EEPPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970	1/2017	576.48 -	576.48	228.31	01/2018 12/2020	01/2020
	National Highways Authority Of India						
21	GWALIOR-JHANSI, NH-75 - [N24000089	12/2003	604.00 364.59	364.59	215.58	12/2009 08/2020	03/2020
22	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655	3/2017	247.02 -	157.49	30.60	03/2020 02/2021	02/2020
23	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691	4/2017	894.00 -	929.32	750.00	04/2020 -	11/2019
24	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503	10/2015	447.29 746.43	746.43	613.57	12/2017 06/2020	12/2019
	Total		4,181.36 -	4,186.88	2,702.30		
	Grand Total		38,694.25	47,139.24	24,201.74		

List of Projects on schedule w.r.t. Latest Schedule

Annexure - XII

Costing Rs. 150 Crore and above							(November 2019)
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
	CIVIL AVIATION						
	Airport Authority Of India Limited						
1	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075	8/2018	951.28 -	951.28	71.55	10/2021 -	10/2021
2	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077	6/2018	1,383.00 -	1,383.00	210.62	09/2021 -	09/2021
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT - [N04000079	3/2017	358.89 -	358.89	29.73	04/2021 -	04/2021
4	CONSTRUCTION OF TERMINAL BUILDING & ASSOCIATED WORKS AT LEH AIRPORT - [N04000078	7/2018	323.19 -	323.19	10.14	09/2021 -	09/2021
5	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081	1/2019	264.99 -	264.99	.42	11/2021 -	11/2021
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083	12/2016	859.86 -	860.00	232.44	03/2021 -	03/2021
7	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085	7/2018	353.27 -	353.27	114.29	09/2020 -	09/2020
8	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082	5/2018	539.20 -	539.20	25.64	10/2022 -	10/2022
	Total		5,033.68 -	5,033.82	694.83		
	COAL						
	Bharat Coking Coal Limited						
9	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106	2/2014	555.52 -	555.52	5.24	03/2021 -	03/2021
10	MADHUBAND NLW WASHERY - [N06000126	8/2010	289.45 -	289.45	260.10	05/2014 03/2020	03/2020
11	MOONIDIH XV SEAM UG - [N06000098	8/2011	1,230.27 -	1,230.27	401.81	04/2015 04/2022	04/2022
	Central Coal Fields Limited						
12	AMRAPALI OC(12MTY) - [N06000103	2/2012	858.11 -	858.11	187.61	03/2020 -	03/2020
13	NORTH URIMARI EXPANSION OCP - [N06000182	3/2019	1,553.06 -	1,553.06	203.46	03/2023 -	03/2023
	Eastern Coal Fields Limited						
14	JHANJRA COMBINED PR(3.50 MTY) - [N06000020	11/2015	602.86 -	602.86	317.12	03/2022 -	03/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning	
						Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
15	NAKRAKONDA KUMARDIH B OCP - [N06000170	8/2018	502.68 -	502.68	-	03/2029 -	03/2029
16	TILABONI UG MINE - [N06000172	2/2019	916.62 -	916.62	-	03/2027 -	03/2027
17	CHITRA EAST (RCE) OCP - [N06000169	8/2018	513.98 -	513.98	92.51	03/2024 -	03/2024
18	HURA - C OC (3 MTY) - [N06000143	10/2015	359.69 -	359.69	84.91	03/2022 -	03/2022
19	SIDULI MINE (OC AND UG) - [N06000165	5/2018	535.18 -	535.18	-	03/2026 -	03/2026
	Mahanadi Coal Fields Limited						
20	SIARMAL OCP (40.00MTY) - [N06000113	5/2014	3,756.36 -	3,756.36	1,205.32	03/2026 -	03/2026
21	GARJANBAHAL OCP - [N06000117	11/2014	1,375.38 -	1,375.38	445.39	03/2021 -	03/2021
22	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171	11/2018	2,838.87 -	2,838.87	1,157.99	03/2029 -	03/2029
23	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167	5/2018	2,434.75 -	2,434.75	123.99	03/2027 -	03/2027
	Neyveli Lignite Corporation						
24	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145	3/2015	513.63 -	513.63	175.30	12/2019 -	12/2019
25	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152	7/2016	17,237.00 -	17,237.80	8,032.77	11/2021 -	11/2021
	Northern Coal Fields Limited						
26	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159	5/2017	1,783.09 -	1,783.09	267.80	03/2021 -	03/2021
27	BLOCK-B EXPANSION OPENCAST PROJECT - [N06000184	7/2019	998.71 -	998.71	-	03/2023 -	03/2023
28	SEMARIA OPENCAST PROJECT - [N06000176	5/2019	396.58 -	396.58	-	03/2026 -	03/2026
29	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162	11/2017	1,255.17 -	1,255.17	95.24	03/2022 -	03/2022
	Singareni Colliers Company Limitted						
30	KALYANIKHANI 6 INCLINE PROJECT - [N06000147	12/2015	477.65 -	477.65	2.11	03/2020 -	03/2020
	South-Eastern Coal Fields Limited						
31	PELMA OCP(15.00MTY) - [N06000045	11/2014	1,624.59 -	1,624.59	6.50	03/2023 -	03/2023
32	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124	12/2014	357.80 -	357.80	104.66	03/2021 -	03/2021
33	AMGAON OPENCAST PROJECT RCE - [N06000135	7/2015	316.10 -	316.10	86.43	03/2020 -	03/2020
34	JHIRIA WEST OPENCAST PROJECT - [N06000166	11/2018	389.97 -	389.97	-	03/2026 -	03/2026
35	MAHAMAYA OPENCAST PROJECT - [N06000164	5/2018	410.26 -	410.26	9.53	03/2026 -	03/2026

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning	
						Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
36	VIJAY WEST OPENCAST PROJECT - [N06000158	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026
37	AMADAND OPENCAST EXPANSION PROJECT - [N06000148	3/2016	869.44 -	869.44	116.75	03/2021 -	03/2021
38	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093	6/2010	11,816.40 -	11,816.40	2,891.13	03/2023 -	03/2023
39	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008	8/2013	7,612.33 -	7,612.33	2,116.58	03/2023 -	03/2023
40	DURGAPUR OPENCAST PROJECT - [N06000136	2/2015	916.24 -	916.24	4.11	03/2023 -	03/2023
41	BATURA HIGHWALL PROJECT - [N06000134	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
42	KANCHAN OC EXPANSION - [N06000125	12/2014	371.04 -	371.04	48.13	03/2021 -	03/2021
43	AMRITDHARA OC PROJECT - [N06000122	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
44	BIJARI OC RCE (1.50 MTY) - [N06000111	5/2014	164.49 -	164.49	82.91	03/2020 -	03/2020
45	CHHAL OC SEAM -III (6.00 MTY) - [N06000104	12/2013	610.63 -	610.63	105.36	03/2022 -	03/2022
46	MADANNAGAR OPENCAST PROJECT - [N06000140	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
47	MALACHUA OPENCAST PROJECT - [N06000139	10/2015	488.33 -	488.33	27.33	03/2023 -	03/2023
	Western Coal Fields Limited						
48	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142	11/2015	498.42 -	498.42	189.52	03/2020 -	03/2020
49	KOLAR PIMPRI EXTENSION OC - [N06000160	3/2017	362.73 -	362.73	322.07	03/2020 -	03/2020
50	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157	2/2017	328.00 -	328.00	167.00	03/2021 -	03/2021
51	DHANKASA UG (1.00 MTY) - [N06000155	9/2016	458.07 -	458.07	20.86	03/2022 -	03/2022
52	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154	8/2016	319.76 -	319.76	238.99	03/2022 -	03/2022
53	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153	7/2016	409.87 -	409.87	19.05	03/2022 -	03/2022
54	PENGANGA OCP(REVISED) - [N06000066	9/2014	441.82 -	441.82	215.48	03/2020 -	03/2020
55	AMALGAMATED YEKONA-I YEKONA-II - [N06000132	8/2015	727.28 -	727.28	260.88	03/2025 -	03/2025
56	AMALGAMATED PAUNI-II III OC MINE - [N06000131	6/2015	483.69 -	483.69	219.00	03/2021 -	03/2021
57	GANDHIGRAM UG MINE - [N06000183	8/2019	414.16 -	414.16	.01	03/2026 -	03/2026
58	BELLORA-NAIGAON DEEP OC - [N06000180	11/2018	252.71 -	252.71	45.09	03/2021 -	03/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning: Original /Revised	Date of Commissioning: Anticipated
1	2	3	4	5	6	7	8
59	UKNI DEEP OC - [N06000179	11/2018	318.14 -	318.14	143.90	03/2021 -	03/2021
60	VISHNUPURI UG TO OC MINE - [N06000178	7/2018	195.57 -	195.57	2.94	03/2025 -	03/2025
61	SAONER I UG TO OC PHASE I - [N06000177	11/2016	162.10 -	162.10	50.64	03/2022 -	03/2022
62	SINGHORI OC MINE - [N06000130	6/2015	205.49 -	205.49	117.56	03/2020 -	03/2020
63	BHANEGAON OC - [N06000121	2/2015	187.94 -	409.68	127.70	03/2023 -	03/2023
64	DINESH OCP - [N06000118	11/2014	611.16 -	611.16	413.02	03/2020 -	03/2020
	Total		76,874.93 -	77,097.47	21,287.76		
	FERTILISERS						
	National Fertiliser Limited						
65	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014	1/2018	215.92 -	215.92	128.60	11/2019 -	11/2019
66	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015	1/2018	218.83 -	218.83	131.34	11/2019 -	11/2019
67	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016	1/2018	239.81 -	239.81	145.72	11/2019 -	11/2019
	Rashtriya Chemical & Fertiliser Limited						
68	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018	4/2018	426.72 -	426.72	249.06	04/2020 -	04/2020
	Total		1,101.28 -	1,101.28	654.72		
	HEALTH AND FAMILY WELFARE						
	HIl Infra Tech Services Limited						
69	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027	5/2017	875.00 -	747.80	110.70	05/2021 10/2021	10/2021
	National Building Construcion Corporation Ltd						
70	AIIMS BILASPUR - [N21000028	4/2018	1,351.00 -	1,351.00	245.85	09/2021 -	09/2021
	Total		2,226.00 -	2,098.80	356.55		
	INFORMATION AND BROADCASTING						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning: Original /Revised	Date of Commissioning: Anticipated
1	2	3	4	5	6	7	8
71	NATIONAL CENTRE OF EXCELLENCE FOR ANIMATION VISUAL EFFECTS GAMING AND COMICS - [N09000003	12/2016	167.70 -	167.70	-	03/2020 -	03/2020
	Total		167.70 -	167.70	.00		
	MINES						
	National Aluminum Company Limited (Nalco)						
72	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010	12/2014	5,540.00 -	5,540.00	114.95	04/2021 04/2021	04/2021
73	UTKAL D AND E COAL BLOCK - [N10000011	5/2016	534.00 -	534.00	320.18	01/2020 -	01/2020
74	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014	9/2017	166.62 -	163.17	135.00	06/2019 03/2020	03/2020
75	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013	11/2017	483.00 -	483.00	1.20	04/2021 04/2021	04/2021
76	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012	12/2015	355.00 -	355.00	82.07	11/2020 -	11/2020
	Total		7,078.62 -	7,075.17	653.40		
	PETROLEUM						
	Bharat Petroleum Corporation Limited						
77	HALDIA LPG IMPORT FACILITY - [N16000223	3/2015	694.00 -	1,097.54	722.99	10/2018 12/2019	12/2019
78	MMPL PIPELINE REROUTING PROJECT - [N16000261	4/2013	449.58 -	449.58	192.13	12/2019 07/2020	07/2020
79	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260	2/2016	554.00 -	554.00	375.80	02/2020 -	02/2020
80	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263	2/2016	3,313.00 -	3,288.96	1,349.99	02/2020 10/2020	10/2020
81	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314	12/2015	1,112.00 -	1,507.24	555.00	06/2019 02/2022	02/2022
82	2ND GENERATION LIGNOCELLUOSIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA) - [N16000374	8/2019	1,607.00 -	1,607.00	37.49	08/2022 -	08/2022
83	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373	11/2018	248.55 -	248.55	23.38	06/2022 -	06/2022
84	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365	12/2017	1,524.06 -	1,524.06	20.02	12/2021 -	12/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning	
						Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
85	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364	7/2017	580.20 -	580.20	47.41	02/2021 -	02/2021
86	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347	10/2018	206.26 -	206.26	2.84	03/2021 -	03/2021
87	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346	9/2018	11,130.00 -	11,130.00	54.40	03/2023 -	03/2023
88	2G ETHANOL BIO REFINERY AT BARGARH - [N16000341	8/2017	750.00 -	750.00	34.73	12/2020 -	12/2020
89	PUNE POL STORAGE DEPOT - [N16000313	8/2016	282.64 -	282.64	145.83	08/2020 -	08/2020
	Chennai Petroleum Corporation Limited						
90	BS-VI PROJECTS - [N16000295	9/2017	1,858.00 -	1,858.00	1,119.38	12/2019 -	12/2019
91	RE-LIQUIFIED NATURAL GAS - [N16000301	8/2017	421.00 -	421.00	159.94	08/2020 -	08/2020
	Gas Authority Of India Limited						
92	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210	2/2015	749.00 -	842.00	606.89	02/2020 -	02/2020
93	BOKARO-ANGUL PIPELINE PROJECT - [N16000274	3/2017	3,437.00 -	3,437.00	1,309.83	12/2020 -	12/2020
94	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275	3/2017	1,740.00 -	1,740.00	462.88	12/2020 -	12/2020
95	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288	4/2017	287.49 -	287.49	133.40	04/2022 -	04/2022
96	BARAUNI-GUWAHATI PIPELINE - [N16000334	6/2018	3,308.00 -	3,308.00	1,349.36	12/2021 -	12/2021
97	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR - [N16000330	10/2017	221.45 -	221.45	51.10	10/2022 -	10/2022
98	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329	10/2017	226.45 -	226.45	56.99	10/2022 -	10/2022
99	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328	7/2017	182.20 -	182.20	32.85	07/2022 -	07/2022
100	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327	10/2017	359.25 -	359.25	75.57	10/2022 -	10/2022
101	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289	7/2017	243.53 -	243.53	55.03	07/2022 -	07/2022
102	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285	6/2009	2,915.00 2,915.00	4,915.00	2,742.24	12/2012 02/2022	02/2022
103	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273	3/2017	2,433.00 -	2,433.00	1,496.03	12/2020 -	12/2020
104	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271	7/2015	2,881.40 -	2,000.00	1,293.26	12/2020 -	12/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning	
						Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
105	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355	8/2018	286.42 -	286.42	1.92	08/2020 09/2020	09/2020
106	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349	9/2018	225.54 -	225.54	2.35	02/2021 -	02/2021
107	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272	3/2017	1,933.00 -	1,933.00	1,055.91	12/2020 -	12/2020
	Hindustan Petroleum Corporation Limited						
108	VISAKH REFINERY MODERNISATION PROJECT - [N16000235	7/2016	20,928.00 -	26,264.00	7,245.30	07/2020 07/2022	07/2022
109	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238	9/2016	1,879.00 -	1,879.00	1,536.16	06/2020 -	06/2020
110	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367	6/2019	2,166.38 -	2,166.38	15.61	06/2022 -	06/2022
111	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369	12/2018	854.00 -	854.00	38.34	12/2022 -	12/2022
112	REDEVELOPMENT/ EXPANSION OF MEERUT DEPOT FOR ENHANCING PRODUCT HANDLING CAPACITY - [N16000366	8/2016	154.84 -	154.84	128.71	11/2019 -	11/2019
113	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296	9/2017	2,677.00 -	2,677.00	971.81	03/2021 -	03/2021
114	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312	11/2017	255.00 -	255.00	94.33	11/2020 -	11/2020
115	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH - [N16000311	12/2016	300.00 -	300.00	1.09	04/2021 -	04/2021
116	MUMBAI REFINERY EXPANSION PROJECT - [N16000281	9/2015	4,199.00 -	5,060.00	3,071.60	03/2020 -	03/2020
	Indian Oil Corporation Limited						
117	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162	5/2013	711.00 -	711.00	11.12	06/2020 -	06/2020
118	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345	10/2018	1,297.50 -	1,297.50	18.30	10/2021 -	10/2021
119	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344	4/2018	522.00 -	522.00	158.65	03/2021 -	03/2021
120	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340	8/2018	1,636.00 -	1,636.00	152.56	08/2020 -	08/2020
121	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338	4/2018	5,654.00 -	5,654.00	467.39	10/2021 -	10/2021
122	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337	7/2018	189.00 -	189.00	23.10	01/2021 -	01/2021
123	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333	3/2018	676.00 -	676.00	251.64	12/2021 -	12/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning	
						Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
124	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324	12/2017	199.36 -	199.36	9.39	10/2020 -	10/2020
125	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323	8/2017	255.40 -	255.40	4.07	08/2020 -	08/2020
126	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321	4/2018	206.63 -	206.63	19.25	02/2020 -	02/2020
127	LPG BP PROJECT MOTIHARI - [N16000317	5/2018	206.50 -	206.50	21.62	03/2021 -	03/2021
128	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309	8/2017	1,342.00 -	1,342.00	6.30	08/2020 -	08/2020
129	AUGMENTATION OF CTMPL - [N16000286	12/2016	228.00 -	228.00	24.50	06/2020 -	06/2020
130	INFRASTRUCTURE DEVLOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284	9/2016	208.35 -	208.35	126.98	07/2020 -	07/2020
131	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI - [N16000276	5/2016	261.00 -	261.00	52.11	01/2021 -	01/2021
132	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
133	R and D CAMPUS II AT FARIDABAD - [N16000375	6/2019	2,281.94 -	2,281.94	-	12/2022 -	12/2022
134	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368	6/2019	371.00 -	371.00	-	09/2022 -	09/2022
135	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT - [N16000363	12/2018	278.60 -	278.60	-	06/2021 -	06/2021
136	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362	5/2019	3,361.00 -	3,361.00	372.43	08/2021 -	08/2021
137	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361	11/2018	462.30 -	462.30	-	09/2021 -	09/2021
138	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353	10/2018	598.00 -	598.00	17.37	02/2020 -	02/2020
139	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352	1/2019	909.00 -	909.00	22.76	01/2021 -	01/2021
140	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351	12/2018	611.00 -	611.00	13.11	04/2022 -	04/2022
141	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350	10/2018	316.20 -	316.20	14.78	10/2021 -	10/2021
142	LAB REVAMP AT GUJARAT REFINERY - [N16000377	10/2019	403.00 -	403.00	43.50	12/2021 -	12/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning	
						Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
143	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376	8/2019	1,255.00 -	1,255.00	99.93	10/2021 -	10/2021
144	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
145	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251	4/2016	1,021.00 -	1,021.00	4.45	12/2020 -	12/2020
146	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249	5/2016	1,945.00 -	1,945.00	1,004.75	08/2021 -	08/2021
147	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193	1/2015	1,823.00 -	3,027.90	955.36	12/2020 -	12/2020
	Mangalore Refinery And Petrochemicals Limited						
148	BSVI UPGRADATION - [N16000257	9/2016	1,810.00 1,810.00	1,810.00	940.45	12/2019 07/2020	07/2020
149	SEA WATER DESALINATION PLANT - [N16000319	11/2017	581.00 -	621.00	102.99	03/2020 11/2020	11/2020
	Oil & Natural Gas Corporation Limited						
150	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061	3/2009	2,465.15 -	2,378.86	2,147.00	03/2013 12/2019	12/2019
151	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128	3/2011	861.79 -	1,683.06	1,356.33	05/2013 12/2019	12/2019
152	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358	4/2019	3,228.80 -	3,228.80	497.01	03/2022 -	03/2022
153	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357	2/2019	2,292.46 -	2,292.46	402.18	05/2021 -	05/2021
154	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335	4/2018	766.37 -	766.37	465.86	12/2019 -	12/2019
155	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297	2/2017	4,006.83 -	4,475.92	2,869.89	05/2021 12/2021	12/2021
156	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294	2/2017	968.61 -	1,033.95	968.11	11/2019 -	11/2019
157	DEVELOPMENT OF BSE-11 BLOCK - [N16000293	2/2017	511.30 -	511.30	523.88	11/2019 -	11/2019
158	DEVELOPMENT OF B-147 FIELD - [N16000292	2/2017	546.15 -	565.15	449.96	11/2019 03/2020	03/2020
159	REDEVELOPMENT OF SANTHAL FIELD - [N16000279	2/2017	1,162.56 -	1,162.56	412.79	03/2026 -	03/2026
160	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278	7/2016	249.85 250.00	265.49	180.20	05/2020 -	05/2020
161	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370	5/2019	763.92 -	763.92	116.82	12/2020 -	12/2020
162	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212	1/2015	4,619.94 -	4,619.94	4,444.58	12/2017 03/2020	03/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning	
						Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
163	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239	12/2015	823.27 -	910.23	403.18	03/2023 03/2022	03/2022
164	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241	11/2015	650.82 -	650.82	415.38	03/2019 05/2020	05/2020
165	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213	12/2015	3,190.69 -	3,247.19	2,298.77	04/2018 05/2020	05/2020
166	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131	12/2011	2,059.63 -	2,665.65	1,932.09	03/2015 12/2019	12/2019
167	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204	8/2015	2,818.88 -	2,818.88	2,302.10	03/2019 05/2020	05/2020
168	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197	11/2014	6,068.80 -	5,296.93	4,767.31	04/2019 12/2019	12/2019
	Oil India Limited						
169	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167	7/2011	352.56 -	438.84	249.73	03/2017 06/2020	06/2020
170	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356	6/2016	224.75 -	224.75	69.99	08/2020 -	08/2020
171	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331	1/2018	543.91 -	682.90	71.46	02/2020 06/2020	06/2020
172	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259	9/2016	571.66 -	571.66	297.66	12/2019 06/2020	06/2020
173	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258	5/2016	406.00 -	406.00	91.19	10/2020 -	10/2020
	Total		1,51,935.72 -	1,62,870.89	61,342.22		
	POWER						
	National Thermal Power Corporation						
174	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151	3/2013	11,638.55 -	12,865.92	12,361.29	01/2018 03/2020	03/2020
175	RAMMAM-III HEPP (3X40 MW) - [N18000178	9/2014	1,381.84 -	1,592.34	502.87	09/2019 05/2024	05/2024
176	BARH STPP(3X660MW) NTPC - [180100242	2/2005	8,692.97 -	21,312.11	16,756.64	10/2011 08/2021	08/2021
177	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193	4/2012	9,750.89 -	12,176.28	10,032.00	02/2017 06/2020	06/2020
178	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140	12/2012	11,846.00 -	12,739.82	12,839.84	10/2017 03/2020	03/2020
179	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212	1/2016	10,598.98 -	10,598.98	5,851.67	11/2020 06/2021	06/2021
180	PATRATU STPP-I (3X800MW) - [N18000275	11/2017	18,668.00 -	18,668.00	2,078.50	03/2023 -	03/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning	
						Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
181	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274	3/2019	349.00 -	349.00	125.00	11/2020 -	11/2020
182	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273	12/2018	587.44 -	587.44	250.00	09/2020 -	09/2020
183	TALAIPALLI COAL MINING PROJECT - [N18000266	9/2015	3,004.00 -	3,004.00	1,782.00	11/2019 -	11/2019
	Power Grid Corporation Of India Limited						
184	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066	2/2009	11,130.19 -	14,719.10	12,816.90	08/2013 03/2022	03/2022
185	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168	6/2014	5,151.37 -	5,151.37	3,216.41	03/2018 12/2019	12/2019
186	TRANSMISSION SYSTEM STRENTHENNING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213	3/2016	808.63 -	808.63	534.82	01/2018 03/2020	03/2020
187	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238	3/2017	283.72 -	283.72	196.10	11/2019 -	11/2019
188	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247	2/2017	5,070.13 -	5,070.13	3,042.59	04/2020 -	04/2020
189	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261	5/2017	175.64 -	175.64	101.85	09/2018 03/2020	03/2020
190	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267	9/2017	198.49 -	198.49	119.50	09/2019 02/2020	02/2020
191	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269	12/2017	193.14 -	193.14	100.18	06/2019 03/2020	03/2020
192	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268	11/2017	358.83 -	358.83	166.27	05/2020 -	05/2020
193	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264	8/2017	1,931.39 -	1,931.39	1,107.54	02/2020 -	02/2020
194	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258	3/2017	3,500.00 3,500.00	3,500.00	1,949.00	07/2020 -	07/2020
195	EASTERN REGION STRENGTHENNING SCHEME-XV - [N18000214	4/2016	454.11 -	454.11	297.16	04/2018 01/2020	01/2020
	Satluj Jal Vidyut Nigam Limited						
196	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194	3/2019	10,439.09 -	10,439.09	836.81	01/2024 -	01/2024
197	NAITWAR MORI HEP - [N18000265	10/2017	648.33 -	648.33	284.44	12/2021 -	12/2021
	Thdc India Limited						
198	AMELIA COAL MINE - [N18000252	1/2017	2,104.21 -	1,587.16	308.34	09/2020 -	09/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning: Original /Revised	Date of Commissioning: Anticipated
1	2	3	4	5	6	7	8
199	KHURJA SUPER THERMAL POWER PROJECT - [N18000272	3/2019	11,089.42 -	11,089.42	672.81	09/2023 -	09/2023
	Total		1,30,054.36 -	1,50,502.44	88,330.53		
	RAILWAYS						
	Central Railways						
200	WARDHA-NANDED MAHARASHTRA - [N22000231	4/2008	3,168.29 -	3,168.29	1,202.21	03/2023 -	03/2023
201	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247	4/2011	184.06 -	312.00	275.98	03/2019 12/2019	12/2019
202	DAUND - MANMAD (236 KM) - [N22000360	2/2016	1,876.00 -	2,081.27	187.09	03/2023 -	03/2023
203	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358	2/2015	2,449.91 -	2,449.91	180.76	03/2023 -	03/2023
204	PUNE-NASIK (265 KM) - [N22000354	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
205	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353	2/2016	9,968.00 -	9,968.00	-	03/2024 -	03/2024
	Dedicated Freight Corridor Corporation Of India Ltd						
206	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	03/2020
	East Central Railways						
207	KOSI BRIDGE (NL), ECR - [220100304	4/2002	499.41 -	516.02	402.55	03/2020 -	03/2020
208	ARARIA-SUPAUL (NL) - [N22000177	4/2008	1,605.17 -	1,605.17	23.49	- 03/2023	03/2023
	East Coast Railway						
209	BHADRAK - NERGUNDI 3RD LINE - [N22000316	3/2013	843.04 -	843.04	141.96	10/2020 03/2023	03/2023
210	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381	4/2015	1,172.92 -	1,172.92	546.12	12/2018 03/2022	03/2022
211	KOTTAVALSA - KORAPUT DOUBLING - [N22000377	4/2015	2,499.71 -	3,382.95	397.90	03/2022 -	03/2022
	North Central Railway						
212	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372	4/2015	668.70 668.00	680.00	330.00	03/2020 -	03/2020
213	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495	3/2018	4,329.53 -	4,329.53	3.90	03/2023 -	03/2023
214	JHANSI BINA DOUBLING - [N22000496	9/2016	2,001.00 -	2,001.00	416.59	03/2021 -	03/2021
	North East Frontier Railway						
215	BHAIRABI SAIRONG, NL, NEFR - [N22000100	4/2008	2,393.47 -	5,021.45	3,131.89	03/2014 03/2022	03/2022
216	KISHANGANJ JALALGARH, NL, NEFR - [N22000101	4/2008	333.76 -	360.00	6.74	- 03/2022	03/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning	
						Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
217	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193	4/2010	221.42 -	380.00	38.18	- 03/2022	03/2022
218	AGARTALA-AKHAURA NL - [N22000195	4/2012	569.63 -	670.00	107.83	03/2020 09/2021	09/2021
219	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205	4/2010	906.46 -	6,000.00	263.12	03/2021 -	03/2021
220	DIGARU-HOJAI (102 KM) - [N22000389	4/2015	870.96 -	2,136.01	580.01	03/2021 -	03/2021
221	MURKONGSELEK-PASIGHAT NL - [N22000208	4/2011	414.84 -	661.00	122.93	03/2020 -	03/2020
222	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206	4/2010	242.22 -	471.00	69.09	03/2020 -	03/2020
223	DIMAPUR-TIZIT NL - [N22000196	4/2013	4,274.00 -	4,274.00	-	03/2020 -	03/2020
	North Eastern Railway						
224	HATHUA-BHATNI (N L) (NER) - [220100319	4/2005	230.03 -	230.03	277.14	12/2022 -	12/2022
225	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457	4/2016	1,900.00 -	1,277.06	-	01/2022 -	01/2022
226	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469	4/2016	600.00 -	600.00	31.72	01/2022 -	01/2022
227	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131	3/2007	243.78 -	895.00	106.55	12/2021 -	12/2021
	Northern Railway						
228	GRADE SEPERATOR AT DAYABASTI - [N22000269	4/1999	156.65 -	197.17	106.97	- 03/2024	03/2024
229	CHANDIGARH-BADDI - [N22000467	4/2007	328.14 -	1,540.00	234.79	03/2023 -	03/2023
230	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274	4/2007	336.91 -	791.39	517.05	- 03/2022	03/2022
	National High Speed Rail Corporation Limited						
231	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463	12/2015	1,08,000.00 -	1,08,000.00	5,969.41	12/2023 12/2023	12/2023
	Rail India Technical And Economic Service						
232	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394	3/2015	636.38 -	636.38	281.85	03/2021 -	03/2021
233	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498	2/2016	393.98 -	393.98	290.45	03/2020 -	03/2020
	Rail Vikas Nigam Ltd.						
234	AHMEDABAD-BOTAD (GC) - [N22000140	4/2012	975.62 -	1,082.32	1,054.93	12/2021 -	12/2021
235	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403	4/2015	773.94 -	773.94	475.85	12/2024 -	12/2024
236	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409	1/1991	2,335.67 -	2,335.68	647.54	12/2024 -	12/2024

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning	
						Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
237	VIJAYAWADA-GUDUR - [N22000369	4/2015	3,246.26 -	3,548.67	1,211.97	12/2023 -	12/2023
238	DHASA-JETALSAR (GC) - [N22000141	4/2012	644.38 -	644.38	418.93	03/2021 -	03/2021
	South Central Railway						
239	BHADRACHALAM ROAD-SATTUPALLI - [N22000287	4/2010	704.31 -	952.16	303.24	03/2020 03/2020	03/2020
240	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432	4/2017	119.73 185.00	390.60	342.54	03/2022 -	03/2022
	South East Central Railway						
241	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	4/2005	383.79 -	1,413.76	1,351.73	- 01/2020	01/2020
242	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420	9/2016	1,908.51 -	2,686.63	515.29	03/2023 03/2023	03/2023
243	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438	4/2010	585.93 -	1,268.32	669.57	02/2019 12/2020	12/2020
244	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483	4/2008	872.00 -	1,226.51	1,062.76	12/2019 03/2020	03/2020
245	ANUPPUR-KATNI - [N22000485	4/2015	1,370.00 -	1,370.94	311.76	12/2021 11/2022	11/2022
246	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484	4/2015	1,973.00 -	1,973.64	174.40	03/2021 03/2023	03/2023
247	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480	6/2018	229.00 -	852.50	39.69	12/2021 03/2023	03/2023
248	GONDIA-JABALPUR(GC),(SECR) - [220100186	2/1997	511.86 -	1,756.00	1,668.96	04/2020 01/2021	01/2021
	South Eastern Railway						
249	BOWAICHANDI-ARAMBAGH - [N22000159	4/2010	267.37 -	620.00	40.99	- 03/2025	03/2025
250	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160	4/2010	651.00 -	1,009.00	7.96	03/2015 03/2025	03/2025
251	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402	4/1998	1,027.40 -	2,373.00	485.04	03/2003 03/2030	03/2030
	South Western Railway						
252	YELAHANKA-PENUKONDA - [N22000328	5/2015	860.43 -	958.00	756.85	03/2020 -	03/2020
253	ARSIKERE-TUMKUR - [N22000332	3/2015	578.00 -	578.00	525.85	03/2020 -	03/2020
	Southern Railway						
254	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449	2/2015	1,700.00 -	1,003.00	252.02	03/2022 -	03/2022
	West Central Railway						
255	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351	12/2015	1,763.93 -	1,762.94	847.47	03/2020 03/2023	03/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning	
						Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
256	KATNI GRADE SEPARATOR/BYE PASS - [N22000416	8/2016	582.13 -	1,247.64	152.01	03/2022 09/2022	09/2022
	Western Railway						
257	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120	4/2008	3,503.69 -	3,975.22	1,758.23	03/2022 03/2023	03/2023
258	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121	4/2008	829.74 -	1,310.23	1,450.40	03/2020 03/2021	03/2021
259	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123	4/2008	318.24 -	321.62	125.76	03/2012 03/2022	03/2022
260	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139	4/2007	1,640.04 -	1,640.04	739.31	03/2022 03/2023	03/2023
261	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494	4/2017	691.84 -	663.29	180.20	03/2020 03/2021	03/2021
262	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493	4/2016	700.00 -	603.69	113.47	06/2020 06/2021	06/2021
263	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487	2/1991	551.51 -	809.07	641.51	03/2019 03/2020	03/2020
264	SURENDRA NAGAR RAJKOT - [N22000392	4/2015	1,002.39 -	1,002.39	396.54	03/2021 03/2021	03/2021
265	VIRAMGAM-SAMAKHIALI (DL) - [N22000145	4/2011	1,037.15 -	1,037.15	1,017.75	03/2021 03/2022	03/2022
266	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143	4/1994	320.66 -	858.96	534.00	03/2019 03/2022	03/2022
267	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142	4/2011	844.10 -	844.10	107.52	- 03/2021	03/2021
268	CHOTTAUDEPUR-DHAR(NL) - [N22000138	4/2007	1,347.26 -	1,347.26	741.93	03/2022 03/2022	03/2022
	Total		2,10,186.25 -	2,69,727.90	59,853.24		
	ROAD TRANSPORT AND HIGHWAYS						
	Ministry Of Road Transport And Highways (State Pwds)						
269	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301	3/2015	271.45 -	271.45	159.15	10/2015 01/2020	01/2020
270	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776	11/2017	232.81 -	232.81	59.44	11/2019 -	11/2019
271	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778	11/2017	266.52 -	266.52	144.27	11/2019 -	11/2019
272	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934	3/2018	228.32 -	228.32	47.96	08/2018 03/2020	03/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning	
						Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
273	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932	1/2017	319.28 -	319.28	108.34	08/2017 03/2020	03/2020
274	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931	11/2016	290.15 -	290.15	70.35	05/2017 03/2020	03/2020
275	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO - [N24000930	11/2016	378.24 -	378.24	287.63	01/2018 01/2020	01/2020
276	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929	9/2016	372.68 -	372.68	185.04	02/2017 12/2019	12/2019
277	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927	3/2018	293.64 -	293.64	28.24	08/2020 -	08/2020
278	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909	10/2017	1,069.59 -	1,069.59	663.50	10/2019 12/2020	12/2020
279	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907	3/2018	293.10 -	293.10	63.14	08/2020 -	08/2020
280	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906	3/2018	173.24 -	173.24	56.66	06/2020 -	06/2020
281	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216	12/2016	196.00 -	196.00	-	09/2021 -	09/2021
282	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209	3/2016	296.50 -	296.50	40.27	09/2020 -	09/2020
283	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208	3/2018	288.30 -	288.30	.34	08/2020 -	08/2020
284	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207	3/2018	185.18 -	185.18	65.66	02/2020 -	02/2020
285	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206	3/2018	263.89 -	242.05	139.38	04/2020 -	04/2020
286	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 - [N24001205	12/2016	209.10 -	209.10	159.51	10/2019 04/2020	04/2020
287	REHABILITATION AND UPGRADATION OF ALLAHABAD - MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203	10/2016	218.90 -	218.90	62.69	03/2020 -	03/2020
288	REHABILITATION AND UPGRADATION OF BARAICH - SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA - [N24001202	3/2016	388.83 -	388.83	304.47	12/2019 -	12/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning	
						Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
289	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198	1/2019	264.50 -	264.50	-	03/2021 -	03/2021
290	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197	3/2018	351.00 -	351.00	.49	06/2021 -	06/2021
291	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180	3/2019	237.51 -	237.51	-	12/2022 -	12/2022
292	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179	3/2017	217.35 -	217.35	35.10	11/2020 -	11/2020
293	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177	10/2016	171.90 -	171.90	14.77	08/2020 -	08/2020
294	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176	10/2016	172.63 -	172.63	45.02	12/2020 -	12/2020
295	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175	10/2016	167.62 -	167.62	42.15	12/2020 -	12/2020
296	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174	10/2016	235.31 -	235.31	91.38	11/2020 -	11/2020
297	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152	9/2018	160.00 -	160.00	.50	09/2021 -	09/2021
298	WARDHA TO ARVI - [N24001150	2/2018	313.58 -	313.58	12.96	04/2020 -	04/2020
299	RISOD TO HINGOLI - [N24001149	2/2018	355.99 -	355.99	131.97	12/2019 -	12/2019
300	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148	3/2016	599.34 -	599.34	485.53	01/2020 -	01/2020
301	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141	3/2016	240.30 240.00	240.30	198.06	01/2020 -	01/2020
302	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139	10/2016	218.94 219.00	218.94	103.89	03/2020 -	03/2020
303	KALMATH TO ZARAP - [N24001137	9/2016	1,338.13 1,338.00	1,338.13	959.51	03/2020 -	03/2020
304	TALGAON TO KALMATH - [N24001136	10/2016	904.70 905.00	904.70	604.05	03/2020 -	03/2020
305	KANTE TO WAKED - [N24001134	3/2016	1,230.02 1,230.00	1,230.02	555.61	11/2019 -	11/2019
306	BHOGAN KHURD TO KASHEDI - [N24001132	9/2017	743.21 743.00	743.21	52.87	06/2021 -	06/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning	
						Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
307	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131	3/2018	212.99 -	212.99	93.80	06/2020 -	06/2020
308	BAMNI TO NAVAEGAON - [N24001110	9/2017	241.69 242.00	241.69	83.29	04/2020 -	04/2020
309	KUSUMBA TO MALEGAON - [N24001109	3/2018	243.45 244.00	243.45	80.02	12/2019 -	12/2019
310	CHALISGAON TO NANDGAON - [N24001108	3/2018	206.97 207.00	206.97	92.89	12/2019 -	12/2019
311	PANCHARAL TO MANDANGHAR - [N24001107	7/2018	381.08 302.00	381.08	13.03	05/2020 -	05/2020
312	WARDHA TO HINGAGHAT - [N24001098	1/2018	216.90 217.00	216.90	55.00	12/2019 -	12/2019
313	SELDOH TO PANVAR - [N24001097	7/2018	404.33 404.00	404.33	30.19	05/2020 -	05/2020
314	ARNI TO NAIGAINBANDI - [N24001093	12/2017	309.94 310.00	309.94	51.32	12/2019 -	12/2019
315	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091	3/2016	536.65 356.00	536.65	465.20	12/2019 -	12/2019
316	MALEGAON TO RISOD - [N24001089	2/2018	303.24 303.00	303.24	131.97	12/2019 -	12/2019
317	JALGAON TO NANDURA - [N24001088	3/2018	177.84 177.00	177.84	73.69	12/2019 -	12/2019
318	MANGRUPHIR TO MAHAN - [N24001087	3/2018	222.13 222.00	222.13	78.63	11/2019 -	11/2019
319	PAHUR TO BODHWAD - [N24001084	1/2017	244.93 -	244.93	59.23	05/2020 -	05/2020
320	CHIKLI TO TAKARKHED - [N24001083	3/2018	393.10 393.00	393.10	153.97	12/2019 -	12/2019
321	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082	3/2018	223.46 -	223.46	21.42	12/2019 -	12/2019
322	HIMAYATNAGAR TO PHULSAWANGI - [N24001081	3/2018	294.87 295.00	294.87	36.30	12/2019 -	12/2019
323	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080	3/2018	256.15 -	256.15	36.50	12/2019 -	12/2019
324	ARDHAPUR TO HIMAYATNAGAR - [N24001079	12/2017	426.06 426.00	426.06	66.97	06/2020 -	06/2020
325	PUNE TO MALE VILLAGE - [N24001078	3/2018	228.31 -	228.31	13.50	12/2019 -	12/2019
326	DEULGAON SAKARSHA TO MEHKAR - [N24001076	3/2018	219.91 -	219.91	126.76	12/2019 -	12/2019
327	KUNDRAL TO WAZAR - [N24001077	1/2018	225.25 225.00	225.25	148.75	12/2019 -	12/2019
328	KHAMGAON TO DEULGAON SAKARSHA - [N24001074	3/2018	249.29 -	249.29	97.20	12/2019 -	12/2019
329	OSMANNAGAR TO KUNDRAL - [N24001075	9/2017	344.25 344.00	344.25	61.02	08/2020 -	08/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning	
						Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
330	KOTHARI TO DHANORA - [N24001073	9/2018	301.38 301.00	301.38	41.00	08/2020 -	08/2020
331	KHERDA TO NAGZARI - [N24001072	3/2018	181.30 -	181.30	72.50	12/2019 -	12/2019
332	JALKOT TO TOGRI - [N24001071	7/2018	299.92 300.00	299.92	19.20	08/2020 -	08/2020
333	DASTAPUR TO KARANJA - [N24001070	3/2018	182.63 -	182.63	82.40	12/2019 -	12/2019
334	WASHIM TO DASTAPUR - [N24001068	3/2018	165.51 -	165.51	34.45	12/2019 -	12/2019
335	OMREGA TO AUSA - [N24001067	3/2018	272.04 272.00	272.04	137.24	12/2019 -	12/2019
336	LATUR TO PANGAON - [N24001066	3/2018	336.47 336.00	336.47	123.48	12/2019 -	12/2019
337	PARBHANI TO GANGKHED - [N24001065	3/2018	238.19 238.00	238.19	45.85	12/2019 -	12/2019
338	DHANGIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064	3/2018	217.14 217.00	217.14	99.77	02/2020 -	02/2020
339	WADIGODRI TO DHANGRIPIMPRI - [N24001063	3/2018	194.23 194.00	194.23	86.23	02/2020 -	02/2020
340	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062	3/2018	336.21 336.00	336.21	71.66	12/2019 -	12/2019
341	CHIKALI TO DHAD - [N24001061	3/2018	189.46 189.00	189.46	35.54	12/2019 -	12/2019
342	PALPHATA TO PHULAMBARI - [N24001060	3/2018	227.19 227.00	227.19	74.23	12/2019 -	12/2019
343	SHIVUR TO YEOLA - [N24001059	3/2018	181.08 -	181.08	7.50	12/2019 -	12/2019
344	KARWANDI TO RAJURI - [N24001058	3/2018	276.95 277.00	276.95	87.47	12/2019 -	12/2019
345	TASGAON TO SHIRDHON - [N24001054	1/2017	195.64 196.00	195.64	169.73	11/2019 -	11/2019
346	SANGOLA TO JATH - [N24001052	1/2018	257.38 257.00	257.38	84.15	12/2019 -	12/2019
347	NALDURG TO AKKALKOT - [N24001051	2/2018	274.50 275.00	274.50	65.39	12/2019 -	12/2019
348	VITA TO NAGAJ - [N24001050	3/2018	304.58 305.00	304.58	24.16	12/2019 -	12/2019
349	KARAD TO VITA - [N24001049	1/2018	344.85 245.00	344.85	96.04	12/2019 -	12/2019
350	BHADGAON TO CHALISGAON - [N24001047	1/2018	259.55 260.00	259.55	145.00	11/2019 -	11/2019
351	JALGAON TO BHADGAON - [N24001045	1/2018	307.54 308.00	307.54	124.59	11/2019 -	11/2019
352	NILAJPHATA TO BHANDARA - [N24001043	1/2018	420.63 421.00	420.63	31.60	05/2020 -	05/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning	
						Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
353	SALAIKHURD TO TIRORA - [N24001042	1/2018	415.25 415.25	415.25	96.22	12/2019 -	12/2019
354	MAHAD TO RAIGAD FORT - [N24001038	7/2018	237.40 -	237.40	8.34	05/2020 -	05/2020
355	JAHIRABAD TO LATUR - [N24001040	1/2017	461.96 -	461.96	160.43	11/2019 -	11/2019
356	MANSAR TO SALAIKHURD - [N24001035	1/2018	418.36 -	418.36	125.13	12/2019 -	12/2019
357	PATGAON KHOPOLI SECTION I - [N24001028	1/2018	170.00 -	170.00	56.57	12/2019 -	12/2019
358	SHAHPUR PATGAON SECTION I - [N24001027	1/2018	150.79 -	150.79	21.42	12/2019 -	12/2019
359	KARASWADA TO BAMBOLIM - [N24001005	3/2017	852.67 -	852.67	86.04	12/2019 -	12/2019
360	PATRADEVI TO KARASWADA 4L - [N24001004	3/2017	634.32 -	634.32	109.33	05/2020 -	05/2020
361	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994	3/2018	626.76 -	626.76	80.66	07/2020 -	07/2020
362	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993	3/2018	322.81 -	322.81	1.66	09/2020 -	09/2020
363	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992	2/2018	426.52 -	426.52	225.51	04/2020 -	04/2020
364	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991	2/2018	220.28 -	220.28	37.58	11/2019 -	11/2019
365	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990	2/2018	294.13 -	294.13	39.44	11/2019 -	11/2019
366	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989	2/2018	206.13 -	206.13	127.86	06/2020 -	06/2020
367	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988	1/2018	230.03 -	230.03	127.98	12/2019 -	12/2019
368	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987	1/2018	283.15 -	283.15	42.22	05/2020 -	05/2020
369	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984	1/2017	283.00 -	283.00	166.22	12/2019 -	12/2019
370	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969	1/2017	263.45 -	263.45	59.79	09/2017 12/2020	12/2020
371	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968	11/2016	376.25 -	376.25	201.42	08/2017 02/2020	02/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning	
						Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
372	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966	1/2016	348.95 -	348.95	161.26	08/2016 03/2020	03/2020
373	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967	3/2016	444.84 -	444.84	251.28	09/2016 03/2020	03/2020
374	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965	1/2016	386.09 -	386.09	183.00	05/2016 12/2019	12/2019
375	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964	8/2016	350.61 -	350.61	310.25	01/2017 04/2020	04/2020
376	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963	1/2018	418.03 -	418.03	170.05	08/2018 08/2020	08/2020
377	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941	3/2018	293.64 -	293.64	134.32	08/2020 -	08/2020
378	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940	3/2016	995.09 995.00	995.09	410.28	05/2016 07/2020	07/2020
379	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939	3/2018	504.19 504.00	504.19	226.14	11/2018 05/2020	05/2020
380	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938	3/2018	297.12 294.00	294.12	291.57	07/2018 01/2020	01/2020
381	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937	3/2018	289.67 290.00	289.67	103.90	08/2018 02/2020	02/2020
382	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU - [N24000936	3/2018	244.95 245.00	244.95	126.99	08/2018 02/2020	02/2020
383	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905	3/2018	322.48 -	322.48	120.18	07/2020 -	07/2020
384	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904	1/2017	247.25 -	247.25	144.71	03/2019 03/2020	03/2020
385	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883	3/2018	254.30 -	254.30	53.02	10/2020 -	10/2020
386	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874	3/2016	271.17 291.20	291.20	89.25	11/2018 11/2019	11/2019
387	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821	11/2017	257.34 -	238.00	41.09	11/2019 -	11/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning	
						Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
388	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 -	238.00	7.48	11/2019 -	11/2019
389	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781	5/2018	248.00 -	248.00	-	05/2020 -	05/2020
390	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779	2/2018	418.88 -	418.88	88.00	02/2020 -	02/2020
391	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777	11/2017	283.51 -	283.51	126.38	11/2019 -	11/2019
392	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774	12/2017	248.22 -	248.22	57.20	12/2019 -	12/2019
393	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478	12/2015	957.54 -	957.54	503.38	02/2020 -	02/2020
394	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475	11/2015	628.45 -	628.45	259.33	01/2020 -	01/2020
395	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773	12/2017	200.34 -	200.34	31.00	12/2019 -	12/2019
396	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772	12/2017	257.34 -	257.34	62.79	12/2019 -	12/2019
	National Highways And Infrastructure Development Corporation Ltd.						
397	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583	1/2016	252.00 -	252.00	4.74	01/2016 12/2021	12/2021
	National Highways Authority Of India						
398	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125	3/2010	1,509.10 -	1,509.10	3,684.44	09/2012 12/2019	12/2019
399	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737	1/2018	1,522.00 -	1,522.00	132.24	- 06/2021	06/2021
400	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	3/2017	2,064.99 -	2,447.00	1,896.03	03/2020 06/2020	06/2020
401	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670	3/2017	239.68 -	235.90	91.24	03/2020 -	03/2020
402	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669	3/2017	165.50 -	172.16	117.09	03/2020 -	03/2020
403	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667	3/2017	648.32 -	512.72	501.52	03/2020 -	03/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning	
						Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
404	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	3/2017	672.89 -	736.01	-	03/2020 -	03/2020
405	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	3/2017	744.64 -	982.00	-	03/2020 -	03/2020
406	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652	3/2017	848.45 -	848.45	87.01	03/2020 -	03/2020
407	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602	8/2016	1,664.20 -	1,664.20	721.93	04/2020 -	04/2020
408	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600	8/2016	1,388.34 -	2,587.50	1,449.00	09/2019 03/2020	03/2020
409	NAGPUR RING ROAD PACKAGE-2 - [N24000560	3/2016	591.66 -	591.66	310.56	07/2019 12/2020	12/2020
410	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559	3/2016	720.00 -	720.00	322.19	- 10/2020	10/2020
411	NAGPUR RING ROAD PACKAGE-1 - [N24000558	3/2016	546.00 -	546.00	269.67	07/2019 12/2020	12/2020
412	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556	3/2016	899.00 -	899.00	561.27	04/2019 07/2020	07/2020
413	CONSTRUCTION OF ROB –FLYOVER AT RANICHAK, HALDIA - [N24000553	3/2016	229.37 -	229.37	110.52	11/2018 03/2020	03/2020
414	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510	12/2015	726.67 -	598.13	414.73	04/2018 03/2020	03/2020
415	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442	12/2015	649.50 -	649.50	137.85	03/2019 04/2021	04/2021
416	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441	10/2015	593.26 -	636.24	461.85	05/2018 06/2020	06/2020
417	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847	3/2018	291.53 -	291.53	46.60	- 11/2020	11/2020
418	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814	3/2018	1,029.96 -	1,261.05	97.55	- 03/2021	03/2021
419	KANDLA - MUNDRA PORT - [N24000175	1/2011	953.88 -	953.88	976.79	07/2013 11/2020	11/2020
420	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183	11/2011	1,535.00 -	1,535.00	3,225.15	05/2014 12/2019	12/2019
421	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432	9/2015	414.51 -	414.00	532.46	05/2018 05/2020	05/2020
	Total		63,864.42 -	65,734.42	31,688.83		

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning	
						Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
	SHIPPING AND PORTS						
	Inland Waterways Authority Of India						
422	JAL MARG VIKAS PROJECT - [N25000072	1/2018	4,200.00 -	5,369.18	1,662.16	03/2023 03/2023	03/2023
	Total		4,200.00 -	5,369.18	1,662.16		
	STEEL						
	National Mineral Development Corporation (Nmdc)						
423	NMDC INTEGRATED STEEL PLANT - [N12000086	1/2010	15,525.00 -	23,140.00	16,244.05	05/2015 07/2020	07/2020
	Rastriya Ispat Nigam Limited						
424	FORGED WHEEL PLANT - [N12000116	4/2014	1,682.85 -	1,682.85	1,270.63	09/2018 12/2019	12/2019
425	CENTRAL DISPATCH YARD - [N12000119	8/2015	320.66 -	320.66	253.54	08/2018 12/2019	12/2019
426	COKE OVEN BATTERY-5 - [N12000117	12/2011	2,858.00 -	2,500.00	1,482.76	12/2017 12/2019	12/2019
	Steel Authority Of India Limited (Sail)						
427	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095	3/2015	1,034.01 -	1,034.01	447.34	10/2017 06/2020	06/2020
428	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121	12/2018	263.36 -	263.36	15.67	09/2020 -	09/2020
429	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118	11/2016	262.87 -	262.87	130.11	06/2019 06/2020	06/2020
	Total		21,946.75 -	29,203.75	19,844.10		
	TELECOMMUNICATIONS						
	Bharat Sanchar Nigam Limited						
430	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113	1/2018	231.80 -	240.10	117.63	10/2018 12/2019	12/2019
	Total		231.80 -	240.10	117.63		
	URBAN DEVELOPMENT						
	Ahmedabad Metro Rail						
431	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137	3/2019	5,384.17 -	5,384.17	4.35	03/2024 -	03/2024
432	SURAT METRO RAIL PROJECT - [N28000138	3/2019	12,020.32 -	12,020.32	4.67	03/2024 -	03/2024
	Central Public Works Department						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning	
						Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
433	NSG AT KOLKATA - [N28000104	10/2014	162.88 -	162.88	144.06	04/2018 06/2020	06/2020
434	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118	10/2017	271.90 -	271.90	61.81	11/2019 08/2020	08/2020
435	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111	11/2017	171.72 -	171.72	32.00	03/2020 -	03/2020
436	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128	10/2016	1,180.00 -	1,180.00	-	07/2021 -	07/2021
437	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT - [N28000132	11/2018	361.60 -	361.60	.45	07/2021 -	07/2021
438	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133	2/2019	186.00 199.00	186.00	-	09/2020 -	09/2020
439	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129	10/2016	1,128.00 -	1,128.00	-	03/2022 -	03/2022
440	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127	12/2018	260.00 -	260.00	12.50	06/2021 -	06/2021
441	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106	11/2017	238.56 -	238.56	63.45	05/2020 -	05/2020
	Chennai Metro Rail Ltd						
442	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097	6/2016	3,770.00 -	3,770.00	2,086.51	03/2018 06/2020	06/2020
	Delhi Metro Rail Corporation						
443	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS - [N28000135	7/2019	24,948.65 -	24,948.65	1.74	03/2025 -	03/2025
444	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136	5/2017	565.00 -	565.00	321.05	12/2020 -	12/2020
	Maharastra Metro Rail Corporation Ltd.						
445	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121	12/2016	11,420.00 -	11,420.00	3,372.86	11/2021 03/2022	03/2022
	Madhya Pradesh Metro Rail Co Limited						
446	BHOPAL METRO RAIL - [N28000124	11/2018	6,941.40 -	6,941.40	41.94	02/2023 -	02/2023
447	INDORE METRO RAIL - [N28000125	11/2018	7,500.80 -	7,500.80	45.70	02/2023 -	02/2023
	National Building Construcion Corporation Ltd						
448	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	6/2012	4,264.00 -	4,439.23	3,246.53	11/2019 -	11/2019
	National Capital Region Transport Corp						
449	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134	3/2019	30,274.00 -	30,274.00	613.92	06/2025 -	06/2025

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning	
						Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
	Total		1,11,049.00 -	1,11,224.23	10,053.54		
	WATER RESOURCES						
	Brahmaputra Board						
450	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001	3/2017	233.57 -	233.57	32.20	12/2019 -	12/2019
	Bihar Urban Infrastructure Development Corporation Ltd						
451	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026	3/2018	230.06 -	230.06	-	07/2021 -	07/2021
452	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027	10/2017	254.13 -	254.13	-	09/2020 -	09/2020
453	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036	3/2018	294.02 -	294.02	-	10/2021 -	10/2021
454	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR - [N30000038	4/2015	184.93 -	184.93	-	04/2020 -	04/2020
455	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040	5/2017	356.37 -	356.37	-	04/2021 -	04/2021
456	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043	5/2017	191.62 -	191.62	-	11/2020 -	11/2020
457	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051	8/2017	824.00 -	824.00	-	06/2022 -	06/2022
458	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050	8/2017	578.89 -	578.89	-	06/2022 -	06/2022
459	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044	3/2017	277.42 -	277.42	-	05/2021 -	05/2021
460	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA - [N30000041	5/2017	184.86 -	184.86	-	05/2021 -	05/2021
461	SAIDPUR SEWER NETWORK PATNA - [N30000039	4/2015	268.63 -	268.63	-	01/2021 -	01/2021
462	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037	12/2014	225.77 -	225.77	-	03/2020 -	03/2020
463	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035	3/2018	305.19 -	305.19	-	08/2021 -	08/2021
464	I AND D AND STP AT CHAPPRA - [N30000028	11/2018	236.15 -	236.15	-	12/2020 -	12/2020
	Delhi Jal Board						
465	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014	3/2017	665.78 -	665.78	-	12/2022 -	12/2022
466	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O&M AT CORONATION PILLAR DELHI - [N30000017	12/2018	515.07 -	515.07	-	01/2021 -	01/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning	
						Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
467	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018	5/2017	344.81 -	344.81	-	05/2020 -	05/2020
468	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016	5/2016	239.11 -	239.11	-	02/2022 -	02/2022
469	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015	5/2016	211.79 -	211.79	-	12/2021 -	12/2021
	Kolkata Metropolitan Development Authority						
470	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029	1/2019	384.96 -	384.96	-	04/2022 -	04/2022
471	INTERCEPTION & DIVERSION WITH STP AT MAHESHTALA - [N30000032	5/2018	198.43 -	198.43	-	02/2022 -	02/2022
472	INTERCEPTION DIVERSION AND TREATMENT WORKS AT TOLLY'S NULLAH ADI GANGA - [N30000034	8/2017	307.12 -	307.12	-	09/2022 -	09/2022
473	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045	8/2017	185.22 -	185.22	-	12/2021 -	12/2021
474	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047	12/2014	272.32 -	272.32	-	04/2020 -	04/2020
475	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049	10/2017	164.93 -	164.93	-	12/2021 -	12/2021
476	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048	1/2018	172.10 -	172.10	-	12/2021 -	12/2021
477	SEWERAGE SYSTEM & STP WORKS AT HALISHAHR - [N30000046	2/2014	274.76 -	274.76	-	12/2019 -	12/2019
478	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH - [N30000042	5/2018	160.00 -	160.00	-	02/2022 -	02/2022
479	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033	3/2018	165.16 -	165.16	-	06/2022 -	06/2022
480	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031	12/2018	234.31 -	234.31	-	04/2022 -	04/2022
481	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPURL - [N30000030	3/2019	287.53 -	287.53	-	04/2022 -	04/2022
	Uttar Pradesh Jal Nigam						
482	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006	5/2017	767.59 -	767.59	-	09/2021 -	09/2021
483	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR - [N30000009	10/2016	370.40 -	370.40	-	08/2020 -	08/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning	
						Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
484	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025	3/2019	298.12 -	298.12	-	07/2021 -	07/2021
485	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024	2/2019	681.78 -	681.78	-	06/2022 -	06/2022
486	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS AT AGRA - [N30000023	2/2019	317.19 -	317.19	-	08/2021 -	08/2021
487	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022	1/2019	206.05 -	206.05	-	10/2021 -	10/2021
488	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021	1/2019	231.79 -	231.79	-	12/2021 -	12/2021
489	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020	2/2011	279.91 -	279.91	-	12/2019 -	12/2019
490	MATHURA SEWERAGE SCHEME - [N30000019	12/2017	460.45 -	460.45	-	12/2020 -	12/2020
491	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA - [N30000011	2/2017	161.31 -	161.31	-	11/2019 -	11/2019
492	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH - [N30000013	3/2019	271.39 -	271.39	-	08/2021 -	08/2021
493	REHABILITATION RENOVATION OF AGRA SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS IN AGRA UTTAR PR - [N30000012	12/2018	857.26 -	857.26	-	08/2021 -	08/2021
494	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010	3/2018	967.23 -	967.23	-	09/2021 -	09/2021
495	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008	10/2017	213.62 -	213.62	-	03/2022 -	03/2022
496	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS - [N30000007	3/2018	904.00 -	904.00	-	09/2021 -	09/2021
	Uttarakhand Pey Jal Nigam						
497	INTERCEPTION AND DIVERSION (I&D)WITH STP AT RISHIKESH - [N30000004	3/2017	158.00 -	158.00	-	11/2019 -	11/2019
	Total		16,575.10 -	16,575.10	32.20		
	Grand Total		8,02,525.61	9,04,022.25	2,96,571.71		

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Annexure - XIII

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Date of Commissioning		Cost Overrun (%)
					Original/ Revised	Antici Pated	
1	2	3	4	5	6	7	8
	ATOMIC ENERGY						
	Bhavini Limited						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044	09/2003	3,492.00 -	6,840.00	09/2010 -	10/2021	95.88
	Nuclear Power Corporation Of India Limited						
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010	10/2009	11,459.00 -	16,580.00	12/2015 -	06/2020	44.69
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027	10/2009	12,320.00 -	17,079.00	12/2016 -	12/2020	38.63
	Total		27,271.00 -	40,499.00			
	CIVIL AVIATION						
	Airport Authority Of India Limited						
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083	12/2016	859.86 -	860.00	03/2021 -	03/2021	.02
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084	09/2015	338.93 -	339.00	06/2019 -	12/2019	.02
	Total		1,513.40 -	1,640.33			
	COAL						
	Eastern Coal Fields Limited						
7	RANIGANJ MASTER PLAN - [N06000163	08/2009	2,661.73 -	5,173.26	08/2019 -	08/2024	94.36
	Neyveli Lignite Corporation						
8	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152	07/2016	17,237.00 -	17,237.80	11/2021 -	11/2021	.00
	Singareni Colliers Company Limitted						
9	RAMAGUNDAM OC-II EXTENSION - [N06000078	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
10	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017	10/2006	249.03 -	448.86	03/2012 -	03/2024	80.24
11	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129	05/2015	397.09 -	442.42	03/2019 -	03/2020	11.42

MoSPI OCMS

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Date of Commissioning: Original/ Revised	Date of Commissioning: Antici Pated	Cost Overrun (%)
1	2	3	4	5	6	7	8
12	JALAGAM VENGALA RAO OCP-II - [N06000094	07/2011	447.06 -	473.22	03/2015 -	03/2021	5.85
13	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093	07/2011	162.76 -	349.28	03/2015 -	03/2021	114.60
	South-Eastern Coal Fields Limited						
14	JAGANNATHPOR OCP(3.00MTY) - [N06000075	09/2008	152.43 -	459.49	03/2015 -	03/2020	201.44
	Western Coal Fields Limited						
15	KAMPTEE DEEP OC MINE - [N06000141	11/2015	277.65 -	313.34	03/2021 -	03/2024	12.85
16	BHANEGAON OC - [N06000121	02/2015	187.94 -	409.68	03/2023 -	03/2023	117.98
17	ADASA UG TO OC - [N06000133	08/2015	288.90 -	333.43	03/2023 -	03/2024	15.41
	Total		22,480.56 -	26,130.40			
	FERTILISERS						
	Rashtriya Chemical & Fertiliser Limited						
18	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009	10/2014	197.79 -	209.44	11/2016 -	09/2019	5.89
	Total		197.79 -	209.44			
	HEALTH AND FAMILY WELFARE						
	Hospital Services Consultancy Corporation Ltd						
19	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003	02/2013	414.11 -	499.23	11/2013 -	09/2020	20.55
20	AIIMS - MOTHER AND CHILD BLOCK - [N21000008	12/2013	204.44 -	270.00	05/2017 -	06/2020	32.07
21	AIIMS - OPD(NEW) - [N21000009	08/2014	293.65 -	325.00	05/2017 -	01/2020	10.68
22	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010	12/2014	168.90 -	191.20	05/2017 -	07/2019	13.20
23	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011	09/2014	505.58 -	585.00	03/2018 -	09/2019	15.71
24	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012	07/2016	152.95 -	177.92	02/2018 -	03/2020	16.33
25	CNCI KOLKATA WEST BENGAL - [N21000015	08/2016	244.00 -	248.00	09/2018 -	05/2019	1.64
26	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017	08/2017	272.19 -	272.54	03/2019 -	03/2020	.13

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Date of Commissioning: Original/ Revised	Date of Commissioning: Antici Pated	Cost Overrun (%)
1	2	3	4	5	6	7	8
27	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019	12/2017	156.56 -	156.65	- -	05/2020	.06
	Total		2,412.38 -	2,725.54			
	HUMAN RESOURCE DEPARTMENT						
	Rail India Technical And Economic Service						
28	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001	09/2013	484.32 -	626.26	09/2014 -	12/2020	29.31
	Total		484.32 -	626.26			
	PETROLEUM						
	Gas Authority Of India Limited						
29	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210	02/2015	749.00 -	842.00	02/2020 -	02/2020	12.42
	Hindustan Petroleum Corporation Limited						
30	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209	11/2011	310.00 -	370.00	03/2013 -	-	19.35
	Indian Oil Corporation Limited						
31	LPG TERMINAL AT KOCHI - [N16000171	10/2015	607.06 -	714.25	10/2017 -	-	17.66
32	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252	05/2016	664.00 -	729.40	12/2020 -	02/2020	9.85
	Indian Strategic Petroleum Reserves Ltd						
33	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169	01/2006	993.00 -	1,693.00	01/2012 -	-	70.49
	Mangalore Refinery And Petrochemicals Limited						
34	SEA WATER DESALINATION PLANT - [N16000319	11/2017	581.00 -	621.00	03/2020 -	11/2020	6.88
	Oil & Natural Gas Corporation Limited						
35	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128	03/2011	861.79 -	1,683.06	05/2013 -	12/2019	95.30
36	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213	12/2015	3,190.69 -	3,247.19	04/2018 -	05/2020	1.77
37	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294	02/2017	968.61 -	1,033.95	11/2019 -	11/2019	6.75
38	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297	02/2017	4,006.83 -	4,475.92	05/2021 -	12/2021	11.71

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Date of Commissioning		Cost Overrun (%)
					Original/ Revised	Antici Pated	
1	2	3	4	5	6	7	8
	Oil India Limited						
39	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167	07/2011	352.56 -	438.84	03/2017 -	06/2020	24.47
40	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148	09/2012	871.35 -	1,200.00	03/2015 -	-	37.72
41	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331	01/2018	543.91 -	682.90	02/2020 -	06/2020	25.55
	Total		14,699.80 -	17,731.51			
	POWER						
	National Hydro-Electric Power Corporation						
42	PARBATI HEP (4X200 MW) (NHPC) II - [180100210	09/2002	3,919.59 -	9,997.11	09/2009 -	12/2021	155.06
43	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221	09/2003	6,285.33 -	19,496.34	09/2010 -	-	210.19
	National Thermal Power Corporation						
44	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151	03/2013	11,638.55 -	12,865.92	01/2018 -	03/2020	10.55
45	TANDA TPP STAGE-II (2X660 MW) - [N18000175	09/2014	9,188.98 -	10,016.10	07/2019 -	07/2020	9.00
46	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176	02/2014	12,532.44 -	13,740.53	12/2018 -	09/2020	9.64
47	NORTH KARANPURA STPP (3X660 MW) - [N18000177	02/2014	14,366.58 -	15,164.05	06/2019 -	03/2022	5.55
48	RAMMAM-III HEPP (3X40 MW) - [N18000178	09/2014	1,381.84 -	1,592.34	09/2019 -	05/2024	15.23
49	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190	01/2007	5,353.00 -	9,583.00	07/2012 -	09/2020	79.02
50	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193	04/2012	9,750.89 -	12,176.28	02/2017 -	06/2020	24.87
51	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140	12/2012	11,846.00 -	12,739.82	10/2017 -	03/2020	7.55
52	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142	07/2012	1,527.00 -	1,801.07	08/2017 -	-	17.95
53	KHARGONE STPP STAGE I (1320 MW) - [N18000205	03/2015	9,870.51 -	11,148.86	01/2020 -	02/2020	12.95
54	PAKRI BARWADIH COAL MINING PROJECT - [N18000225	10/2004	4,237.96 4,238.00	4,552.00	10/2017 -	-	7.41
	Power Grid Corporation Of India Limited						
55	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	05/2005	1,779.29 -	2,187.32	11/2008 -	-	22.93

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Date of Commissioning		Cost Overrun (%)
					Original/ Revised	Antici Pated	
1	2	3	4	5	6	7	8
56	COMPREHENSIVE SCHEME FOR THE STRENGHTENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249	12/2014	4,754.42 -	9,072.36	12/2018 -	12/2020	90.82
57	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250	12/2014	5,111.33 -	6,880.36	12/2018 -	12/2020	34.61
	Thdc India Limited						
58	DHUKWAN SMALL HYDRO PROJECT - [N18000189	05/2011	195.42 -	294.60	02/2014 -	12/2019	50.75
59	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042	08/2008	2,491.58 -	4,397.80	06/2013 -	12/2022	76.51
60	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00 -	5,024.35	02/2016 -	06/2022	203.22
	Total		1,17,887.71 -	1,62,730.21			
	RAILWAYS						
	Central Railways						
61	KALYAN-KASARA 3RD LINE - [N22000233	04/2011	792.89 -	1,377.48	03/2021 -	03/2022	73.73
62	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247	04/2011	184.06 -	312.00	03/2019 -	12/2019	69.51
63	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181	02/1997	2,271.50 -	3,712.50	03/2021 -	03/2022	63.44
64	PUNE-NASIK (265 KM) - [N22000354	02/2016	2,425.00 -	5,341.68	03/2024 -	03/2024	120.28
65	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355	02/2016	2,750.00 -	3,438.51	03/2024 -	-	25.04
66	PUNE-MIRAJ-LONDA (467 KM) - [N22000359	02/2015	3,627.47 3,627.00	3,627.47	03/2024 -	03/2023	.01
67	DAUND - MANMAD (236 KM) - [N22000360	02/2016	1,876.00 -	2,081.27	03/2023 -	03/2023	10.94
	Container Corporation Of India						
68	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431	08/2016	234.50 -	235.00	03/2019 -	12/2020	.21
	East Central Railways						
69	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222	03/1999	1,033.07 -	3,376.00	- -	03/2021	226.79
70	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240	04/1997	324.73 -	1,050.00	03/2012 -	03/2020	223.35
71	GAYA-CHATRA (NL) - [N22000169	04/2008	415.67 -	549.75	- -	-	32.26
72	BIHTA-AURANGABAD (NL) - [N22000170	04/2008	326.20 -	2,995.01	- -	03/2024	818.15

MoSPI OCMS

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Date of Commissioning		Cost Overrun (%)
					Original/ Revised	Antici Pated	
1	2	3	4	5	6	7	8
73	CHHAPRA-MUZAFFARPUR (NL) - [N22000172	04/2006	378.56 -	1,858.75	- -	03/2022	391.01
74	MOTIHARI-SITAMARHI (NL) - [N22000174	04/2006	211.00 -	1,006.00	- -	-	376.78
75	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182	04/2013	213.01 -	425.17	- -	01/2020	99.60
76	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476	04/1991	329.39 -	1,483.14	- -	12/2021	350.27
	East Coast Railway						
77	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	810.78 -	1,928.07	06/2021 -	06/2024	137.80
78	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319	03/2012	155.81 -	238.03	03/2020 -	03/2021	52.77
79	KOTTAVALSA - KORAPUT DOUBLING - [N22000377	04/2015	2,499.71 -	3,382.95	03/2022 -	03/2022	35.33
80	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380	04/2015	701.61 -	810.02	11/2018 -	03/2022	15.45
	Eastern Railways						
81	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	1,188.91 -	1,619.48	03/2019 12/2009	03/2025	36.22
82	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	607.09 -	1,425.44	02/2013 -	03/2024	134.80
83	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235	04/2010	365.17 -	527.54	- -	03/2025	44.46
84	HANSDIHA-GODDA NL - [N22000236	04/2011	542.18 -	693.80	03/2020 -	03/2021	27.96
85	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238	04/2011	175.80 -	251.18	- -	03/2021	42.88
86	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239	04/2011	299.60 -	335.62	03/2017 -	03/2026	12.02
87	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240	04/2010	494.54 -	494.59	03/2005 -	03/2025	.01
88	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241	04/2000	297.47 -	298.22	- -	03/2025	.25
89	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243	04/2009	499.96 -	680.68	02/2012 -	03/2025	36.15
90	MONIGRAM- NIMTITA - [N22000301	04/2012	250.93 -	310.70	- -	03/2024	23.82
91	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302	04/2012	255.64 -	272.20	- -	09/2021	6.48

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Date of Commissioning		Cost Overrun (%)
					Original/ Revised	Antici Pated	
1	2	3	4	5	6	7	8
92	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216	04/1987	406.99 -	545.70	03/2006 -	03/2025	34.08
93	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217	04/2007	450.00 -	1,261.34	- -	03/2025	180.30
94	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218	04/2010	172.03 -	260.10	- -	03/2025	51.19
95	PIRPAINTI-JASIDIH - [N22000219	04/2013	915.98 -	2,137.81	03/2022 -	03/2025	133.39
96	BANDEL-BOINCHI 3RD LINE - [N22000221	04/2011	288.35 -	393.00	- -	03/2020	36.29
97	PIRPAINTI-BHAGALPUR - [N22000222	04/2011	261.38 -	478.08	- -	05/2019	82.91
98	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224	04/2001	923.52 -	995.10	03/2016 -	03/2025	7.75
99	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225	04/2005	595.51 -	769.40	03/2017 -	03/2025	29.20
	Indian Railway Construction Company Limited						
100	GEVRA ROAD PENDRA ROAD - [N22000488	02/2014	2,288.00 -	4,970.11	03/2022 -	12/2022	117.23
	Metropolitan Rapid Transport Projects						
101	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
102	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	2,980.41	03/2004 -	03/2021	501.57
103	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028	04/2006	495.74 -	734.01	06/2013 -	-	48.06
104	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135	03/2013	4,874.58 -	8,574.97	03/2016 -	06/2021	75.91
	North Central Railway						
105	ETAWAH-MAINPURI (NL),NCR - [220100318	04/1997	120.00 -	346.00	12/2008 -	-	188.33
106	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	04/2011	2,912.96 -	3,845.60	03/2022 -	12/2024	32.02
107	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372	04/2015	668.70 668.00	680.00	03/2020 -	03/2020	1.80
	North East Frontier Railway						
108	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135	04/1983	297.32 -	614.00	03/2019 -	03/2020	106.51
109	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	2,393.47 -	5,021.45	03/2014 -	03/2022	109.80

MoSPI OCMS

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Date of Commissioning		Cost Overrun (%)
					Original/ Revised	Antici Pated	
1	2	3	4	5	6	7	8
110	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	1,180.19 -	4,541.00	12/2008 -	03/2021	284.77
111	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124	04/2006	2,326.52 -	4,600.00	03/2015 -	10/2021	97.72
112	KISHANGANJ JALALGARH, NL, NEFR - [N22000101	04/2008	333.76 -	360.00	- -	03/2022	7.86
113	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	4,084.69	12/2015 -	-	204.95
114	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183	04/2013	1,798.00 -	2,496.67	03/2019 -	-	38.86
115	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193	04/2010	221.42 -	380.00	- -	03/2022	71.62
116	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205	04/2010	906.46 -	6,000.00	03/2021 -	03/2021	561.92
117	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206	04/2010	242.22 -	471.00	03/2020 -	03/2020	94.45
118	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207	04/2010	241.52 -	373.87	- -	06/2021	54.80
119	MURKONGSELEK-PASIGHAT NL - [N22000208	04/2011	414.84 -	661.00	03/2020 -	03/2020	59.34
120	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209	04/1999	819.23 -	1,871.00	- -	-	128.39
121	DIGARU-HOJAI (102 KM) - [N22000389	04/2015	870.96 -	2,136.01	03/2021 -	03/2021	145.25
122	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390	04/2016	602.27 -	612.00	12/2021 -	03/2020	1.62
123	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499	02/1999	380.60 -	1,871.00	04/2010 -	-	391.59
	North Eastern Railway						
124	KICHHA-KHATIMA (NL) - NER - [220100317	04/2003	142.45 -	228.40	- -	-	60.34
125	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321	04/2014	182.92 -	197.73	- -	-	8.10
126	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130	03/2013	307.00 -	1,409.09	- -	-	358.99
127	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131	03/2007	243.78 -	895.00	12/2021 -	12/2021	267.13
128	CHHAPRA-BALLIA UP - [N22000134	03/2013	295.00 -	477.31	01/2019 -	01/2020	61.80
129	KAPILVASTU-BASTI VIA BANSI SIDHARTHNAGAR BASTI NAUGARH UP - [N22000136	03/2013	643.00 -	644.00	- -	-	.16

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Date of Commissioning		Cost Overrun (%)
					Original/ Revised	Antici Pated	
1	2	3	4	5	6	7	8
130	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456	04/2016	213.00 -	213.35	04/2016 -	06/2020	.16
131	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460	04/2017	1,343.00 -	1,476.15	01/2018 -	-	9.91
132	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468	04/2016	602.50 -	714.34	- -	-	18.56
	North Western Railway						
133	DAUSA-GANGAPUR CITY(NL),NWR - [220100184	02/1997	410.08 -	886.41	02/2019 -	03/2021	116.16
134	PHULERA - DIGANA DOUBLING - [N22000326	05/2015	600.00 -	685.99	03/2020 -	04/2022	14.33
135	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330	05/2015	873.71 -	1,980.21	- -	-	126.64
136	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137	04/2012	246.08 -	348.55	12/2019 -	06/2020	41.64
137	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147	04/2011	2,082.75 -	4,079.15	- -	-	95.85
138	THIYAT HAMIRA-SANU - [N22000149	04/2013	236.93 -	294.90	10/2018 -	12/2019	24.47
139	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150	04/2013	822.00 -	1,099.54	- -	-	33.76
140	PUSHKAR-MERTA - [N22000151	04/2013	323.00 -	432.22	- -	-	33.81
141	AJMER-BANGURGRAM - [N22000155	04/2011	213.39 -	303.56	11/2019 -	05/2020	42.26
142	ALWAR-BANDIKUI DOUBLING - [N22000157	04/2013	242.09 -	410.00	02/2019 -	03/2020	69.36
	Northern Railway						
143	GRADE SEPERATOR AT DAYABASTI - [N22000269	04/1999	156.65 -	197.17	- -	03/2024	25.87
144	ROHTAK-MEHAM HANSI - [N22000272	04/2012	287.00 -	694.00	12/2011 -	03/2021	141.81
145	UNCHAHAR-AMETHI - [N22000294	04/2012	1,229.00 -	1,230.00	- -	03/2023	.08
146	QADIAN-BEAS - [N22000295	04/2011	205.22 -	841.90	- -	03/2024	310.24
147	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	450.00 -	2,200.00	07/2012 -	03/2024	388.89
148	CHANDIGARH-BADDI - [N22000467	04/2007	328.14 -	1,540.00	03/2023 -	03/2023	369.31
149	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492	03/2002	625.00 -	859.00	03/2016 -	03/2021	37.44
	Rail Vikas Nigam Ltd.						

MoSPI OCMS

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Date of Commissioning: Original/ Revised	Date of Commissioning: Antici Pated	Cost Overrun (%)
1	2	3	4	5	6	7	8
150	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	1,185.64 -	1,844.47	12/2017 -	03/2020	55.57
151	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	385.00	03/2009 03/2009	06/2020	85.99
152	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111	04/2010	2,913.51 -	4,639.00	03/2016 -	03/2025	59.22
153	BHANUPALI-BILASPUR BERI NL - [N22000273	04/2008	2,966.99 -	7,000.00	12/2026 -	12/2025	135.93
154	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297	04/2010	2,127.00 -	2,900.00	03/2023 -	03/2024	36.34
155	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110	04/2010	3,951.98 -	4,724.30	03/2016 -	03/2025	19.54
156	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95
157	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313	03/2012	1,503.71 -	2,200.00	03/2020 -	03/2022	46.30
158	AHMEDABAD-BOTAD (GC) - [N22000140	04/2012	975.62 -	1,082.32	12/2021 -	12/2021	10.94
159	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213	04/2012	632.68 -	816.55	03/2016 -	12/2020	29.06
160	VIJAYAWADA-GUDUR - [N22000369	04/2015	3,246.26 -	3,548.67	12/2023 -	12/2023	9.32
161	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404	04/2011	927.01 -	1,200.00	03/2019 -	03/2020	29.45
162	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407	03/2009	713.48 -	2,300.00	03/2020 -	03/2021	222.36
163	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409	01/1991	2,335.67 -	2,335.68	12/2024 -	12/2024	.00
164	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410	03/2006	948.04 -	1,500.00	03/2020 -	03/2021	58.22
165	BANASPANI- JAKHPURA - DOUBLING - [N22000412	03/2009	942.95 -	1,120.00	03/2019 -	06/2022	18.78
	Railway Electrification						
166	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094	02/2008	171.10 -	275.08	03/2012 -	-	60.77
	South Central Railway						
167	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192	03/1996	164.36 -	1,050.00	02/2009 -	-	538.84
168	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	458.25 -	458.26	- -	-	.00

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Date of Commissioning: Original/ Revised	Date of Commissioning: Antici Pated	Cost Overrun (%)
1	2	3	4	5	6	7	8
169	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432	04/2017	119.73 185.00	390.60	03/2022 -	03/2022	111.14
	South Eastern Railway						
170	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	564.94
171	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	04/2012	148.77 -	377.00	12/2016 -	01/2020	153.41
172	BOWAICHANDI-ARAMBAGH - [N22000159	04/2010	267.37 -	620.00	- -	03/2025	131.89
173	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160	04/2010	651.00 -	1,009.00	03/2015 -	03/2025	54.99
174	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162	04/2010	149.90 -	230.00	03/2015 -	-	53.44
175	BONDAMUNDA RANCHI DOUBLING - [N22000396	03/2016	1,724.20 -	1,993.24	03/2021 -	12/2021	15.60
176	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402	04/1998	1,027.40 -	2,373.00	03/2003 -	03/2030	130.97
	South Western Railway						
177	TORANAGALLU-RANJITPURA DL - [N22000298	04/2011	146.75 -	167.50	- -	12/2023	14.14
178	YELAHANKA-PENUKONDA - [N22000328	05/2015	860.43 -	958.00	03/2020 -	03/2020	11.34
179	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486	03/1996	644.78 -	890.00	03/2017 -	03/2020	38.03
	Southern Railway						
180	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079	09/2007	724.69 -	2,072.50	02/2019 -	02/2020	185.98
181	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084	09/2006	227.40 -	900.00	- -	-	295.78
182	TIDIVANAM-NAGARI (NL) - [N22000085	09/2006	582.83 -	2,300.00	- -	-	294.63
183	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	303.98 -	980.00	03/2020 -	03/2021	222.39
184	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	1,566.00 -	2,815.62	- -	-	79.80
185	ATTIPPATTU PUTTUR - [N22000184	04/2008	151.84 -	1,105.00	02/2019 -	-	627.74
186	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185	04/2008	523.52 -	2,300.00	- -	-	339.33
187	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186	04/2013	839.00 -	1,500.00	- -	-	78.78

MoSPI OCMS

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Date of Commissioning: Original/ Revised	Date of Commissioning: Antici Pated	Cost Overrun (%)
1	2	3	4	5	6	7	8
188	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187	04/1999	198.68 -	556.64	- -	-	180.17
189	KURUPPANTHARA-CHINGAVANAM - [N22000190	04/2007	270.14 -	457.08	- -	-	69.20
190	ERODE-PALANI - [N22000199	04/2008	288.57 -	1,140.00	- -	-	295.05
191	MADURAI-BODINAYAKKANUR - [N22000201	04/2008	164.41 -	450.00	- -	03/2020	173.71
192	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202	04/2007	931.98 -	951.24	- -	03/2020	2.07
193	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215	04/2011	120.70 -	1,800.00	03/2019 -	12/2019	1,391.30
194	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373	10/2013	187.26 -	231.67	04/2014 -	03/2020	23.72
195	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441	02/1996	268.87 -	950.00	03/2005 -	-	253.33
196	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451	02/2015	760.00 -	1,182.31	03/2020 -	06/2021	55.57
	West Central Railway						
197	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	04/2001	424.60 -	2,909.99	03/2021 -	03/2023	585.35
198	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	8,248.50	05/2008 -	03/2023	3,230.57
199	KATNI GRADE SEPARATOR/BYE PASS - [N22000416	08/2016	582.13 -	1,247.64	03/2022 -	09/2022	114.32
	Western Railway						
200	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125	04/2006	117.36 196.95	202.35	03/2011 -	03/2017	2.74
201	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121	04/2008	829.74 -	1,310.23	03/2020 -	03/2021	57.91
202	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143	04/1994	320.66 -	858.96	03/2019 -	03/2022	167.87
	Total		1,16,490.96 -	2,27,563.72			
	ROAD TRANSPORT AND HIGHWAYS						
	Ministry Of Road Transport And Highways (State Pwds)						
203	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276	12/2011	156.26 227.00	247.95	- -	-	9.23

MoSPI OCMS

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Date of Commissioning		Cost Overrun (%)
					Original/ Revised	Antici Pated	
1	2	3	4	5	6	7	8
204	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306	11/2010	624.41 -	992.67	03/2011 -	12/2019	58.98
205	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308	08/2010	193.69 -	327.92	10/2010 -	12/2019	69.30
206	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314	01/2013	182.28 -	269.14	02/2013 -	12/2019	47.65
207	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316	03/2015	258.97 -	268.92	08/2015 -	-	3.84
208	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259	03/2015	280.16 -	290.59	- -	-	3.72
209	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	12/2019	.12
210	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371	10/2013	445.89 -	653.29	03/2017 -	-	46.51
211	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388	11/2013	497.05 -	881.05	05/2017 -	05/2020	77.26
212	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391	11/2015	889.24 -	904.82	- -	-	1.75
213	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396	11/2010	470.20 -	630.36	02/2011 -	-	34.06
214	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398	01/1991	282.41 -	322.01	08/2016 -	-	14.02
215	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402	01/1991	358.22 -	377.64	10/2016 -	-	5.42
216	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407	10/2015	333.21 -	353.89	11/2015 -	-	6.21
217	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411	11/2014	218.31 -	307.47	02/2018 -	-	40.84
218	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415	08/2010	195.04 -	377.99	10/2010 -	06/2020	93.80
219	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531	01/1991	319.68 -	369.77	- -	-	15.67

MoSPI OCMS

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Date of Commissioning		Cost Overrun (%)
					Original/ Revised	Antici Pated	
1	2	3	4	5	6	7	8
220	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646	06/2016	157.30 157.00	157.30	06/2018 -	-	.19
221	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782	03/2018	460.73 -	461.00	- -	-	.06
222	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 -	238.00	11/2019 -	-	.08
223	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928	10/2015	333.21 -	355.89	12/2015 -	12/2020	6.81
224	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938	03/2018	297.12 294.00	294.12	07/2018 -	01/2020	.04
225	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939	03/2018	504.19 504.00	504.19	11/2018 -	05/2020	.04
226	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940	03/2016	995.09 995.00	995.09	05/2016 -	07/2020	.01
227	KHAMGAON TO SHEGAON - [N24001009	02/2017	203.21 203.00	203.21	05/2019 -	12/2019	.10
228	SHEGAON TO DEORI PHATA - [N24001010	02/2017	373.10 373.00	373.10	05/2019 -	12/2019	.03
229	MEHKAR TO CHIKALI - [N24001011	02/2017	322.48 322.00	322.48	05/2019 -	-	.15
230	CHIKALI TO KHAMGAON - [N24001012	02/2017	548.03 548.00	548.03	06/2019 -	10/2019	.01
231	DIGRAS DARWAH KARANJA - [N24001013	01/2017	391.06 391.00	391.06	06/2019 -	06/2020	.02
232	MORSHI TO ACHALPUR - [N24001015	01/2017	341.16 341.00	341.16	06/2019 -	12/2019	.05
233	KARAD TO VITA - [N24001049	01/2018	344.85 245.00	344.85	12/2019 -	12/2019	40.76
234	SANGOLA TO JATH - [N24001052	01/2018	257.38 257.00	257.38	12/2019 -	12/2019	.15
235	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056	02/2017	422.02 422.00	422.02	07/2019 -	-	.00
236	KARAD PATAN CHIPLUN GUHAGAR - [N24001057	02/2017	407.19 407.00	407.19	06/2019 -	06/2020	.05
237	PALPHATA TO PHULAMBARI - [N24001060	03/2018	227.19 227.00	227.19	12/2019 -	12/2019	.08
238	CHIKALI TO DHAD - [N24001061	03/2018	189.46 189.00	189.46	12/2019 -	12/2019	.24
239	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062	03/2018	336.21 336.00	336.21	12/2019 -	12/2019	.06

MoSPI OCMS

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Date of Commissioning		Cost Overrun (%)
					Original/ Revised	Antici Pated	
1	2	3	4	5	6	7	8
240	WADIGODRI TO DHANGRIPIMPRI - [N24001063	03/2018	194.23 194.00	194.23	02/2020 -	02/2020	.12
241	DHANGIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064	03/2018	217.14 217.00	217.14	02/2020 -	02/2020	.06
242	PARBHANI TO GANGKHED - [N24001065	03/2018	238.19 238.00	238.19	12/2019 -	12/2019	.08
243	LATUR TO PANGAON - [N24001066	03/2018	336.47 336.00	336.47	12/2019 -	12/2019	.14
244	OMREGA TO AUSA - [N24001067	03/2018	272.04 272.00	272.04	12/2019 -	12/2019	.01
245	KOTHARI TO DHANORA - [N24001073	09/2018	301.38 301.00	301.38	08/2020 -	08/2020	.13
246	OSMANNAGAR TO KUNDRAL - [N24001075	09/2017	344.25 344.00	344.25	08/2020 -	08/2020	.07
247	KUNDRAL TO WAZAR - [N24001077	01/2018	225.25 225.00	225.25	12/2019 -	12/2019	.11
248	ARDHAPUR TO HIMAYATNAGAR - [N24001079	12/2017	426.06 426.00	426.06	06/2020 -	06/2020	.01
249	JALGAON TO NANDURA - [N24001088	03/2018	177.84 177.00	177.84	12/2019 -	12/2019	.47
250	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091	03/2016	536.65 356.00	536.65	12/2019 -	12/2019	50.74
251	NAIGAONBANDI TO MANGRULPIR - [N24001094	12/2017	244.04 244.00	244.04	03/2019 -	12/2019	.02
252	TALEGAON TO GONAPUR - [N24001096	01/2018	264.41 264.00	264.41	03/2019 -	12/2019	.16
253	SELDOH TO PANVAR - [N24001097	07/2018	404.33 404.00	404.33	05/2020 -	05/2020	.08
254	PANCHARAL TO MANDANGHAR - [N24001107	07/2018	381.08 302.00	381.08	05/2020 -	05/2020	26.19
255	VADPALE TO BHOGAN KHURD - [N24001115	01/2017	1,598.47 1,560.00	1,598.47	11/2019 -	03/2020	2.47
256	BHOKAR TO SARSAM - [N24001128	02/2017	295.09 -	295.99	07/2019 -	-	.31
257	BHOGAN KHURD TO KASHEDI - [N24001132	09/2017	743.21 743.00	743.21	06/2021 -	06/2021	.03
258	PARSHURAM GHAT TO ARAWALI - [N24001133	04/2016	983.14 983.00	983.14	12/2019 -	-	.01
259	KANTE TO WAKED - [N24001134	03/2016	1,230.02 1,230.00	1,230.02	11/2019 -	-	.00
260	KALMATH TO ZARAP - [N24001137	09/2016	1,338.13 1,338.00	1,338.13	03/2020 -	03/2020	.01
261	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140	11/2016	215.16 215.00	215.16	09/2019 -	10/2019	.07

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Date of Commissioning		Cost Overrun (%)
					Original/ Revised	Antici Pated	
1	2	3	4	5	6	7	8
262	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141	03/2016	240.30 240.00	240.30	01/2020 -	01/2020	.13
263	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144	10/2013	445.89 653.00	653.29	03/2017 -	10/2019	.04
264	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	08/2010	186.96 -	305.61	09/2014 -	12/2019	63.46
	National Highways And Infrastructure Development Corporation Ltd.						
265	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687	03/2016	396.52 -	396.52	08/2016 -	06/2020	.00
266	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688	03/2016	429.52 -	429.52	08/2016 -	08/2019	.00
267	RHENOK-RORAHTHANG-PAKYONG ON NH 717A - [N24000695	04/2017	388.00 -	447.37	10/2017 -	-	15.30
268	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754	03/2018	339.57 -	339.57	09/2018 -	-	.00
269	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759	03/2018	237.72 -	237.72	09/2018 -	-	.00
270	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760	03/2018	251.97 -	251.97	09/2018 -	-	.00
	National Highways Authority Of India						
271	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	525.00	02/2009 -	07/2019	87.50
272	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049	12/2003	160.00 -	167.98	05/2008 -	06/2019	4.99
273	INDORE-DEWAS(NH-3) - [N24000159	11/2010	325.00 -	475.00	05/2013 -	-	46.15
274	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063	12/2003	217.61 -	360.84	04/2010 -	07/2019	65.82
275	NALBARI T BIJNI (AS-7) - [N24000048	12/2003	208.00 -	230.00	04/2008 -	03/2020	10.58
276	NASHRI- CHANANI - [N24000162	05/2011	2,159.00 -	2,519.00	06/2015 -	-	16.67
277	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188	05/2011	511.54 -	591.00	11/2013 -	03/2020	15.53
278	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224	10/2012	1,928.22 -	2,945.00	04/2015 -	06/2020	52.73

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Date of Commissioning		Cost Overrun (%)
					Original/ Revised	Antici Pated	
1	2	3	4	5	6	7	8
279	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435	10/2015	531.13 -	727.00	05/2018 -	09/2020	36.88
280	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441	10/2015	593.26 -	636.24	05/2018 -	06/2020	7.24
281	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459	06/2015	845.24 -	941.00	- -	01/2020	11.33
282	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482	08/2015	814.04 -	825.17	- -	01/2020	1.37
283	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	05/2013	1,055.00 -	1,601.77	11/2015 -	-	51.83
284	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501	08/2015	322.09 -	322.09	04/2018 -	12/2020	.00
285	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506	01/1991	642.41 -	681.67	- -	10/2020	6.11
286	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508	07/2015	1,871.34 -	1,871.34	01/2018 -	12/2019	.00
287	MEERUT-BULANDSHAHAR - [N24000539	01/2016	683.24 -	987.94	- -	02/2020	44.60
288	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542	03/2016	197.69 -	197.69	07/2018 -	-	.00
289	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551	03/2016	1,587.49 -	2,982.00	04/2019 -	-	87.84
290	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571	05/2016	425.60 -	425.60	- -	-	.00
291	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572	05/2016	364.56 -	392.00	- -	12/2019	7.53
292	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600	08/2016	1,388.34 -	2,587.50	09/2019 -	03/2020	86.37
293	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622	09/2016	950.69 -	1,108.00	08/2019 -	12/2020	16.55
294	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623	09/2016	1,100.19 -	1,145.31	- -	05/2020	4.10
295	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638	11/2012	605.84 -	722.46	07/2018 -	02/2020	19.25
296	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 -	1,310.00	03/2020 -	08/2020	10.58
297	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	03/2017	744.64 -	982.00	03/2020 -	03/2020	31.88

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Date of Commissioning		Cost Overrun (%)
					Original/ Revised	Antici Pated	
1	2	3	4	5	6	7	8
298	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	03/2017	1,030.44 -	1,065.51	03/2020 -	05/2020	3.40
299	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	03/2017	988.34 -	1,043.28	03/2020 -	08/2020	5.56
300	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659	03/2017	1,059.73 -	1,071.00	03/2017 -	11/2020	1.06
301	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	03/2017	1,098.06 -	1,160.64	03/2020 -	08/2020	5.70
302	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 -	756.27	03/2020 -	04/2020	.23
303	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 -	736.01	03/2020 -	03/2020	9.38
304	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 -	1,187.10	03/2020 -	05/2020	13.97
305	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669	03/2017	165.50 -	172.16	03/2020 -	03/2020	4.02
306	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	03/2020 -	03/2021	10.24
307	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 -	2,447.00	03/2020 -	06/2020	18.50
308	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	03/2020 -	07/2020	41.54
309	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	06/2020	44.39
310	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691	04/2017	894.00 -	929.32	04/2020 -	11/2019	3.95
311	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704	09/2017	1,124.11 -	1,232.76	09/2017 -	06/2020	9.67
312	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726	01/2018	1,155.16 -	1,155.16	- -	-	.00
313	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729	01/2018	607.00 -	607.00	- -	08/2021	.00
314	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730	01/2018	621.00 -	621.00	- -	04/2021	.00
315	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784	02/2018	1,424.77 -	1,853.42	- -	-	30.09

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Date of Commissioning		Cost Overrun (%)
					Original/ Revised	Antici Pated	
1	2	3	4	5	6	7	8
316	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787	02/2018	1,995.34 -	2,400.00	- -	11/2021	20.28
317	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789	02/2018	2,177.80 -	2,450.00	- -	-	12.50
318	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814	03/2018	1,029.96 -	1,261.05	- -	03/2021	22.44
319	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829	03/2018	1,016.92 -	1,071.00	- -	04/2021	5.32
320	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830	03/2018	2,065.96 -	2,169.00	- -	-	4.99
321	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831	03/2018	1,294.47 -	1,296.00	- -	-	.12
322	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842	03/2018	199.90 -	199.90	- -	-	.00
323	SIX LANING AND STREGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841	03/2018	795.50 -	799.30	- -	07/2021	.48
324	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843	03/2018	196.05 -	196.05	- -	01/2020	.00
325	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853	03/2018	642.13 -	807.00	- -	12/2020	25.68
	Total		78,118.44 -	90,540.72			
	TELECOMMUNICATIONS						
	Department Of Telecommunication						
326	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 -	24,664.00	07/2015 -	05/2020	84.97
	Total		13,334.00 -	24,664.00			
	URBAN DEVELOPMENT						
	Central Public Works Department						
327	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088	02/2014	388.00 -	488.28	05/2017 -	12/2019	25.85

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Date of Commissioning: Original/ Revised	Date of Commissioning: Antici Pated	Cost Overrun (%)
1	2	3	4	5	6	7	8
328	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	2,000.00	10/2019 -	03/2021	64.04
329	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076	06/2014	157.84 -	169.16	03/2017 -	-	7.17
330	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100	02/2016	496.18 496.00	498.99	06/2017 -	03/2021	.60
331	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126	01/2019	790.79 -	800.00	03/2022 -	06/2022	1.16
	Chennai Metro Rail Ltd						
332	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084	02/2009	14,600.00 -	19,058.00	12/2015 -	-	30.53
	Hindustan Steelwork Construction Limited						
333	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101	05/2005	768.88 1,070.97	1,113.34	02/2014 -	-	3.96
334	CONSTRUCTION AND MAINTEINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098	03/2007	149.73 173.00	175.94	12/2015 -	-	1.70
	National Building Construcion Corporation Ltd						
335	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	06/2012	4,264.00 -	4,439.23	11/2019 -	-	4.11
	Total		22,834.63 -	28,742.94			
	WATER RESOURCES						
	Polavaram Project Authority						
336	POLAVARAM IRRIGATION PROJECT - [N30000002	02/2009	10,151.04 -	55,548.87	03/2020 -	06/2021	447.22
	Total		10,151.04 -	55,548.87			
	Grand Total		4,27,876.03	6,79,352.94			

List of Delayed Projects w.r.t. Latest Schedule

Annexure-XIV

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning: Original / Revised	Date of Commissioning: Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	ATOMIC ENERGY								
	Bhavini Limited								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 -	6,840.00	5,837.84	09/2010 -	10/2021	133	-
	Nuclear Power Corporation Of India Limited								
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	16,580.00	14,137.00	12/2015 -	06/2020	54	-
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	17,079.00	11,387.00	12/2016 -	12/2020	48	-
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU	03/2013	39,849.00 -	39,849.00	15,706.00	11/2020 -	11/2023	36	-
	Total		67,120.00 -	80,348.00	47,067.84				
	CIVIL AVIATION								
	Airport Authority Of India Limited								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI,TRIPURA	09/2015	338.93 -	339.00	213.50	06/2019 -	12/2019	6	-
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,A & N ISLANDS	10/2013	314.61 -	441.33	85.79	09/2018 -	06/2020	21	-
7	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI	11/2016	233.38 -	233.38	84.73	04/2020 -	12/2020	8	-
8	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA - [N04000080]AAI,WEST BENGAL	01/2016	219.91 -	219.91	65.45	03/2020 -	12/2020	9	-
9	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI,TAMIL NADU	06/2018	2,467.00 -	2,467.00	213.17	02/2022 -	08/2022	6	-
	Total		3,573.83 -	3,700.62	662.64				
	COAL								
	Bharat Coking Coal Limited								
10	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	269.82	180.83	04/2014 -	01/2020	69	-
	Central Coal Fields Limited								
11	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	106.41	03/2011 -	03/2021	120	-
12	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	181.17	03/2012 -	03/2021	108	-
13	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	365.62	03/2016 -	03/2021	60	-

MoSPI OCMS

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning: Original / Revised	Date of Commissioning: Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
14	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	90.75	03/2014 -	03/2021	84	-
15	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40 -	706.40	432.82	07/2012 -	03/2022	116	-
	Eastern Coal Fields Limited								
16	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	528.96	03/2018 -	10/2020	31	-
17	RANIGANJ MASTER PLAN - [N06000163]ECL,WEST BENGAL	08/2009	2,661.73 -	5,173.26	336.63	08/2019 -	08/2024	60	-
	Mahanadi Coal Fields Limited								
18	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	272.73	03/2010 -	03/2020	120	-
19	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA	05/2014	337.66 -	337.66	188.48	03/2019 -	03/2020	12	-
20	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.10 -	490.10	508.91	03/2017 -	03/2021	48	-
21	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	296.22	03/2012 -	03/2021	108	-
22	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.53	389.52	03/2013 -	03/2021	96	-
23	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA	06/2014	289.03 -	289.03	-	03/2018 -	03/2021	36	-
24	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	539.88	03/2013 -	03/2022	108	-
25	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	347.93	03/2010 -	03/2022	144	-
26	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA	05/2014	479.15 -	479.15	211.71	03/2019 -	03/2024	60	-
	Neyveli Lignite Corporation								
27	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 7,080.41	7,080.41	6,867.42	12/2015 -	12/2019	48	-
	Singareni Colliers Company Limitted								
28	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	143.61	03/2015 -	03/2020	60	-
29	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	159.81	06/2015 -	03/2020	57	-
30	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	384.32	112.52	07/2016 -	03/2020	44	-
31	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 -	415.37	187.89	03/2016 -	03/2020	48	-
32	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]SCCL,TELANGANA	05/2015	397.09 -	442.42	99.42	03/2019 -	03/2020	12	-
33	KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL,TELANGANA	10/2015	426.79 -	426.79	.72	03/2018 -	03/2020	24	-
34	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL,TELANGANA	11/2016	272.73 -	272.73	162.62	- 04/2017	03/2020	-	35
35	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	164.04	119.85	03/2015 -	03/2021	72	-
36	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	349.28	7.49	03/2015 -	03/2021	72	-

MoSPI OCMS

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
37	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	473.22	18.35	03/2015 -	03/2021	72	-
38	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA	03/2017	413.84 -	413.84	56.86	03/2019 -	03/2022	36	-
39	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	489.62	353.10	03/2012 -	03/2023	132	-
40	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	448.86	296.17	03/2012 -	03/2024	144	-
	South-Eastern Coal Fields Limited								
41	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	459.49	193.35	03/2015 -	03/2020	60	-
42	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	2.92	03/2014 -	03/2020	72	-
43	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	181.44	03/2016 -	03/2020	48	-
44	AMERA OC RCE - [N06000123]SECL,CHHATISGARH	02/2015	335.97 -	335.97	51.21	03/2018 -	03/2020	24	-
45	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	197.28	03/2014 -	03/2021	84	-
	Western Coal Fields Limited								
46	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA	08/2015	288.90 -	333.43	27.21	03/2023 -	03/2024	12	-
47	KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA	11/2015	277.65 -	313.34	117.85	03/2021 -	03/2024	36	-
	Total		21,183.75 -	25,658.01	14,335.66				
	INFORMATION AND BROADCASTING								
	Central Public Works Department								
48	FILM AND TELEVISION INSTITUTE ARUNACHAL PRADESH - [N09000002]CPWD,ANDHRA PRADESH	11/2016	204.32 -	204.32	-	02/2019 -	11/2019	9	-
	Total		204.32 -	204.32	.00				
	STEEL								
	Steel Authority Of India Limited (Sail)								
49	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA	04/2015	3,127.30 -	3,127.30	3,119.34	04/2018 11/2019	01/2020	21	2
50	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	1,154.18	978.83	12/2017 11/2019	01/2020	25	2
	Total		4,281.48 -	4,281.48	4,098.17				
	PETROLEUM								
	Bharat Petroleum Corporation Limited								
51	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA	11/2014	4,588.29 5,245.96	5,245.96	3,877.61	08/2018 11/2019	12/2019	16	1

MoSPI OCMS

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
52	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 -	678.00	7.28	02/2017 -	10/2021	56	-
	Gas Authority Of India Limited								
53	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT	04/2016	327.78 -	200.00	150.72	04/2018 -	12/2019	20	-
	Hindustan Petroleum Corporation Limited								
54	180 TMTPA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA	06/2017	249.26 -	249.26	60.45	06/2020 -	09/2021	15	-
55	120 TMTPA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND	06/2017	161.50 -	161.50	17.78	06/2020 -	09/2021	15	-
	Indian Oil Corporation Limited								
56	JAIPUR-PANIPAT NAPTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE	02/2015	890.00 -	887.00	609.28	10/2019 -	12/2019	2	-
57	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]IOCL,UTTAR PRADESH	01/2018	666.64 -	666.64	468.46	09/2019 -	01/2020	4	-
58	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]IOCL,ASSAM	02/2016	2,582.00 -	2,582.00	1,613.96	11/2019 -	02/2020	3	-
59	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]IOCL,HARYANA	12/2017	3,529.00 -	3,529.00	1,895.18	07/2019 -	02/2020	7	-
60	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]IOCL,GUJARAT	03/2018	3,380.00 -	3,380.00	2,238.63	09/2019 -	03/2020	6	-
61	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]IOCL,ASSAM	05/2018	1,222.00 -	1,222.00	606.24	09/2019 -	04/2020	7	-
62	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]IOCL,WEST BENGAL	05/2018	2,934.40 -	2,934.40	1,780.52	09/2019 -	04/2020	7	-
63	FUEL QUALITY UPGRADATION (NSU,NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY - [N16000348]IOCL,BIHAR	06/2017	951.64 -	951.64	490.98	10/2019 -	05/2020	7	-
64	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]IOCL,ODISHA	05/2016	429.00 -	429.00	318.90	01/2019 -	06/2020	17	-
65	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM	08/2018	557.00 -	557.00	249.46	02/2020 -	06/2020	4	-
66	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00 -	236.00	30.20	06/2020 -	08/2020	2	-
67	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	326.08	07/2018 -	10/2020	27	-
68	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND	02/2017	160.10 -	160.10	51.57	02/2020 -	10/2020	8	-
69	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT	10/2017	906.00 -	906.00	98.97	02/2020 -	10/2020	8	-
70	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM	06/2016	423.00 -	423.00	282.50	08/2019 -	12/2020	16	-

MoSPI OCMS

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning: Original / Revised	Date of Commissioning: Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
71	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00 6,025.00	6,025.00	990.22	12/2018 -	02/2021	26	-
72	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL,WEST BENGAL	04/2017	163.02 -	163.02	54.53	04/2020 -	03/2021	11	-
73	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	212.00	46.99	01/2021 -	04/2021	3	-
74	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA	12/2016	161.59 -	161.59	38.65	12/2019 -	07/2021	19	-
75	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00 -	466.00	96.28	04/2021 -	07/2021	3	-
76	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	466.43	35.01	10/2020 -	08/2021	10	-
77	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	348.00	37.01	01/2021 -	10/2021	9	-
78	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	318.80	52.67	08/2021 -	11/2021	3	-
79	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	355.00	14.89	04/2022 -	02/2023	10	-
	Oil & Natural Gas Corporation Limited								
80	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 345.92	345.92	155.61	01/2014 -	11/2019	70	-
81	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]ONGC,MAHARASHTRA	02/2019	3,660.71 3,740.05	3,740.05	274.07	04/2021 -	05/2021	1	-
82	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH	03/2016	34,012.00 -	34,012.00	4,204.96	06/2020 -	08/2021	14	-
83	HEERA REDEVELOPMENT - PHASE III - [N16000360]ONGC,MAHARASHTRA	05/2019	2,494.68 -	2,494.68	48.07	12/2021 -	03/2022	3	-
	Total		72,919.78 -	75,196.99	21,223.73				
	POWER								
	National Hydro-Electric Power Corporation								
84	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	9,997.11	7,715.06	09/2009 -	12/2021	147	-
	National Thermal Power Corporation								
85	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH	03/2015	9,870.51 -	11,148.86	9,055.78	01/2020 -	02/2020	1	-
86	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA	05/2016	1,885.13 -	1,885.13	527.90	12/2018 -	03/2020	15	-

MoSPI OCMS

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
87	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL	12/2016	529.68 -	529.68	140.10	11/2018 -	03/2020	16	-
88	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH	09/2014	9,188.98 -	10,016.10	6,633.23	07/2019 03/2020	07/2020	12	4
89	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA	02/2014	12,532.44 -	13,740.53	9,944.45	12/2018 02/2020	09/2020	21	7
90	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 7,998.00	9,583.00	7,981.46	07/2012 -	09/2020	98	-
91	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 5,867.38	5,867.38	4,264.84	03/2013 12/2020	01/2021	94	1
92	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	15,164.05	9,861.12	06/2019 09/2019	03/2022	33	30
	Power Grid Corporation Of India Limited								
93	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 -	871.62	584.94	10/2017 09/2019	11/2019	25	2
94	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 260.03	260.03	199.56	07/2017 06/2019	11/2019	28	5
95	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA	04/2016	844.64 -	844.64	435.25	04/2019 04/2019	11/2019	7	7
96	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 639.46	639.46	568.44	06/2014 09/2019	12/2019	66	3
97	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 1,891.41	1,891.41	1,280.93	04/2016 08/2019	12/2019	44	4
98	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 374.63	374.63	214.62	04/2016 12/2017	12/2019	44	24
99	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 197.40	197.40	83.94	03/2018 -	12/2019	21	-
100	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	431.80	05/2017 06/2019	12/2019	31	6
101	GREEN ENERGY CORRIDORS - INTER STATE TRANSSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	3,519.59	2,534.01	05/2019 -	12/2019	7	-
102	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE	09/2016	562.25 -	562.25	420.20	03/2019 -	12/2019	9	-
103	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE	10/2016	608.24 -	608.24	416.24	04/2019 -	12/2019	8	-
104	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE	03/2017	337.75 -	337.75	99.94	06/2019 -	12/2019	6	-
105	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE	12/2015	3,654.00 -	3,654.00	3,485.19	04/2019 -	12/2019	8	-

Costing Rs. 150 Crore and above									(November 2019)
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
106	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 -	408.46	311.82	01/2019 09/2019	01/2020	12	4
107	TRANSMISSION SYSTEM FOR EVACUTION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 -	186.17	110.60	07/2019 -	01/2020	6	-
108	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE	05/2016	14,733.37 -	14,733.37	9,317.26	11/2019 -	02/2020	3	-
109	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 5,071.94	5,071.94	4,570.22	10/2012 12/2019	03/2020	89	3
110	EASTERN REGION STRENTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	235.53	130.55	06/2019 -	03/2020	9	-
111	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 -	379.95	93.48	12/2019 -	03/2020	3	-
112	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA	05/2017	445.89 -	445.89	295.78	02/2019 12/2019	03/2020	13	3
113	COMPREHENSIVE SCHEME FOR THE STRENGHTENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	9,072.36	1,352.46	12/2018 -	12/2020	24	-
114	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	6,880.36	1,779.00	12/2018 -	12/2020	24	-
	Thdc India Limited								
115	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 -	294.60	321.11	02/2014 -	12/2019	70	-
116	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 -	5,024.35	3,118.00	02/2016 -	06/2022	76	-
117	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	4,397.80	1,823.10	06/2013 -	12/2022	114	-
	Total		1,10,467.56 -	1,40,218.16	90,102.38				
	HEAVY INDUSTRY								
	Bharat Heavy Electricals Limited								
118	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI	08/2016	1,554.00 -	1,554.00	665.35	09/2019 -	03/2020	6	-
	Total		1,554.00 -	1,554.00	665.35				
	HEALTH AND FAMILY WELFARE								
	HII Infra Tech Services Limited								

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning: Original / Revised	Date of Commissioning: Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
119	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	715.06	345.41	04/2020 06/2020	10/2020	6	4
120	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	557.48	283.12	06/2020 08/2020	10/2020	4	2
	Hospital Services Consultancy Corporation Ltd								
121	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	325.00	297.16	05/2017 -	01/2020	32	-
122	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	177.92	139.70	02/2018 -	03/2020	25	-
123	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	274.19	241.58	03/2019 -	03/2020	12	-
124	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	272.54	191.86	03/2019 -	03/2020	12	-
125	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	270.00	204.70	05/2017 -	06/2020	37	-
126	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	363.99	208.29	05/2018 -	07/2020	26	-
127	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL	08/2017	355.15 -	355.15	217.00	03/2019 -	07/2020	16	-
128	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	499.23	302.02	11/2013 -	09/2020	82	-
	Total		3,818.67 -	3,810.56	2,430.84				
	RAILWAYS								
	Central Railways								
129	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	3,712.50	2,434.24	03/2021 -	03/2022	12	-
130	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 -	1,377.48	316.79	03/2021 -	03/2022	12	-
131	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	1,272.19	319.94	03/2022 -	03/2023	12	-
132	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	540.02	252.82	03/2022 -	03/2024	24	-
133	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	1,035.16	117.02	03/2022 -	03/2024	24	-
134	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	637.95	73.16	03/2023 -	03/2024	12	-
	Container Corporation Of India								
135	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	305.00	261.28	03/2019 -	12/2019	9	-
136	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	343.00	222.83	03/2019 -	12/2019	9	-
137	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	174.00	152.48	03/2019 -	02/2020	11	-
138	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	493.17	441.09	03/2018 -	03/2020	24	-

MoSPI OCMS

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning: Original / Revised	Date of Commissioning: Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
139	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	346.32	288.65	03/2019 -	03/2020	12	-
140	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	235.00	10.88	03/2019 -	12/2020	21	-
	East Central Railways								
141	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	118.49	03/2019 -	12/2019	9	-
142	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 898.53	1,050.00	1,043.03	03/2012 -	03/2020	96	-
143	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88 751.55	751.55	674.58	03/2012 -	03/2020	96	-
144	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	678.54 678.54	678.54	495.04	03/2019 -	02/2021	23	-
145	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	597.94	03/2020 -	03/2021	12	-
146	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR	12/2015	1,200.20 1,200.20	1,200.20	397.15	03/2020 -	10/2021	19	-
147	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 819.01	819.01	489.11	03/2020 -	03/2022	24	-
148	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 1,215.54	1,215.54	79.18	03/2021 -	03/2022	12	-
149	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 1,185.73	1,185.73	35.74	03/2021 -	03/2022	12	-
150	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR	12/2015	1,491.47 -	1,491.47	443.64	03/2020 -	12/2022	33	-
	East Coast Railway								
151	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	238.03	204.79	03/2020 -	03/2021	12	-
152	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 1,539.28	1,539.28	937.49	02/2019 -	03/2022	37	-
153	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 701.61	810.02	129.40	11/2018 -	03/2022	40	-
154	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	1,160.00 1,160.83	1,160.83	699.40	03/2020 -	03/2023	36	-
155	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 1,547.38	1,547.38	366.66	03/2022 -	03/2023	12	-
156	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 3,791.66	3,791.66	1,243.45	03/2009 -	06/2024	183	-
157	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 198.07	1,928.07	770.82	06/2021 -	06/2024	36	-
158	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	2,361.74	208.19	03/2022 -	03/2025	36	-
	Eastern Railways								
159	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	157.94	51.75	11/2018 -	03/2021	28	-
160	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	542.18 -	693.80	458.91	03/2020 -	03/2021	12	-
161	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	1,425.44	637.54	02/2013 -	03/2024	133	-

MoSPI OCMS

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning: Original / Revised	Date of Commissioning: Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
162	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	1,619.48	871.86	03/2019 12/2009	03/2025	72	183
163	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62 -	1,091.59	860.08	12/2010 12/2017	03/2025	171	87
164	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	545.70	148.48	03/2006 -	03/2025	228	-
165	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	2,137.81	297.68	03/2022 -	03/2025	36	-
166	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	995.10	501.00	03/2016 -	03/2025	108	-
167	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51 -	769.40	103.08	03/2017 -	03/2025	96	-
168	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	266.32	162.57	03/2016 -	03/2025	108	-
169	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	296.43	248.70	03/2017 -	03/2025	96	-
170	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	494.59	32.00	03/2005 -	03/2025	240	-
171	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	680.68	159.45	02/2012 -	03/2025	157	-
172	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	257.42	107.49	03/2014 -	03/2025	132	-
173	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108	-
	Indian Railway Construction Company Limited								
174	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH	04/2013	3,055.00 -	3,055.00	1,951.07	09/2018 -	12/2020	27	-
175	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH	02/2014	2,288.00 -	4,970.11	628.61	03/2022 -	12/2022	9	-
176	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA	04/2016	5,200.00 -	1,700.43	48.00	03/2020 -	06/2023	39	-
	Metropolitan Rapid Transport Projects								
177	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	2,980.41	1,431.38	03/2004 -	03/2021	204	-
178	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 -	918.53	284.75	03/2014 -	03/2021	84	-

MoSPI OCMS

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
179	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	63	-
	North Central Railway								
180	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	2,912.96 -	3,845.60	148.26	03/2022 -	12/2024	33	-
	North East Frontier Railway								
181	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	297.32 -	614.00	275.07	03/2019 -	03/2020	12	-
182	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 1,532.00	1,532.00	642.09	03/2019 -	03/2020	12	-
183	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 2,145.00	2,145.00	935.60	03/2019 -	03/2020	12	-
184	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	314.00 728.00	728.00	727.55	03/2019 -	03/2020	12	-
185	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	1,180.19 3,300.00	4,541.00	3,344.19	12/2008 -	03/2021	147	-
186	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 -	4,600.00	842.42	03/2015 -	10/2021	79	-
187	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 13,809.00	12,524.00	9,541.58	03/2011 -	03/2022	132	-
	North Eastern Railway								
188	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	477.31	336.89	01/2019 -	01/2020	12	-
189	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	426.74	195.35	04/2017 -	01/2020	33	-
190	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	213.35	9.62	04/2016 -	06/2020	50	-
191	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	1,028.95	26.06	12/2019 -	04/2021	16	-
192	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	-
193	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	150.00	-	04/2017 -	10/2022	66	-
	North Western Railway								
194	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	294.90	226.61	10/2018 -	12/2019	14	-
195	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 281.03	410.00	362.96	02/2019 -	03/2020	13	-
196	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	303.56	274.18	11/2019 -	05/2020	6	-
197	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	348.55	229.00	12/2019 -	06/2020	6	-
198	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 -	420.18	184.64	03/2020 -	06/2020	3	-

MoSPI OCMS

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
199	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 780.98	886.41	559.84	02/2019 -	03/2021	25	-
200	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	685.99	74.80	03/2020 -	04/2022	25	-
201	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	808.85	60.28	08/2022 -	09/2022	1	-
	Northern Railway								
202	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	694.00	220.42	12/2011 -	03/2021	111	-
203	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 781.00	859.00	835.35	03/2016 -	03/2021	60	-
204	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	27,949.00	19,767.15	11/2002 -	06/2022	235	-
205	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 2,010.00	2,200.00	666.00	07/2012 -	03/2024	140	-
	Rail Vikas Nigam Ltd.								
206	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64 -	1,844.47	1,829.53	12/2017 -	03/2020	27	-
207	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	1,200.00	1,178.67	03/2019 -	03/2020	12	-
208	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	385.00	387.92	03/2009 03/2009	06/2020	135	135
209	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02 -	1,100.00	1,088.23	03/2020 -	06/2020	3	-
210	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	816.55	701.83	03/2016 -	12/2020	57	-
211	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48 -	2,300.00	2,056.99	03/2020 -	03/2021	12	-
212	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	1,500.00	1,374.96	03/2020 -	03/2021	12	-
213	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.85 -	1,485.85	1,158.89	12/2020 -	03/2021	3	-
214	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 -	1,202.70	947.96	02/2015 -	12/2021	82	-
215	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,548.66 -	1,548.66	1,339.35	12/2021 -	03/2022	3	-
216	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	2,200.00	1,722.18	03/2020 -	03/2022	24	-
217	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	1,120.00	1,028.76	03/2019 -	06/2022	39	-
218	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	1,183.25	1,136.44	12/2020 -	12/2022	24	-
219	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA	04/2010	2,127.00 -	2,900.00	1,737.30	03/2023 -	03/2024	12	-
220	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	750.56	409.09	03/2022 -	12/2024	33	-
221	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	650.11	03/2023 -	12/2024	21	-

MoSPI OCMS

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning: Original / Revised	Date of Commissioning: Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
222	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	4,724.30	2,278.26	03/2016 -	03/2025	108	-
223	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	4,639.00	855.74	03/2016 -	03/2025	108	-
224	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	16,216.00	1,790.80	12/2024 -	03/2025	3	-
225	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	2,733.86	40.13	03/2014 -	12/2025	141	-
	South Central Railway								
226	MUNEERABAD-MAHABOOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1,780.29	1,780.09	1,478.40	03/2000 -	03/2021	252	-
227	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 2,120.16	2,120.16	524.57	03/2009 -	03/2023	168	-
228	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	1,160.48 1,160.48	1,160.48	323.09	03/2010 -	03/2023	156	-
229	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 2,063.03	2,063.03	792.70	03/2021 -	03/2023	24	-
230	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 3,631.00	3,631.00	617.19	03/2022 -	03/2023	12	-
231	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 2,200.00	2,200.00	290.92	03/2023 -	03/2024	12	-
232	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	2,288.70 2,643.25	2,643.25	810.35	03/2021 -	03/2024	36	-
233	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,132.77 2,132.77	2,132.77	331.15	03/2014 -	03/2024	120	-
	South Eastern Railway								
234	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	377.00	182.63	12/2016 08/2018	01/2020	37	17
235	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 358.68	358.68	265.54	12/2018 -	06/2020	18	-
236	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 1,312.96	1,312.96	562.50	03/2020 03/2020	06/2020	3	3
237	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	1,993.24	411.64	03/2021 03/2021	12/2021	9	9
	South Western Railway								
238	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 644.78	890.00	443.52	03/2017 -	03/2020	36	-
239	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,156.94 1,140.94	1,140.94	773.28	03/2020 -	03/2021	12	-
240	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 1,870.41	1,870.41	885.55	03/2019 -	03/2021	24	-
241	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	986.30 986.30	986.30	302.38	03/2016 -	12/2023	93	-

MoSPI OCMS

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning: Original / Revised	Date of Commissioning: Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
242	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 279.54	279.54	30.34	03/2016 -	12/2023	93	-
243	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 1,382.78	1,382.78	7.35	03/2002 -	03/2024	264	-
244	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 832.47	832.47	.94	03/2016 -	03/2024	96	-
245	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 2,841.84	2,841.84	169.45	12/2018 -	12/2024	72	-
	Southern Railway								
246	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	1,800.00	187.30	03/2019 -	12/2019	9	-
247	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	2,072.50	1,440.83	02/2019 -	02/2020	12	-
248	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	231.67	162.06	04/2014 -	03/2020	71	-
249	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	980.00	681.66	03/2020 -	03/2021	12	-
250	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	1,182.31	446.00	03/2020 -	06/2021	15	-
251	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	-
	West Central Railway								
252	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 6,672.85	8,248.50	1,986.78	05/2008 03/2022	03/2023	178	12
253	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	424.60 -	2,909.99	1,975.34	03/2021 -	03/2023	24	-
254	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH	06/2016	2,478.23 -	2,478.23	477.93	03/2022 -	03/2023	12	-
	Total		1,59,990.66 -	2,43,218.94	1,09,463.96				
	ROAD TRANSPORT AND HIGHWAYS								
	Ministry Of Road Transport And Highways (State Pwds)								
255	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA	08/2013	171.96 172.00	172.00	88.30	06/2016 -	11/2019	41	-
256	SAKOLI TO BHANDARA - [N24001118]MoRTH,MAHARASHTRA	01/2017	362.96 362.96	362.96	37.83	06/2019 -	11/2019	5	-
257	NASHIK TO PETH - [N24001121]MoRTH,MAHARASHTRA	12/2015	289.60 -	289.60	118.81	11/2018 -	11/2019	12	-
258	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH,KERALA	01/2014	255.75 348.00	348.43	290.12	09/2017 -	12/2019	27	-

MoSPI OCMS

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning: Original / Revised	Date of Commissioning: Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
259	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM	11/2010	624.41 -	992.67	853.82	03/2011 -	12/2019	105	-
260	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM	08/2010	193.69 -	327.92	254.24	10/2010 -	12/2019	110	-
261	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]MoRTH,ARUNACHAL PRADESH	03/2012	207.03 389.45	389.45	291.55	05/2012 05/2015	12/2019	91	55
262	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]MoRTH,SIKKIM	04/2013	151.59 -	151.59	196.76	08/2013 -	12/2019	76	-
263	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]MoRTH,SIKKIM	01/2013	182.28 -	269.14	185.49	02/2013 -	12/2019	82	-
264	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH	05/2013	164.54 -	164.54	126.41	08/2015 -	12/2019	52	-
265	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA	12/2011	191.08 -	191.08	99.98	08/2015 -	12/2019	52	-
266	WIDENING AND STRENFTHENING OF EXISITNG SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA	03/2014	191.50 192.00	192.00	136.19	05/2016 -	12/2019	43	-
267	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND	06/2017	282.08 -	282.08	77.05	06/2019 -	12/2019	6	-
268	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]MoRTH,MADHYA PRADESH	09/2016	287.34 -	287.34	148.65	01/2019 -	12/2019	11	-
269	REHABILITATION AND UPGRADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942]MoRTH,UTTAR PRADESH	03/2016	208.50 -	208.50	139.97	11/2019 -	12/2019	1	-
270	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA	01/2017	244.54 -	244.54	138.52	05/2019 09/2019	12/2019	7	3
271	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA	01/2017	196.52 -	196.52	103.22	10/2019 -	12/2019	2	-
272	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA	01/2017	359.27 -	359.27	237.90	05/2019 -	12/2019	7	-
273	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA	03/2018	192.67 -	192.67	107.37	07/2019 -	12/2019	5	-

MoSPI OCMS

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
274	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA	02/2017	203.21 203.00	203.21	109.79	05/2019 -	12/2019	7	-
275	SHEGAON TO DEORI PHATA - [N24001010]MoRTH,MAHARASHTRA	02/2017	373.10 373.00	373.10	143.43	05/2019 -	12/2019	7	-
276	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA	01/2017	385.87 386.00	385.87	203.75	06/2019 -	12/2019	6	-
277	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA	01/2017	341.16 341.00	341.16	156.29	06/2019 -	12/2019	6	-
278	NAGAJ TO VAIJAPUR - [N24001023]MoRTH,MAHARASHTRA	01/2017	376.72 377.00	376.72	183.81	06/2019 -	12/2019	6	-
279	INDAPAUR TO AGARDANDA - [N24001025]MoRTH,MAHARASHTRA	01/2017	355.17 -	355.17	164.87	07/2019 -	12/2019	5	-
280	TAKARKHED TO JALNA - [N24001085]MoRTH,MAHARASHTRA	09/2017	417.90 418.00	417.90	119.26	06/2019 -	12/2019	6	-
281	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA	12/2017	244.04 244.00	244.04	40.94	03/2019 -	12/2019	9	-
282	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA	01/2018	264.41 264.00	264.41	36.71	03/2019 -	12/2019	9	-
283	PEN TO KHOPOLI - [N24001106]MoRTH,MAHARASHTRA	03/2018	301.39 302.00	301.39	-	03/2018 -	12/2019	21	-
284	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND	08/2016	234.88 -	208.89	118.26	12/2017 -	12/2019	24	-
285	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]MoRTH,ASSAM	11/2010	197.37 -	197.37	88.86	02/2014 -	12/2019	70	-
286	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM	08/2010	186.96 -	305.61	275.06	09/2014 -	12/2019	63	-
287	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH	07/2016	208.88 -	208.88	88.62	10/2019 -	12/2019	2	-
288	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH	03/2015	511.83 -	511.83	261.31	08/2017 -	02/2020	30	-
289	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH	01/2016	809.16 -	809.16	236.96	07/2018 -	02/2020	19	-
290	AKKALKOT TO DHUDHNI - [N24001120]MoRTH,MAHARASHTRA	04/2016	211.42 -	211.42	131.85	02/2019 -	02/2020	12	-
291	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]MoRTH,MADHYA PRADESH	11/2011	954.43 -	954.43	235.61	09/2015 -	03/2020	54	-
292	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH	03/2018	162.56 -	162.56	88.47	03/2018 -	03/2020	24	-
293	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]MoRTH,MADHYA PRADESH	11/2017	235.91 -	235.91	144.76	02/2018 -	03/2020	25	-

MoSPI OCMS

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
294	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH	11/2017	184.62 -	184.62	65.06	02/2018 -	03/2020	25	-
295	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH	03/2018	233.04 -	233.04	109.26	03/2018 -	03/2020	24	-
296	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH	11/2017	249.05 -	249.05	127.30	07/2018 -	03/2020	20	-
297	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH	11/2017	254.17 -	254.17	152.81	02/2018 -	03/2020	25	-
298	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA	10/2016	248.83 -	248.83	91.52	03/2019 -	03/2020	12	-
299	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA	01/2017	300.00 -	300.00	100.33	05/2019 -	03/2020	10	-
300	INDAPUR TO VADPALE - [N24001114]MoRTH,MAHARASHTRA	01/2017	1,202.52 1,202.52	1,202.52	635.90	12/2019 -	03/2020	3	-
301	VADPALE TO BHOGAN KHURD - [N24001115]MoRTH,MAHARASHTRA	01/2017	1,598.47 1,560.00	1,598.47	751.91	11/2019 -	03/2020	4	-
302	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH	03/2016	249.50 -	249.50	156.70	05/2019 -	03/2020	10	-
303	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH	02/2018	279.44 -	279.44	76.00	03/2018 -	04/2020	25	-
304	KOLHA TO NASRATPUR - [N24001111]MoRTH,MAHARASHTRA	04/2016	281.78 282.00	281.78	47.73	04/2019 -	04/2020	12	-
305	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]MoRTH,MADHYA PRADESH	11/2013	497.05 -	881.05	544.84	05/2017 -	05/2020	36	-
306	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH	01/2017	373.82 -	373.82	116.34	09/2019 -	05/2020	8	-
307	WAKAN PALI KHOPOLI - [N24001026]MoRTH,MAHARASHTRA	01/2017	376.19 376.19	376.19	34.03	05/2019 -	05/2020	12	-
308	DEORI TO AMGAON - [N24001032]MoRTH,MAHARASHTRA	01/2017	409.62 410.00	409.62	181.78	05/2019 -	05/2020	12	-
309	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA	05/2018	171.60 -	171.60	.86	05/2018 -	05/2020	24	-
310	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM	08/2010	195.04 -	377.99	305.38	10/2010 -	06/2020	116	-
311	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH	03/2018	166.21 -	166.21	40.28	08/2018 -	06/2020	22	-

MoSPI OCMS

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning: Original / Revised	Date of Commissioning: Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
312	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]MoRTH,MADHYA PRADESH	03/2018	191.21 -	191.21	72.02	11/2019 -	06/2020	7	-
313	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH	01/2017	205.05 -	205.05	79.65	03/2017 -	06/2020	39	-
314	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH	03/2018	214.69 -	214.69	25.88	03/2018 -	06/2020	27	-
315	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH	03/2018	217.22 -	217.22	45.76	08/2018 -	06/2020	22	-
316	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA	10/2016	298.32 -	298.32	83.57	02/2019 -	06/2020	16	-
317	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA	01/2017	391.06 391.00	391.06	107.00	06/2019 -	06/2020	12	-
318	KARAD TO TAGAON - [N24001053]MoRTH,MAHARASHTRA	01/2017	537.81 538.00	537.81	89.97	06/2019 -	06/2020	12	-
319	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MoRTH,MAHARASHTRA	02/2017	407.19 407.00	407.19	25.00	06/2019 -	06/2020	12	-
320	MALEWADA TO CHIMUR - [N24001104]MoRTH,MAHARASHTRA	10/2016	322.55 -	322.55	156.91	06/2019 -	06/2020	12	-
321	PARLI PIMPLA DAHIGUDA - [N24001138]MoRTH,MAHARASHTRA	02/2017	205.72 205.72	205.72	30.42	06/2019 -	06/2020	12	-
322	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH	11/2017	392.33 -	392.33	242.88	03/2018 -	06/2020	27	-
323	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH	02/2018	169.63 -	169.63	11.39	03/2018 -	07/2020	28	-
324	MANGAON TO DIGHI PORT - [N24001024]MoRTH,MAHARASHTRA	01/2017	457.52 457.52	457.52	277.98	07/2019 -	07/2020	12	-
325	WADI TO ASOLA - [N24001022]MoRTH,MAHARASHTRA	01/2017	363.82 363.82	363.82	41.10	09/2019 -	09/2020	12	-
326	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH	03/2016	877.79 -	877.79	436.12	06/2019 -	12/2020	18	-
327	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MoRTH,ANDHRA PRADESH	10/2015	333.21 -	355.89	265.48	12/2015 01/2020	12/2020	60	11
328	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]MoRTH,BIHAR	05/2014	199.98 -	199.98	153.43	08/2016 -	12/2020	52	-
329	BARASGAON TO RAHATEE - [N24001113]MoRTH,MAHARASHTRA	07/2016	289.11 290.00	289.11	23.82	09/2018 -	04/2021	31	-

MoSPI OCMS

Costing Rs. 150 Crore and above									(November 2019)
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
330	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB	03/2018	170.57 192.48	170.57	46.23	11/2020 -	05/2021	6	-
331	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA	02/2017	157.32 188.00	157.32	-	05/2019 -	05/2021	24	-
332	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH,WEST BENGAL	03/2016	160.27 213.97	213.97	20.11	08/2019 -	08/2021	24	-
333	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH,WEST BENGAL	06/2016	236.78 263.26	263.26	59.92	08/2019 -	08/2021	24	-
	National Highways And Infrastructure Development Corporation Ltd.								
334	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 - [N24001184]NHIDCL,DELHI	07/2017	269.69 -	269.69	-	09/2019 -	12/2019	3	-
335	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	155.00	75.99	01/2017 -	01/2020	36	-
336	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH	03/2015	394.00 -	394.00	272.92	06/2018 -	03/2020	21	-
337	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 339.55	396.52	235.52	08/2016 -	06/2020	46	-
338	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM	05/2015	454.89 -	454.89	123.20	05/2018 05/2020	12/2020	31	7
339	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH	02/2017	168.32 168.32	168.32	34.87	04/2017 02/2018	02/2021	46	36
340	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 180.57	180.57	14.27	04/2017 02/2018	02/2021	46	36
341	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH	02/2017	216.71 216.71	216.71	19.67	04/2017 02/2018	02/2021	46	36
342	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 167.28	167.28	19.83	04/2017 02/2018	02/2021	46	36
343	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D - [N24000974]NHIDCL,ARUNACHAL PRADESH	02/2017	199.02 199.02	199.02	11.87	- 02/2018	02/2021	-	36

MoSPI OCMS

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
344	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D - [N24000975]NHIDCL,ARUNACHAL PRADESH	02/2017	184.88 184.88	184.88	97.50	- 02/2018	02/2021	-	36
345	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH	03/2017	284.09 284.09	284.09	77.42	04/2017 03/2018	03/2021	47	36
346	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM	01/2016	294.17 -	294.17	63.00	01/2016 02/2019	04/2021	63	26
347	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL,MANIPUR	08/2017	517.57 -	457.77	137.04	10/2018 -	10/2021	36	-
348	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM	06/2015	437.39 -	437.39	9.30	06/2018 12/2020	12/2021	42	12
349	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM	06/2015	463.49 -	463.49	22.32	06/2018 01/2021	12/2021	42	11
350	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH	01/2017	1,253.10 -	1,253.10	158.90	03/2017 -	03/2022	60	-
351	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH	02/2017	175.06 175.06	175.06	14.08	- 04/2019	04/2022	-	36
352	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH	02/2017	176.12 176.12	176.12	14.79	- 04/2019	04/2022	-	36
	National Highways Authority Of India								
353	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 537.16	537.16	503.20	07/2018 -	11/2019	16	-
354	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	763.23	439.88	06/2019 -	11/2019	5	-
355	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 881.00	688.70	701.76	- 05/2017	11/2019	-	30
356	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	2,016.00	1,996.00	04/2019 -	11/2019	7	-
357	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	232.49	-	10/2017 -	11/2019	25	-
358	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	946.00	818.53	06/2018 -	12/2019	18	-

MoSPI OCMS

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
359	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	943.17	08/2012 -	12/2019	88	-
360	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,401.00	03/2013 -	12/2019	81	-
361	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	1,364.18	03/2013 -	12/2019	81	-
362	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	530.07	556.02	08/2016 -	12/2019	40	-
363	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 -	1,083.00	1,487.87	06/2018 -	12/2019	18	-
364	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 67.34	1,871.34	3,512.79	01/2018 12/2018	12/2019	23	12
365	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	458.03	325.89	- 12/2017	12/2019	-	24
366	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	227.49	129.93	01/2019 -	12/2019	11	-
367	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	244.90	251.87	05/2019 -	12/2019	7	-
368	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	825.17	646.72	- 07/2017	01/2020	-	30
369	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	323.72	232.58	08/2018 -	01/2020	17	-
370	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	248.97	236.19	05/2019 -	01/2020	8	-
371	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	639.97	331.84	10/2017 -	01/2020	27	-
372	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	478.00	315.11	10/2013 -	02/2020	76	-
373	MEERUT-BULANDSHAHAR - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 868.77	987.94	727.69	- 10/2019	02/2020	-	4
374	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	722.46	723.95	07/2018 12/2019	02/2020	19	2
375	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	230.00	339.22	04/2008 -	03/2020	143	-
376	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	470.01	05/2010 -	03/2020	118	-
377	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 2,967.50	2,967.50	3,990.72	11/2011 -	03/2020	100	-
378	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	1,132.48	02/2013 -	03/2020	85	-

MoSPI OCMS

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
379	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	850.24	07/2013 -	03/2020	80	-
380	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 585.00	591.00	571.22	11/2013 12/2019	03/2020	76	3
381	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	1,396.18	2,894.94	09/2014 -	03/2020	66	-
382	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	597.00	587.64	10/2017 04/2018	03/2020	29	23
383	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	972.50	3,512.79	07/2017 12/2019	03/2020	32	3
384	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 1,302.98	934.46	531.34	03/2018 -	03/2020	24	-
385	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 897.03	897.03	757.88	11/2018 07/2019	03/2020	16	8
386	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	1,388.00	1,185.00	08/2018 -	03/2020	19	-
387	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	707.82	375.47	08/2018 -	03/2020	19	-
388	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 2,257.49	667.00	464.05	07/2018 -	04/2020	21	-
389	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 3,007.86	667.00	549.07	06/2018 -	04/2020	22	-
390	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	804.97	456.79	06/2018 -	04/2020	22	-
391	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	756.27	181.12	03/2020 -	04/2020	1	-
392	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	244.27	168.40	09/2017 -	04/2020	31	-
393	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,181.00	08/2013 -	05/2020	81	-
394	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	923.04	764.07	11/2016 -	05/2020	42	-
395	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	641.17	369.23	07/2018 -	05/2020	22	-
396	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 911.07	904.16	854.25	02/2020 11/2017	05/2020	3	30
397	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	1,065.51	1,005.76	03/2020 -	05/2020	2	-
398	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 2,602.09	1,989.00	882.41	03/2020 11/2017	05/2020	2	30

MoSPI OCMS

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning: Original / Revised	Date of Commissioning: Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
399	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	1,187.10	807.76	03/2020 -	05/2020	2	-
400	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	641.17	369.23	07/2016 -	05/2020	46	-
401	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 3,207.63	1,087.00	502.12	- 02/2018	05/2020	-	27
402	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,333.68	12/2013 -	06/2020	78	-
403	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,159.10	03/2014 04/2017	06/2020	75	38
404	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	2,945.00	2,467.00	04/2015 01/2017	06/2020	62	41
405	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 2,182.03	815.28	520.89	06/2018 -	06/2020	24	-
406	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 2,433.38	1,027.53	601.13	06/2018 -	06/2020	24	-
407	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	1,434.00	695.33	03/2020 -	06/2020	3	-
408	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	1,232.76	292.23	09/2017 -	06/2020	33	-
409	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	2,136.97	1,214.48	12/2018 -	07/2020	19	-
410	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	1,177.00	657.59	03/2020 -	07/2020	4	-
411	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	306.00	152.56	06/2017 -	07/2020	37	-
412	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	174.34	225.34	03/2008 -	08/2020	149	-
413	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	329.92	06/2013 01/2019	08/2020	86	19
414	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 870.00	870.00	265.48	03/2019 03/2017	08/2020	17	41
415	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	1,310.00	563.15	03/2020 -	08/2020	5	-
416	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 988.00	1,043.28	1,034.00	03/2020 -	08/2020	5	-

MoSPI OCMS

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning: Original / Revised	Date of Commissioning: Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
417	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	1,160.64	1,056.76	03/2020 -	08/2020	5	-
418	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	1,227.87	330.29	09/2017 -	08/2020	35	-
419	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	2,864.02	07/2015 12/2019	09/2020	62	9
420	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	727.00	509.85	05/2018 -	09/2020	28	-
421	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	504.00	235.19	05/2018 04/2019	09/2020	28	17
422	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	1,176.37	193.39	08/2017 -	09/2020	37	-
423	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	2,898.25	06/2014 09/2017	10/2020	76	37
424	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	681.67	402.94	- 04/2018	10/2020	-	30
425	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	701.40	29.48	03/2019 -	11/2020	20	-
426	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	870.00	36.30	03/2019 -	11/2020	20	-
427	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	1,373.28	571.96	03/2020 -	11/2020	8	-
428	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	1,071.00	582.87	03/2017 05/2018	11/2020	44	30
429	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	964.17	390.91	10/2017 -	11/2020	37	-
430	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020	52	-
431	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	2,168.66	684.57	06/2019 -	12/2020	18	-
432	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 247.00	322.09	77.53	04/2018 -	12/2020	32	-
433	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 1,008.00	1,108.00	1,385.71	08/2019 -	12/2020	16	-
434	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	207.00	34.77	- 03/2020	12/2020	-	9
435	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	990.61	397.89	09/2017 -	01/2021	40	-

MoSPI OCMS

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning: Original / Revised	Date of Commissioning: Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
436	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	2,043.00	-	- 05/2018	01/2021	-	32
437	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	400.25	64.89	03/2019 -	02/2021	23	-
438	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	1,958.88	1,116.85	06/2020 02/2018	02/2021	8	36
439	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,807.21	08/2013 -	03/2021	91	-
440	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	2,510.04	313.18	08/2019 -	03/2021	19	-
441	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	446.17	38.97	03/2019 -	03/2021	24	-
442	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	1,420.00	446.76	03/2020 -	03/2021	12	-
443	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 1,073.10	1,005.08	-	- 03/2019	03/2021	-	24
444	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00 565.02	621.00	327.15	- 10/2018	04/2021	-	30
445	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH	03/2018	1,532.62 2,499.00	2,499.00	584.50	03/2021 -	04/2021	1	-
446	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	227.77	11.00	03/2020 -	05/2021	14	-
447	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	476.56	-	07/2017 11/2020	06/2021	47	7
448	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	686.65	91.47	- 07/2020	06/2021	-	11
449	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	953.09	126.71	- 05/2020	06/2021	-	13
450	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	668.86	134.42	- 05/2020	06/2021	-	13

MoSPI OCMS

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning: Original / Revised	Date of Commissioning: Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
451	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	686.65	89.80	- 03/2020	06/2021	-	15
452	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 1,687.00	1,437.64	564.11	- 12/2018	07/2021	-	31
453	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00 512.99	607.00	163.98	- 02/2019	08/2021	-	30
454	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 2,946.82	2,485.93	359.79	06/2020 -	09/2021	15	-
455	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 2,190.00	2,400.00	1,558.83	- 05/2019	11/2021	-	30
456	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	950.64	102.51	08/2017 -	02/2022	54	-
	Total		1,34,266.76 -	1,40,399.42	93,060.53				
	TELECOMMUNICATIONS								
	Department Of Telecommunication								
457	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	24,664.00	12,146.00	07/2015 -	05/2020	58	-
	Total		13,334.00 -	24,664.00	12,146.00				
	URBAN DEVELOPMENT								
	Ahmedabad Metro Rail								
458	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	10,773.00	6,296.85	12/2018 -	07/2020	19	-
	Bangalore Metro Rail Corporation Limited								
459	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	26,405.14	499.85	02/2019 -	03/2020	13	-
	Central Public Works Department								
460	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	205.00	165.95	03/2012 -	12/2019	93	-
461	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB	02/2014	388.00 -	488.28	440.59	05/2017 -	12/2019	31	-
462	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD,PUNJAB	08/2016	294.00 -	294.00	208.99	04/2019 -	02/2020	10	-
463	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	94.62	10/2012 -	03/2020	89	-

Costing Rs. 150 Crore and above (November 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning: Original / Revised	Date of Commissioning: Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
464	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN	12/2016	549.31 559.47	559.47	373.45	07/2019 12/2019	04/2020	9	4
465	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	209.00	150.71	10/2019 -	07/2020	9	-
466	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2016	248.20 -	248.20	45.03	04/2018 02/2020	08/2020	28	6
467	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	89.53	03/2016 -	09/2020	54	-
468	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]CPWD,KARNATAKA	12/2016	246.31 -	246.31	80.34	02/2020 -	09/2020	7	-
469	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR	02/2014	216.69 -	216.69	52.00	03/2015 -	10/2020	67	-
470	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 -	197.33	61.47	04/2019 -	11/2020	19	-
471	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD,MAHARASHTRA	01/2018	223.37 -	223.37	42.19	07/2020 -	11/2020	4	-
472	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]CPWD,PUNJAB	01/2018	430.00 -	430.00	97.92	05/2020 -	01/2021	8	-
473	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	2,000.00	408.23	10/2019 -	03/2021	17	-
474	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	498.99	97.67	06/2017 -	03/2021	45	-
475	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITIUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST - [N28000112]CPWD,KERALA	09/2017	150.29 -	150.29	21.82	03/2020 11/2020	03/2021	12	4
476	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 -	392.00	12.56	- 08/2020	03/2021	-	7
477	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA	10/2016	209.84 -	209.84	58.75	03/2020 -	05/2021	14	-
478	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD,ODISHA	01/2019	790.79 -	800.00	11.01	03/2022 -	06/2022	3	-
	Hindustan Steelwork Construction Limited								
479	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72	-

Costing Rs. 150 Crore and above									(November 2019)
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticip ated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	Kochi Metro Rail Corporation Ltd								
480	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 5,687.79	5,687.79	5,656.62	07/2017 -	03/2020	32	-
	Mumbai Metro Rail Corporation Ltd								
481	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	05/2020	64	-
	Nagpur Metro Rail Corporation Ltd								
482	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	8,680.00	6,405.74	03/2018 -	12/2019	21	-
	Total		81,934.54 -	83,343.79	22,023.10				
	WATER RESOURCES								
	Polavaram Project Authority								
483	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA,ANDHRA PRADESH	02/2009	10,151.04 -	55,548.87	16,417.99	03/2020 -	06/2021	15	-
	Total		10,151.04 -	55,548.87	16,417.99				
	HUMAN RESOURCE DEPARTMENT								
	Rail India Technical And Economic Service								
484	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES,MEGHALAYA	09/2013	484.32 -	626.26	-	09/2014 -	12/2020	75	-
	Total		484.32 -	626.26	.00				
	Grand Total		6,85,284.71	8,82,773.42	4,33,698.19				

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2019)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2020	12320	48
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	06/2020	11459	54
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2021	3492	133
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	NPCIL	03/2013	11/2020	11/2023	39849	36

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	AAI	09/2015	06/2019	12/2019	338.93	6
6	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	AAI	01/2016	03/2020	12/2020	219.91	9
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	21
8	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	AAI	11/2016	04/2020	12/2020	233.38	8
9	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	AAI	06/2018	02/2022	08/2022	2467	6

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
10	RANIGANJ MASTER PLAN	ECL	08/2009	08/2019	08/2024	2661.73	60
11	RG OC -III EXTENSION (PHASE -II) PROJECT	SCCL	06/2012	06/2015	03/2020	365.01	57
12	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2021	162.76	72
13	RAJRAPPA RCE OCP (3.0 MTY)	CCL	12/2009	03/2016	03/2021	510.85	60
14	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	03/2013	03/2022	457.77	108
15	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2021	321.5	84
16	BHUBANESWARI OCP, MCL (20.0 MTY)	MCL	12/2007	03/2017	03/2021	490.1	48
17	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2021	207.28	108
18	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2021	479.53	96
19	RKP OCP PHASE-I	SCCL	03/2010	03/2015	03/2020	209.78	60
20	BALRAM OCP EXTENSION,MCL 8.00 MTY	MCL	12/2007	03/2010	03/2022	172.08	144

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
21	MOONIDIH XV SEAM UG	BCCL	08/2011	04/2015	04/2022	1230.27	84
22	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2021	163.51	120
23	TAPIN OCP (2.5 MTY)	CCL	08/2008	03/2012	03/2021	264.68	108
24	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2021	162.46	84
25	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2024	249.03	144
26	KISTARAM OCP	SCCL	11/2010	03/2015	03/2021	242.29	72
27	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2020	178.44	72
28	KAMPTEE DEEP OC MINE	WCL	11/2015	03/2021	03/2024	277.65	36
29	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	ECL	08/2012	03/2018	10/2020	1055.05	31
30	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	MCL	05/2014	03/2019	03/2024	479.15	60
31	JAGANNATH RE-ORGANISATION OC.(6.00 MTY)	MCL	05/2014	03/2019	03/2020	337.66	12
32	KULDA EXPN OC. (5.00 MTY)	MCL	06/2014	03/2018	03/2021	289.03	36
33	AMERA OC RCE	SECL	02/2015	03/2018	03/2020	335.97	24
34	MADHUBAND NLW WASHERY	BCCL	08/2010	05/2014	03/2020	289.45	70
35	PATHERDIH NLW WASHERY	BCCL	10/2012	04/2014	01/2020	269.82	69
36	KAKATIYAKHANI OPENCAST-2 PROJECT	SCCL	05/2015	03/2019	03/2020	397.09	12
37	ADASA UG TO OC	WCL	08/2015	03/2023	03/2024	288.9	12
38	KULDA OCP (MAHANADI COALFIELDS LTD)	MCL	01/2005	03/2010	03/2020	302.96	120
39	KOYAGUDEM OPENCAST PROJECT	SCCL	10/2015	03/2018	03/2020	426.79	24
40	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	60
41	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2022	706.4	116
42	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2023	418.97	132
43	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	12/2019	5907.11	48

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
44	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2021	447.06	72
45	BAROUD OC EXPANSION (RCE)- 3MTY	SECL	04/2012	03/2016	03/2020	258.56	48
46	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2020	417.33	44
47	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1	SCCL	03/2017	03/2019	03/2022	413.84	36
48	RFR OF MANUGURU OC PROJECT	SCCL	11/2012	03/2016	03/2020	430.45	48

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
49	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	HITES	07/2016	04/2020	10/2020	785	6
50	AIIMS - OPD(NEW)	HSCC	08/2014	05/2017	01/2020	293.65	32
51	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA	HSCC	08/2017	03/2019	03/2020	274.19	12
52	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH	HSCC	08/2017	03/2019	03/2020	272.19	12
53	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	HSCC	08/2017	03/2019	07/2020	355.15	16
54	LHMC NEW DELHI-RE-DEVELOPMENT	HSCC	02/2013	11/2013	09/2020	414.11	82
55	AIIMS - MOTHER AND CHILD BLOCK	HSCC	12/2013	05/2017	06/2020	204.44	37
56	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	HSCC	07/2016	02/2018	03/2020	152.95	25
57	NEIGRIHMS SHILLONG MEGHALYA	HSCC	10/2016	05/2018	07/2020	363.99	26

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
58	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	BHEL	08/2016	09/2019	03/2020	1554	6

HUMAN RESOURCE DEPARTMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
59	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	RITES	09/2013	09/2014	12/2020	484.32	75

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2019)

INFORMATION AND BROADCASTING

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
60	FILM AND TELEVISION INSTITUTE ARUNACHAL PRADESH	CPWD	11/2016	02/2019	11/2019	204.32	9

MINES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
61	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU	NALCO	09/2017	06/2019	03/2020	166.62	9

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
62	FUEL QUALITY UPGRADATION (NSU,NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY	IOCL	06/2017	10/2019	05/2020	951.64	7
63	REVAMPING OF FACILITIES AT VIZAG TERMINAL	IOCL	04/2018	04/2022	02/2023	355	10
64	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II	OIL	09/2016	12/2019	06/2020	571.66	6
65	MMPL PIPELINE REROUTING PROJECT	BPCL	04/2013	12/2019	07/2020	449.58	7
66	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY	BPCL	02/2016	02/2020	10/2020	3313	8
67	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	IOCL	05/2016	01/2021	10/2021	348	9
68	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY	IOCL	05/2016	01/2019	06/2020	429	17
69	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	ONGC	02/2017	05/2021	12/2021	4006.83	7
70	KHARAGPUR LPG BOTTLING PLANT	IOCL	04/2017	04/2020	03/2021	163.02	11
71	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	IOCL	12/2017	10/2020	08/2021	466.43	10
72	BS-VI PROJECT AT GUJARAT REFINERY	IOCL	03/2018	09/2019	03/2020	3380	6
73	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	12/2019	2059.63	57
74	HALDIA LPG IMPORT FACILITY	BPCL	03/2015	10/2018	12/2019	694	14
75	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	12/2019	4588.29	16
76	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	GAIL	04/2016	04/2018	12/2019	327.78	20
77	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	10/2021	678	56
78	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	07/2022	20928	24
79	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM	IOCL	06/2016	08/2019	12/2020	423	16

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	AS RESITEMENT OF RAMNAGAR DEPOT						
80	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	ONGC	11/2015	03/2019	05/2020	650.82	14
81	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	ONGC	03/2016	06/2020	08/2021	34012	14
82	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	02/2021	4497	26
83	BSVI UPGRADATION	MANGALORE REFI	09/2016	12/2019	07/2020	1810	7
84	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA	ONGC	01/2015	12/2017	03/2020	4619.94	27
85	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	05/2020	3190.69	25
86	SITARGANJ LPG PROJECT	IOCL	02/2017	02/2020	10/2020	160.1	8
87	LPG BP PROJECT KHORDHA	IOCL	12/2016	12/2019	07/2021	161.59	19
88	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2022	2915	110
89	SEA WATER DESALINATION PLANT	MANGALORE REFI	11/2017	03/2020	11/2020	581	8
90	ASSAM RENEWAL PROJECT FOR GROUP A	ONGC	03/2009	03/2013	12/2019	2465.15	81
91	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	OIL	07/2011	03/2017	06/2020	352.56	39
92	PARADIP LPG IMPORT FACILITY	IOCL	01/2015	07/2018	10/2020	690	27
93	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III	ONGC	11/2014	04/2019	12/2019	6068.8	8
94	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY	ONGC	08/2015	03/2019	05/2020	2818.88	14
95	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	11/2019	202.94	70
96	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	12/2019	861.79	79
97	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	02/2022	1112	32
98	180 TMTPA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA	HPCL	06/2017	06/2020	09/2021	249.26	15
99	120 TMTPA NEW LPG PLANT AT BARHI JHARKAND STATE	HPCL	06/2017	06/2020	09/2021	161.5	15
100	BS-VI PROJECT AT BONGAIGAON REFINERY	IOCL	05/2018	09/2019	04/2020	1222	7
101	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY	IOCL	05/2018	09/2019	04/2020	2934.4	7

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
102	BS-VI PROJECT AT PANIPAT REFINERY	IOCL	12/2017	07/2019	02/2020	3529	7
103	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	IOCL	10/2017	02/2020	10/2020	906	8

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
104	DURGAPUR PP-III (2X20 MW) - NSPCL	NTPC	12/2016	11/2018	03/2020	529.68	16
105	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	08/2021	8692.97	118
106	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	10/2017	03/2020	11846	29
107	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	NTPC	01/2016	11/2020	06/2021	10598.98	7
108	TRANSMISSION SYSTEM STRENTHENNING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	PGCIL	03/2016	01/2018	03/2020	808.63	26
109	EASTERN REGION STRENGTHENNING SCHEME-XV	PGCIL	04/2016	04/2018	01/2020	454.11	21
110	GREEN ENERGY CORRIDORS - INTER STATE TRANSSMISSION SCHEME PART-D	PGCIL	05/2016	05/2019	12/2019	3519.59	7
111	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA	PGCIL	04/2016	04/2019	11/2019	844.64	7
112	SOUTHERN REGION STRENGTHENING SCHEME-XXI	PGCIL	09/2016	03/2019	12/2019	562.25	9
113	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II)	PGCIL	10/2016	01/2019	01/2020	408.46	12
114	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	PGCIL	10/2016	04/2019	12/2019	608.24	8
115	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	PGCIL	02/2017	02/2019	03/2020	322.3	13
116	EASTERN REGION STRENTHENING SCHEME XVII(PART B)	PGCIL	02/2017	06/2019	03/2020	235.53	9
117	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII	PGCIL	03/2017	06/2019	12/2019	337.75	6
118	COMPREHENSIVE SCHEME FOR THE STRENGHTENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	12/2020	4754.42	24
119	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2020	5111.33	24
120	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP)	PGCIL	01/2015	10/2017	11/2019	871.62	25
121	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	PGCIL	01/2015	07/2017	11/2019	203.28	28
122	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	PGCIL	03/2015	03/2018	12/2019	197.4	21

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
123	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	PGCIL	03/2015	05/2017	12/2019	1394.52	31
124	DHUKWAN SMALL HYDRO PROJECT	THDCIL	05/2011	02/2014	12/2019	195.42	70
125	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	09/2020	5353	98
126	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2022	2491.58	114
127	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	06/2022	1657	76
128	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	12/2019	487.49	66
129	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	12/2019	1364.52	44
130	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	PGCIL	01/2014	04/2016	12/2019	374.63	44
131	EASTERN REGION STRENGTHENING SCHEME-XII	PGCIL	05/2014	11/2016	03/2020	522.29	40
132	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	01/2021	2978.48	94
133	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH	PGCIL	06/2014	03/2018	12/2019	5151.37	21
134	TANDA TPP STAGE-II (2X660 MW)	NTPC	09/2014	07/2019	07/2020	9188.98	12
135	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	12/2018	09/2020	12532.44	21
136	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	03/2022	14366.58	33
137	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	05/2024	1381.84	56
138	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	PGCIL	12/2015	04/2019	12/2019	3654	8
139	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT	PGCIL	05/2017	09/2018	03/2020	175.64	18
140	TRANSMISSION SYSTEM FOR EVACUTION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY	PGCIL	05/2017	07/2019	01/2020	186.17	6
141	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B)	PGCIL	05/2017	02/2019	03/2020	445.89	13
142	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	06/2021	12964.6	37
143	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	02/2017	06/2020	9750.89	40
144	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2021	3919.59	147
145	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	03/2020	4824.12	89

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
146	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	01/2018	03/2020	11638.55	26
147	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	03/2022	11130.19	103
148	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL	NTPC	05/2016	12/2018	03/2020	1885.13	15
149	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT	PGCIL	12/2017	06/2019	03/2020	193.14	9

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
150	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM	WR	04/2017	03/2020	03/2021	691.84	12
151	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	12/2022	2288	9
152	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	03/2020	644.78	36
153	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	03/2023	1973	24
154	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM	ECR	04/2016	03/2021	03/2022	731.64	12
155	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	NER	04/2016	12/2019	04/2021	1177.96	16
156	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	ECOR	04/2015	12/2018	03/2022	1172.92	39
157	KAZIPET-BALHRSHA	SCR	04/2015	03/2021	03/2023	2063.03	24
158	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	12/2021	1724.2	9
159	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	RVNL	04/2015	03/2022	12/2024	943.6	33
160	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	03/2030	1027.4	324
161	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	03/2020	927.01	12
162	MAU-GHAZIPUR-TARIGHAT NEW LINE	RVNL	04/2015	03/2023	12/2024	1765.92	21
163	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	03/2021	713.48	12
164	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	03/2021	948.04	12
165	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2020	632.68	57
166	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	SR	04/2011	03/2019	12/2019	120.7	9
167	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY	ER	04/1987	03/2006	03/2025	406.99	228

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG						
168	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	03/2025	915.98	36
169	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	ER	04/2001	03/2016	03/2025	923.52	108
170	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	03/2025	595.51	96
171	KIUL - GAYA DOUBLING PROJECT	ECR	12/2015	03/2020	10/2021	1200.2	19
172	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	ECR	12/2015	03/2020	12/2022	1491.47	33
173	KATNI - SINGRAULI DOUBLING PROJECT	WCR	12/2015	03/2020	03/2023	1763.93	36
174	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2025	1188.91	72
175	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	03/2024	607.09	133
176	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	03/2020	1185.64	27
177	RAMGANJMUNDI-BHOPAL (NL),WCR	WCR	04/2001	03/2021	03/2023	424.6	24
178	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	12/2021	1202.7	82
179	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	06/2020	133.41	135
180	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	06/2024	810.78	36
181	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	02/2019	02/2020	724.69	12
182	BARDHAMAN-KATWA (GC)	ER	04/2007	12/2010	03/2025	1106.62	171
183	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	03/2022	2393.47	96
184	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	03/2020	477.88	96
185	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	03/2010	03/2023	1160.48	156
186	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	03/2025	2913.51	108
187	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	03/2023	3503.69	12
188	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	ER	04/2010	03/2016	03/2025	277.28	108
189	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	ER	04/2010	03/2017	03/2025	365.17	96
190	HOWRAH DIVISION- PLATFORM SHELTER (40	ER	04/2010	11/2018	03/2021	157.94	28

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	C CATEGORY STATIONS)						
191	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	03/2022	792.89	12
192	HANSDIHA-GODDA NL	ER	04/2011	03/2020	03/2021	542.18	12
193	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY	ER	04/2011	03/2017	03/2026	299.6	108
194	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	ER	04/2010	03/2005	03/2025	494.54	240
195	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	03/2025	499.96	157
196	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL	ER	04/2009	03/2014	03/2025	257.42	132
197	3RD LINE BETWEEN BHUSAWAL-JALGAON	CR	04/2011	03/2019	12/2019	184.06	9
198	WARDHA-SEWAGRAM NGP 3RD LINE	CR	04/2012	03/2022	03/2024	540.02	24
199	BAGALKOT-KUDACHI NL	SWR	04/2010	03/2016	12/2023	986.3	93
200	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	03/2024	1856.95	12
201	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	03/2021	287	111
202	SHIMOGA-HARIHAR NL	SWR	04/2011	03/2016	03/2024	832.47	96
203	NADIKUDE-SRI KALAHASTI	SCR	04/2011	03/2021	03/2024	2288.7	36
204	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	SCR	04/2008	03/2014	03/2024	2132.77	120
205	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	RVNL	04/2010	03/2023	03/2024	2127	12
206	GADAG-WADI NL	SWR	04/2013	12/2018	12/2024	2841.84	72
207	MARIKUPPAM - KUPPAM	SWR	04/2012	03/2016	12/2023	279.54	93
208	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	03/2022	2271.5	12
209	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	MRTP	03/1996	03/2004	03/2021	495.44	204
210	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	178
211	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	ECR	04/1997	03/2012	03/2020	324.73	96
212	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NFR	04/2000	12/2008	03/2021	1180.19	147

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
213	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	06/2024	2923.13	183
214	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2022	4454.17	132
215	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2020	385.2	12
216	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2020	532.87	12
217	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	10/2021	2326.52	79
218	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	MRTP	04/2008	03/2014	03/2021	5300	84
219	DAUSA-GANGAPUR CITY(NL),NWR	NWR	02/1997	02/2019	03/2021	410.08	25
220	NANGALDAM-TALWARA(NL),NR	NR	03/1981	07/2012	03/2024	450	140
221	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	NR	03/1995	11/2002	06/2022	2500	235
222	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2025	3951.98	108
223	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	141
224	MUNEERABAD-MAHABOOBNAGAR(NL),SCR	SCR	04/1997	03/2000	03/2021	1723	252
225	GONDIA-JABALPUR(GC),(SECR)	SECR	02/1997	04/2020	01/2021	511.86	9
226	BANGLORE - SATYAMANGALAM (NL)(SWR)	SWR	04/1996	03/2002	03/2024	1382.78	264
227	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	09/1995	03/2020	03/2021	303.98	12
228	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	WR	04/2008	03/2012	03/2022	318.24	120
229	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	03/2021	829.74	12
230	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	03/2022	1503.71	24
231	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	03/2022	1111.99	37
232	BHADRAK - NERGUNDI 3RD LINE	ECOR	03/2013	10/2020	03/2023	843.04	29
233	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	03/2020	03/2023	1160	36
234	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	ECOR	03/2012	03/2020	03/2021	155.81	12
235	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE	SER	04/2012	12/2016	01/2020	148.77	37

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	(20 KM) JHARKHAND						
236	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	03/2021	1156.94	12
237	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	04/2022	600	25
238	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	03/2021	1614.59	24
239	HAJIPUR - BACHAWARA	ECR	05/2015	03/2019	02/2021	678.54	23
240	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	01/2020	295	12
241	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	MRTP	03/2013	03/2016	06/2021	4874.58	63
242	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	12/2019	06/2020	246.08	6
243	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	WR	04/2007	03/2022	03/2023	1640.04	12
244	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2022	320.66	36
245	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	03/2021	03/2022	1037.15	12
246	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	12/2024	2912.96	33
247	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	NFR	04/1983	03/2019	03/2020	297.32	12
248	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2023	1045.2	168
249	THIYAT HAMIRA-SANU	NWR	04/2013	10/2018	12/2019	236.93	14
250	AJMER-BANGURGRAM	NWR	04/2011	11/2019	05/2020	213.39	6
251	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	02/2019	03/2020	242.09	13
252	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	03/2025	651	120
253	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	12/2018	06/2020	258.2	18
254	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	03/2022	548	24
255	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	09/2021	569.63	18
256	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	03/2019	03/2020	314	12
257	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	CR	02/2015	03/2022	03/2023	1272.19	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
258	MANMAD - JALGAON - 3RD LINE (160 KM)	CR	02/2016	03/2022	03/2024	1035.16	24
259	WARDHA - NAGPUR - 4TH LINE (76 KM)	CR	02/2016	03/2023	03/2024	637.95	12
260	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	03/2023	3631	12
261	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM	SR	10/2013	04/2014	03/2020	187.26	71
262	JAGADALPUR-KORAPUT DOUBLING	ECOR	04/2015	03/2022	03/2023	1547.38	12
263	KORAPUT - SINGAPUR ROAD DOUBLING	ECOR	04/2015	03/2022	03/2025	2361.74	36
264	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2022	701.61	40
265	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	06/2022	942.95	39
266	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	RVNL	03/2012	12/2020	12/2022	1183.25	24
267	KATNI-BINA 3RD LINE (263 KM)	WCR	06/2016	03/2022	03/2023	2478.23	12
268	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	09/2022	582.13	6
269	RAMNA - SINGRAULI DOUBLING	ECR	08/2015	03/2020	03/2021	2436.21	12
270	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	IRCON	04/2016	03/2020	06/2023	5200	39
271	KARAILA ROAD - SHAKTINAGAR DOUBLING	ECR	08/2015	03/2019	12/2019	528.57	9
272	MULTI MODAL LOGISTICS PARK AT VARNAMA	CCOI	10/2013	03/2019	12/2019	343	9
273	MULTI MODAL LOGISTICS PARK AT KAKINADA	CCOI	08/2016	03/2019	12/2020	234.5	21
274	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	12/2020	585.93	22
275	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	SR	02/2017	03/2024	03/2026	1567	24
276	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	06/2021	760	15
277	INDARA - DOHRIGHAT GAUGE CONVERSION.	NER	04/2016	04/2016	06/2020	213	50
278	NANPARA - NEPALGANJ GAUGE CONVERSION.	NER	04/2017	04/2017	10/2022	150	66
279	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION	NER	04/2017	04/2017	01/2020	622.5	33
280	ETAH - KASGANJ - NEW LINE	NER	04/2017	04/2017	04/2022	276.9	60

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
281	MULTI MODAL LOGISTICS PARK AT KATHUWAS	CCOI	01/2011	03/2018	03/2020	493.17	24
282	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN	CCOI	10/2013	03/2019	12/2019	305	9
283	MULTI MODAL LOGISTICS PARK AT BARHI	CCOI	12/2015	03/2019	03/2020	346.32	12
284	MULTI MODAL LOGISTICS PARK AT TIHI	CCOI	12/2015	03/2019	02/2020	174	11
285	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	03/2022	744.04	12
286	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	03/2023	229	15
287	ANUPPUR-KATNI	SECR	04/2015	12/2021	11/2022	1370	11
288	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	WR	02/1991	03/2019	03/2020	551.51	12
289	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	IRCON	04/2013	09/2018	12/2020	3055	27
290	INDORE-DEWAS-UJJAIN (80 KMS)	WR	04/2016	06/2020	06/2021	700	12
291	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	03/2021	625	60

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
292	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404	MoRTH	12/2016	10/2019	04/2020	209.1	6
293	NAIGAONBANDI TO MANGRULPIR	MoRTH	12/2017	03/2019	12/2019	244.04	9
294	TALEGAON TO GONAPUR	MoRTH	01/2018	03/2019	12/2019	264.41	9
295	MALEWADA TO CHIMUR	MoRTH	10/2016	06/2019	06/2020	322.55	12
296	PEN TO KHOPOLI	MoRTH	03/2018	03/2018	12/2019	301.39	21
297	KOLHA TO NASRATPUR	MoRTH	04/2016	04/2019	04/2020	281.78	12
298	BARASGAON TO RAHATEE	MoRTH	07/2016	09/2018	04/2021	289.11	31
299	AKKALKOT TO DHUDHNI	MoRTH	04/2016	02/2019	02/2020	211.42	12
300	NASHIK TO PETH	MoRTH	12/2015	11/2018	11/2019	289.6	12
301	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER	MoRTH	08/2016	12/2017	12/2019	234.88	24
302	WIDENING TO TWO LANE WITH PAVED	MoRTH	01/2017	05/2019	12/2019	244.54	7

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE						
303	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT	MoRTH	01/2017	05/2019	12/2019	359.27	7
304	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION	MoRTH	01/2017	05/2019	03/2020	300	10
305	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC	MoRTH	05/2014	08/2016	12/2020	199.98	52
306	KHAMGAON TO SHEGAON	MoRTH	02/2017	05/2019	12/2019	203.21	7
307	SHEGAON TO DEORI PHATA	MoRTH	02/2017	05/2019	12/2019	373.1	7
308	DIGRAS DARWAH KARANJA	MoRTH	01/2017	06/2019	06/2020	391.06	12
309	NANDGAON TO MORSHI	MoRTH	01/2017	06/2019	12/2019	385.87	6
310	MORSHI TO ACHALPUR	MoRTH	01/2017	06/2019	12/2019	341.16	6
311	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V	MoRTH	02/2017	11/2017	11/2019	429.43	24
312	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3	MoRTH	03/2018	08/2018	03/2020	228.32	19
313	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU	MoRTH	03/2018	08/2018	02/2020	244.95	18
314	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG	MoRTH	03/2018	08/2018	02/2020	289.67	18
315	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (	MoRTH	03/2018	07/2018	01/2020	297.12	18
316	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA	MoRTH	03/2018	11/2018	05/2020	504.19	18
317	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O	MoRTH	03/2016	05/2016	07/2020	995.09	50
318	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P	MoRTH	01/2018	08/2018	08/2020	418.03	24
319	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD	MoRTH	08/2016	01/2017	04/2020	350.61	39
320	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	NHAI	08/2017	08/2017	02/2022	950.64	54
321	FOUR LANNING OF CHOLOPURAM-THANJAVUR	NHAI	08/2017	08/2017	09/2020	1176.37	37
322	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	NHAI	07/2017	07/2017	06/2021	476.56	47
323	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40)	NHAI	06/2017	06/2017	07/2020	648.33	37
324	JUNAGADH BYPASS	NHAI	10/2017	10/2017	11/2019	232.49	25

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
325	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124.	NHAI	10/2017	10/2017	01/2020	639.97	27
326	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540	NHAI	10/2017	10/2017	11/2020	964.17	37
327	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	06/2020	1124.11	33
328	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69	NHAI	09/2017	09/2017	01/2021	990.61	40
329	4-LANNING OF OTTANCHATRAM BYPASS	NHAI	09/2017	09/2017	04/2020	244.27	31
330	4-LANNING OF STHIYATHOPU-CHOLOPURAM	NHAI	09/2017	09/2017	08/2020	1227.87	35
331	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	MoRTH	03/2015	10/2015	01/2020	271.45	51
332	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	NHIDCL	05/2015	05/2018	12/2020	454.89	31
333	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	NHIDCL	06/2015	06/2018	12/2021	437.39	42
334	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	NHIDCL	06/2015	06/2018	12/2021	463.49	42
335	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	NHIDCL	03/2015	06/2018	03/2020	394	21
336	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1	MoRTH	01/2014	09/2017	12/2019	255.75	27
337	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	MoRTH	11/2013	05/2017	05/2020	497.05	36
338	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE	MoRTH	05/2013	08/2015	12/2019	164.54	52
339	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	MoRTH	03/2015	08/2017	02/2020	511.83	30
340	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA	MoRTH	12/2011	08/2015	12/2019	191.08	52
341	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	NHIDCL	01/2016	01/2016	04/2021	294.17	63
342	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	NHIDCL	01/2016	01/2016	12/2021	252	71
343	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	MoRTH	11/2011	09/2015	03/2020	954.43	54
344	GWALIOR-JHANSI, NH-75	NHAI	12/2003	12/2009	03/2020	604	123
345	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	NHAI	07/2010	07/2015	09/2020	1987	62
346	PATNA-MUZZAFFARPUR	NHAI	08/2010	02/2013	03/2020	671.3	85
347	4-LANNING OF CHAPRA-HAJIPUR	NHAI	01/2011	07/2013	03/2020	575	80

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
348	2 LANNING OF MUZAFFARPUR - SONBARSA	NHAI	05/2011	11/2013	03/2020	511.54	76
349	SRINAGAR TO BANIHAL	NHAI	06/2011	06/2014	10/2020	1100.7	76
350	DELHI/ HARYANA BORDER TO ROHTAK	NHAI	04/2007	05/2010	03/2020	486	118
351	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	03/2020	1108	100
352	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	NHAI	02/2010	08/2012	12/2019	617	88
353	PUNE-SATARA(NH-4)	NHAI	10/2010	03/2013	12/2019	1724.55	81
354	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	09/2012	12/2019	1509.1	87
355	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	12/2013	06/2020	1250	78
356	KANDLA - MUNDRA PORT	NHAI	01/2011	07/2013	11/2020	953.88	88
357	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	06/2020	2848	75
358	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	NHAI	11/2011	05/2014	12/2019	1535	67
359	MUZAFFARNAGAR-HARIDWAR	NHAI	09/2011	03/2013	12/2019	754	81
360	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	08/2013	05/2020	1078.84	81
361	4-LANING OF BRAHAMPORE-FARAKA	NHAI	02/2011	08/2013	03/2021	998.79	91
362	6-LANING OF DHANKUNI-KHARAGPUR SECTION	NHAI	04/2012	09/2014	03/2020	1396.18	66
363	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	06/2020	1928.22	62
364	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA	NHAI	11/2012	08/2016	12/2019	530.07	40
365	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	NHAI	01/2015	07/2017	03/2020	972.5	32
366	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION	NHAI	06/2014	11/2016	05/2020	923.04	42
367	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	NHAI	05/2014	08/2016	12/2020	1655.01	52
368	FOUR LANING OF HOSPET - CHITRADURGA	NHAI	03/2015	08/2018	03/2020	1388	19
369	FOUR LANING OF AURANGABAD - YEDISHI	NHAI	07/2015	01/2018	12/2019	1871.34	23
370	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	MoRTH	04/2013	08/2013	12/2019	151.59	76

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
371	SONAPUR TO GUWAHTI (AS-3)	NHAI	12/2003	03/2008	08/2020	245	149
372	NALBARI T BIJNI (AS-7)	NHAI	12/2003	04/2008	03/2020	208	143
373	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	NHAI	09/2010	06/2018	12/2019	946	18
374	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	NHAI	06/2011	06/2013	08/2020	600	86
375	HARIDWAR DEHRADUN APPROVED LENGTH 69	NHAI	11/2011	10/2013	02/2020	478.51	76
376	2 LANING WITH PS OF GULABPURA - UNIARA	NHAI	10/2015	10/2017	03/2020	597	29
377	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D	NHAI	09/2015	05/2018	05/2020	414.51	24
378	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	09/2020	531.13	28
379	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	NHAI	10/2015	05/2018	06/2020	593.26	25
380	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	NHAI	12/2015	03/2019	04/2021	649.5	25
381	4 LANING OF AMBALA - KAITHAL - PACKAGE -2	NHAI	01/2016	07/2018	11/2019	574.28	16
382	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	NHAI	08/2015	05/2018	09/2020	505	28
383	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	NHAI	12/2015	06/2018	12/2019	1083	18
384	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A	NHAI	12/2015	06/2019	12/2020	2168.66	18
385	FOUR LANING OF PARWANOO -SOLAN	NHAI	09/2015	03/2018	03/2020	934.46	24
386	FOUR LANING OF YADGIRI - WARANGAL	NHAI	12/2015	11/2018	03/2020	1423.96	16
387	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A	NHAI	12/2015	12/2018	07/2020	2136.97	19
388	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II)	NHAI	01/2016	06/2018	06/2020	815.28	24
389	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	NHAI	01/2016	06/2018	06/2020	1027.53	24
390	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)	NHAI	06/2016	07/2018	04/2020	667	21
391	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	NHAI	12/2015	06/2018	04/2020	667	22
392	FOUR LANING OF FORBESGANJ - JOGBANI	NHAI	08/2015	04/2018	12/2020	322.09	32
393	FOUR LANING OF CHANDIGARH - KHARAR	NHAI	10/2015	12/2017	12/2019	447.29	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
394	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1)	NHAI	12/2015	04/2018	03/2020	726.67	23
395	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	NHAI	03/2016	03/2019	11/2020	701.4	20
396	CONSTRUCTION OF ROB –FLYOVER AT RANICHAK, HALDIA	NHAI	03/2016	11/2018	03/2020	229.37	16
397	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL	NHAI	03/2016	03/2019	11/2020	870	20
398	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	NHAI	02/2016	08/2018	03/2020	707.82	19
399	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791	NHAI	03/2016	04/2019	07/2020	899	15
400	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K	NHAI	02/2016	07/2018	05/2020	641.17	22
401	NAGPUR RING ROAD PACKAGE-1	NHAI	03/2016	07/2019	12/2020	546	17
402	NAGPUR RING ROAD PACKAGE-2	NHAI	03/2016	07/2019	12/2020	591.66	17
403	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	NHAI	04/2016	06/2018	04/2020	804.97	22
404	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	NHAI	08/2016	09/2019	03/2020	1388.34	6
405	FOUR LANING OF BARHI-HAZARIBAGH NH-33	NHAI	08/2016	08/2018	01/2020	323.72	17
406	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION	NHAI	08/2016	01/2019	12/2019	227.49	11
407	HOSPET-BELLARY-KARNATAKA AP BORDER	NHAI	08/2016	03/2019	08/2020	1167.42	17
408	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500	NHAI	08/2016	04/2019	11/2019	2016	7
409	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73	NHAI	08/2016	05/2019	01/2020	248.97	8
410	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S	NHAI	09/2016	08/2019	03/2021	2510.04	19
411	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	NHAI	09/2016	08/2019	12/2020	950.69	16
412	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI	NHAI	11/2016	03/2019	02/2021	400.25	23
413	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	NHAI	11/2016	03/2019	03/2021	446.17	24
414	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	07/2018	02/2020	605.84	19
415	WIDENING AND STRENFTHENING OF EXISITNG SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO	MoRTH	03/2014	05/2016	12/2019	191.5	43
416	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER	MoRTH	08/2013	06/2016	11/2019	171.96	41

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	CONFIGURATION AND STRENGTHENING OF NAUPAR						
417	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST	NHAI	01/2017	05/2019	12/2019	244.9	7
418	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	NHIDCL	03/2017	04/2017	03/2021	284.09	47
419	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS	NHIDCL	02/2017	04/2017	02/2021	168.32	46
420	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	NHIDCL	02/2017	04/2017	02/2021	180.57	46
421	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS	NHIDCL	02/2017	04/2017	02/2021	216.71	46
422	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	NHIDCL	02/2017	04/2017	02/2021	167.28	46
423	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	NHIDCL	03/2016	08/2016	06/2020	396.52	46
424	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P	NHAI	06/2017	06/2020	09/2021	2485.93	15
425	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT	NHAI	06/2017	06/2020	02/2021	1958.88	8
426	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS	MoRTH	03/2018	08/2018	06/2020	217.22	22
427	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	NHAI	03/2017	03/2020	11/2020	1373.28	8
428	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	NHAI	03/2017	03/2017	11/2020	1059.73	44
429	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE	NHAI	03/2017	03/2020	05/2021	235.48	14
430	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	03/2021	1288.07	12
431	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	NHIDCL	12/2016	01/2017	01/2020	138.93	36
432	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	NHIDCL	01/2017	03/2017	03/2022	1253.1	60
433	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS	MoRTH	03/2018	03/2018	03/2020	233.04	24
434	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	MoRTH	11/2017	07/2018	03/2020	249.05	20
435	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS	MoRTH	11/2017	02/2018	03/2020	254.17	25
436	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS	MoRTH	02/2018	03/2018	04/2020	279.44	25
437	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175	MoRTH	09/2016	01/2019	12/2019	287.34	11
438	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A	MoRTH	01/2017	09/2019	05/2020	373.82	8
439	REHABILITATION AND UPGRADATION OF	MoRTH	01/2016	07/2018	02/2020	809.16	19

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS						
440	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM	MoRTH	03/2016	06/2019	12/2020	877.79	18
441	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	MoRTH	11/2010	03/2011	12/2019	624.41	105
442	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MoRTH	08/2010	10/2010	12/2019	193.69	110
443	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	MoRTH	03/2012	05/2012	12/2019	207.03	91
444	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	MoRTH	01/2013	02/2013	12/2019	182.28	82
445	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	MoRTH	08/2010	10/2010	06/2020	195.04	116
446	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	NHAI	03/2016	07/2016	05/2020	641.17	46
447	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	MoRTH	06/2017	06/2019	12/2019	282.08	6
448	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	NHIDCL	08/2017	10/2018	10/2021	517.57	36
449	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS	MoRTH	03/2018	03/2018	03/2020	162.56	24
450	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS	MoRTH	03/2018	08/2018	06/2020	166.21	22
451	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H	MoRTH	03/2016	11/2018	11/2019	271.17	12
452	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA	MoRTH	02/2018	03/2018	07/2020	169.63	28
453	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID	MoRTH	11/2017	02/2018	03/2020	235.91	25
454	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS	MoRTH	11/2017	02/2018	03/2020	184.62	25
455	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP	MoRTH	03/2018	11/2019	06/2020	191.21	7
456	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND	MoRTH	03/2016	08/2019	08/2021	160.27	24
457	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N	MoRTH	06/2016	08/2019	08/2021	236.78	24
458	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH.	MoRTH	01/2017	03/2017	06/2020	205.05	39
459	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	MoRTH	03/2018	03/2018	06/2020	214.69	27
460	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS	MoRTH	01/2017	03/2019	03/2020	247.25	12
461	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200	MoRTH	10/2017	10/2019	12/2020	1069.59	14

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
462	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000	MoRTH	03/2018	11/2020	05/2021	170.57	6
463	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12	MoRTH	10/2015	12/2015	12/2020	333.21	60
464	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU	MoRTH	09/2016	02/2017	12/2019	372.68	34
465	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO	MoRTH	11/2016	01/2018	01/2020	378.24	24
466	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69	MoRTH	11/2016	05/2017	03/2020	290.15	34
467	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD	MoRTH	01/2017	08/2017	03/2020	319.28	31
468	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21	MoRTH	01/2016	05/2016	12/2019	386.09	43
469	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216	MoRTH	03/2016	09/2016	03/2020	444.84	42
470	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT	MoRTH	01/2016	08/2016	03/2020	348.95	43
471	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2	MoRTH	11/2016	08/2017	02/2020	376.25	30
472	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216	MoRTH	01/2017	09/2017	12/2020	263.45	39
473	REHABILITAITON AND UPGRADATION OF REPALLE TO EEPPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH	MoRTH	01/2017	01/2018	01/2020	576.48	24
474	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON	MoRTH	10/2016	02/2019	06/2020	298.32	16
475	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ	MoRTH	10/2016	03/2019	03/2020	248.83	12
476	WADI TO ASOLA	MoRTH	01/2017	09/2019	09/2020	363.82	12
477	NAGAJ TO VAIJAPUR	MoRTH	01/2017	06/2019	12/2019	376.72	6
478	MANGAON TO DIGHI PORT	MoRTH	01/2017	07/2019	07/2020	457.52	12
479	WAKAN PALI KHOPOLI	MoRTH	01/2017	05/2019	05/2020	376.19	12
480	DEORI TO AMGAON	MoRTH	01/2017	05/2019	05/2020	409.62	12
481	KARAD TO TAGAON	MoRTH	01/2017	06/2019	06/2020	537.81	12
482	KARAD PATAN CHIPLUN GUHAGAR	MoRTH	02/2017	06/2019	06/2020	407.19	12
483	TAKARKHED TO JALNA	MoRTH	09/2017	06/2019	12/2019	417.9	6
484	ESTIMATE FOR WIDENING TWO LANE TO	MoRTH	05/2018	05/2018	05/2020	171.6	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT						
485	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM	MoRTH	11/2010	02/2014	12/2019	197.37	70
486	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM.	MoRTH	11/2017	03/2018	06/2020	392.33	27
487	PARLI PIMPLA DAHIGUDA	MoRTH	02/2017	06/2019	06/2020	205.72	12
488	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730	MoRTH	03/2016	05/2019	03/2020	249.5	10
489	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION	MoRTH	02/2017	05/2019	05/2021	157.32	24
490	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MoRTH	08/2010	09/2014	12/2019	186.96	63

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
491	CENTRAL DISPATCH YARD	RINL	08/2015	08/2018	12/2019	320.66	16
492	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	07/2020	15525	62
493	FORGED WHEEL PLANT	RINL	04/2014	09/2018	12/2019	1682.85	15
494	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	SAIL	05/2015	12/2017	01/2020	1154.18	25
495	NEW SINTER PLANT AT BOKARO STEEL PLANT	SAIL	03/2015	10/2017	06/2020	1034.01	32
496	INSTALLATION OF NEW HOT STRIP MILL AT RSP	SAIL	04/2015	04/2018	01/2020	3127.3	21
497	COKE OVEN BATTERY-5	RINL	12/2011	12/2017	12/2019	2858	24
498	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	SAIL	11/2016	06/2019	06/2020	262.87	12

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
499	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	05/2020	13334	58
500	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	BSNL	01/2018	10/2018	12/2019	231.8	14

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
501	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	07/2020	10773	19

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
502	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	CPWD	02/2014	03/2015	10/2020	216.69	67
503	NSG AT KOLKATA	CPWD	10/2014	04/2018	06/2020	162.88	26
504	BANGALORE METRO RAIL PROJECT PHASE-2	BMRCL	02/2014	02/2019	03/2020	26405.14	13
505	IRRIGATION WORK OF BAGMATI	HSCL	10/2005	03/2015	03/2021	956	72
506	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	CPWD	06/2015	04/2019	11/2020	197.33	19
507	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	CPWD	02/2014	05/2017	12/2019	388	31
508	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	CPWD	12/2015	10/2019	07/2020	209	9
509	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	03/2021	1219.21	17
510	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	CPWD	06/2010	03/2012	12/2019	205	93
511	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	CPWD	01/2010	10/2012	03/2020	165.23	89
512	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	03/2020	5181.79	32
513	NAGPUR METRO RAIL	NMRCL	08/2014	03/2018	12/2019	8680	21
514	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	01/2015	05/2020	23136	64
515	CHENNAI METRO RAIL LTD (PHASE 1 EXT)	CMRL	06/2016	03/2018	06/2020	3770	27
516	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	CPWD	10/2016	03/2020	05/2021	209.84	14
517	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	CPWD	02/2016	06/2017	03/2021	496.18	45
518	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	CPWD	09/2012	03/2016	09/2020	171.86	54
519	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	CPWD	10/2017	11/2019	08/2020	271.9	9
520	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	CPWD	10/2016	04/2018	08/2020	248.2	28
521	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITIUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST	CPWD	09/2017	03/2020	03/2021	150.29	12
522	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	CPWD	08/2016	04/2019	02/2020	294	10
523	RESIDENTIAL QUATERS FOR HAL,BANGLORE	CPWD	12/2016	02/2020	09/2020	246.31	7
524	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	CPWD	12/2016	07/2019	04/2020	549.31	9

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
525	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	CPWD	01/2018	05/2020	01/2021	430	8

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
526	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	06/2021	10151.04	15

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(NOVEMBER 2019)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	6840	3348
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	11459	16580	5121
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12320	17079	4759

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	314.61	441.33	126.72

COAL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
5	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	152.43	459.49	307.06
6	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	5907.11	7080.41	1173.3
7	RANIGANJ MASTER PLAN	ECL	08/2009	08/2019	2661.73	5173.26	2511.53
8	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	162.76	349.28	186.52
9	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	249.03	448.86	199.83
10	BHANEGAON OC	WCL	02/2015	03/2023	187.94	409.68	221.74

HUMAN RESOURCE DEPARTMENT

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
11	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	RITES	09/2013	09/2014	484.32	626.26	141.94

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
12	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	993	1693	700
13	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	607.06	714.25	107.19
14	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	202.94	345.92	142.98
15	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	ONGC	02/2017	05/2021	4006.83	4475.92	469.09
16	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	2915	4915	2000
17	MUMBAI REFINERY EXPANSION PROJECT	HPCL	09/2015	03/2020	4199	5060	861

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
18	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	4497	6025	1528
19	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	20928	26264	5336
20	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	4588.29	5245.96	657.67
21	HALDIA LPG IMPORT FACILITY	BPCL	03/2015	10/2018	694	1097.54	403.54
22	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	871.35	1200	328.65
23	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	2059.63	2665.65	606.02
24	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	OIL	01/2018	02/2020	543.91	682.9	138.99
25	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	1112	1507.24	395.24
26	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	861.79	1683.06	821.27
27	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	IOCL	01/2015	12/2020	1823	3027.9	1204.9
28	PARADIP HYDERABAD PIPLEINE	IOCL	01/2015	12/2020	2321	3338	1017

POWER

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
29	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	9997.11	6077.52
30	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	01/2018	11638.55	12865.92	1227.37
31	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	11130.19	14719.1	3588.91
32	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	19496.34	13211.01
33	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	4824.12	5071.94	247.82
34	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	5111.33	6880.36	1769.03
35	COMPREHENSIVE SCHEME FOR THE STRENGHTENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	4754.42	9072.36	4317.94
36	PAKRI BARWADIH COAL MINING PROJECT	NTPC	10/2004	10/2017	4237.96	4552	314.04
37	KHARGONE STPP STAGE I (1320 MW)	NTPC	03/2015	01/2020	9870.51	11148.86	1278.35
38	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	NTPC	07/2012	08/2017	1527	1801.07	274.07

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
39	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	10/2017	11846	12739.82	893.82
40	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	2491.58	4397.8	1906.22
41	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	02/2017	9750.89	12176.28	2425.39
42	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	12964.6	17304	4339.4
43	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	5353	9583	4230
44	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	1381.84	1592.34	210.5
45	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	14366.58	15164.05	797.47
46	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	12/2018	12532.44	13740.53	1208.09
47	TANDA TPP STAGE-II (2X660 MW)	NTPC	09/2014	07/2019	9188.98	10016.1	827.12
48	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	5867.38	2888.9
49	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	8692.97	21312.11	12619.14
50	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	1779.29	2187.32	408.03
51	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	487.49	639.46	151.97
52	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	1657	5024.35	3367.35
53	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	7927.34	5430.44
54	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	1364.52	1891.41	526.89

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
55	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	NFR	04/1983	03/2019	297.32	614	316.68
56	KODERMA-RANCHI VIA BARKAKANA (NL),ECR	ECR	03/1999	N.A.	1033.07	3376	2342.93
57	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	1045.2	2120.16	1074.96
58	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	MRTP	03/2000	12/2006	1049.69	3404.92	2355.23
59	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	1188.91	1619.48	430.57
60	RAMGANJMUNDI-BHOPAL (NL),WCR	WCR	04/2001	03/2021	424.6	2909.99	2485.39

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
61	CHHINDWARA - NAGPUR (GC)(SECR)	SECR	04/2005	N.A.	383.79	1413.76	1029.97
62	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	477.88	751.55	273.67
63	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	ECR	04/2003	N.A.	528.65	2066.78	1538.13
64	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	2393.47	5021.45	2627.98
65	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
66	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	582.83	2300	1717.17
67	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	SR	09/2006	N.A.	227.4	900	672.6
68	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	02/2019	724.69	2072.5	1347.81
69	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	810.78	1928.07	1117.29
70	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	385	251.59
71	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65
72	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43
73	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	NR	04/2007	N.A.	336.91	791.39	454.48
74	BHANUPALI-BILASPUR BERI NL	RVNL	04/2008	12/2026	2966.99	7000	4033.01
75	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	287	694	407
76	BHADRACHALAM-KOVVUR	SCR	04/2012	N.A.	923.23	2184.83	1261.6
77	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	1856.95	2200	343.05
78	MANUGURU-RAMAGUNDAM	SCR	04/2013	N.A.	1112	2911.84	1799.84
79	3RD LINE BETWEEN BHUSAWAL-JALGAON	CR	04/2011	03/2019	184.06	312	127.94
80	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	2326.52	4600	2273.48
81	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	532.87	2145	1612.13
82	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	385.2	1532	1146.8

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
83	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	MRTP	04/2006	06/2013	495.74	734.01	238.27
84	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	4454.17	12524	8069.83
85	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	2923.13	3791.66	868.53
86	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NFR	04/2000	12/2008	1180.19	4541	3360.81
87	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	614.45	451.58
88	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	ECR	04/1997	03/2012	324.73	1050	725.27
89	AHMEDABAD-BOTAD (GC)	RVNL	04/2012	12/2021	975.62	1082.32	106.7
90	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	12/2019	246.08	348.55	102.47
91	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	MRTP	03/2013	03/2016	4874.58	8574.97	3700.39
92	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	295	477.31	182.31
93	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	NER	03/2007	12/2021	243.78	895	651.22
94	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	NER	03/2013	N.A.	307	1409.09	1102.09
95	ANGAMALI-SABARIMALA (N.L.)(SR)	SR	10/1998	N.A.	1566	2815.62	1249.62
96	KODERMA-TILAIYA (NL), ECR	ECR	04/2002	N.A.	459.91	1625.87	1165.96
97	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	1614.59	1870.41	255.82
98	WESTERN DEDICATED FREIGHT CORRIDOR	DFCC	11/2007	03/2020	16592	51101	34509
99	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE	NER	04/2017	01/2018	1343	1476.15	133.15
100	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	760	1182.31	422.31
101	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	SR	02/1996	03/2005	268.87	950	681.13
102	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	585.93	1268.32	682.39
103	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	SCR	04/2017	03/2022	119.73	390.6	270.87
104	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	1908.51	2686.63	778.12
105	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	582.13	1247.64	665.51

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
106	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	942.95	1120	177.05
107	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	948.04	1500	551.96
108	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	713.48	2300	1586.52
109	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	927.01	1200	272.99
110	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	1027.4	2373	1345.6
111	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	1724.2	1993.24	269.04
112	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	969.83	1312.96	343.13
113	DIGARU-HOJAI (102 KM)	NFR	04/2015	03/2021	870.96	2136.01	1265.05
114	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	701.61	810.02	108.41
115	KOTTAVALSA - KORAPUT DOUBLING	ECOR	04/2015	03/2022	2499.71	3382.95	883.24
116	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	07/2014	332.15	546.71	214.56
117	VIJAYAWADA-GUDUR	RVNL	04/2015	12/2023	3246.26	3548.67	302.41
118	DAUND - MANMAD (236 KM)	CR	02/2016	03/2023	1876	2081.27	205.27
119	VAIBHAVWADI -KOLHAPUR (107 KM)	CR	02/2016	03/2024	2750	3438.51	688.51
120	PUNE-NASIK (265 KM)	CR	02/2016	03/2024	2425	5341.68	2916.68
121	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	DFCC	10/2006	N.A.	11589	28181	16592
122	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	595.51	769.4	173.89
123	PIRPAINTI-BHAGALPUR	ER	04/2011	N.A.	261.38	478.08	216.7
124	BANDEL-BOINCHI 3RD LINE	ER	04/2011	N.A.	288.35	393	104.65
125	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	915.98	2137.81	1221.83
126	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	ER	04/2007	N.A.	450	1261.34	811.34
127	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	406.99	545.7	138.71
128	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	SR	04/2011	03/2019	120.7	1800	1679.3

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
129	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	632.68	816.55	183.87
130	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	03/2019	314	728	414
131	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	NFR	04/1999	N.A.	819.23	1871	1051.77
132	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	03/2020	414.84	661	246.16
133	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	373.87	132.35
134	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	03/2020	242.22	471	228.78
135	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	03/2021	906.46	6000	5093.54
136	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	450	285.59
137	ERODE-PALANI	SR	04/2008	N.A.	288.57	1140	851.43
138	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	569.63	670	100.37
139	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	380	158.58
140	KURUPPANTHARA-CHINGAVANAM	SR	04/2007	N.A.	270.14	457.08	186.94
141	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	SR	04/1999	N.A.	198.68	556.64	357.96
142	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
143	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	2300	1776.48
144	ATTIPPATTU PUTTUR	SR	04/2008	02/2019	151.84	1105	953.16
145	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	NFR	04/2013	03/2019	1798	2496.67	698.67
146	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	425.17	212.16
147	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	548	819.01	271.01
148	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	ECR	04/2004	N.A.	372.14	1470.5	1098.36
149	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	1006	795
150	CHHAPRA-MUZAFFARPUR (NL)	ECR	04/2006	N.A.	378.56	1858.75	1480.19
151	SAKRI-HASANPUR ROAD (NL)	ECR	04/1999	N.A.	325	735.2	410.2

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
152	BIHTA-AURANGABAD (NL)	ECR	04/2008	N.A.	326.2	2995.01	2668.81
153	GAYA-CHATRA (NL)	ECR	04/2008	N.A.	415.67	549.75	134.08
154	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	12/2018	258.2	358.68	100.48
155	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	651	1009	358
156	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	620	352.63
157	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	02/2019	242.09	410	167.91
158	PUSHKAR-MERTA	NWR	04/2013	N.A.	323	432.22	109.22
159	AJMER-KOTA (NASIRABAD-JAUNDRI)	NWR	04/2013	N.A.	822	1099.54	277.54
160	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	2912.96	3845.6	932.64
161	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	4079.15	1996.4
162	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	320.66	858.96	538.3
163	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	NWR	05/2015	N.A.	873.71	1980.21	1106.5
164	SAMASTIPUR-DARBANGHA	ECR	05/2015	N.A.	380	519.33	139.33
165	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	148.77	377	228.23
166	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	1111.99	1539.28	427.29
167	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	1503.71	2200	696.29
168	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	829.74	1310.23	480.49
169	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	09/1995	03/2020	303.98	980	676.02
170	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54
171	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN	NFR	02/1999	04/2010	380.6	1871	1490.4
172	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	625	859	234
173	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	2288	4970.11	2682.11
174	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	WR	02/1991	03/2019	551.51	809.07	257.56

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
175	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	644.78	890	245.22
176	CHAMPA-JHARSUGUDA 3RD LINE	SECR	04/2008	12/2019	872	1226.51	354.51
177	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	229	852.5	623.5
178	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	ECR	04/1991	N.A.	329.39	1483.14	1153.75
179	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR	ECR	04/1998	N.A.	180.82	726.31	545.49
180	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM	ECR	04/2016	03/2021	731.64	1185.73	454.09
181	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	744.04	1215.54	471.5
182	BURHWAL - GONDA - 3RD RUNNING LINE.	NER	04/2016	N.A.	602.5	714.34	111.84
183	CHANDIGARH-BADDI	NR	04/2007	03/2023	328.14	1540	1211.86
184	GONDIA-JABALPUR(GC),(SECR)	SECR	02/1997	04/2020	511.86	1756	1244.14
185	NANDYAL-YERRAGUNTLA(NL),SCR	SCR	03/1996	02/2009	164.36	1050	885.64
186	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	2298.42	2733.86	435.44
187	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	3951.98	4724.3	772.32
188	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	NR	03/1995	11/2002	2500	27949	25449
189	NANGALDAM-TALWARA(NL),NR	NR	03/1981	07/2012	450	2200	1750
190	DAUSA-GANGAPUR CITY(NL),NWR	NWR	02/1997	02/2019	410.08	886.41	476.33
191	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	4084.69	2745.21
192	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	8248.5	8000.84
193	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	MRTP	03/1996	03/2004	495.44	2980.41	2484.97
194	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	2271.5	3712.5	1441
195	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	RVNL	04/2010	03/2023	2127	2900	773
196	QADIAN-BEAS	NR	04/2011	N.A.	205.22	841.9	636.68
197	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	346.63	126.8

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
198	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	03/2020	704.31	952.16	247.85
199	NADIKUDE-SRI KALAHASTI	SCR	04/2011	03/2021	2288.7	2643.25	354.55
200	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	499.96	680.68	180.72
201	HANSDIHA-GODDA NL	ER	04/2011	03/2020	542.18	693.8	151.62
202	TARAKESHWAR-MAGRA NEW BG LINE	ER	04/2010	N.A.	365.17	527.54	162.37
203	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	792.89	1377.48	584.59
204	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	3503.69	3975.22	471.53
205	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	2913.51	4639	1725.49
206	ETAWAH-MAINPURI (NL),NCR	NCR	04/1997	12/2008	120	346	226
207	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	607.09	1425.44	818.35
208	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	1185.64	1844.47	658.83

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
209	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	02/2009	280	525	245
210	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2967.5	1859.5
211	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	655.17	459.17
212	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	340.14	140.33
213	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	MoRTH	12/2011	02/2012	156.63	276	119.37
214	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	MoRTH	03/2012	05/2012	207.03	389.45	182.42
215	BRAHMPUTRA BRIDGE,NH NO-31	NHAI	12/2003	04/2010	217.61	360.84	143.23
216	DEVELOPMENT AND OPERATION OF BIKANER-SURATGARH SECTION OF NH-15 BY 2L+PS IN THE STATE OF RAJASTHAN	MoRTH	03/2009	09/2013	501	671.54	170.54
217	NAGAUR-BIKANER OF NH-11 (2L+PS) UNDER PPP.	MoRTH	01/2012	01/2014	378.07	478.73	100.66
218	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	MoRTH	04/2014	08/2017	279.7	398.52	118.82
219	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR	MoRTH	08/2014	11/2017	823.2	937.76	114.56

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
	COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O						
220	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O	MoRTH	08/2014	11/2017	600.87	720.97	120.1
221	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4	NHAI	03/2018	N.A.	642.13	807	164.87
222	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA	NHAI	03/2018	N.A.	634.7	931.21	296.51
223	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N	NHAI	03/2018	N.A.	2065.96	2169	103.04
224	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT	NHAI	02/2018	N.A.	1995.34	2400	404.66
225	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1	MoRTH	12/2010	01/2019	169.26	299	129.74
226	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MoRTH	08/2010	09/2014	186.96	305.61	118.65
227	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH	MoRTH	10/2013	03/2017	445.89	653.29	207.4
228	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	NHAI	02/2018	N.A.	1424.77	1853.42	428.65
229	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	1124.11	1232.76	108.65
230	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O	NHAI	03/2017	03/2020	993.16	1434	440.84
231	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	NHAI	03/2017	03/2020	831.58	1177	345.42
232	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	NHAI	03/2017	03/2020	2064.99	2447	382.01
233	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	1288.07	1420	131.93
234	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	NHAI	03/2017	03/2020	1041.62	1187.1	145.48
235	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	NHAI	03/2017	03/2020	744.64	982	237.36
236	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF	NHAI	03/2018	N.A.	1029.96	1261.05	231.09
237	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	NHAI	03/2018	03/2021	1532.62	2499	966.38
238	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF	NHAI	02/2018	N.A.	1052.21	1449	396.79
239	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C	NHAI	03/2018	N.A.	1120.57	1332	211.43
240	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR.	NHAI	03/2018	N.A.	925.4	1197	271.6
241	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA	NHAI	02/2018	N.A.	2177.8	2450	272.2

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
242	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	NHAI	03/2017	03/2020	1184.71	1310	125.29
243	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	07/2018	605.84	722.46	116.62
244	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	NHAI	09/2016	08/2019	950.69	1108	157.31
245	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	NHAI	08/2016	09/2019	1388.34	2587.5	1199.16
246	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	NHAI	03/2016	04/2019	1587.49	2982	1394.51
247	MEERUT-BULANDSHAHAR	NHAI	01/2016	N.A.	683.24	987.94	304.7
248	FOUR LANING OF CHANDIGARH - KHARAR	NHAI	10/2015	12/2017	447.29	746.43	299.14
249	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	1055	1601.77	546.77
250	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2	NHAI	11/2015	05/2018	867.66	1464.24	596.58
251	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	531.13	727	195.87
252	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	MoRTH	08/2010	10/2010	195.04	377.99	182.95
253	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	MoRTH	11/2010	02/2011	470.2	630.36	160.16
254	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	MoRTH	11/2013	05/2017	497.05	881.05	384
255	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	MoRTH	10/2013	03/2017	445.89	653.29	207.4
256	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I	NHAI	08/2015	02/2018	723.54	1286.84	563.3
257	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	1928.22	2945	1016.78
258	NASHRI- CHANANI	NHAI	05/2011	06/2015	2159	2519	360
259	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	1266.6	1544	277.4
260	INDORE-DEWAS(NH-3)	NHAI	11/2010	05/2013	325	475	150
261	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MoRTH	08/2010	10/2010	193.69	327.92	134.23
262	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	MoRTH	11/2010	03/2011	624.41	992.67	368.26
263	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	11/2008	167.64	408.77	241.13
264	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	255.23	100.19

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(NOVEMBER 2019)

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
265	JAL MARG VIKAS PROJECT	IWAI	01/2018	03/2023	4200	5369.18	1169.18

STEEL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
266	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	15525	23140	7615

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
267	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	13334	24664	11330

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
268	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	02/2014	768.88	1113.34	344.46
269	REDEVELOPMENT OF EAST KIDWAI NAGAR	NBCC	06/2012	11/2019	4264	4439.23	175.23
270	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	5181.79	5687.79	506
271	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	114.26	266	151.74
272	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	14600	19058	4458
273	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	1219.21	2000	780.79
274	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	CPWD	02/2014	05/2017	388	488.28	100.28

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
275	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	10151.04	55548.87	45397.83

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVII

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

(NOVEMBER 2019)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2020	1,2320.00	1,7079.00	4759	48
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	06/2020	1,1459.00	1,6580.00	5121	54
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2021	3492.00	6840.00	3348	133

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	441.33	126.72	21

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
5	RANIGANJ MASTER PLAN	ECL	08/2009	08/2019	08/2024	2661.73	5173.26	2511.53	60
6	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2021	162.76	349.28	186.52	72
7	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	12/2019	5907.11	7080.41	1173.3	48
8	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	459.49	307.06	60
9	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2024	249.03	448.86	199.83	144

HUMAN RESOURCE DEPARTMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
10	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	RITES	09/2013	09/2014	12/2020	484.32	626.26	141.94	75

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
11	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	02/2022	1112.00	1507.24	395.24	32
12	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	02/2021	4497.00	6025.00	1528	26

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

COR -> Cost Overrun

Annexure - XVII

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
13	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	ONGC	02/2017	05/2021	12/2021	4006.83	4475.92	469.09	7
14	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	07/2022	2,0928.00	2,6264.00	5336	24
15	HALDIA LPG IMPORT FACILITY	BPCL	03/2015	10/2018	12/2019	694.00	1097.54	403.54	14
16	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2022	2915.00	4915.00	2000	110
17	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	11/2019	202.94	345.92	142.98	70
18	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	12/2019	861.79	1683.06	821.27	79
19	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	12/2019	2059.63	2665.65	606.02	57
20	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	12/2019	4588.29	5245.96	657.67	16

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
21	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2020	5111.33	6880.36	1769.03	24
22	COMPREHENSIVE SCHEME FOR THE STRENGHTENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	12/2020	4754.42	9072.36	4317.94	24
23	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2022	2491.58	4397.80	1906.22	114
24	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	05/2024	1381.84	1592.34	210.5	56
25	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	06/2021	1,2964.60	1,7304.00	4339.4	37
26	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	02/2017	06/2020	9750.89	1,2176.28	2425.39	40
27	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2021	3919.59	9997.11	6077.52	147
28	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	03/2020	4824.12	5071.94	247.82	89

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

COR -> Cost Overrun

Annexure - XVII

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
29	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	01/2018	03/2020	1,1638.55	1,2865.92	1227.37	26
30	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	03/2022	1,1130.19	1,4719.10	3588.91	103
31	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	12/2019	1364.52	1891.41	526.89	44
32	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	01/2021	2978.48	5867.38	2888.9	94
33	TANDA TPP STAGE-II (2X660 MW)	NTPC	09/2014	07/2019	07/2020	9188.98	1,0016.10	827.12	12
34	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	12/2018	09/2020	1,2532.44	1,3740.53	1208.09	21
35	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	03/2022	1,4366.58	1,5164.05	797.47	33
36	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	09/2020	5353.00	9583.00	4230	98
37	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	12/2019	487.49	639.46	151.97	66
38	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	06/2022	1657.00	5024.35	3367.35	76
39	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	08/2021	8692.97	2,1312.11	12619.1	118
40	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	10/2017	03/2020	1,1846.00	1,2739.82	893.82	29

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
41	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	03/2021	625.00	859.00	234	60
42	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	12/2022	2288.00	4970.11	2682.11	9
43	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	03/2020	644.78	890.00	245.22	36
44	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	03/2025	595.51	769.40	173.89	96

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

COR -> Cost Overrun

Annexure - XVII

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
45	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2022	701.61	810.02	108.41	40
46	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	12/2021	1724.20	1993.24	269.04	9
47	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	03/2030	1027.40	2373.00	1345.6	324
48	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	03/2020	927.01	1200.00	272.99	12
49	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	03/2021	713.48	2300.00	1586.52	12
50	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	03/2021	948.04	1500.00	551.96	12
51	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	06/2022	942.95	1120.00	177.05	39
52	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	09/2022	582.13	1247.64	665.51	6
53	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2022	4454.17	1,2524.00	8069.83	132
54	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2020	385.20	1532.00	1146.8	12
55	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2020	532.87	2145.00	1612.13	12
56	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	10/2021	2326.52	4600.00	2273.48	79
57	DAUSA-GANGAPUR CITY(NL),NWR	NWR	02/1997	02/2019	03/2021	410.08	886.41	476.33	25
58	NANGALDAM-TALWARA(NL),NR	NR	03/1981	07/2012	03/2024	450.00	2200.00	1750	140
59	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	NR	03/1995	11/2002	06/2022	2500.00	2,7949.00	25449	235
60	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2025	3951.98	4724.30	772.32	108
61	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	2733.86	435.44	141
62	MANSI-PURNIA (EXTENSION OF	ECR	04/1996	03/2012	03/2020	477.88	751.55	273.67	96

DOA -> Date of Approval

DOC -> Date of Commissioning

COR -> Cost Overrun

TOR -> Time Overrun

Annexure - XVII

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	MANSI-SAHARSA) GAN ECR								
63	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	03/2025	2913.51	4639.00	1725.49	108
64	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	03/2023	3503.69	3975.22	471.53	12
65	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	03/2022	792.89	1377.48	584.59	12
66	HANSDIHA-GODDA NL	ER	04/2011	03/2020	03/2021	542.18	693.80	151.62	12
67	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	03/2025	499.96	680.68	180.72	157
68	3RD LINE BETWEEN BHUSAWAL-JALGAON	CR	04/2011	03/2019	12/2019	184.06	312.00	127.94	9
69	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	03/2024	1856.95	2200.00	343.05	12
70	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	03/2021	287.00	694.00	407	111
71	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	NFR	04/1983	03/2019	03/2020	297.32	614.00	316.68	12
72	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2023	1045.20	2120.16	1074.96	168
73	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2025	1188.91	1619.48	430.57	72
74	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	03/2024	607.09	1425.44	818.35	133
75	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	03/2020	1185.64	1844.47	658.83	27
76	RAMGANJMUNDI-BHOPAL (NL),WCR	WCR	04/2001	03/2021	03/2023	424.60	2909.99	2485.39	24
77	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	06/2020	133.41	385.00	251.59	135
78	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	06/2024	810.78	1928.07	1117.29	36
79	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-	SR	09/2007	02/2019	02/2020	724.69	2072.50	1347.81	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

COR -> Cost Overrun

Annexure - XVII

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	AGASTIYAMPALLI								
80	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	03/2022	2393.47	5021.45	2627.98	96
81	NADIKUDE-SRI KALAHASTI	SCR	04/2011	03/2021	03/2024	2288.70	2643.25	354.55	36
82	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	RVNL	04/2010	03/2023	03/2024	2127.00	2900.00	773	12
83	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	03/2022	2271.50	3712.50	1441	12
84	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	MRTP	03/1996	03/2004	03/2021	495.44	2980.41	2484.97	204
85	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	8248.50	8000.84	178
86	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	ECR	04/1997	03/2012	03/2020	324.73	1050.00	725.27	96
87	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NFR	04/2000	12/2008	03/2021	1180.19	4541.00	3360.81	147
88	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	06/2024	2923.13	3791.66	868.53	183
89	GONDIA-JABALPUR(GC),(SECR)	SECR	02/1997	04/2020	01/2021	511.86	1756.00	1244.14	9
90	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	09/1995	03/2020	03/2021	303.98	980.00	676.02	12
91	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	03/2021	829.74	1310.23	480.49	12
92	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	03/2022	1503.71	2200.00	696.29	24
93	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	03/2022	1111.99	1539.28	427.29	37
94	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	01/2020	148.77	377.00	228.23	37
95	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	03/2021	1614.59	1870.41	255.82	24
96	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	03/2025	651.00	1009.00	358	120

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

COR -> Cost Overrun

Annexure - XVII

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
97	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	12/2018	06/2020	258.20	358.68	100.48	18
98	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	03/2022	548.00	819.01	271.01	24
99	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	09/2021	569.63	670.00	100.37	18
100	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	03/2019	03/2020	314.00	728.00	414	12
101	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2020	632.68	816.55	183.87	57
102	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	SR	04/2011	03/2019	12/2019	120.70	1800.00	1679.3	9
103	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	03/2025	406.99	545.70	138.71	228
104	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	03/2025	915.98	2137.81	1221.83	36
105	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	01/2020	295.00	477.31	182.31	12
106	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	MRTP	03/2013	03/2016	06/2021	4874.58	8574.97	3700.39	63
107	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	12/2019	06/2020	246.08	348.55	102.47	6
108	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2022	320.66	858.96	538.3	36
109	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	12/2024	2912.96	3845.60	932.64	33
110	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	02/2019	03/2020	242.09	410.00	167.91	13
111	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM	ECR	04/2016	03/2021	03/2022	731.64	1185.73	454.09	12
112	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	12/2020	585.93	1268.32	682.39	22
113	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	06/2021	760.00	1182.31	422.31	15

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

COR -> Cost Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
114	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	03/2022	744.04	1215.54	471.5	12
115	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	03/2023	229.00	852.50	623.5	15
116	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	WR	02/1991	03/2019	03/2020	551.51	809.07	257.56	12

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
117	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MoRTH	08/2010	09/2014	12/2019	186.96	305.61	118.65	63
118	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	03/2021	1288.07	1420.00	131.93	12
119	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	MoRTH	03/2012	05/2012	12/2019	207.03	389.45	182.42	91
120	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	MoRTH	08/2010	10/2010	06/2020	195.04	377.99	182.95	116
121	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	06/2020	1124.11	1232.76	108.65	33
122	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	MoRTH	11/2013	05/2017	05/2020	497.05	881.05	384	36
123	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	03/2020	1108.00	2967.50	1859.5	100
124	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	06/2020	1928.22	2945.00	1016.78	62
125	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	09/2020	531.13	727.00	195.87	28
126	FOUR LANING OF CHANDIGARH - KHARAR	NHAI	10/2015	12/2017	12/2019	447.29	746.43	299.14	24
127	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	NHAI	08/2016	09/2019	03/2020	1388.34	2587.50	1199.16	6
128	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	MoRTH	11/2010	03/2011	12/2019	624.41	992.67	368.26	105
129	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MoRTH	08/2010	10/2010	12/2019	193.69	327.92	134.23	110

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

COR -> Cost Overrun

Annexure - XVII

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

(NOVEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
130	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	07/2018	02/2020	605.84	722.46	116.62	19
131	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	NHAI	09/2016	08/2019	12/2020	950.69	1108.00	157.31	16

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
132	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	07/2020	1,5525.00	2,3140.00	7615	62

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
133	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	05/2020	1,3334.00	2,4664.00	11330	58

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
134	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	03/2020	5181.79	5687.79	506	32
135	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	CPWD	02/2014	05/2017	12/2019	388.00	488.28	100.28	31
136	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	03/2021	1219.21	2000.00	780.79	17

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
137	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	06/2021	1,0151.04	5,5548.87	45397.8	15

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

COR -> Cost Overrun

Details of Ongoing Projects Under -Public Private Partnership Mode

Annexure-XVIII

Costing Rs. 150 Crore and above								(November 2019)
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Antici Pated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	ROAD TRANSPORT AND HIGHWAYS							
	National Highways Authority Of India							
1	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - PPP (BOT) - [N24000208]	07/2012	291.36 -	291.36	01/2014 -	-	.00	0
2	GWALIOR-JHANSI, NH-75 - PPP (ANNUITY) - [N24000089]	12/2003	604.00 -	364.59	12/2009 -	03/2020	-39.64	123
3	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - PPP (ANNUITY) - [N24000176]	05/2010	374.00 -	374.00	05/2013 -	-	.00	0
4	INDORE-DEWAS(NH-3) - PPP (BOT) - [N24000159]	11/2010	325.00 -	475.00	05/2013 -	-	46.15	0
5	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - PPP (ANNUITY) - [N24000177]	09/2011	485.00 -	485.00	08/2013 -	-	.00	0
6	DELHI/ HARYANA BORDER TO ROHTAK - PPP (BOT) - [N24000122]	04/2007	486.00 -	486.00	05/2010 -	03/2020	.00	118
7	TRICHY - KARUR - PPP (BOT) - [N24000528]	03/2007	516.00 -	516.00	07/2008 -	-	.00	0
8	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - PPP (BOT) - [N24000426]	11/2012	530.07 -	530.07	08/2016 -	12/2019	.00	40
9	TIRUPATI - TIRUTHANI - CHENNAI - PPP (BOT) - [N24000178]	04/2011	571.00 -	571.00	10/2013 -	-	.00	0
10	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - PPP (BOT) - [N24000185]	09/2011	574.00 -	574.00	03/2014 -	-	.00	0
11	4-LANNING OF CHAPRA-HAJIPUR - PPP (ANNUITY) - [N24000187]	01/2011	575.00 -	575.00	07/2013 -	03/2020	.00	80
12	2 LANNING OF MUZAFFARPUR - SONBARSA - PPP (ANNUITY) - [N24000188]	05/2011	511.54 -	591.00	11/2013 -	03/2020	15.53	76
13	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - PPP (BOT) - [N24000149]	02/2010	617.00 -	617.00	08/2012 -	12/2019	.00	88
14	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHTH 170 KM) - PPP (ANNUITY) - [N24000213]	04/2012	624.00 -	624.00	04/2014 -	-	.00	0
15	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - PPP (BOT) - [N24000586]	06/2016	637.18 -	637.18	06/2019 -	09/2019	.00	3
16	PATNA-MUZZAFFARPUR - PPP (ANNUITY) - [N24000165]	08/2010	671.30 -	671.30	02/2013 -	03/2020	.00	85

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
17	MUZAFFARNAGAR-HARIDWAR - PPP (BOT) - [N24000201]	09/2011	754.00 -	754.00	03/2013 -	12/2019	.00	81
18	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - PPP (BOT) - [N24000587]	06/2016	763.23 -	763.23	06/2019 -	11/2019	.00	5
19	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - PPP (BOT) - [N24000445]	08/2014	822.90 -	822.90	04/2018 -	-	.00	0
20	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - PPP (BOT) - [N24000454]	06/2014	923.04 -	923.04	11/2016 -	05/2020	.00	42
21	KANDLA - MUNDRA PORT - PPP (BOT) - [N24000175]	01/2011	953.88 -	953.88	07/2013 -	11/2020	.00	88
22	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - PPP (BOT) - [N24000453]	01/2015	972.50 -	972.50	07/2017 -	03/2020	.00	32
23	4-LANING OF BRAHAMPORE-FARAKA - PPP (BOT) - [N24000203]	02/2011	998.79 -	998.79	08/2013 -	03/2021	.00	91
24	BAREILY-SITAPUR (NH-24) - PPP (BOT) - [N24000200]	03/2011	1,046.00 -	1,046.00	09/2013 -	-	.00	0
25	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - PPP (BOT) - [N24000205]	12/2011	1,047.00 -	1,047.00	06/2014 -	03/2019	.00	57
26	4-LANING OF FARAKA-RAIGANJ - PPP (BOT) - [N24000202]	02/2011	1,078.84 -	1,078.84	08/2013 -	05/2020	.00	81
27	SRINAGAR TO BANIHAL - PPP (ANNUITY) - [N24000189]	06/2011	1,100.70 -	1,100.70	06/2014 -	10/2020	.00	76
28	GHAZIABAD-ALIGARH NH-91 - PPP (BOT) - [N24000170]	02/2011	1,141.00 -	1,141.00	08/2013 -	-	.00	0
29	INDORE-JHABUA-GUJRAT/MP - PPP (BOT) - [N24000136]	10/2010	1,175.00 -	1,175.00	04/2013 -	-	.00	0
30	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - PPP (BOT) - [N24000172]	09/2011	1,250.00 -	1,250.00	12/2013 -	06/2020	.00	78
31	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - PPP (BOT) - [N24000230]	05/2013	1,348.20 -	1,348.20	02/2014 -	-	.00	0
32	FOUR LANING OF HOSPET - CHITRADURGA - PPP (BOT) - [N24000490]	03/2015	1,388.00 -	1,388.00	08/2018 -	03/2020	.00	19
33	6-LANING OF DHANKUNI-KHARAGPUR SECTION - PPP (BOT) - [N24000206]	04/2012	1,396.18 -	1,396.18	09/2014 -	03/2020	.00	66
34	PANIKHOLI-RIMOLI - PPP (BOT) - [N24000197]	03/2012	1,410.00 -	1,410.00	09/2014 -	-	.00	0
35	RANCHI-RARGA-JAMSETHPUR - PPP (ANNUITY) - [N24000215]	12/2012	1,479.00 -	1,479.00	06/2015 -	-	.00	0
36	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - PPP (BOT) - [N24000125]	03/2010	1,509.10 -	1,509.10	09/2012 -	12/2019	.00	87

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
37	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - PPP (BOT) - [N24000183]	11/2011	1,535.00 -	1,535.00	05/2014 -	12/2019	.00	67
38	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - PPP (BOT) - [N24000233]	04/2014	1,266.60 -	1,544.00	09/2016 -	09/2019	21.90	36
39	ETAWAH CHAKERI - PPP (BOT) - [N24000219]	03/2013	1,573.00 -	1,573.00	09/2015 -	-	.00	0
40	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - PPP (BOT) - [N24000505]	06/2015	1,583.79 -	1,583.79	01/2019 -	10/2019	.00	9
41	FOUR LANING OF GWALIOR-SHIVPURI - PPP (BOT) - [N24000494]	05/2013	1,055.00 -	1,601.77	11/2015 -	-	51.83	0
42	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - PPP (BOT) - [N24000462]	05/2014	1,655.01 -	1,655.01	08/2016 -	12/2020	.00	52
43	6 LANING OF AGRA - ETAWAH BYPASS - PPP (BOT) - [N24000452]	07/2015	1,657.20 -	1,657.20	01/2019 -	-	.00	0
44	SIX-LANING OF BARWA ADDA-PANAGARH - PPP (BOT) - [N24000515]	04/2014	1,665.00 -	1,665.00	- -	06/2019	.00	0
45	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - PPP (BOT) - [N24000477]	02/2008	1,673.70 -	1,673.70	10/2011 -	-	.00	0
46	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - PPP (BOT) - [N24000131]	02/2009	1,693.75 -	1,693.75	08/2011 -	-	.00	0
47	PUNE-SATARA(NH-4) - PPP (BOT) - [N24000156]	10/2010	1,724.55 -	1,724.55	03/2013 -	12/2019	.00	81
48	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - PPP (ANNUITY) - [N24000163]	07/2010	1,813.76 -	1,813.76	07/2013 -	-	.00	0
49	FOUR LANING OF AURANGABAD - YEDISHI - PPP (BOT) - [N24000508]	07/2015	1,871.34 -	1,871.34	01/2018 -	12/2019	.00	23
50	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - PPP (BOT) - [N24000232]	11/2013	1,916.79 -	1,916.79	11/2016 -	-	.00	0
51	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - PPP (ANNUITY) - [N24000161]	07/2010	1,987.00 -	1,987.00	07/2015 -	09/2020	.00	62
52	AHMEDABAD TO VADODARA SECTION - PPP (BOT) - [N24000222]	01/2013	2,125.24 -	2,125.24	12/2015 -	-	.00	0
53	8 LANING OF MUKARBA CHOWK TO PANIPAT - PPP (BOT) - [N24000449]	07/2015	2,128.72 -	2,128.72	04/2019 -	-	.00	0
54	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH – 14 - PPP BOT (Hybrid Annuity) - [N24001185]	11/2017	2,159.00 -	2,159.00	01/2019 -	-	.00	0
55	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - PPP (BOT) - [N24000425]	07/2015	2,288.18 -	2,288.18	05/2019 -	-	.00	0
56	4 LANING OF NAGPUR-BETUL - PPP (ANNUITY) - [N24000155]	02/2011	2,498.76 -	2,498.76	08/2014 -	-	.00	0
57	NASHRI- CHANANI - PPP (ANNUITY) - [N24000162]	05/2011	2,159.00 -	2,519.00	06/2015 -	-	16.67	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above (November 2019)

Sl.No	Project	Date of Approval (Month/ Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Date of Commissioning (Month/Year) Original / Revised	Date of Commissioning (Month/Year) Antici Pated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
58	VARANASI-AURANGABAD KM.786 TO KM.978.40 - PPP (BOT) - [N24000182]	09/2011	2,848.00 -	2,848.00	03/2014 -	06/2020	.00	75
59	DELHI AGRA APPROVED LENGTH 180.0 KM - PPP (BOT) - [N24000224]	10/2012	1,928.22 -	2,945.00	04/2015 -	06/2020	52.73	62
60	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - PPP (BOT) - [N24000133]	05/2009	1,108.00 -	2,967.50	11/2011 -	03/2020	167.82	100
	Total		74,864.42 -	78,914.92				
	Grand Total		74,864.42	78,914.92				

State-Wise Central Sector Ongoing Project List

Annexure-XIX

Details of Central Sector Projects Costing Rs.150 crore and above (as on 30.11.2019)					
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	A & N ISLANDS				
	Civil Aviation				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	9/2018 (-) [6/2020]	314.61 (-) [441.33]	85.79 (126.72) [21]
	Road Transport And Highways				
2	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N	3/2017	12/2017 (-) [0/0]	409.85 (-) [409.85]	21.11 (0.00) [0]
3	AJANTHA TO BULDHANA	2/2017	7/2019 (-) [7/2019]	401.00 (401.00) [401.00]	107.81 (0.00) [0]
4	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C	3/2015	4/2017 (-) [0/0]	277.17 (-) [277.17]	158.36 (0.00) [0]
5	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (	3/2015	10/2018 (-) [0/0]	262.97 (-) [262.97]	0.00 (0.00) [0]
6	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (-) [11/2019]	257.34 (-) [238.00]	41.09 (-19.34) [0]
7	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM	2/2018	10/2018 (-) [0/0]	391.00 (-) [391.00]	22.17 (0.00) [0]
8	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O	3/2018	10/2018 (-) [0/0]	234.27 (-) [234.27]	11.03 (0.00) [0]
9	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00	11/2017	11/2019 (-) [11/2019]	237.80 (-) [238.00]	7.48 (0.20) [0]
	ANDHRA PRADESH				
	Health And Family Welfare				
10	HOSPITAL AND TEACHING- AIIMS GUNTUR	3/2018	/ (-) [7/2020]	601.02 (-) [601.02]	169.38 (0.00) [-]
11	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH	8/2017	3/2019 (-) [3/2020]	272.19 (-) [272.54]	191.86 (0.35) [12]
	Information And Broadcasting				
12	FILM AND TELEVISION INSTITUTE ARUNACHAL PRADESH	11/2016	2/2019 (-) [11/2019]	204.32 (-) [204.32]	0.00 (0.00) [9]
	Petroleum				

13	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE	1/2015	3/2021 (-) [3/2021]	342.00 (-) [342.00]	0.00 (0.00) [0]
14	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH	8/2018	4/2021 (-) [7/2021]	466.00 (-) [466.00]	96.28 (0.00) [3]
15	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP	8/2017	4/2021 (-) [9/2020]	384.58 (-) [384.58]	105.36 (0.00) [-7]
16	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT	7/2017	2/2021 (-) [2/2021]	580.20 (-) [580.20]	47.41 (0.00) [0]
17	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	3/2016	6/2020 (-) [8/2021]	34,012.00 (-) [34,012.00]	4,204.96 (0.00) [14]
18	REVAMPING OF FACILITIES AT VIZAG TERMINAL	4/2018	4/2022 (-) [2/2023]	355.00 (-) [355.00]	14.89 (0.00) [10]
19	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM	7/2014	3/2021 (-) [3/2021]	247.00 (-) [247.00]	0.00 (0.00) [0]
20	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP	10/2018	10/2021 (-) [10/2021]	316.20 (-) [316.20]	14.78 (0.00) [0]
21	VISAKH REFINERY MODERNISATION PROJECT	7/2016	7/2020 (7/2022) [7/2022]	20,928.00 (26,264.00) [26,264.00]	7,245.30 (5,336.00) [24]
	Railways				
22	CUMBUM-PRODDATUR	4/2013	/ (-) [0/0]	829.00 (829.00) [829.00]	0.94 (0.00) [0]
23	DUVVADA-VIJAYAWADA	4/2015	/ (-) [0/0]	3,873.07 (3,873.07) [3,873.07]	0.38 (0.00) [0]
24	GUDUR-DURGARAJAPATNAM	4/2011	/ (-) [0/0]	761.37 (761.37) [761.37]	0.52 (0.00) [0]
25	GUNTUR-GUNTAKAL	4/2016	3/2022 (-) [3/2023]	3,631.00 (3,631.00) [3,631.00]	617.19 (0.00) [12]
26	KOTLPALLI-NARASAPUR (NL) (SCR)	12/2001	3/2009 (-) [3/2023]	1,045.20 (2,120.16) [2,120.16]	524.57 (1,074.96) [168]
27	KOTTAVALSA - KORAPUT DOUBLING	4/2015	3/2022 (-) [3/2022]	2,499.71 (2,499.71) [3,382.95]	397.90 (883.24) [0]
28	MULTI MODAL LOGISTICS PARK AT KAKINADA	8/2016	3/2019 (-) [12/2020]	234.50 (-) [235.00]	10.88 (0.50) [21]
29	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM	1/2013	3/2018 (-) [0/0]	387.70 (-) [387.70]	323.91 (0.00) [0]
30	NADIKUDE-SRI KALAHASTI	4/2011	3/2021 (-) [3/2024]	2,288.70 (2,643.25) [2,643.25]	810.35 (354.55) [36]
31	NANDYAL-YERRAGUNTLA(NL),SCR	3/1996	2/2009 (-) [0/0]	164.36 (-) [1,050.00]	999.64 (885.64) [0]
32	VIJAYAWADA-GUDUR	4/2015	12/2023 (-) [12/2023]	3,246.26 (-) [3,548.67]	1,211.97 (302.41) [0]

33	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	3/2012	3/2020 (-) [3/2022]	1,503.71 (-) [2,200.00]	1,722.18 (696.29) [24]
	Road Transport And Highways				
34	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM	12/2017	/ (-) [11/2019]	328.67 (-) [328.67]	176.29 (0.00) [-]
35	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O	12/2017	/ (-) [0/0]	357.00 (-) [357.00]	70.71 (0.00) [0]
36	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415	3/2018	/ (-) [3/2020]	557.30 (-) [557.30]	208.96 (0.00) [-]
37	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216	1/2017	9/2017 (12/2020) [12/2020]	263.45 (-) [263.45]	59.79 (0.00) [39]
38	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V	2/2017	11/2017 (3/2020) [11/2019]	429.43 (-) [429.43]	209.09 (0.00) [24]
39	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1	3/2018	/ (-) [12/2020]	314.43 (-) [314.43]	24.90 (0.00) [-]
40	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD	8/2016	1/2017 (4/2020) [4/2020]	350.61 (-) [350.61]	310.25 (0.00) [39]
41	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C	10/2015	11/2015 (-) [0/0]	333.21 (-) [353.89]	256.11 (20.68) [0]
42	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C	7/2015	12/2015 (-) [0/0]	333.21 (333.21) [333.21]	256.11 (0.00) [0]
43	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0)	7/2015	12/2015 (-) [0/0]	333.21 (-) [333.21]	256.11 (0.00) [0]
44	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12	10/2015	12/2015 (1/2020) [12/2020]	333.21 (-) [355.89]	265.48 (22.68) [60]
45	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	3/2018	3/2021 (-) [4/2021]	1,532.62 (2,499.00) [2,499.00]	584.50 (966.38) [1]
46	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40)	6/2017	6/2017 (-) [7/2020]	648.33 (-) [306.00]	152.56 (-342.33) [37]
47	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800)	1/2016	11/2018 (-) [0/0]	1,134.97 (-) [1,134.97]	783.67 (0.00) [0]
48	REHABILITAITON AND UPGRADATION OF REPALLE TO EEPPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH	1/2017	1/2018 (12/2020) [1/2020]	576.48 (-) [576.48]	228.31 (0.00) [24]
49	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT	1/2016	8/2016 (3/2020) [3/2020]	348.95 (-) [348.95]	161.26 (0.00) [43]
50	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S	7/2014	2/2015 (-) [0/0]	251.55 (-) [251.55]	7.74 (0.00) [0]
51	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21	1/2016	5/2016 (12/2019) [12/2019]	386.09 (-) [386.09]	183.00 (0.00) [43]
52	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69	11/2016	5/2017 (3/2020) [3/2020]	290.15 (-) [290.15]	70.35 (0.00) [34]

53	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T	1/2014	11/2014 (-) [0/0]	195.45 (-) [195.45]	0.00 (0.00) [0]
54	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS	3/2018	/ (-) [2/2021]	565.09 (-) [565.09]	167.77 (0.00) [-]
55	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O	3/2016	5/2016 (7/2020) [7/2020]	995.09 (995.00) [995.09]	410.28 (0.00) [50]
56	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216	3/2016	9/2016 (3/2020) [3/2020]	444.84 (-) [444.84]	251.28 (0.00) [42]
57	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2	11/2016	8/2017 (2/2020) [2/2020]	376.25 (-) [376.25]	201.42 (0.00) [30]
58	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (	3/2018	7/2018 (1/2020) [1/2020]	297.12 (294.00) [294.12]	291.57 (-3.00) [18]
59	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG	3/2018	8/2018 (2/2020) [2/2020]	289.67 (290.00) [289.67]	103.90 (0.00) [18]
60	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA	3/2018	11/2018 (5/2020) [5/2020]	504.19 (504.00) [504.19]	226.14 (0.00) [18]
61	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	3/2015	10/2015 (1/2020) [1/2020]	271.45 (-) [271.45]	159.15 (0.00) [51]
62	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD	1/2017	8/2017 (3/2020) [3/2020]	319.28 (-) [319.28]	108.34 (0.00) [31]
63	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER	3/2017	3/2020 (-) [3/2020]	648.32 (-) [512.72]	501.52 (-135.60) [0]
64	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU	3/2018	8/2018 (2/2020) [2/2020]	244.95 (245.00) [244.95]	126.99 (0.00) [18]
65	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU	9/2016	2/2017 (12/2019) [12/2019]	372.68 (-) [372.68]	185.04 (0.00) [34]
66	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3	3/2018	8/2018 (3/2020) [3/2020]	228.32 (-) [228.32]	47.96 (0.00) [19]
67	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P	1/2018	8/2018 (8/2020) [8/2020]	418.03 (-) [418.03]	170.05 (0.00) [24]
68	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO	11/2016	1/2018 (1/2020) [1/2020]	378.24 (-) [378.24]	287.63 (0.00) [24]
69	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM	2/2018	/ (-) [7/2021]	1,959.00 (-) [1,959.00]	657.85 (0.00) [-]
70	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN	12/2017	/ (-) [7/2021]	1,323.15 (-) [1,323.15]	403.93 (0.00) [-]
71	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG	3/2018	/ (-) [7/2021]	1,550.98 (-) [1,550.98]	673.04 (0.00) [-]
72	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	11/2011	5/2014 (12/2019) [12/2019]	1,535.00 (-) [1,535.00]	3,225.15 (0.00) [67]
73	SIX LANNING OF RANASTALAM-ANANDAPURAM	3/2017	3/2020	1,041.62	807.76

	SECTION OF NH-16 FROM KM 634.000 TO KM 681.000		(-) [5/2020]	(-) [1,187.10]	(145.48) [2]
74	TIRUPATI - TIRUTHANI - CHENNAI	4/2011	10/2013 (-) [0/0]	571.00 (-) [571.00]	582.53 (0.00) [0]
75	VIJAYAWADA-GUNDUGOLANU SECTION	9/2014	2/2017 (-) [0/0]	1,684.00 (-) [1,684.00]	54.13 (0.00) [0]
	Steel				
76	CENTRAL DISPATCH YARD	8/2015	8/2018 (12/2019) [12/2019]	320.66 (-) [320.66]	253.54 (0.00) [16]
77	COKE OVEN BATTERY-5	12/2011	12/2017 (12/2019) [12/2019]	2,858.00 (-) [2,500.00]	1,482.76 (-358.00) [24]
	Urban Development				
78	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P.	2/2019	9/2020 (-) [9/2020]	186.00 (199.00) [186.00]	0.00 (0.00) [0]
79	CONSTRACTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP	1/2018	3/2019 (-) [0/0]	206.58 (-) [206.58]	177.73 (0.00) [0]
80	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA	7/2014	/ (-) [0/0]	232.00 (-) [232.00]	0.00 (0.00) [0]
81	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD	6/2014	3/2017 (-) [0/0]	157.84 (-) [169.16]	163.98 (11.32) [0]
82	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	8/2007	/ (-) [0/0]	246.90 (-) [246.90]	0.00 (0.00) [0]
	Water Resources				
83	POLAVARAM IRRIGATION PROJECT	2/2009	3/2020 (-) [6/2021]	10,151.04 (-) [55,548.87]	16,417.99 (45,397.83) [15]
	ARUNACHAL PRADESH				
	Power				
84	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009 (10/2019) [10/2019]	2,496.90 (7,927.34) [7,927.34]	7,599.10 (5,430.44) [0]
85	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (-) [0/0]	6,285.33 (-) [19,496.34]	11,098.20 (13,211.01) [0]
	Road Transport And Highways				
86	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN	3/2015	/ (-) [0/0]	172.75 (-) [172.75]	118.30 (0.00) [0]
87	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [3/2020]	394.00 (-) [394.00]	272.92 (0.00) [21]
88	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59	3/2015	5/2018 (-) [8/2019]	194.11 (-) [194.11]	181.03 (0.00) [0]
89	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS	10/2015	1/2019 (-) [0/0]	179.82 (-) [179.82]	197.77 (0.00) [0]
90	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX	10/2015	/ (1/2016) [1/2019]	210.50 (210.50) [210.50]	120.60 (0.00) [0]
91	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE	1/2016	11/2016 (-)	183.65 (-)	107.04 (0.00)

	FROMKM.583.450		[0/0]	[183.65]	[0]
92	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST	11/2016	/ (-) [9/2020]	243.89 (-) [243.89]	121.47 (0.00) [-]
93	BORDUMSA NAMCHIK (BURIDEHING - JAIRAMPUR) ROAD ON NH-52B (NEW NH-215) FROM KM. 0.15 (STARTING CHAIN	7/2015	/ (-) [0/0]	189.91 (-) [189.91]	154.43 (0.00) [0]
94	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM	5/2016	/ (-) [0/0]	259.52 (-) [259.52]	184.51 (0.00) [0]
95	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120.	12/2016	/ (-) [0/0]	200.44 (-) [200.44]	75.98 (0.00) [0]
96	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50	9/2016	/ (-) [0/0]	568.92 (-) [568.92]	134.41 (0.00) [0]
97	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5	12/2016	/ (-) [0/0]	188.78 (-) [188.78]	38.37 (0.00) [0]
98	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	12/2016	1/2017 (-) [1/2020]	138.93 (155.00) [155.00]	75.99 (16.07) [36]
99	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/ (-) [9/2020]	245.79 (-) [245.79]	105.26 (0.00) [-]
100	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	4/2016	10/2016 (-) [10/2019]	198.00 (-) [198.00]	184.62 (0.00) [0]
101	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	7/2015	10/2018 (9/2015) [9/2018]	197.16 (197.16) [197.16]	75.57 (0.00) [0]
102	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF	3/2017	/ (-) [0/0]	1,718.59 (-) [1,718.59]	158.90 (0.00) [0]
103	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	1/2017	3/2017 (-) [3/2022]	1,253.10 (-) [1,253.10]	158.90 (0.00) [60]
104	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	4/2017 (2/2018) [2/2021]	167.28 (167.28) [167.28]	19.83 (0.00) [46]
105	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS	2/2017	4/2017 (2/2018) [2/2021]	216.71 (216.71) [216.71]	19.67 (0.00) [46]
106	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/ (-) [0/0]	392.60 (-) [392.60]	0.00 (0.00) [0]
107	FUNDED)CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH	11/2015	/ (-) [12/2020]	434.06 (-) [434.06]	133.38 (0.00) [-]
108	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017 (3/2018) [3/2021]	284.09 (284.09) [284.09]	77.42 (0.00) [47]
109	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017 (-) [0/0]	195.23 (-) [195.23]	49.25 (0.00) [0]
110	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017 (-) [0/0]	203.36 (-) [203.36]	62.53 (0.00) [0]
111	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	194.66 (-) [194.66]	83.66 (0.00) [0]

112	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	198.22 (-) [198.22]	83.66 (0.00) [0]
113	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	3/2012	5/2012 (5/2015) [12/2019]	207.03 (389.45) [389.45]	291.55 (182.42) [91]
114	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	4/2017 (2/2018) [2/2021]	180.57 (180.57) [180.57]	14.27 (0.00) [46]
115	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS	2/2017	4/2017 (2/2018) [2/2021]	168.32 (168.32) [168.32]	34.87 (0.00) [46]
116	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	2/2012 (-) [0/0]	156.63 (276.00) [276.00]	147.65 (119.37) [0]
117	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P	11/2010	3/2011 (-) [0/0]	305.49 (-) [305.49]	131.08 (0.00) [0]
118	TWO-LANING OF HAYULIANG– HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI	1/2017	/ (-) [0/0]	256.66 (-) [256.66]	24.14 (0.00) [0]
119	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0	2/2017	/ (4/2019) [4/2022]	175.06 (175.06) [175.06]	14.08 (0.00) [-]
120	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1	2/2017	/ (4/2019) [4/2022]	176.12 (176.12) [176.12]	14.79 (0.00) [-]
121	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D	2/2017	/ (2/2018) [2/2021]	199.02 (199.02) [199.02]	11.87 (0.00) [-]
122	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D	2/2017	/ (2/2018) [2/2021]	184.88 (184.88) [184.88]	97.50 (0.00) [-]
123	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU	9/2011	/ (3/2020) [0/0]	1,979.00 (-) [1,979.00]	1,143.00 (0.00) [0]
	ASSAM				
	Civil Aviation				
124	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	3/2021 (-) [3/2021]	859.86 (-) [860.00]	232.44 (0.14) [0]
	Health And Family Welfare				
125	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (10/2021) [10/2021]	875.00 (-) [747.80]	110.70 (-127.20) [5]
	Petroleum				
126	ASSAM RENEWAL PROJECT FOR GROUP A	3/2009	3/2013 (12/2019) [12/2019]	2,465.15 (-) [2,378.86]	2,147.00 (-86.29) [81]
127	BS VI PROJECT AT GUWAHATI REFINERY	8/2018	2/2020 (-) [6/2020]	557.00 (-) [557.00]	249.46 (0.00) [4]
128	BS-VI PROJECT AT BONGAIGAON REFINERY	5/2018	9/2019 (-) [4/2020]	1,222.00 (-) [1,222.00]	606.24 (0.00) [7]
129	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN	6/2016	8/2020 (-) [8/2020]	224.75 (-) [224.75]	69.99 (0.00) [0]
130	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	7/2011	1/2019 (-) [0/0]	350.00 (-) [350.00]	2.06 (0.00) [0]

131	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	6/2010	1/2014 (-) [11/2019]	202.94 (345.92) [345.92]	155.61 (142.98) [70]
132	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	6/2016	8/2019 (-) [12/2020]	423.00 (-) [423.00]	282.50 (0.00) [16]
133	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (6/2020) [6/2020]	543.91 (-) [682.90]	71.46 (138.99) [4]
134	INDMAX PROJECT AT BONGAIGAON REFINERY	2/2016	11/2019 (-) [2/2020]	2,582.00 (-) [2,582.00]	1,613.96 (0.00) [3]
135	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020 (-) [5/2020]	249.85 (265.49) [265.49]	180.20 (15.64) [0]
136	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	9/2012	3/2015 (-) [0/0]	871.35 (-) [1,200.00]	565.63 (328.65) [0]
	Railways				
137	AMBARI FALAKATA TO NEW MAYNAGURI	4/2011	3/2019 (-) [3/2020]	314.00 (728.00) [728.00]	727.55 (414.00) [12]
138	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2020]	2,232.32 (-) [2,182.00]	756.32 (-50.32) [-24]
139	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-) [3/2021]	870.96 (-) [2,136.01]	580.01 (1,265.05) [0]
140	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2020]	385.20 (1,532.00) [1,532.00]	642.09 (1,146.80) [12]
	Road Transport And Highways				
141	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (-) [0/0]	268.08 (-) [268.08]	203.15 (0.00) [0]
142	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	11/2010	2/2011 (-) [0/0]	470.20 (-) [630.36]	344.32 (160.16) [0]
143	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS	12/2015	12/2018 (-) [0/0]	225.02 (-) [159.20]	26.00 (-65.82) [0]
144	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	12/2015	6/2018 (-) [0/0]	223.30 (-) [223.30]	73.39 (0.00) [0]
145	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [0/0]	520.01 (-) [520.01]	50.38 (0.00) [0]
146	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [0/0]	588.95 (-) [588.95]	382.22 (0.00) [0]
147	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [0/0]	289.99 (-) [289.99]	13.26 (0.00) [0]
148	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (12/2021) [12/2021]	252.00 (-) [252.00]	4.74 (0.00) [71]
149	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (12/2020) [12/2021]	437.39 (-) [437.39]	9.30 (0.00) [42]
150	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700)	1/2016	1/2016 (2/2019)	294.17 (-)	63.00 (0.00)

	O		[4/2021]	[294.17]	[63]
151	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	4/2010 (-) [7/2019]	217.61 (-) [360.84]	453.70 (143.23) [0]
152	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM	11/2010	2/2014 (-) [12/2019]	197.37 (-) [197.37]	88.86 (0.00) [70]
153	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	5/2008 (-) [6/2019]	160.00 (-) [167.98]	223.81 (7.98) [0]
154	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52	6/2016	1/2019 (-) [0/0]	829.00 (-) [829.00]	304.25 (0.00) [0]
155	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [0/0]	168.39 (-) [168.39]	73.37 (0.00) [0]
156	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE	10/2017	/ (-) [6/2020]	818.00 (-) [818.00]	62.91 (0.00) [-]
157	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (1/2021) [12/2021]	463.49 (-) [463.49]	22.32 (0.00) [42]
158	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [0/0]	829.00 (-) [829.00]	304.27 (0.00) [0]
159	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (5/2020) [12/2020]	454.89 (-) [454.89]	123.20 (0.00) [31]
160	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (7/2019) [7/2019]	280.00 (490.00) [525.00]	492.41 (245.00) [0]
161	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (10/2018) [10/2018]	196.00 (655.17) [655.17]	655.17 (459.17) [0]
162	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (1/2011) [8/2013]	155.04 (255.23) [255.23]	251.39 (100.19) [0]
163	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (3/2011) [8/2019]	199.81 (340.14) [340.14]	319.96 (140.33) [0]
164	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (7/2011) [1/2014]	167.64 (408.77) [408.77]	395.78 (241.13) [0]
165	NALBARI T BIJNI (AS-7)	12/2003	4/2008 (-) [3/2020]	208.00 (-) [230.00]	339.22 (22.00) [143]
166	NALBARI TO BIJNI (AS-6)	12/2003	6/2008 (-) [9/2019]	225.00 (-) [225.00]	328.47 (0.00) [0]
167	OUR LANNNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST	3/2017	/ (-) [0/0]	1,049.51 (-) [1,049.51]	89.16 (0.00) [0]
168	SONAPUR TO GUWAHTI (AS-3)	12/2003	3/2008 (-) [8/2020]	245.00 (-) [174.34]	225.34 (-70.66) [149]
169	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ	11/2014	2/2018 (-) [0/0]	218.31 (-) [307.47]	263.85 (89.16) [0]
170	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN	9/2018	9/2021 (-) [9/2021]	160.00 (-) [160.00]	0.50 (0.00) [0]

	BIHAR				
	Civil Aviation				
171	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II	5/2018	10/2022 (-) [10/2022]	539.20 (-) [539.20]	25.64 (0.00) [0]
	Petroleum				
172	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL	5/2016	12/2020 (-) [2/2020]	664.00 (-) [729.40]	663.70 (65.40) [-10]
173	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA	10/2017	10/2022 (-) [10/2022]	359.25 (-) [359.25]	75.57 (0.00) [0]
174	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR	4/2018	3/2021 (-) [3/2021]	522.00 (-) [522.00]	158.65 (0.00) [0]
175	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY	12/2017	10/2020 (-) [10/2020]	199.36 (-) [199.36]	9.39 (0.00) [0]
176	FUEL QUALITY UPGRADATION (NSU,NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY	6/2017	10/2019 (-) [5/2020]	951.64 (-) [951.64]	490.98 (0.00) [7]
177	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY	7/2018	1/2021 (-) [1/2021]	189.00 (-) [189.00]	23.10 (0.00) [0]
178	LPG BP PROJECT MOTIHARI	5/2018	3/2021 (-) [3/2021]	206.50 (-) [206.50]	21.62 (0.00) [0]
179	MOTIHARI AMLEKHGANJ PIPELINE	9/2015	6/2020 (-) [3/2020]	324.00 (-) [324.00]	192.32 (0.00) [-3]
	Power				
180	BARH STPP(3X660MW) NTPC	2/2005	10/2011 (8/2021) [8/2021]	8,692.97 (21,312.11) [21,312.11]	16,756.64 (12,619.14) [118]
181	BRBCL-NABINAGAR TPP- JV (4X250 MW)	1/2007	7/2012 (-) [9/2020]	5,353.00 (7,998.00) [9,583.00]	7,981.46 (4,230.00) [98]
182	BUXAR THERMAL POWER PLANT (1320 MW)	3/2019	1/2024 (-) [1/2024]	10,439.09 (10,439.09) [10,439.09]	836.81 (0.00) [0]
183	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	1/2013	5/2018 (12/2021) [6/2021]	12,964.60 (17,304.00) [17,304.00]	14,229.00 (4,339.40) [37]
	Railways				
184	ARA-BHABHUA ROAD (NL)	4/2008	/ (-) [0/0]	633.87 (-) [633.87]	0.40 (0.00) [0]
185	ARARIA-SUPAUL (NL)	4/2008	/ (3/2023) [3/2023]	1,605.17 (1,605.17) [1,605.17]	23.49 (0.00) [-]
186	BIHTA-AURANGABAD (NL)	4/2008	/ (-) [3/2024]	326.20 (-) [2,995.01]	1.94 (2,668.81) [-]
187	CHHAPRA-MUZAFFARPUR (NL)	4/2006	/ (-) [3/2022]	378.56 (-) [1,858.75]	377.77 (1,480.19) [-]
188	DANIAWAN-BIHARSARIF (NL), ECR	4/2001	/ (-) [0/0]	406.92 (-) [339.00]	200.00 (-67.92) [0]
189	DARBANGHA-KUSHESHWARSTHAN (NL)	4/2005	/ (-)	205.00 (-)	5.21 (0.00)

			[0/0]	[205.00]	[0]
190	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	4/1991	/ (-) [12/2021]	329.39 (803.11) [1,483.14]	1,053.89 (1,153.75) [-]
191	GAYA-DALTONGANJ VIA RAFIGANJ (NL)	4/2008	/ (-) [0/0]	445.25 (-) [445.25]	1.15 (0.00) [0]
192	HAJIPUR-RAMDAYALUNAGAR DOUBLING	4/2013	/ (-) [1/2020]	213.01 (367.17) [425.17]	423.55 (212.16) [-]
193	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	4/2003	/ (-) [3/2023]	528.65 (2,066.78) [2,066.78]	1,441.80 (1,538.13) [-]
194	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	4/1997	3/2012 (-) [3/2020]	324.73 (898.53) [1,050.00]	1,043.03 (725.27) [96]
195	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	4/2009	3/2020 (-) [3/2022]	548.00 (819.01) [819.01]	489.11 (271.01) [24]
196	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	4/1997	/ (-) [3/2022]	162.87 (614.45) [614.45]	309.76 (451.58) [-]
197	KISHANGANJ JALALGARH, NL, NEFR	4/2008	/ (3/2022) [3/2022]	333.76 (-) [360.00]	6.74 (26.24) [-]
198	KIUL - GAYA DOUBLING PROJECT	12/2015	3/2020 (-) [10/2021]	1,200.20 (1,200.20) [1,200.20]	397.15 (0.00) [19]
199	KOSI BRIDGE (NL), ECR	4/2002	3/2020 (-) [3/2020]	499.41 (516.02) [516.02]	402.55 (16.61) [0]
200	KURSELA-BIHARIGANJ (NL)	4/2008	/ (-) [0/0]	192.56 (-) [192.56]	0.39 (0.00) [0]
201	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	4/1996	3/2012 (-) [3/2020]	477.88 (751.55) [751.55]	674.58 (273.67) [96]
202	MOTIHARI-SITAMARHI (NL)	4/2006	/ (-) [0/0]	211.00 (-) [1,006.00]	24.16 (795.00) [0]
203	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM	4/2016	3/2021 (-) [3/2022]	731.64 (1,185.73) [1,185.73]	35.74 (454.09) [12]
204	MUZAFFARPUR-DARBANGHA (NL)	4/2008	/ (-) [0/0]	281.30 (-) [281.30]	0.60 (0.00) [0]
205	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL)	4/2008	/ (-) [3/2024]	228.05 (-) [228.05]	1.53 (0.00) [-]
206	MUZAFFARPUR-SITAMARHI NEW LINE	1/1991	7/2014 (-) [0/0]	332.15 (546.71) [546.71]	541.43 (214.56) [0]
207	NAWADA-LAXMIPUR (NL)	4/2008	/ (-) [0/0]	620.57 (-) [620.57]	0.32 (0.00) [0]
208	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	9/2006	3/2019 (-) [3/2020]	532.87 (2,145.00) [2,145.00]	935.60 (1,612.13) [12]
209	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR	4/1998	/ (-) [10/2019]	180.82 (726.31) [726.31]	510.91 (545.49) [0]

210	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	12/2015	3/2020 (-) [12/2022]	1,491.47 (-) [1,491.47]	443.64 (0.00) [33]
211	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM	4/2016	3/2021 (-) [3/2022]	744.04 (1,215.54) [1,215.54]	79.18 (471.50) [12]
212	SAKRI-HASANPUR ROAD (NL)	4/1999	/ (-) [3/2021]	325.00 (735.20) [735.20]	363.83 (410.20) [-]
213	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	4/2004	/ (-) [3/2021]	372.14 (1,470.50) [1,470.50]	824.49 (1,098.36) [-]
214	SAMASTIPUR-DARBANGHA	5/2015	/ (-) [2/2023]	380.00 (519.33) [519.33]	164.77 (139.33) [-]
215	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	4/2008	/ (-) [0/0]	678.62 (-) [678.62]	17.20 (0.00) [0]
	Road Transport And Highways				
216	2 LANNING OF MUZAFFARPUR - SONBARSA	5/2011	11/2013 (12/2019) [3/2020]	511.54 (585.00) [591.00]	571.22 (79.46) [76]
217	2-LANNING WITH PS MOTIHARI-RAXAUL	10/2011	4/2014 (-) [0/0]	375.09 (-) [375.09]	494.33 (0.00) [0]
218	4-LANNING OF CHAPRA-HAJIPUR	1/2011	7/2013 (-) [3/2020]	575.00 (-) [575.00]	850.24 (0.00) [80]
219	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ	5/2015	5/2017 (4/2019) [4/2019]	581.84 (-) [581.84]	89.69 (0.00) [0]
220	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00	2/2019	/ (-) [0/0]	2,926.42 (-) [2,926.42]	0.00 (0.00) [0]
221	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND	9/2018	/ (-) [0/0]	1,478.40 (-) [1,478.40]	0.00 (0.00) [0]
222	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE	8/2015	11/2015 (-) [0/0]	288.24 (-) [288.24]	286.46 (0.00) [0]
223	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15	12/2017	/ (-) [0/0]	2,598.00 (-) [2,598.00]	0.00 (0.00) [0]
224	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE	3/2017	3/2020 (-) [5/2021]	235.48 (-) [227.77]	11.00 (-7.71) [14]
225	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER	3/2018	/ (-) [0/0]	496.20 (-) [496.20]	0.00 (0.00) [0]
226	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	11/2013	7/2016 (-) [0/0]	683.83 (-) [560.70]	597.00 (-123.13) [0]
227	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	6/2016 (-) [0/0]	369.77 (-) [369.77]	0.00 (0.00) [0]
228	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016 (-) [0/0]	553.30 (-) [478.35]	289.14 (-74.95) [0]
229	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016 (-) [0/0]	178.85 (-) [152.62]	40.44 (-26.23) [0]

230	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31	12/2015	/ (-) [12/2019]	1,167.45 (-) [1,167.45]	113.26 (0.00) [-]
231	FOUR LANING OF BHOJPUR TO BUXAR	1/1991	/ (4/2018) [10/2020]	642.41 (-) [681.67]	402.94 (39.26) [-]
232	FOUR LANING OF FORBESGANJ - JOGBANI	8/2015	4/2018 (-) [12/2020]	322.09 (247.00) [322.09]	77.53 (0.00) [32]
233	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR	1/2014	10/2016 (-) [0/0]	1,408.85 (-) [925.87]	586.18 (-482.98) [0]
234	FOUR LANING OF KOILWAR TO BHOJPUR	8/2015	/ (7/2017) [1/2020]	814.04 (-) [825.17]	646.72 (11.13) [-]
235	FOUR LANING OF PATNA TO KOILWAR	8/2015	/ (-) [0/0]	556.07 (-) [556.07]	0.00 (0.00) [0]
236	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31	12/2015	4/2019 (-) [0/0]	1,041.10 (-) [1,041.10]	214.34 (0.00) [0]
237	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	9/2011	3/2014 (-) [0/0]	574.00 (-) [574.00]	768.73 (0.00) [0]
238	PATNA-MUZZAFFARPUR	8/2010	2/2013 (-) [3/2020]	671.30 (-) [671.30]	1,132.48 (0.00) [85]
239	REHABILIATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM	8/2016	12/2016 (-) [0/0]	1,742.01 (-) [1,742.01]	1,034.37 (0.00) [0]
240	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I	1/2018	/ (-) [0/0]	573.70 (-) [573.70]	0.00 (0.00) [0]
241	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH	10/2013	8/2014 (-) [0/0]	278.39 (-) [278.39]	0.00 (0.00) [0]
242	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	1/1991	/ (-) [0/0]	478.35 (-) [478.35]	0.00 (0.00) [0]
243	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	1/1991	/ (-) [0/0]	319.68 (-) [369.77]	113.67 (50.09) [0]
244	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING	2/2014	7/2016 (-) [0/0]	665.50 (-) [665.50]	0.00 (0.00) [0]
245	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/1991	8/2016 (-) [0/0]	282.41 (-) [322.01]	278.45 (39.60) [0]
246	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/1991	10/2016 (-) [0/0]	358.22 (-) [377.64]	325.19 (19.42) [0]
247	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	1/1991	/ (-) [0/0]	675.00 (-) [675.00]	154.56 (0.00) [0]
248	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40	1/1991	/ (-) [0/0]	154.62 (-) [154.62]	0.00 (0.00) [0]
249	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION	1/2018	/ (-) [0/0]	895.39 (-) [895.39]	0.00 (0.00) [0]
250	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH	8/2017	8/2017	950.64	102.51

	APPROACH ROADS) SECTION OF NH-31		(-) [2/2022]	(-) [950.64]	(0.00) [54]
251	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH	3/2018	/ (-) [0/0]	153.24 (-) [153.24]	2.06 (0.00) [0]
252	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPR	3/2015	7/2016 (-) [0/0]	206.80 (-) [206.80]	74.04 (0.00) [0]
253	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA	8/2015	4/2019 (10/2017) [10/2019]	399.54 (-) [297.27]	509.75 (-102.27) [0]
254	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ	8/2015	/ (-) [0/0]	854.80 (-) [854.80]	558.04 (0.00) [0]
255	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR	8/2015	4/2018 (-) [0/0]	516.13 (-) [516.13]	395.25 (0.00) [0]
256	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN	3/2017	3/2020 (-) [3/2020]	672.89 (-) [736.01]	0.00 (63.12) [0]
257	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC	5/2014	8/2016 (-) [12/2020]	199.98 (-) [199.98]	153.43 (0.00) [52]
258	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C	11/2016	10/2019 (-) [0/0]	230.34 (-) [230.34]	178.39 (0.00) [0]
	Urban Development				
259	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	2/2016	6/2017 (-) [3/2021]	496.18 (496.00) [498.99]	97.67 (2.81) [45]
260	IRRIGATION WORK OF BAGMATI	10/2005	3/2015 (-) [3/2021]	956.00 (-) [956.00]	651.21 (0.00) [72]
	Water Resources				
261	I AND D AND STP AT CHAPPRA	11/2018	12/2020 (-) [12/2020]	236.15 (-) [236.15]	0.00 (0.00) [0]
262	I AND D AND STP WORKS FOR BHAGALPUR	10/2017	9/2020 (-) [9/2020]	254.13 (-) [254.13]	0.00 (0.00) [0]
263	SAIDPUR SEWER NETWORK PATNA	4/2015	1/2021 (-) [1/2021]	268.63 (-) [268.63]	0.00 (0.00) [0]
264	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR	4/2015	4/2020 (-) [4/2020]	184.93 (-) [184.93]	0.00 (0.00) [0]
265	SEWER NETWORK SPS AND STP BEGUSARAI	3/2018	7/2021 (-) [7/2021]	230.06 (-) [230.06]	0.00 (0.00) [0]
266	SEWER NETWORKS SPS AND STP HAJIPUR	3/2018	8/2021 (-) [8/2021]	305.19 (-) [305.19]	0.00 (0.00) [0]
267	SEWER NETWORKS, SPS AND STP, MUNGER	3/2018	10/2021 (-) [10/2021]	294.02 (-) [294.02]	0.00 (0.00) [0]
268	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA	5/2017	5/2021 (-) [5/2021]	184.86 (-) [184.86]	0.00 (0.00) [0]
269	SEWERAGE SCHEME AT PAHARI ZONE V PATNA	5/2017	4/2021 (-) [4/2021]	356.37 (-) [356.37]	0.00 (0.00) [0]

270	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA	8/2017	6/2022 (-) [6/2022]	824.00 (-) [824.00]	0.00 (0.00) [0]
271	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA	8/2017	6/2022 (-) [6/2022]	578.89 (-) [578.89]	0.00 (0.00) [0]
272	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	3/2020 (-) [3/2020]	225.77 (-) [225.77]	0.00 (0.00) [0]
273	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK	3/2017	5/2021 (-) [5/2021]	277.42 (-) [277.42]	0.00 (0.00) [0]
274	SEWERAGE TREATMENT PLANT AT PAHARI PATNA	5/2017	11/2020 (-) [11/2020]	191.62 (-) [191.62]	0.00 (0.00) [0]
	CHANDIGARH				
	Road Transport And Highways				
275	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221	3/2010	3/2013 (-) [3/2013]	179.89 (271.00) [271.00]	0.00 (91.11) [0]
276	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1	12/2010	1/2019 (-) [1/2019]	169.26 (299.00) [299.00]	0.00 (129.74) [0]
	CHHATISGARH				
	Coal				
277	AMERA OC RCE	2/2015	3/2018 (-) [3/2020]	335.97 (-) [335.97]	51.21 (0.00) [24]
278	AMGAON OPENCAST PROJECT RCE	7/2015	3/2020 (-) [3/2020]	316.10 (-) [316.10]	86.43 (0.00) [0]
279	BAROUD OC EXPANSION (RCE)- 3MTY	4/2012	3/2016 (-) [3/2020]	258.56 (-) [258.56]	181.44 (0.00) [48]
280	BIJARI OC RCE (1.50 MTY)	5/2014	3/2020 (-) [3/2020]	164.49 (-) [164.49]	82.91 (0.00) [0]
281	CHHAL OC SEAM -III (6.00 MTY)	12/2013	3/2022 (-) [3/2022]	610.63 (-) [610.63]	105.36 (0.00) [0]
282	DURGAPUR OPENCAST PROJECT	2/2015	3/2023 (-) [3/2023]	916.24 (-) [916.24]	4.11 (0.00) [0]
283	GEVRA EXPANSION OCP (SECL) (35-70) MTY	6/2010	3/2023 (-) [3/2023]	11,816.40 (-) [11,816.40]	2,891.13 (0.00) [0]
284	JAGANNATHPOR OCP(3.00MTY)	9/2008	3/2015 (-) [3/2020]	152.43 (-) [459.49]	193.35 (307.06) [60]
285	JHIRIA WEST OPENCAST PROJECT	11/2018	3/2026 (-) [3/2026]	389.97 (-) [389.97]	0.00 (0.00) [0]
286	KARTALI (EAST) OCP (2.50 MTY)	7/2008	3/2014 (-) [3/2020]	178.44 (-) [178.44]	2.92 (0.00) [72]
287	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY	8/2013	3/2023 (-) [3/2023]	7,612.33 (-) [7,612.33]	2,116.58 (0.00) [0]
288	MADANNAGAR OPENCAST PROJECT	10/2015	3/2024 (-) [3/2024]	1,875.32 (-) [1,875.32]	0.00 (0.00) [0]

289	MAHAMAYA OPENCAST PROJECT	5/2018	3/2026 (-) [3/2026]	410.26 (-) [410.26]	9.53 (0.00) [0]
290	MANIKPUR OC EXPANSION (3.5 MTY)	12/2009	3/2014 (-) [3/2021]	321.50 (-) [321.50]	197.28 (0.00) [84]
291	PELMA OCP(15.00MTY)	11/2014	3/2023 (-) [3/2023]	1,624.59 (-) [1,624.59]	6.50 (0.00) [0]
292	VIJAY WEST OPENCAST PROJECT	5/2017	3/2026 (-) [3/2026]	976.95 (-) [976.95]	75.96 (0.00) [0]
	Petroleum				
293	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH	12/2016	4/2021 (-) [4/2021]	300.00 (-) [300.00]	1.09 (0.00) [0]
	Power				
294	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	12/2012	10/2017 (3/2020) [3/2020]	11,846.00 (-) [12,739.82]	12,839.84 (893.82) [29]
295	TALAIPALLI COAL MINING PROJECT	9/2015	11/2019 (-) [11/2019]	3,004.00 (-) [3,004.00]	1,782.00 (0.00) [0]
	Railways				
296	CHAMPA-JHARSUGUDA 3RD LINE	4/2008	12/2019 (3/2020) [3/2020]	872.00 (1,226.51) [1,226.51]	1,062.76 (354.51) [3]
297	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW	2/2016	3/2020 (-) [3/2020]	393.98 (-) [393.98]	290.45 (0.00) [0]
298	GEVRA ROAD PENDRA ROAD	2/2014	3/2022 (-) [12/2022]	2,288.00 (-) [4,970.11]	628.61 (2,682.11) [9]
299	JHARSUGUDA-BILASPUR 4TH LINE	4/2015	3/2021 (3/2023) [3/2023]	1,973.00 (1,973.64) [1,973.64]	174.40 (0.64) [24]
300	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	4/2013	9/2018 (-) [12/2020]	3,055.00 (-) [3,055.00]	1,951.07 (0.00) [27]
301	KIRANDUL - JAGDALPUR DOUBLING	12/2012	3/2020 (-) [3/2023]	1,160.00 (1,160.83) [1,160.83]	699.40 (0.83) [36]
302	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR	5/2014	3/2018 (-) [0/0]	207.00 (-) [207.00]	153.83 (0.00) [0]
303	RAIPUR - TITLAGARH - DOUBLING	3/2007	3/2020 (-) [6/2020]	1,402.02 (-) [1,100.00]	1,088.23 (-302.02) [3]
	Road Transport And Highways				
304	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF	3/2018	/ (3/2021) [3/2021]	1,029.96 (-) [1,261.05]	97.55 (231.09) [-]
305	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1)	12/2015	4/2018 (3/2020) [3/2020]	726.67 (598.13) [598.13]	414.73 (-128.54) [23]
306	FOUR LANING OF SARAGAON - BILASPUR	12/2015	4/2018 (8/2018) [8/2018]	509.13 (-) [509.13]	412.66 (0.00) [0]
307	FOUR LANING OF SIMGA - SARAGAON	12/2015	5/2018 (10/2019) [10/2019]	596.67 (-) [596.67]	399.92 (0.00) [0]

308	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION.	12/2015	/ (-) [0/0]	291.05 (-) [291.05]	182.16 (0.00) [0]
309	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION	11/2015	6/2017 (-) [6/2017]	335.32 (-) [335.32]	0.00 (0.00) [0]
310	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 127.500 TO 178.944 DARRIGHAT TO BANARI SECTION	3/2016	9/2016 (-) [9/2016]	491.52 (-) [491.52]	0.00 (0.00) [0]
311	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V	1/2016	9/2016 (-) [9/2016]	476.20 (544.00) [544.00]	0.00 (67.80) [0]
312	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION	12/2014	3/2015 (-) [3/2015]	496.02 (-) [496.02]	0.00 (0.00) [0]
313	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180	1/2016	8/2016 (-) [8/2016]	497.14 (-) [497.14]	0.00 (0.00) [0]
314	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	1/2016	10/2016 (-) [10/2016]	624.98 (-) [624.98]	0.00 (0.00) [0]
315	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI	3/2016	7/2016 (-) [7/2016]	452.94 (-) [452.94]	0.00 (0.00) [0]
316	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO	3/2017	1/2018 (-) [1/2018]	423.79 (-) [423.79]	0.00 (0.00) [0]
317	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION	11/2015	12/2015 (-) [0/0]	485.44 (-) [485.44]	447.13 (0.00) [0]
318	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A	11/2017	5/2019 (-) [5/2019]	188.80 (-) [188.80]	0.00 (0.00) [0]
319	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331	12/2014	11/2017 (-) [11/2017]	379.16 (-) [379.16]	0.00 (0.00) [0]
	Steel				
320	NMDC INTEGRATED STEEL PLANT	1/2010	5/2015 (7/2020) [7/2020]	15,525.00 (23,140.00) [23,140.00]	16,244.05 (7,615.00) [62]
	D & N HAVELI				
	Petroleum				
321	DAMAN DEVELOPMENT PROJECT	8/2014	5/2019 (10/2019) [10/2019]	6,086.08 (5,842.31) [5,842.31]	4,784.88 (-243.77) [0]
	DELHI				
	Civil Aviation				
322	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	4/2020 (-) [12/2020]	233.38 (-) [233.38]	84.73 (0.00) [8]
	Health And Family Welfare				
323	AIIMS - MOTHER AND CHILD BLOCK	12/2013	5/2017 (-) [6/2020]	204.44 (-) [270.00]	204.70 (65.56) [37]
324	AIIMS - OPD(NEW)	8/2014	5/2017 (-) [1/2020]	293.65 (-) [325.00]	297.16 (31.35) [32]
325	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	/ (-) [5/2020]	156.56 (-) [156.65]	76.53 (0.09) [-]
326	LHMC NEW DELHI-RE-DEVELOPMENT	2/2013	11/2013	414.11	302.02

			(-) [9/2020]	(-) [499.23]	(85.12) [82]
	Heavy Industry				
327	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	8/2016	9/2019 (-) [3/2020]	1,554.00 (-) [1,554.00]	665.35 (0.00) [6]
	Power				
328	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	3/2015	5/2017 (6/2019) [12/2019]	1,394.52 (-) [1,394.52]	431.80 (0.00) [31]
	Railways				
329	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE	4/2012	/ (-) [3/2023]	295.68 (-) [295.68]	92.91 (0.00) [-]
330	GRADE SEPERATOR AT DAYABASTI	4/1999	/ (3/2024) [3/2024]	156.65 (-) [197.17]	106.97 (40.52) [-]
	Road Transport And Highways				
331	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8	7/2017	9/2019 (-) [12/2019]	269.69 (-) [269.69]	0.00 (0.00) [3]
	Telecommunications				
332	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	6/2016	6/2017 (-) [0/0]	418.26 (-) [418.26]	367.04 (0.00) [0]
	Urban Development				
333	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	6/2015	4/2019 (-) [11/2020]	197.33 (-) [197.33]	61.47 (0.00) [19]
334	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI	7/2017	/ (-) [0/0]	218.72 (218.72) [218.72]	57.71 (0.00) [0]
335	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	7/2012	12/2015 (-) [0/0]	884.30 (-) [884.30]	729.63 (0.00) [0]
336	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	10/2017	11/2019 (8/2020) [8/2020]	271.90 (-) [271.90]	61.81 (0.00) [9]
337	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU	12/2017	6/2019 (-) [0/0]	188.00 (-) [188.00]	146.45 (0.00) [0]
338	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT	11/2018	7/2021 (-) [7/2021]	361.60 (-) [361.60]	0.45 (0.00) [0]
339	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS	7/2019	3/2025 (-) [3/2025]	24,948.65 (-) [24,948.65]	1.74 (0.00) [0]
340	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND	5/2017	12/2020 (-) [12/2020]	565.00 (-) [565.00]	321.05 (0.00) [0]
341	DELHI MRTS PHASE-III	9/2011	3/2016 (-) [0/0]	38,585.00 (-) [38,585.00]	34,763.00 (0.00) [0]
342	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	10/2019 (-) [3/2021]	1,219.21 (-) [2,000.00]	408.23 (780.79) [17]
343	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B	11/2017	5/2020 (-) [5/2020]	238.56 (-) [238.56]	63.45 (0.00) [0]
344	REDEVELOPMENT OF EAST KIDWAI NAGAR	6/2012	11/2019 (-)	4,264.00 (-)	3,246.53 (175.23)

			[11/2019]	[4,439.23]	[0]
345	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I	10/2016	7/2021 (-) [7/2021]	1,180.00 (-) [1,180.00]	0.00 (0.00) [0]
346	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI-CONSTRUCTION OF 380 N	10/2016	/ (8/2020) [3/2021]	392.00 (-) [392.00]	12.56 (0.00) [-]
347	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I	10/2016	3/2022 (-) [3/2022]	1,128.00 (-) [1,128.00]	0.00 (0.00) [0]
348	REDEVELOPMENT OF GPRA AT MOHAMMADPUR	10/2016	/ (-) [12/2020]	422.00 (-) [422.00]	14.20 (0.00) [-]
349	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR	7/2016	/ (-) [0/0]	2,694.00 (-) [2,694.00]	0.00 (0.00) [0]
350	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	10/2016	4/2018 (2/2020) [8/2020]	248.20 (-) [248.20]	45.03 (0.00) [28]
	Water Resources				
351	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO	5/2017	5/2020 (-) [5/2020]	344.81 (-) [344.81]	0.00 (0.00) [0]
352	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O&M AT CORONATION PILLAR DELHI	12/2018	1/2021 (-) [1/2021]	515.07 (-) [515.07]	0.00 (0.00) [0]
353	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L	3/2017	12/2022 (-) [12/2022]	665.78 (-) [665.78]	0.00 (0.00) [0]
354	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2	5/2016	12/2021 (-) [12/2021]	211.79 (-) [211.79]	0.00 (0.00) [0]
355	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S	5/2016	2/2022 (-) [2/2022]	239.11 (-) [239.11]	0.00 (0.00) [0]
	GOA				
	Health And Family Welfare				
356	SUPER SPECIALITY BLOCK PMSSY GOA	1/2018	/ (-) [5/2020]	249.01 (-) [249.01]	126.78 (0.00) [-]
	Road Transport And Highways				
357	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE	3/2015	/ (-) [0/0]	280.16 (-) [290.59]	219.47 (10.43) [0]
358	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD	3/2015	/ (-) [0/0]	184.05 (-) [184.05]	96.58 (0.00) [0]
359	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE	10/2015	/ (-) [0/0]	936.40 (-) [936.40]	262.25 (0.00) [0]
360	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K	3/2015	/ (-) [0/0]	298.33 (-) [298.33]	160.33 (0.00) [0]
361	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDEAPAR BRIDGE	3/2015	4/2018 (-) [0/0]	297.00 (-) [297.00]	290.64 (0.00) [0]
362	KARASWADA TO BAMBOLIM	3/2017	12/2019 (-) [12/2019]	852.67 (852.67) [852.67]	86.04 (0.00) [0]
363	PATRADEVI TO KARASWADA 4L	3/2017	5/2020 (-)	634.32 (634.32)	109.33 (0.00)

			[5/2020]	[634.32]	[0]
364	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER	12/2015	/ (-) [0/0]	773.98 (-) [773.98]	259.66 (0.00) [0]
365	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR	12/2015	/ (-) [0/0]	819.95 (-) [819.95]	193.63 (0.00) [0]
	GUJARAT				
	Atomic Energy				
366	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015 (-) [6/2020]	11,459.00 (-) [16,580.00]	14,137.00 (5,121.00) [54]
	Petroleum				
367	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT	3/2018	/ (-) [8/2022]	588.20 (-) [588.20]	1.24 (0.00) [-]
368	BS-VI PROJECT AT GUJARAT REFINERY	3/2018	9/2019 (-) [3/2020]	3,380.00 (-) [3,380.00]	2,238.63 (0.00) [6]
369	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	4/2016	4/2018 (-) [12/2019]	327.78 (-) [200.00]	150.72 (-127.78) [20]
370	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY	8/2017	8/2020 (-) [8/2020]	1,342.00 (-) [1,342.00]	6.30 (0.00) [0]
371	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	10/2017	2/2020 (-) [10/2020]	906.00 (-) [906.00]	98.97 (0.00) [8]
372	INFRASTRUCTURE DEVLOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY	9/2016	7/2020 (-) [7/2020]	208.35 (-) [208.35]	126.98 (0.00) [0]
373	LAB REVAMP AT GUJARAT REFINERY	10/2019	12/2021 (-) [12/2021]	403.00 (-) [403.00]	43.50 (0.00) [0]
374	REDEVELOPMENT OF SANTHAL FIELD	2/2017	3/2026 (-) [3/2026]	1,162.56 (-) [1,162.56]	412.79 (0.00) [0]
375	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI	9/2018	2/2021 (-) [2/2021]	225.54 (-) [225.54]	2.35 (0.00) [0]
	Power				
376	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT	12/2017	6/2019 (3/2020) [3/2020]	193.14 (-) [193.14]	100.18 (0.00) [9]
377	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT	5/2017	9/2018 (3/2020) [3/2020]	175.64 (-) [175.64]	101.85 (0.00) [18]
	Railways				
378	AHMEDABAD-BOTAD (GC)	4/2012	12/2021 (-) [12/2021]	975.62 (-) [1,082.32]	1,054.93 (106.70) [0]
379	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	4/2008	3/2020 (3/2021) [3/2021]	829.74 (1,215.34) [1,310.23]	1,450.40 (480.49) [12]
380	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	4/2006	3/2011 (3/2017) [3/2017]	117.36 (196.95) [202.35]	809.40 (84.99) [0]
381	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	2/1991	3/2019 (3/2020) [3/2020]	551.51 (809.07) [809.07]	641.51 (257.56) [12]
382	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO	4/2008	3/2012	318.24	125.76

	VAYOR (WR)		(3/2022) [3/2022]	(321.62) [321.62]	(3.38) [120]
383	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM	4/2017	3/2020 (3/2021) [3/2021]	691.84 (663.29) [663.29]	180.20 (-28.55) [12]
384	DHASA-JETALSAR (GC)	4/2012	3/2021 (-) [3/2021]	644.38 (-) [644.38]	418.93 (0.00) [0]
385	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO	3/2017	/ (-) [0/0]	243.60 (-) [243.60]	0.00 (0.00) [0]
386	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)	4/2011	/ (3/2021) [3/2021]	844.10 (844.10) [844.10]	107.52 (0.00) [-]
387	MULTI MODAL LOGISTICS PARK AT VARNAMA	10/2013	3/2019 (-) [12/2019]	343.00 (-) [343.00]	222.83 (0.00) [9]
388	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220	3/2012	/ (-) [0/0]	153.83 (-) [153.83]	0.00 (0.00) [0]
389	PALANPUR-SAMAKHAYALI (DL)	4/2013	12/2021 (-) [3/2022]	1,548.66 (-) [1,548.66]	1,339.35 (0.00) [3]
390	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	4/1994	3/2019 (3/2022) [3/2022]	320.66 (858.56) [858.96]	534.00 (538.30) [36]
391	SURENDRA NAGAR RAJKOT	4/2015	3/2021 (3/2021) [3/2021]	1,002.39 (1,002.39) [1,002.39]	396.54 (0.00) [0]
392	VIRAMGAM-SAMAKHIALI (DL)	4/2011	3/2021 (3/2022) [3/2022]	1,037.15 (1,037.15) [1,037.15]	1,017.75 (0.00) [12]
393	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON	3/2012	/ (-) [0/0]	248.26 (-) [248.26]	0.00 (0.00) [0]
	Road Transport And Highways				
394	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION	12/2016	/ (-) [9/2019]	417.19 (-) [417.19]	262.83 (0.00) [0]
395	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000	7/2016	/ (-) [1/2020]	829.97 (-) [829.97]	192.41 (0.00) [-]
396	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT	6/2017	6/2020 (2/2018) [2/2021]	1,958.88 (-) [1,958.88]	1,116.85 (0.00) [8]
397	AHMEDABAD TO VADODARA SECTION	1/2013	12/2015 (-) [0/0]	2,125.24 (2,125.24) [2,125.24]	4,669.71 (0.00) [0]
398	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS	5/2016	/ (-) [12/2019]	364.56 (-) [392.00]	260.72 (27.44) [-]
399	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR	3/2018	/ (11/2021) [0/0]	1,161.39 (1,404.00) [1,161.39]	0.00 (0.00) [0]
400	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S	3/2018	/ (12/2018) [7/2021]	1,437.64 (1,687.00) [1,437.64]	564.11 (0.00) [-]
401	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S	3/2018	/ (5/2018) [1/2021]	2,702.05 (-) [2,043.00]	0.00 (-659.05) [-]
402	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN	10/2018	5/2019	400.76	29.00

	LAKHPAT GADULI HAJIPIR ODMA KHAVDA DHOLAVIRA MAUVANA		(-) [0/0]	(-) [400.76]	(0.00) [0]
403	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU	8/2017	3/2018 (-) [0/0]	962.43 (-) [962.43]	81.55 (0.00) [0]
404	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE	12/2017	11/2018 (-) [0/0]	867.97 (-) [867.97]	172.70 (0.00) [0]
405	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6.	5/2016	/ (-) [0/0]	998.18 (-) [998.18]	441.80 (0.00) [0]
406	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST	5/2016	/ (-) [0/0]	723.64 (-) [723.64]	313.19 (0.00) [0]
407	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR	5/2016	/ (-) [0/0]	834.64 (-) [834.64]	319.33 (0.00) [0]
408	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU	5/2016	/ (-) [0/0]	763.08 (-) [763.08]	386.86 (0.00) [0]
409	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	3/2010	9/2012 (12/2019) [12/2019]	1,509.10 (3,787.21) [1,509.10]	3,684.44 (0.00) [87]
410	JUNAGADH BYPASS	10/2017	10/2017 (-) [11/2019]	232.49 (-) [232.49]	0.00 (0.00) [25]
411	KANDLA - MUNDRA PORT	1/2011	7/2013 (11/2020) [11/2020]	953.88 (-) [953.88]	976.79 (0.00) [88]
412	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF	2/2018	/ (-) [1/2021]	1,052.21 (1,449.00) [1,449.00]	336.43 (396.79) [-]
413	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG.	1/2017	/ (-) [1/2021]	1,251.11 (-) [1,251.11]	1,084.26 (0.00) [-]
414	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME	5/2016	/ (-) [0/0]	425.60 (241.41) [425.60]	103.13 (0.00) [0]
415	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4	3/2018	6/2021 (-) [6/2021]	351.00 (-) [351.00]	0.49 (0.00) [0]
416	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEE	3/2018	11/2018 (-) [0/0]	464.07 (-) [464.07]	125.89 (0.00) [0]
417	UPGRADATION TO 2 LANE WITH PAVED SHOULDER WITH RIGID PAVEMETS FROM 37/400 TO KM 66/700 ON NH 848 ON	3/2016	2/2016 (-) [0/0]	208.34 (-) [208.34]	112.87 (0.00) [0]
418	VADODARA-SURAT SECTION	3/2014	8/2016 (-) [10/2017]	503.16 (-) [503.16]	389.50 (0.00) [0]
419	WIDENING FROM TWO LANE TO FOUR LANE WITH PAVED SHOULDER AND STRENGTHNING OF EXISTING PAVEMENT BETWEE	3/2016	2/2017 (-) [0/0]	223.67 (-) [223.67]	112.81 (0.00) [0]
	Urban Development				
420	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	12/2018 (-) [7/2020]	10,773.00 (-) [10,773.00]	6,296.85 (0.00) [19]
421	AHMEDABAD METRO RAIL PROJECT PHASE II	3/2019	3/2024 (-) [3/2024]	5,384.17 (-) [5,384.17]	4.35 (0.00) [0]
422	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER	1/2013	/	175.00	1.83

	AT GANDHINAGAR, GUJARAT		(-) [0/0]	(-) [175.00]	(0.00) [0]
423	SURAT METRO RAIL PROJECT	3/2019	3/2024 (-) [3/2024]	12,020.32 (-) [12,020.32]	4.67 (0.00) [0]
	HARYANA				
	Fertilisers				
424	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	1/2018	11/2019 (-) [11/2019]	215.92 (-) [215.92]	128.60 (0.00) [0]
	Health And Family Welfare				
425	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	9/2014	3/2018 (-) [9/2019]	505.58 (-) [585.00]	586.96 (79.42) [0]
	Petroleum				
426	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY	1/2019	1/2021 (-) [1/2021]	909.00 (-) [909.00]	22.76 (0.00) [0]
427	BS-VI PROJECT AT PANIPAT REFINERY	12/2017	7/2019 (-) [2/2020]	3,529.00 (-) [3,529.00]	1,895.18 (0.00) [7]
428	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	4/2018	2/2020 (-) [2/2020]	206.63 (-) [206.63]	19.25 (0.00) [0]
429	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA	11/2017	11/2020 (-) [11/2020]	255.00 (-) [255.00]	94.33 (0.00) [0]
430	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY	10/2018	2/2020 (-) [2/2020]	598.00 (-) [598.00]	17.37 (0.00) [0]
431	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT	12/2018	6/2021 (-) [6/2021]	278.60 (-) [278.60]	0.00 (0.00) [0]
432	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT	8/2018	8/2020 (-) [8/2020]	1,636.00 (-) [1,636.00]	152.56 (0.00) [0]
433	PX-PTA REVAMP AT PANIPAT REFINERY	8/2019	10/2021 (-) [10/2021]	1,255.00 (-) [1,255.00]	99.93 (0.00) [0]
434	R and D CAMPUS II AT FARIDABAD	6/2019	12/2022 (-) [12/2022]	2,281.94 (-) [2,281.94]	0.00 (0.00) [0]
435	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT	8/2018	8/2020 (9/2020) [9/2020]	286.42 (-) [286.42]	1.92 (0.00) [1]
	Railways				
436	MULTI MODAL LOGISTICS PARK AT BARHI	12/2015	3/2019 (-) [3/2020]	346.32 (-) [346.32]	288.65 (0.00) [12]
437	ROHTAK-MEHAM HANSI	4/2012	12/2011 (-) [3/2021]	287.00 (-) [694.00]	220.42 (407.00) [111]
	Road Transport And Highways				
438	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	12/2015	6/2016 (-) [10/2019]	602.95 (507.70) [507.70]	496.22 (-95.25) [0]
439	4 LANING OF AMBALA - KAITHAL - PACKAGE -2	1/2016	7/2018 (-) [11/2019]	574.28 (537.16) [537.16]	503.20 (-37.12) [16]
440	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON	3/2017	3/2020 (-)	639.79 (-)	558.40 (-86.89)

	DBFOT TOLL		[0/0]	[552.90]	[0]
441	8 LANING OF MUKARBA CHOWK TO PANIPAT	7/2015	4/2019 (-) [0/0]	2,128.72 (-) [2,128.72]	971.24 (0.00) [0]
442	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC)	1/2017	3/2019 (7/2019) [0/0]	276.01 (-) [276.01]	187.39 (0.00) [0]
443	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS	1/2017	3/2019 (3/2020) [3/2020]	247.25 (-) [247.25]	144.71 (0.00) [12]
444	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73	8/2016	5/2019 (-) [1/2020]	248.97 (-) [248.97]	236.19 (0.00) [8]
445	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P	3/2018	/ (-) [12/2020]	1,484.30 (-) [1,484.30]	111.66 (0.00) [-]
446	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211	9/2016	5/2019 (-) [2/2019]	1,004.67 (-) [813.45]	577.21 (-191.22) [0]
447	DELHI/ HARYANA BORDER TO ROHTAK	4/2007	5/2010 (-) [3/2020]	486.00 (-) [486.00]	470.01 (0.00) [118]
448	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2	11/2015	5/2018 (2/2018) [0/0]	867.66 (1,464.24) [1,464.24]	1,255.55 (596.58) [0]
449	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I	8/2015	2/2018 (10/2017) [0/0]	723.54 (1,286.84) [1,286.84]	1,163.65 (563.30) [0]
450	ISMAILABAD-NARNAUL PKG-1	1/2019	/ (-) [0/0]	996.65 (-) [996.65]	320.30 (0.00) [0]
451	ISMAILABAD-NARNAUL PKG-2	1/2019	/ (-) [0/0]	1,243.45 (-) [1,243.45]	357.82 (0.00) [0]
452	ISMAILABAD-NARNAUL PKG-3	1/2019	/ (-) [0/0]	889.36 (-) [889.36]	284.61 (0.00) [0]
453	ISMAILABAD-NARNAUL PKG-4	1/2019	/ (-) [0/0]	1,018.79 (-) [1,018.79]	226.56 (0.00) [0]
454	ISMAILABAD-NARNAUL PKG-5	1/2019	/ (-) [0/0]	1,051.91 (-) [1,051.91]	213.79 (0.00) [0]
455	ISMAILABAD-NARNAUL PKG-6	1/2019	/ (-) [0/0]	1,120.06 (-) [1,120.06]	228.53 (0.00) [0]
456	ISMAILABAD-NARNAUL PKG-7	1/2019	/ (-) [0/0]	1,137.42 (-) [1,137.42]	305.85 (0.00) [0]
457	ISMAILABAD-NARNAUL PKG-8	1/2019	/ (-) [0/0]	1,033.19 (-) [1,033.19]	209.69 (0.00) [0]
458	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	5/2009	11/2011 (-) [3/2020]	1,108.00 (2,967.50) [2,967.50]	3,990.72 (1,859.50) [100]
459	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS	3/2018	/ (-) [3/2020]	551.58 (-) [551.58]	305.46 (0.00) [-]
460	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE	3/2018	/ (-) [3/2020]	275.12 (-) [275.12]	129.75 (0.00) [-]

461	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROMEXISTI	3/2018	/ (-) [3/2020]	307.79 (-) [307.79]	147.50 (0.00) [-]
462	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN	3/2018	/ (-) [6/2020]	181.78 (-) [181.78]	66.03 (0.00) [-]
463	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN	3/2018	/ (-) [3/2020]	198.05 (-) [198.05]	98.90 (0.00) [-]
464	SIX LANING AND STREGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I)	3/2018	/ (-) [7/2021]	795.50 (-) [799.30]	115.56 (3.80) [-]
465	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA	3/2018	/ (-) [7/2021]	634.70 (931.21) [931.21]	125.31 (296.51) [-]
	HIMACHAL PRADESH				
	Health And Family Welfare				
466	AIIMS BILASPUR	4/2018	9/2021 (-) [9/2021]	1,351.00 (1,471.00) [1,351.00]	245.85 (0.00) [0]
	Power				
467	PARBATI HEP (4X200 MW) (NHPC) II	9/2002	9/2009 (-) [12/2021]	3,919.59 (-) [9,997.11]	7,715.06 (6,077.52) [147]
	Railways				
468	BHANUPALI-BILASPUR BERI NL	4/2008	12/2026 (-) [12/2025]	2,966.99 (-) [7,000.00]	446.46 (4,033.01) [-12]
	Road Transport And Highways				
469	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345)	2/2016	2/2019 (-) [6/2019]	273.20 (725.87) [273.20]	659.81 (0.00) [0]
470	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P	6/2017	6/2020 (-) [9/2021]	2,485.93 (2,946.82) [2,485.93]	359.79 (0.00) [15]
471	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM)	11/2013	11/2016 (-) [0/0]	1,916.79 (-) [1,916.79]	1,948.92 (0.00) [0]
472	FOUR LANING OF PARWANOO -SOLAN	9/2015	3/2018 (-) [3/2020]	934.46 (1,302.98) [934.46]	531.34 (0.00) [24]
473	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M	3/2018	/ (-) [5/2021]	478.74 (1,071.75) [478.74]	15.06 (0.00) [-]
474	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH	9/2016	/ (-) [7/2020]	1,273.71 (1,464.12) [1,273.71]	573.04 (0.00) [-]
475	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000)	10/2016	/ (-) [11/2019]	447.75 (1,238.21) [447.75]	1,028.99 (0.00) [-]
476	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS	8/2016	/ (-) [9/2020]	1,583.18 (2,170.44) [1,583.18]	271.06 (0.00) [-]
	Urban Development				
477	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH	12/2018	6/2021 (-) [6/2021]	260.00 (-) [260.00]	12.50 (0.00) [0]
478	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	11/2012	11/2014 (-) [0/0]	270.83 (-) [270.83]	199.91 (0.00) [0]
	JAMMU AND KASHMIR				

	Civil Aviation				
479	CONSTRUCTION OF TERMINAL BUILDING & ASSOCIATED WORKS AT LEH AIRPORT	7/2018	9/2021 (-) [9/2021]	323.19 (-) [323.19]	10.14 (0.00) [0]
	Railways				
480	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	3/1995	11/2002 (-) [6/2022]	2,500.00 (27,949.00) [27,949.00]	19,767.15 (25,449.00) [235]
	Road Transport And Highways				
481	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE	12/2017	/ (-) [1/2021]	1,471.75 (1,339.00) [1,339.00]	399.89 (-132.75) [-]
482	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A	12/2015	6/2019 (-) [12/2020]	2,168.66 (-) [2,168.66]	684.57 (0.00) [18]
483	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A	12/2015	12/2018 (-) [7/2020]	2,136.97 (-) [2,136.97]	1,214.48 (0.00) [19]
484	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	7/2010	7/2013 (-) [0/0]	1,813.76 (-) [1,813.76]	2,393.99 (0.00) [0]
485	NASHRI- CHANANI	5/2011	6/2015 (-) [0/0]	2,159.00 (-) [2,519.00]	4,706.90 (360.00) [0]
486	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	7/2010	7/2015 (12/2019) [9/2020]	1,987.00 (-) [1,987.00]	2,864.02 (0.00) [62]
487	SRINAGAR TO BANIHAL	6/2011	6/2014 (9/2017) [10/2020]	1,100.70 (-) [1,100.70]	2,898.25 (0.00) [76]
488	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA	3/2018	7/2019 (-) [0/0]	253.44 (-) [253.44]	0.00 (0.00) [0]
489	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0	3/2018	8/2018 (-) [0/0]	404.17 (-) [404.17]	46.34 (0.00) [0]
490	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM	3/2018	11/2018 (-) [0/0]	216.00 (-) [216.00]	12.70 (0.00) [0]
	Urban Development				
491	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C)	1/2018	/ (-) [0/0]	676.00 (-) [676.00]	0.00 (0.00) [0]
492	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1)	3/2019	/ (-) [0/0]	329.00 (-) [329.00]	0.00 (0.00) [0]
	JHARKHAND				
	Coal				
493	AMRAPALI OC(12MTY)	2/2012	3/2020 (-) [3/2020]	858.11 (-) [858.11]	187.61 (0.00) [0]
494	CHITRA EAST (RCE) OCP	8/2018	3/2024 (-) [3/2024]	513.98 (-) [513.98]	92.51 (0.00) [0]
495	CHURI BENTI UG (0.81 MTY)	8/2007	3/2011 (-) [3/2021]	163.51 (-) [163.51]	106.41 (0.00) [120]
496	HURA - C OC (3 MTY)	10/2015	3/2022 (-) [3/2022]	359.69 (-) [359.69]	84.91 (0.00) [0]
497	KAPURIA UG(PSLW)	8/2011	4/2017	988.35	45.26

			(-) [0/0]	(-) [988.35]	(0.00) [0]
498	KARMA OCP (1.0MTY)	6/2009	3/2014 (-) [3/2021]	162.46 (-) [162.46]	90.75 (0.00) [84]
499	MADHUBAND NLW WASHERY	8/2010	5/2014 (3/2020) [3/2020]	289.45 (-) [289.45]	260.10 (0.00) [70]
500	MAGADH OC 20 MTY (CCL)	8/2008	7/2012 (-) [3/2022]	706.40 (-) [706.40]	432.82 (0.00) [116]
501	MOONIDIH XV SEAM UG	8/2011	4/2015 (4/2022) [4/2022]	1,230.27 (-) [1,230.27]	401.81 (0.00) [84]
502	MURAIDIH UG TURN-KEY PROJECT	2/2011	4/2014 (-) [0/0]	339.88 (-) [339.88]	12.08 (0.00) [0]
503	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	2/2014	3/2021 (-) [3/2021]	555.52 (-) [555.52]	5.24 (0.00) [0]
504	NORTH URIMARI EXPANSION OCP	3/2019	3/2023 (-) [3/2023]	1,553.06 (-) [1,553.06]	203.46 (0.00) [0]
505	PATHERDIH NLW WASHERY	10/2012	4/2014 (-) [1/2020]	269.82 (-) [269.82]	180.83 (0.00) [69]
506	RAJRAPPA RCE OCP (3.0 MTY)	12/2009	3/2016 (-) [3/2021]	510.85 (-) [510.85]	365.62 (0.00) [60]
507	TAPIN OCP (2.5 MTY)	8/2008	3/2012 (-) [3/2021]	264.68 (-) [264.68]	181.17 (0.00) [108]
	Petroleum				
508	120 TMTPA NEW LPG PLANT AT BARHI JHARKAND STATE	6/2017	6/2020 (-) [9/2021]	161.50 (-) [161.50]	17.78 (0.00) [15]
509	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR	10/2017	10/2022 (-) [10/2022]	221.45 (-) [221.45]	51.10 (0.00) [0]
510	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI	10/2017	10/2022 (-) [10/2022]	226.45 (-) [226.45]	56.99 (0.00) [0]
511	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	12/2015	3/2023 (3/2022) [3/2022]	823.27 (910.23) [910.23]	403.18 (86.96) [-12]
512	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO.	11/2018	6/2022 (-) [6/2022]	248.55 (-) [248.55]	23.38 (0.00) [0]
	Power				
513	NORTH KARANPURA STPP (3X660 MW)	2/2014	6/2019 (9/2019) [3/2022]	14,366.58 (-) [15,164.05]	9,861.12 (797.47) [33]
514	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017 (-) [0/0]	4,237.96 (4,238.00) [4,552.00]	3,293.00 (314.04) [0]
515	PATRATU STPP-I (3X800MW)	11/2017	3/2023 (-) [3/2023]	18,668.00 (-) [18,668.00]	2,078.50 (0.00) [0]
	Railways				
516	BONDAMUNDA RANCHI DOUBLING	3/2016	3/2021 (3/2021)	1,724.20 (-)	411.64 (269.04)

			[12/2021]	[1,993.24]	[9]
517	GARHWA ROAD-RAMNA	3/2015	3/2021 (-) [12/2020]	348.23 (-) [348.23]	187.91 (0.00) [-3]
518	KODERMA-RANCHI VIA BARKAKANA (NL),ECR	3/1999	/ (-) [3/2021]	1,033.07 (3,020.95) [3,376.00]	3,328.43 (2,342.93) [-]
519	KODERMA-TILAIYA (NL), ECR	4/2002	/ (-) [3/2021]	459.91 (1,625.87) [1,625.87]	544.36 (1,165.96) [-]
520	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	4/2012	12/2018 (-) [6/2020]	258.20 (358.68) [358.68]	265.54 (100.48) [18]
521	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	4/2012	12/2016 (8/2018) [1/2020]	148.77 (-) [377.00]	182.63 (228.23) [37]
	Road Transport And Highways				
522	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00)	3/2017	3/2020 (-) [3/2020]	239.68 (-) [235.90]	91.24 (-3.78) [0]
523	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00)	3/2017	3/2020 (-) [3/2020]	165.50 (-) [172.16]	117.09 (6.66) [0]
524	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K	3/2018	/ (3/2019) [3/2021]	1,005.08 (1,073.10) [1,005.08]	0.00 (0.00) [-]
525	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION	2/2016	3/2019 (-) [0/0]	997.15 (-) [997.15]	728.62 (0.00) [0]
526	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31	1/2018	/ (-) [0/0]	273.46 (-) [273.46]	0.00 (0.00) [0]
527	FOUR LANING OF BARHI-HAZARIBAGH NH-33	8/2016	8/2018 (-) [1/2020]	323.72 (-) [323.72]	232.58 (0.00) [17]
528	RANCHI-RARGA-JAMSETHPUR	12/2012	6/2015 (-) [0/0]	1,479.00 (-) [1,479.00]	740.26 (0.00) [0]
529	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L	3/2018	6/2020 (-) [6/2020]	212.99 (-) [212.99]	93.80 (0.00) [0]
530	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION	1/2018	/ (6/2019) [0/0]	1,155.16 (999.00) [1,155.16]	30.13 (0.00) [0]
531	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH-	7/2016	/ (12/2017) [12/2019]	458.03 (-) [458.03]	325.89 (0.00) [-]
532	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I	12/2016	9/2021 (-) [9/2021]	196.00 (-) [196.00]	0.00 (0.00) [0]
	Steel				
533	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	5/2015	12/2017 (11/2019) [1/2020]	1,154.18 (-) [1,154.18]	978.83 (0.00) [25]
534	NEW SINTER PLANT AT BOKARO STEEL PLANT	3/2015	10/2017 (6/2020) [6/2020]	1,034.01 (-) [1,034.01]	447.34 (0.00) [32]
535	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	11/2016	6/2019 (6/2020) [6/2020]	262.87 (-) [262.87]	130.11 (0.00) [12]
	Urban Development				

536	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	9/2012	3/2016 (-) [9/2020]	171.86 (-) [171.86]	89.53 (0.00) [54]
537	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT	12/2007	3/2018 (-) [0/0]	200.00 (-) [200.00]	131.15 (0.00) [0]
538	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY	4/2013	4/2018 (-) [0/0]	170.00 (-) [170.00]	88.91 (0.00) [0]
539	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII	2/2014	12/2016 (-) [0/0]	787.29 (-) [787.29]	285.30 (0.00) [0]
540	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTEINANCE UNDER PMGSY-JHARKHAND	12/2007	6/2016 (-) [0/0]	253.92 (253.92) [253.92]	193.97 (0.00) [0]
	KARNATAKA				
	Petroleum				
541	BSVI UPGRADATION	9/2016	12/2019 (7/2020) [7/2020]	1,810.00 (1,810.00) [1,810.00]	940.45 (0.00) [7]
542	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU	5/2015	4/2019 (-) [0/0]	224.00 (207.00) [185.00]	164.61 (-39.00) [0]
543	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE	12/2018	12/2022 (-) [12/2022]	854.00 (-) [854.00]	38.34 (0.00) [0]
544	GAIL GAS LTD BENGALURU CGD PROJECT	2/2015	2/2020 (-) [2/2020]	749.00 (-) [842.00]	606.89 (93.00) [0]
545	HASSAN CHERLAPALLI LPG PIPELINE	6/2019	6/2022 (-) [6/2022]	2,166.38 (-) [2,166.38]	15.61 (0.00) [0]
546	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE	10/2015	3/2019 (10/2019) [10/2019]	135.00 (170.70) [170.70]	156.65 (35.70) [0]
547	RESITEMENT OF RAICHUR DEPOT TO GULBARGA	10/2018	3/2021 (-) [3/2021]	206.26 (-) [206.26]	2.84 (0.00) [0]
548	SEA WATER DESALINATION PLANT	11/2017	3/2020 (11/2020) [11/2020]	581.00 (-) [621.00]	102.99 (40.00) [8]
549	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	1/2006	1/2012 (-) [0/0]	993.00 (-) [1,693.00]	1,549.85 (700.00) [0]
	Power				
550	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B)	5/2017	2/2019 (12/2019) [3/2020]	445.89 (-) [445.89]	295.78 (0.00) [13]
	Railways				
551	ARSIKERE-TUMKUR	3/2015	3/2020 (-) [3/2020]	578.00 (578.00) [578.00]	525.85 (0.00) [0]
552	BAGALKOT-KUDACHI NL	4/2010	3/2016 (-) [12/2023]	986.30 (986.30) [986.30]	302.38 (0.00) [93]
553	BANGLORE - SATYAMANGALAM (NL)(SWR)	4/1996	3/2002 (-) [3/2024]	1,382.78 (1,382.78) [1,382.78]	7.35 (0.00) [264]
554	CHIKBALLA-PUR-GOWRIBIDANUR NL	4/2013	/ (-) [12/2023]	327.25 (367.77) [367.77]	0.00 (40.52) [-]

555	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL	4/2013	/ (-) [12/2023]	558.00 (692.43) [692.43]	0.00 (134.43) [-]
556	GADAG-WADI NL	4/2013	12/2018 (-) [12/2024]	2,841.84 (2,841.84) [2,841.84]	169.45 (0.00) [72]
557	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	4/2010	3/2023 (-) [3/2024]	2,127.00 (-) [2,900.00]	1,737.30 (773.00) [12]
558	HUBLI- CHIKJAJUR	3/2015	3/2020 (-) [3/2021]	1,156.94 (1,140.94) [1,140.94]	773.28 (-16.00) [12]
559	HUBLI-ANKOLA(NL),SWR	4/1997	/ (-) [12/2024]	2,315.00 (-) [2,315.00]	149.76 (0.00) [-]
560	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	3/1996	3/2017 (-) [3/2020]	644.78 (644.78) [890.00]	443.52 (245.22) [36]
561	MARIKUPPAM - KUPPAM	4/2012	3/2016 (-) [12/2023]	279.54 (279.54) [279.54]	30.34 (0.00) [93]
562	SHIMOGA-HARIHAR NL	4/2011	3/2016 (-) [3/2024]	832.47 (832.47) [832.47]	0.94 (0.00) [96]
563	TORANAGALLU-RANJITPURA DL	4/2011	/ (-) [12/2023]	146.75 (146.75) [167.50]	0.34 (20.75) [-]
564	TUMKUR-CHITRADURGA-DAVENGERE NL	4/2011	/ (-) [12/2023]	1,801.01 (1,801.01) [1,801.01]	48.41 (0.00) [-]
565	WHITE FIELD-KOLAR NL	4/2011	/ (-) [12/2023]	348.85 (348.85) [348.85]	0.36 (0.00) [-]
	Road Transport And Highways				
566	HOSPET-BELLARY-KARNATAKA AP BORDER	8/2016	3/2019 (3/2017) [8/2020]	1,167.42 (870.00) [870.00]	265.48 (-297.42) [17]
567	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM	2/2018	/ (-) [0/0]	486.78 (-) [486.78]	113.59 (0.00) [0]
568	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	5/2014	8/2016 (-) [12/2020]	1,655.01 (-) [1,655.01]	1,867.51 (0.00) [52]
569	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	3/2016	3/2019 (-) [11/2020]	701.40 (-) [701.40]	29.48 (0.00) [20]
570	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL	3/2016	3/2019 (-) [11/2020]	870.00 (-) [870.00]	36.30 (0.00) [20]
571	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION	2/2017	5/2019 (-) [5/2021]	157.32 (188.00) [157.32]	0.00 (0.00) [24]
572	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT	5/2018	5/2018 (-) [5/2020]	171.60 (-) [171.60]	0.86 (0.00) [24]
573	FOUR LANING OF HOSPET - CHITRADURGA	3/2015	8/2018 (-) [3/2020]	1,388.00 (-) [1,388.00]	1,185.00 (0.00) [19]
574	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB	8/2016	4/2020 (-) [4/2020]	1,664.20 (-) [1,664.20]	721.93 (0.00) [0]

575	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	9/2010	6/2018 (-) [12/2019]	946.00 (-) [946.00]	818.53 (0.00) [18]
576	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN	3/2018	10/2018 (-) [0/0]	325.86 (-) [325.86]	62.54 (0.00) [0]
577	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH	8/2016	2/2017 (-) [0/0]	175.50 (-) [175.50]	86.54 (0.00) [0]
578	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2	3/2018	6/2019 (-) [0/0]	159.97 (-) [159.97]	0.00 (0.00) [0]
579	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM.	1/2014	8/2014 (-) [0/0]	471.16 (-) [471.16]	128.32 (0.00) [0]
580	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	1/1991	1/2018 (-) [0/0]	219.40 (-) [219.40]	0.00 (0.00) [0]
581	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O	3/2017	3/2020 (-) [6/2020]	993.16 (-) [1,434.00]	695.33 (440.84) [3]
582	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	3/2017	3/2020 (-) [7/2020]	831.58 (-) [1,177.00]	657.59 (345.42) [4]
583	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA	2/2018	/ (10/2019) [0/0]	2,177.80 (2,283.50) [2,450.00]	898.52 (272.20) [0]
584	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT	2/2018	/ (5/2019) [11/2021]	1,995.34 (2,190.00) [2,400.00]	1,558.83 (404.66) [-]
585	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	3/2015	11/2015 (-) [0/0]	165.67 (-) [165.67]	0.00 (0.00) [0]
586	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU	3/2015	11/2015 (-) [0/0]	159.12 (-) [159.12]	0.00 (0.00) [0]
587	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	9/2016	8/2019 (-) [12/2020]	950.69 (1,008.00) [1,108.00]	1,385.71 (157.31) [16]
588	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN	10/2016	3/2017 (-) [0/0]	396.96 (-) [396.96]	113.98 (0.00) [0]
589	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT	11/2016	3/2017 (-) [0/0]	314.90 (-) [314.90]	104.40 (0.00) [0]
590	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT	8/2016	1/2017 (-) [0/0]	367.44 (-) [367.44]	61.95 (0.00) [0]
591	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT	8/2016	2/2017 (-) [0/0]	329.01 (-) [329.01]	135.50 (0.00) [0]
592	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR	9/2017	10/2018 (-) [0/0]	191.60 (-) [191.60]	26.24 (0.00) [0]
593	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U	1/2017	8/2017 (-) [0/0]	291.49 (-) [291.49]	130.00 (0.00) [0]
594	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA	1/2017	9/2017 (-) [0/0]	166.67 (-) [166.67]	117.05 (0.00) [0]
595	WIDENING TO TWO LANE WITH PAVED SHOULDERS	8/2016	1/2017	175.20	113.38

	FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT		(-) [0/0]	(-) [175.20]	(0.00) [0]
596	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH-	12/2017	1/2019 (-) [0/0]	297.30 (-) [297.30]	0.00 (0.00) [0]
597	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION	1/2018	7/2018 (-) [0/0]	159.70 (-) [159.70]	22.79 (0.00) [0]
598	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776)	3/2015	1/2016 (-) [0/0]	165.67 (-) [165.67]	87.63 (0.00) [0]
599	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775)	3/2015	1/2016 (-) [0/0]	159.12 (-) [159.12]	96.22 (0.00) [0]
	Urban Development				
600	BANGALORE METRO RAIL PROJECT PHASE-2	2/2014	2/2019 (-) [3/2020]	26,405.14 (-) [26,405.14]	499.85 (0.00) [13]
601	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	5/2005	2/2014 (-) [0/0]	768.88 (1,070.97) [1,113.34]	1,085.64 (344.46) [0]
602	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA	7/2011	12/2015 (-) [0/0]	324.87 (324.87) [324.87]	262.93 (0.00) [0]
603	RESIDENTIAL QUATERS FOR HAL,BANGLORE	12/2016	2/2020 (-) [9/2020]	246.31 (-) [246.31]	80.34 (0.00) [7]
	KERALA				
	Petroleum				
604	KOCHI SALEM LPG PIPELINE PROJECT	12/2015	6/2019 (2/2022) [2/2022]	1,112.00 (1,507.24) [1,507.24]	555.00 (395.24) [32]
605	LPG TERMINAL AT KOCHI	10/2015	10/2017 (-) [0/0]	607.06 (-) [714.25]	356.46 (107.19) [0]
606	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY	2/2016	2/2020 (10/2020) [10/2020]	3,313.00 (3,288.96) [3,288.96]	1,349.99 (-24.04) [8]
607	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	11/2014	8/2018 (11/2019) [12/2019]	4,588.29 (5,245.96) [5,245.96]	3,877.61 (657.67) [16]
608	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC	9/2018	3/2023 (-) [3/2023]	11,130.00 (-) [11,130.00]	54.40 (0.00) [0]
	Railways				
609	ANGAMALI-SABARIMALA (N.L.)(SR)	10/1998	/ (-) [0/0]	1,566.00 (-) [2,815.62]	264.28 (1,249.62) [0]
610	ERNAKULAM-KUMBALAM	4/2010	/ (-) [0/0]	189.24 (-) [189.24]	6.72 (0.00) [0]
611	KUMBALAM-TURAVUR	4/2011	/ (-) [0/0]	252.96 (-) [252.96]	8.50 (0.00) [0]
612	PALAKKAD - SETTING UP OF RAIL COACH FACTORY	2/2012	3/2016 (-) [0/0]	550.00 (-) [550.00]	0.00 (0.00) [0]
613	TRIVANDRUM-KANYAKUMARI DOUBLING	2/2015	/ (-) [0/0]	1,431.90 (-) [1,431.90]	75.00 (0.00) [0]
614	TURAVUR-AMBALAPUZHA DOUBLING	2/2015	/	1,000.00	0.08

			(-) [0/0]	(-) [828.50]	(-171.50) [0]
	Road Transport And Highways				
615	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47	6/2015	/ (-) [1/2020]	845.24 (-) [941.00]	847.81 (95.76) [-]
616	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	4/2016	6/2018 (-) [4/2020]	804.97 (-) [804.97]	456.79 (0.00) [22]
617	4-LANNING OF THALSERRY -MAHE BYPASS	9/2017	9/2017 (-) [6/2020]	1,124.11 (-) [1,232.76]	292.23 (108.65) [33]
618	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	2/2018	/ (-) [0/0]	1,424.77 (-) [1,853.42]	14.19 (428.65) [0]
619	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1	1/2014	9/2017 (-) [12/2019]	255.75 (348.00) [348.43]	290.12 (92.68) [27]
620	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	2/2010	8/2012 (-) [12/2019]	617.00 (-) [617.00]	943.17 (0.00) [88]
	Urban Development				
621	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITIUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST	9/2017	3/2020 (11/2020) [3/2021]	150.29 (-) [150.29]	21.82 (0.00) [12]
622	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	1/2010	10/2012 (-) [3/2020]	165.23 (-) [165.23]	94.62 (0.00) [89]
623	KOCHI METRO RAIL PROJECT	7/2012	7/2017 (-) [3/2020]	5,181.79 (5,687.79) [5,687.79]	5,656.62 (506.00) [32]
	MADHYA PRADESH				
	Coal				
624	AMADAND OPENCAST EXPANSION PROJECT	3/2016	3/2021 (-) [3/2021]	869.44 (-) [869.44]	116.75 (0.00) [0]
625	AMRITDHARA OC PROJECT	2/2015	3/2023 (-) [3/2023]	481.60 (-) [481.60]	0.00 (0.00) [0]
626	BATURA HIGHWALL PROJECT	7/2015	3/2022 (-) [3/2022]	231.92 (-) [231.92]	0.00 (0.00) [0]
627	BATURA OCP (2.0 MTY)	8/2015	3/2023 (-) [3/2021]	1,186.64 (-) [203.82]	123.05 (-982.82) [-24]
628	BLOCK-B EXPANSION OPENCAST PROJECT	7/2019	3/2023 (-) [3/2023]	998.71 (-) [998.71]	0.00 (0.00) [0]
629	COAL PROJECT NAME JAMUNIA UG (0.84 MTY)	7/2016	3/2022 (-) [3/2022]	409.87 (-) [409.87]	19.05 (0.00) [0]
630	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA)	11/2017	3/2022 (-) [3/2022]	1,255.17 (-) [1,255.17]	95.24 (0.00) [0]
631	GANDHIGRAM UG MINE	8/2019	3/2026 (-) [3/2026]	414.16 (-) [414.16]	0.01 (0.00) [0]
632	JAYANT EXPANSION OCP 10 TO 20 MTPA	5/2017	3/2021 (-) [3/2021]	1,783.09 (-) [1,783.09]	267.80 (0.00) [0]
633	KANCHAN OC EXPANSION	12/2014	3/2021	371.04	48.13

			(-) [3/2021]	(-) [371.04]	(0.00) [0]
634	MALACHUA OPENCAST PROJECT	10/2015	3/2023 (-) [3/2023]	488.33 (-) [488.33]	27.33 (0.00) [0]
635	RAJNAGAR OCP RPR (1.70 MTY)	12/2014	3/2021 (-) [3/2021]	357.80 (-) [357.80]	104.66 (0.00) [0]
636	SEMARIA OPENCAST PROJECT	5/2019	3/2026 (-) [3/2026]	396.58 (-) [396.58]	0.00 (0.00) [0]
637	VISHNUPURI UG TO OC MINE	7/2018	3/2025 (-) [3/2025]	195.57 (-) [195.57]	2.94 (0.00) [0]
	Petroleum				
638	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND	8/2017	6/2020 (-) [8/2020]	236.00 (-) [236.00]	30.20 (0.00) [2]
	Power				
639	AMELIA COAL MINE	1/2017	9/2020 (-) [9/2020]	2,104.21 (-) [1,587.16]	308.34 (-517.05) [0]
640	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	3/2013	1/2018 (3/2020) [3/2020]	11,638.55 (-) [12,865.92]	12,361.29 (1,227.37) [26]
641	KHARGONE STPP STAGE I (1320 MW)	3/2015	1/2020 (-) [2/2020]	9,870.51 (-) [11,148.86]	9,055.78 (1,278.35) [1]
	Railways				
642	ANUPPUR-KATNI	4/2015	12/2021 (11/2022) [11/2022]	1,370.00 (1,370.94) [1,370.94]	311.76 (0.94) [11]
643	BINA - KOTA DOUBLING WITH RE	4/2011	12/2020 (-) [3/2021]	1,485.85 (-) [1,485.85]	1,158.89 (0.00) [3]
644	CHHINDWARA - NAGPUR (GC)(SECR)	4/2005	/ (1/2020) [1/2020]	383.79 (1,473.76) [1,413.76]	1,351.73 (1,029.97) [-]
645	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	4/2010	2/2019 (12/2020) [12/2020]	585.93 (1,268.32) [1,268.32]	669.57 (682.39) [22]
646	INDORE-DEWAS-UJJAIN (80 KMS)	4/2016	6/2020 (6/2021) [6/2021]	700.00 (603.69) [603.69]	113.47 (-96.31) [12]
647	KATNI - SINGRAULI DOUBLING PROJECT	12/2015	3/2020 (3/2023) [3/2023]	1,763.93 (-) [1,762.94]	847.47 (-0.99) [36]
648	KATNI GRADE SEPARATOR/BYE PASS	8/2016	3/2022 (9/2022) [9/2022]	582.13 (-) [1,247.64]	152.01 (665.51) [6]
649	KATNI-BINA 3RD LINE (263 KM)	6/2016	3/2022 (-) [3/2023]	2,478.23 (-) [2,478.23]	477.93 (0.00) [12]
650	MULTI MODAL LOGISTICS PARK AT TIHI	12/2015	3/2019 (-) [2/2020]	174.00 (-) [174.00]	152.48 (0.00) [11]
651	RAMGANJMUNDI-BHOPAL (NL),WCR	4/2001	3/2021 (-) [3/2023]	424.60 (-) [2,909.99]	1,975.34 (2,485.39) [24]
652	RATLAM-MHOW-KHANDWA-AKOLA (GC)	4/2008	3/2022 (3/2023)	3,503.69 (3,975.22)	1,758.23 (471.53)

			[3/2023]	[3,975.22]	[12]
	Road Transport And Highways				
653	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP	3/2018	11/2019 (-) [6/2020]	191.21 (-) [191.21]	72.02 (0.00) [7]
654	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	11/2017	7/2018 (-) [3/2020]	249.05 (-) [249.05]	127.30 (0.00) [20]
655	ANJANGAON TO MAH/MP BORDER	1/2017	6/2019 (-) [0/0]	359.00 (359.00) [359.00]	201.80 (0.00) [0]
656	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN	12/2017	/ (-) [0/0]	950.27 (-) [950.27]	168.05 (0.00) [0]
657	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM.	11/2017	3/2018 (-) [6/2020]	392.33 (-) [392.33]	242.88 (0.00) [27]
658	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION	8/2016	1/2019 (-) [12/2019]	227.49 (-) [227.49]	129.93 (0.00) [11]
659	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12	9/2017	9/2017 (-) [0/0]	374.40 (218.85) [204.65]	155.83 (-169.75) [0]
660	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69	9/2017	9/2017 (-) [1/2021]	990.61 (-) [990.61]	397.89 (0.00) [40]
661	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP	8/2015	/ (-) [0/0]	257.80 (-) [257.00]	12.38 (-0.80) [0]
662	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A	6/2015	/ (-) [3/2020]	390.51 (-) [390.51]	198.91 (0.00) [-]
663	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V	12/2017	/ (-) [0/0]	656.98 (-) [656.98]	2.48 (0.00) [0]
664	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA	10/2019	/ (-) [0/0]	743.88 (-) [743.88]	0.00 (0.00) [0]
665	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA	12/2017	/ (-) [0/0]	1,094.97 (-) [1,094.97]	1.51 (0.00) [0]
666	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM	12/2017	/ (-) [0/0]	217.96 (-) [217.96]	0.50 (0.00) [0]
667	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH.	1/2017	3/2017 (-) [6/2020]	205.05 (-) [205.05]	79.65 (0.00) [39]
668	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD	1/2019	3/2021 (-) [3/2021]	264.50 (-) [264.50]	0.00 (0.00) [0]
669	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR	6/2015	1/2019 (10/2019) [10/2019]	1,583.79 (-) [1,583.79]	1,648.90 (0.00) [0]
670	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO	1/2018	/ (-) [0/0]	960.24 (-) [960.24]	328.34 (0.00) [0]
671	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA	6/2015	3/2016 (-) [0/0]	1,012.90 (-) [1,012.90]	226.10 (0.00) [0]
672	FOUR LANING OF GWALIOR-SHIVPURI	5/2013	11/2015 (-)	1,055.00 (-)	1,393.40 (546.77)

			[0/0]	[1,601.77]	[0]
673	FOUR LANING OF JABALPUR - LAKHNADON	3/2015	/ (6/2015) [6/2015]	928.83 (-) [928.83]	630.61 (0.00) [0]
674	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I	3/2015	/ (-) [12/2019]	794.30 (622.00) [622.00]	592.72 (-172.30) [-]
675	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II	3/2015	/ (-) [12/2019]	795.76 (622.00) [622.00]	638.13 (-173.76) [-]
676	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV	3/2015	/ (6/2015) [6/2015]	810.22 (-) [810.22]	695.69 (0.00) [0]
677	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124.	10/2017	10/2017 (-) [1/2020]	639.97 (-) [639.97]	331.84 (0.00) [27]
678	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER	1/2018	/ (-) [0/0]	770.73 (-) [770.73]	59.45 (0.00) [0]
679	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93	12/2015	2/2020 (-) [2/2020]	957.54 (-) [957.54]	503.38 (0.00) [0]
680	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	11/2013	5/2017 (-) [5/2020]	497.05 (-) [881.05]	544.84 (384.00) [36]
681	INDORE-DEWAS(NH-3)	11/2010	5/2013 (-) [0/0]	325.00 (-) [475.00]	469.54 (150.00) [0]
682	INDORE-JHABUA-GUJRAT/MP	10/2010	4/2013 (-) [0/0]	1,175.00 (-) [1,175.00]	1,509.96 (0.00) [0]
683	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400	11/2015	1/2020 (-) [1/2020]	628.45 (-) [628.45]	259.33 (0.00) [0]
684	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	1/2012	4/2015 (-) [10/2019]	410.72 (-) [410.72]	216.14 (0.00) [0]
685	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA	2/2018	3/2018 (-) [7/2020]	169.63 (-) [169.63]	11.39 (0.00) [28]
686	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86	9/2016	9/2018 (-) [8/2019]	178.23 (-) [178.23]	114.16 (0.00) [0]
687	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175	9/2016	1/2019 (-) [12/2019]	287.34 (-) [287.34]	148.65 (0.00) [11]
688	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM	3/2016	6/2019 (-) [12/2020]	877.79 (-) [877.79]	436.12 (0.00) [18]
689	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID	11/2017	2/2018 (-) [3/2020]	235.91 (-) [235.91]	144.76 (0.00) [25]
690	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS	1/2016	7/2018 (-) [2/2020]	809.16 (-) [809.16]	236.96 (0.00) [19]
691	SATANA-BELA SECTION OF NH-75(4L) IN MP	1/2012	8/2015 (-) [0/0]	320.48 (-) [320.48]	189.49 (0.00) [0]
692	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	11/2011	9/2015 (-) [3/2020]	954.43 (-) [954.43]	235.61 (0.00) [54]

693	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	3/2015	8/2017 (-) [2/2020]	511.83 (-) [511.83]	261.31 (0.00) [30]
694	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS	11/2017	2/2018 (-) [3/2020]	254.17 (-) [254.17]	152.81 (0.00) [25]
695	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS	3/2018	3/2018 (-) [3/2020]	233.04 (-) [233.04]	109.26 (0.00) [24]
696	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS	2/2018	3/2018 (-) [4/2020]	279.44 (-) [279.44]	76.00 (0.00) [25]
697	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS	3/2018	8/2018 (-) [6/2020]	166.21 (-) [166.21]	40.28 (0.00) [22]
698	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS	11/2017	2/2018 (-) [3/2020]	184.62 (-) [184.62]	65.06 (0.00) [25]
699	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	3/2018	3/2018 (-) [6/2020]	214.69 (-) [214.69]	25.88 (0.00) [27]
700	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS	3/2018	8/2018 (-) [6/2020]	217.22 (-) [217.22]	45.76 (0.00) [22]
701	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS	3/2018	3/2018 (-) [3/2020]	162.56 (-) [162.56]	88.47 (0.00) [24]
702	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A	1/2017	9/2019 (-) [5/2020]	373.82 (-) [373.82]	116.34 (0.00) [8]
	Urban Development				
703	BHOPAL METRO RAIL	11/2018	2/2023 (-) [2/2023]	6,941.40 (-) [6,941.40]	41.94 (0.00) [0]
704	INDORE METRO RAIL	11/2018	2/2023 (-) [2/2023]	7,500.80 (-) [7,500.80]	45.70 (0.00) [0]
	MAHARASHTRA				
	Civil Aviation				
705	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT	3/2017	4/2021 (-) [4/2021]	358.89 (-) [358.89]	29.73 (0.00) [0]
	Coal				
706	ADASA UG TO OC	8/2015	3/2023 (-) [3/2024]	288.90 (-) [333.43]	27.21 (44.53) [12]
707	AMALGAMATED GONDEGAON GHATROHAN OC	2/2016	3/2019 (-) [0/0]	198.68 (-) [198.68]	185.01 (0.00) [0]
708	AMALGAMATED PAUNI-II III OC MINE	6/2015	3/2021 (-) [3/2021]	483.69 (-) [483.69]	219.00 (0.00) [0]
709	AMALGAMATED YEKONA-I YEKONA-II	8/2015	3/2025 (-) [3/2025]	727.28 (-) [727.28]	260.88 (0.00) [0]
710	BELLORA-NAIGAON DEEP OC	11/2018	3/2021 (-) [3/2021]	252.71 (-) [252.71]	45.09 (0.00) [0]
711	BHANEGAON OC	2/2015	3/2023 (-) [3/2023]	187.94 (-) [409.68]	127.70 (221.74) [0]

712	BHATADI EXPANSION OC MINE	2/2016	3/2019 (-) [0/0]	304.52 (-) [304.52]	153.54 (0.00) [0]
713	DINESH OCP	11/2014	3/2020 (-) [3/2020]	611.16 (-) [611.16]	413.02 (0.00) [0]
714	GAURI DEEP OC	10/2016	3/2019 (-) [0/0]	164.96 (-) [164.96]	93.86 (0.00) [0]
715	KAMPTEE DEEP OC MINE	11/2015	3/2021 (-) [3/2024]	277.65 (-) [313.34]	117.85 (35.69) [36]
716	KOLAR PIMPRI EXTENSION OC	3/2017	3/2020 (-) [3/2020]	362.73 (-) [362.73]	322.07 (0.00) [0]
717	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE	11/2015	3/2020 (-) [3/2020]	498.42 (-) [498.42]	189.52 (0.00) [0]
718	NEW MAJRI UG TO OC	5/2015	3/2019 (-) [0/0]	295.56 (-) [295.56]	120.81 (0.00) [0]
719	PENGANGA OCP(REVISED)	9/2014	3/2020 (-) [3/2020]	441.82 (-) [441.82]	215.48 (0.00) [0]
720	SAONER I UG TO OC PHASE I	11/2016	3/2022 (-) [3/2022]	162.10 (-) [162.10]	50.64 (0.00) [0]
721	SINGHORI OC MINE	6/2015	3/2020 (-) [3/2020]	205.49 (-) [205.49]	117.56 (0.00) [0]
722	UKNI DEEP OC	11/2018	3/2021 (-) [3/2021]	318.14 (-) [318.14]	143.90 (0.00) [0]
	Fertilisers				
723	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	4/2018	4/2020 (-) [4/2020]	426.72 (-) [426.72]	249.06 (0.00) [0]
724	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	11/2016 (-) [9/2019]	197.79 (-) [209.44]	185.68 (11.65) [0]
	Health And Family Welfare				
725	HOSPITAL AND TEACHING- AIIMS NAGPUR	3/2018	/ (-) [6/2020]	582.99 (-) [582.99]	211.20 (0.00) [-]
726	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA	8/2017	3/2019 (-) [3/2020]	274.19 (-) [274.19]	241.58 (0.00) [12]
	Information And Broadcasting				
727	NATIONAL CENTRE OF EXCELLENCE FOR ANIMATION VISUAL EFFECTS GAMING AND COMICS	12/2016	3/2020 (-) [3/2020]	167.70 (-) [167.70]	0.00 (0.00) [0]
728	NATIONAL FILM HERITAGE MISSION	11/2014	/ (-) [0/0]	597.41 (-) [597.41]	29.80 (0.00) [0]
	Petroleum				
729	180 TMTPA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA	6/2017	6/2020 (-) [9/2021]	249.26 (-) [249.26]	60.45 (0.00) [15]
730	4TH PHASE DEVELOPMENT OF NBP FIELD	2/2017	11/2019 (-) [11/2019]	968.61 (-) [1,033.95]	968.11 (65.34) [0]

731	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI	5/2016	1/2021 (-) [1/2021]	261.00 (-) [261.00]	52.11 (0.00) [0]
732	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [4/2021]	212.00 (-) [212.00]	46.99 (0.00) [3]
733	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [10/2021]	348.00 (-) [348.00]	37.01 (0.00) [9]
734	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	3/2011	5/2013 (12/2019) [12/2019]	861.79 (-) [1,683.06]	1,356.33 (821.27) [79]
735	DEVELOPMENT OF B-147 FIELD	2/2017	11/2019 (3/2020) [3/2020]	546.15 (565.15) [565.15]	449.96 (19.00) [4]
736	DEVELOPMENT OF BSE-11 BLOCK	2/2017	11/2019 (-) [11/2019]	511.30 (-) [511.30]	523.88 (0.00) [0]
737	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION	2/2019	5/2021 (-) [5/2021]	2,292.46 (-) [2,292.46]	402.18 (0.00) [0]
738	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	2/2017	5/2021 (12/2021) [12/2021]	4,006.83 (-) [4,475.92]	2,869.89 (469.09) [7]
739	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA	1/2015	12/2017 (3/2020) [3/2020]	4,619.94 (-) [4,619.94]	4,444.58 (0.00) [27]
740	HEERA REDEVELOPMENT - PHASE III	5/2019	12/2021 (-) [3/2022]	2,494.68 (-) [2,494.68]	48.07 (0.00) [3]
741	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY	2/2016	2/2020 (-) [2/2020]	554.00 (-) [554.00]	375.80 (0.00) [0]
742	INTEGRATED DEVELOPMENT OF B-127 FIELDS	12/2011	3/2015 (12/2019) [12/2019]	2,059.63 (2,665.65) [2,665.65]	1,932.09 (606.02) [57]
743	KOYALI AHMEDNAGAR SOLAPUR PIPELINE	5/2016	8/2021 (-) [8/2021]	1,945.00 (-) [1,945.00]	1,004.75 (0.00) [0]
744	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	12/2015	4/2018 (5/2020) [5/2020]	3,190.69 (-) [3,247.19]	2,298.77 (56.50) [25]
745	MMPL PIPELINE REROUTING PROJECT	4/2013	12/2019 (7/2020) [7/2020]	449.58 (-) [449.58]	192.13 (0.00) [7]
746	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	4/2019	3/2022 (-) [3/2022]	3,228.80 (-) [3,228.80]	497.01 (0.00) [0]
747	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III	11/2014	4/2019 (12/2019) [12/2019]	6,068.80 (-) [5,296.93]	4,767.31 (-771.87) [8]
748	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV	2/2019	4/2021 (-) [5/2021]	3,660.71 (3,740.05) [3,740.05]	274.07 (79.34) [1]
749	MUMBAI REFINERY EXPANSION PROJECT	9/2015	3/2020 (-) [3/2020]	4,199.00 (5,060.00) [5,060.00]	3,071.60 (861.00) [0]
750	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY	8/2015	3/2019 (5/2020) [5/2020]	2,818.88 (-) [2,818.88]	2,302.10 (0.00) [14]
751	PIPELINE REPLACEMENT PROJECT (PRP-VI)	5/2019	12/2020	763.92	116.82

			(-) [12/2020]	(-) [763.92]	(0.00) [0]
752	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE)	4/2018	12/2019 (-) [12/2019]	766.37 (-) [766.37]	465.86 (0.00) [0]
753	PUNE POL STORAGE DEPOT	8/2016	8/2020 (-) [8/2020]	282.64 (-) [282.64]	145.83 (0.00) [0]
	Power				
754	MOUDA STPP STAGE 2	3/2012	9/2016 (-) [0/0]	7,921.47 (-) [7,921.47]	5,302.00 (0.00) [0]
	Railways				
755	3RD LINE BETWEEN BHUSAWAL-JALGAON	4/2011	3/2019 (12/2019) [12/2019]	184.06 (199.12) [312.00]	275.98 (127.94) [9]
756	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	2/1997	3/2021 (-) [3/2022]	2,271.50 (-) [3,712.50]	2,434.24 (1,441.00) [12]
757	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	3/1996	3/2004 (-) [3/2021]	495.44 (1,781.98) [2,980.41]	1,431.38 (2,484.97) [204]
758	DAUND - MANMAD (236 KM)	2/2016	3/2023 (-) [3/2023]	1,876.00 (-) [2,081.27]	187.09 (205.27) [0]
759	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	3/2009	3/2020 (-) [3/2021]	713.48 (-) [2,300.00]	2,056.99 (1,586.52) [12]
760	DIGHI PORT NEW LINE	4/2015	12/2025 (-) [3/2025]	723.78 (-) [723.78]	0.19 (0.00) [-9]
761	INDORE - MANMAD VIA MALEGAON (368 KM)	2/2016	3/2024 (-) [3/2024]	9,968.00 (-) [9,968.00]	0.00 (0.00) [0]
762	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	2/2015	3/2023 (-) [3/2023]	2,449.91 (-) [2,449.91]	180.76 (0.00) [0]
763	KALYAN-KASARA 3RD LINE	4/2011	3/2021 (-) [3/2022]	792.89 (-) [1,377.48]	316.79 (584.59) [12]
764	MANMAD - JALGAON - 3RD LINE (160 KM)	2/2016	3/2022 (-) [3/2024]	1,035.16 (-) [1,035.16]	117.02 (0.00) [24]
765	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN	10/2013	3/2019 (-) [12/2019]	305.00 (-) [305.00]	261.28 (0.00) [9]
766	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM	3/2010	/ (-) [0/0]	265.88 (-) [265.88]	0.00 (0.00) [0]
767	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	4/2008	3/2014 (-) [3/2021]	5,300.00 (-) [918.53]	284.75 (-4,381.47) [84]
768	PUNE-MIRAJ-LONDA (467 KM)	2/2015	3/2024 (-) [3/2023]	3,627.47 (3,627.00) [3,627.47]	761.03 (0.00) [-12]
769	PUNE-NASIK (265 KM)	2/2016	3/2024 (-) [3/2024]	2,425.00 (-) [5,341.68]	0.00 (2,916.68) [0]
770	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	9/2016	3/2023 (3/2023) [3/2023]	1,908.51 (2,686.63) [2,686.63]	515.29 (778.12) [0]

771	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	4/2012	4/2016 (-) [0/0]	714.10 (-) [714.10]	65.20 (0.00) [0]
772	VAIBHAVWADI -KOLHAPUR (107 KM)	2/2016	3/2024 (-) [0/0]	2,750.00 (-) [3,438.51]	0.00 (688.51) [0]
773	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A	3/2012	/ (-) [0/0]	217.38 (-) [217.38]	0.00 (0.00) [0]
774	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	6/2018	12/2021 (3/2023) [3/2023]	229.00 (852.50) [852.50]	39.69 (623.50) [15]
775	WARDHA - NAGPUR - 4TH LINE (76 KM)	2/2016	3/2023 (-) [3/2024]	637.95 (-) [637.95]	73.16 (0.00) [12]
776	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	2/2015	3/2022 (-) [3/2023]	1,272.19 (-) [1,272.19]	319.94 (0.00) [12]
777	WARDHA-NANDED MAHARASHTRA	4/2008	3/2023 (-) [3/2023]	3,168.29 (-) [3,168.29]	1,202.21 (0.00) [0]
778	WARDHA-SEWAGRAM NGP 3RD LINE	4/2012	3/2022 (-) [3/2024]	540.02 (-) [540.02]	252.82 (0.00) [24]
	Road Transport And Highways				
779	4 LANING OF AMRAVATI - CHIKHLI (PKG-I)	7/2015	5/2019 (-) [0/0]	2,288.18 (-) [2,288.18]	487.81 (0.00) [0]
780	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3)	7/2015	5/2019 (-) [0/0]	1,885.74 (-) [1,885.74]	1,636.02 (0.00) [0]
781	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	1/2015	7/2017 (12/2019) [3/2020]	972.50 (-) [972.50]	3,512.79 (0.00) [32]
782	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104)	1/2018	/ (2/2019) [8/2021]	607.00 (512.99) [607.00]	163.98 (0.00) [-]
783	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000)	1/2018	/ (10/2018) [4/2021]	621.00 (565.02) [621.00]	327.15 (0.00) [-]
784	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION	6/2014	11/2016 (-) [5/2020]	923.04 (-) [923.04]	764.07 (0.00) [42]
785	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	3/2017	3/2020 (-) [3/2020]	744.64 (-) [982.00]	0.00 (237.36) [0]
786	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700)	11/2016	/ (-) [7/2021]	1,071.61 (-) [1,071.61]	404.89 (0.00) [-]
787	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	11/2016	3/2019 (-) [3/2021]	446.17 (-) [446.17]	38.97 (0.00) [24]
788	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575)	3/2017	3/2020 (-) [8/2020]	1,098.06 (-) [1,160.64]	1,056.76 (62.58) [5]
789	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [0/0]	1,142.62 (-) [1,142.62]	813.85 (0.00) [0]
790	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [0/0]	1,101.58 (-) [1,101.58]	315.00 (0.00) [0]

791	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI	11/2016	3/2019 (-) [2/2021]	400.25 (-) [400.25]	64.89 (0.00) [23]
792	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00)	11/2016	/ (-) [7/2021]	1,064.88 (-) [1,064.88]	0.00 (0.00) [-]
793	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	3/2017	3/2017 (5/2018) [11/2020]	1,059.73 (-) [1,071.00]	582.87 (11.27) [44]
794	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690)	3/2017	3/2020 (-) [5/2020]	1,030.44 (-) [1,065.51]	1,005.76 (35.07) [2]
795	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500)	3/2017	3/2020 (-) [8/2020]	988.34 (988.00) [1,043.28]	1,034.00 (54.94) [5]
796	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	8/2015	5/2018 (4/2019) [9/2020]	505.00 (-) [504.00]	235.19 (-1.00) [28]
797	AHMADPUR TO PIMPLA	1/2017	8/2019 (-) [8/2019]	422.38 (422.38) [422.38]	169.58 (0.00) [0]
798	AHMEDNAGAR TO BARAMATI	1/2017	8/2019 (-) [8/2019]	955.40 (-) [955.40]	347.50 (0.00) [0]
799	AKKALKOT TO DHUDHNI	4/2016	2/2019 (-) [2/2020]	211.42 (-) [211.42]	131.85 (0.00) [12]
800	AKOLA TO AKOT	1/2017	6/2019 (-) [0/0]	313.95 (-) [313.95]	41.05 (0.00) [0]
801	AKOT TO ANJANGAON	1/2017	6/2019 (-) [0/0]	245.77 (246.00) [245.77]	119.98 (0.00) [0]
802	AMDI TO SAONER	1/2017	6/2019 (-) [8/2019]	396.91 (396.91) [396.91]	254.48 (0.00) [0]
803	ARDHAPUR TO HIMAYATNAGAR	12/2017	6/2020 (-) [6/2020]	426.06 (426.00) [426.06]	66.97 (0.00) [0]
804	ARNI TO NAIGAINBANDI	12/2017	12/2019 (-) [12/2019]	309.94 (310.00) [309.94]	51.32 (0.00) [0]
805	AURANGABAD TO SILLOD	2/2017	6/2019 (-) [0/0]	456.32 (-) [456.32]	91.75 (0.00) [0]
806	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62	3/2016	7/2018 (-) [0/0]	197.69 (151.11) [197.69]	151.11 (0.00) [0]
807	BAMNI TO NAVAEGAON	9/2017	4/2020 (-) [4/2020]	241.69 (242.00) [241.69]	83.29 (0.00) [0]
808	BARASGAON TO RAHATEE	7/2016	9/2018 (-) [4/2021]	289.11 (290.00) [289.11]	23.82 (0.00) [31]
809	BHADGAON TO CHALISGAON	1/2018	11/2019 (-) [11/2019]	259.55 (260.00) [259.55]	145.00 (0.00) [0]
810	BHANDARA TO GHOTITOK	1/2017	6/2019 (-) [0/0]	392.83 (393.00) [392.83]	286.60 (0.00) [0]
811	BHOGAN KHURD TO KASHEDI	9/2017	6/2021	743.21	52.87

			(-) [6/2021]	(743.00) [743.21]	(0.00) [0]
812	BHOKAR TO SARSAM	2/2017	7/2019 (-) [0/0]	295.09 (-) [295.99]	162.64 (0.90) [0]
813	BODHWAD TO STATE BORDER	1/2017	7/2019 (-) [0/0]	178.26 (-) [178.26]	118.95 (0.00) [0]
814	CHALISGAON TO NANDGAON	3/2018	12/2019 (-) [12/2019]	206.97 (207.00) [206.97]	92.89 (0.00) [0]
815	CHIKALI TO DHAD	3/2018	12/2019 (-) [12/2019]	189.46 (189.00) [189.46]	35.54 (0.00) [0]
816	CHIKALI TO KHAMGAON	2/2017	6/2019 (-) [10/2019]	548.03 (548.00) [548.03]	319.00 (0.00) [0]
817	CHIKLI TO TAKARKHED	3/2018	12/2019 (-) [12/2019]	393.10 (393.10) [393.10]	153.97 (0.00) [0]
818	CHIMUR TO WARORA	11/2016	3/2019 (-) [0/0]	467.70 (-) [467.70]	156.72 (0.00) [0]
819	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF	3/2018	/ (-) [7/2021]	1,162.92 (-) [1,162.92]	14.76 (0.00) [-]
820	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	12/2015	3/2019 (4/2021) [4/2021]	649.50 (-) [649.50]	137.85 (0.00) [25]
821	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6)	3/2018	/ (11/2020) [11/2020]	291.53 (-) [291.53]	46.60 (0.00) [-]
822	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST	1/2017	5/2019 (-) [12/2019]	244.90 (-) [244.90]	251.87 (0.00) [7]
823	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6)	3/2018	/ (-) [11/2020]	289.21 (-) [289.21]	27.87 (0.00) [-]
824	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	10/2015	5/2018 (6/2020) [6/2020]	593.26 (41.54) [636.24]	461.85 (42.98) [25]
825	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION	12/2011	/ (-) [0/0]	156.26 (227.00) [247.95]	175.00 (91.69) [0]
826	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	10/2015	5/2018 (-) [9/2020]	531.13 (-) [727.00]	509.85 (195.87) [28]
827	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16)	3/2015	/ (-) [0/0]	168.30 (-) [168.30]	52.00 (0.00) [0]
828	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO	8/2014	7/2016 (-) [0/0]	187.79 (-) [187.79]	76.62 (0.00) [0]
829	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST	3/2017	3/2020 (2/2021) [2/2020]	247.02 (-) [157.49]	30.60 (-89.53) [-1]
830	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D	9/2015	5/2018 (5/2020) [5/2020]	414.51 (414.00) [414.00]	532.46 (-0.51) [24]
831	DAHEGAON TO KUHI	1/2017	6/2019 (-)	228.89 (228.89)	115.00 (0.00)

			[0/0]	[228.89]	[0]
832	DASTAPUR TO KARANJA	3/2018	12/2019 (-) [12/2019]	182.63 (-) [182.63]	82.40 (0.00) [0]
833	DEORI TO AMGAON	1/2017	5/2019 (-) [5/2020]	409.62 (410.00) [409.62]	181.78 (0.00) [12]
834	DEULGAON SAKARSHA TO MEHKAR	3/2018	12/2019 (-) [12/2019]	219.91 (-) [219.91]	126.76 (0.00) [0]
835	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000)	3/2017	3/2020 (-) [9/2019]	296.19 (-) [254.00]	254.85 (-42.19) [0]
836	DHAD BHOKARDAN TO BHOKARDHAN SILLOD	3/2018	12/2019 (-) [12/2019]	336.21 (336.00) [336.21]	71.66 (0.00) [0]
837	DHANGIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK	3/2018	2/2020 (-) [2/2020]	217.14 (217.00) [217.14]	99.77 (0.00) [0]
838	DIGRAS DARWAH KARANJA	1/2017	6/2019 (-) [6/2020]	391.06 (391.00) [391.06]	107.00 (0.00) [12]
839	FARDAPUR TO JALGAON	2/2017	6/2019 (-) [0/0]	456.45 (-) [456.45]	67.74 (0.00) [0]
840	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS	4/2010	6/2012 (-) [0/0]	1,170.52 (-) [1,170.52]	2,051.36 (0.00) [0]
841	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4	3/2018	/ (-) [12/2020]	642.13 (-) [807.00]	341.71 (164.87) [-]
842	FOUR LANING OF AURANGABAD - YEDISHI	7/2015	1/2018 (12/2018) [12/2019]	1,871.34 (67.34) [1,871.34]	3,512.79 (0.00) [23]
843	FOUR LANNING OF TULJAPUR-AUSA SECTION	2/2017	2/2020 (11/2017) [5/2020]	904.16 (911.07) [904.16]	854.25 (0.00) [3]
844	GADCHIROLI TO MUL	12/2016	6/2019 (-) [0/0]	484.15 (-) [484.15]	160.31 (0.00) [0]
845	HELWAK TO KARAD	2/2017	7/2019 (-) [0/0]	416.99 (-) [416.99]	127.40 (0.00) [0]
846	HIMAYATNAGAR TO PHULSAWANGI	3/2018	12/2019 (-) [12/2019]	294.87 (295.00) [294.87]	36.30 (0.00) [0]
847	INDAPAUR TO AGARDANDA	1/2017	7/2019 (-) [12/2019]	355.17 (-) [355.17]	164.87 (0.00) [5]
848	INDAPUR TO VADPALE	1/2017	12/2019 (-) [3/2020]	1,202.52 (1,202.52) [1,202.52]	635.90 (0.00) [3]
849	JAHIRABAD TO LATUR	1/2017	11/2019 (-) [11/2019]	461.96 (461.96) [461.96]	160.43 (0.00) [0]
850	JALGAON TO BHADGAON	1/2018	11/2019 (-) [11/2019]	307.54 (308.00) [307.54]	124.59 (0.00) [0]
851	JALGAON TO NANDURA	3/2018	12/2019 (-) [12/2019]	177.84 (177.00) [177.84]	73.69 (0.00) [0]

852	JALKOT TO TOGRI	7/2018	8/2020 (-) [8/2020]	299.92 (300.00) [299.92]	19.20 (0.00) [0]
853	JINTUR TO PARBHANI	1/2017	/ (-) [0/0]	356.66 (356.66) [356.66]	33.88 (0.00) [0]
854	KAIJ TO KUSALAM	1/2017	7/2019 (-) [7/2019]	554.78 (554.78) [554.78]	163.90 (0.00) [0]
855	KALMAB TO RALEGAON	1/2017	6/2019 (-) [0/0]	467.78 (-) [467.78]	301.91 (0.00) [0]
856	KALMATH TO ZARAP	9/2016	3/2020 (-) [3/2020]	1,338.13 (1,338.00) [1,338.13]	959.51 (0.00) [0]
857	KANTE TO WAKED	3/2016	11/2019 (-) [11/2019]	1,230.02 (1,230.00) [1,230.02]	555.61 (0.00) [0]
858	KARAD PATAN CHIPLUN GUHAGAR	2/2017	6/2019 (-) [6/2020]	407.19 (407.00) [407.19]	25.00 (0.00) [12]
859	KARAD TO TAGAON	1/2017	6/2019 (-) [6/2020]	537.81 (538.00) [537.81]	89.97 (0.00) [12]
860	KARAD TO VITA	1/2018	12/2019 (-) [12/2019]	344.85 (245.00) [344.85]	96.04 (0.00) [0]
861	KARWANDI TO RAJURI	3/2018	12/2019 (-) [12/2019]	276.95 (277.00) [276.95]	87.47 (0.00) [0]
862	KATOL TO WARUD	1/2017	6/2019 (-) [8/2019]	463.62 (664.00) [463.62]	125.34 (0.00) [0]
863	KHAMGAON TO DEULGAON SAKARSHA	3/2018	12/2019 (-) [12/2019]	249.29 (-) [249.29]	97.20 (0.00) [0]
864	KHAMGAON TO SHEGAON	2/2017	5/2019 (-) [12/2019]	203.21 (203.00) [203.21]	109.79 (0.00) [7]
865	KHERDA TO NAGZARI	3/2018	12/2019 (-) [12/2019]	181.30 (-) [181.30]	72.50 (0.00) [0]
866	KOLDE TO KHETIYA	1/2017	7/2019 (-) [0/0]	509.18 (-) [509.18]	205.93 (0.00) [0]
867	KOLHA TO NASRATPUR	4/2016	4/2019 (-) [4/2020]	281.78 (282.00) [281.78]	47.73 (0.00) [12]
868	KOTHARI TO DHANORA	9/2018	8/2020 (-) [8/2020]	301.38 (301.00) [301.38]	41.00 (0.00) [0]
869	KUMBHARI PHTA TO DEULGAON RAJA	2/2017	6/2019 (-) [0/0]	406.51 (-) [406.51]	280.69 (0.00) [0]
870	KUNDRAL TO WAZAR	1/2018	12/2019 (-) [12/2019]	225.25 (225.00) [225.25]	148.75 (0.00) [0]
871	KURUDWADI TO PANDHARPUR	1/2017	7/2019 (-) [0/0]	307.63 (-) [307.63]	157.17 (0.00) [0]
872	KUSUMBA TO MALEGAON	3/2018	12/2019	243.45	80.02

			(-) [12/2019]	(244.00) [243.45]	(0.00) [0]
873	LATUR TO PANGAON	3/2018	12/2019 (-) [12/2019]	336.47 (336.00) [336.47]	123.48 (0.00) [0]
874	MAHAD TO RAIGAD FORT	7/2018	5/2020 (-) [5/2020]	237.40 (-) [237.40]	8.34 (0.00) [0]
875	MAJALGAON TO KAIJ	1/2017	7/2019 (-) [7/2019]	413.99 (-) [413.99]	299.33 (0.00) [0]
876	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER	3/2018	12/2019 (-) [12/2019]	256.15 (-) [256.15]	36.50 (0.00) [0]
877	MALEGAON TO RISOD	2/2018	12/2019 (-) [12/2019]	303.24 (303.24) [303.24]	131.97 (0.00) [0]
878	MALEWADA TO CHIMUR	10/2016	6/2019 (-) [6/2020]	322.55 (-) [322.55]	156.91 (0.00) [12]
879	MANGAON TO DIGHI PORT	1/2017	7/2019 (-) [7/2020]	457.52 (457.52) [457.52]	277.98 (0.00) [12]
880	MANGRUPHIR TO MAHAN	3/2018	11/2019 (-) [11/2019]	222.13 (222.13) [222.13]	78.63 (0.00) [0]
881	MANJUSUMBA TO CHUMBALI	1/2017	8/2019 (-) [8/2019]	228.54 (228.54) [228.54]	102.30 (0.00) [0]
882	MANSAR TO SALAIKHURD	1/2018	12/2019 (-) [12/2019]	418.36 (-) [418.36]	125.13 (0.00) [0]
883	MANTHA TALUKAS BORDER TO PARTUR	1/2017	7/2019 (-) [7/2019]	486.19 (486.19) [486.19]	218.55 (0.00) [0]
884	MEHKAR TO AJISPUR	1/2017	7/2019 (-) [0/0]	232.77 (-) [232.77]	89.51 (0.00) [0]
885	MEHKAR TO CHIKALI	2/2017	5/2019 (-) [0/0]	322.48 (322.00) [322.48]	185.08 (0.00) [0]
886	MHASWAD TO TEMBHURNI	1/2017	7/2019 (-) [0/0]	488.60 (-) [488.60]	184.71 (0.00) [0]
887	MORSHI TO ACHALPUR	1/2017	6/2019 (-) [12/2019]	341.16 (341.00) [341.16]	156.29 (0.00) [6]
888	MORSHI TO MAH/MP BORDER	1/2017	6/2019 (-) [0/0]	471.61 (472.00) [471.61]	259.90 (0.00) [0]
889	MUL TO CHANDRAPUR	12/2016	7/2019 (-) [7/2019]	162.34 (-) [162.34]	32.80 (0.00) [0]
890	NAGAJ TO VAIJAPUR	1/2017	6/2019 (-) [12/2019]	376.72 (377.00) [376.72]	183.81 (0.00) [6]
891	NAGBHID TO ARMORI	9/2016	7/2019 (-) [0/0]	269.05 (-) [269.05]	221.91 (0.00) [0]
892	NAGPUR RING ROAD PACKAGE-1	3/2016	7/2019 (12/2020)	546.00 (-)	269.67 (0.00)

			[12/2020]	[546.00]	[17]
893	NAGPUR RING ROAD PACKAGE-2	3/2016	7/2019 (12/2020) [12/2020]	591.66 (-) [591.66]	310.56 (0.00) [17]
894	NAIGAONBANDI TO MANGRULPIR	12/2017	3/2019 (-) [12/2019]	244.04 (244.00) [244.04]	40.94 (0.00) [9]
895	NALDURG TO AKKALKOT	2/2018	12/2019 (-) [12/2019]	274.50 (275.00) [274.50]	65.39 (0.00) [0]
896	NANDED TO JALKOT	12/2017	9/2019 (-) [9/2019]	456.93 (457.00) [456.93]	78.50 (0.00) [0]
897	NANDGAON TO MORSHI	1/2017	6/2019 (-) [12/2019]	385.87 (386.00) [385.87]	203.75 (0.00) [6]
898	NASHIK TO PETH	12/2015	11/2018 (-) [11/2019]	289.60 (-) [289.60]	118.81 (0.00) [12]
899	NASRATPUR TO BARASGAON	7/2016	9/2019 (-) [9/2019]	406.54 (406.54) [406.54]	142.00 (0.00) [0]
900	NILAJPHATA TO BHANDARA	1/2018	5/2020 (-) [5/2020]	420.63 (421.00) [420.63]	31.60 (0.00) [0]
901	OMREGA TO AUSA	3/2018	12/2019 (-) [12/2019]	272.04 (272.00) [272.04]	137.24 (0.00) [0]
902	OSMANNAGAR TO KUNDRAL	9/2017	8/2020 (-) [8/2020]	344.25 (344.00) [344.25]	61.02 (0.00) [0]
903	PAHUR TO BODHWAD	1/2017	5/2020 (-) [5/2020]	244.93 (-) [244.93]	59.23 (0.00) [0]
904	PAITHAN TO SHIRUR	3/2017	6/2019 (-) [0/0]	341.80 (-) [341.80]	107.89 (0.00) [0]
905	PALPHATA TO PHULAMBARI	3/2018	12/2019 (-) [12/2019]	227.19 (227.00) [227.19]	74.23 (0.00) [0]
906	PANCHARAL TO MANDANGHAR	7/2018	5/2020 (-) [5/2020]	381.08 (302.00) [381.08]	13.03 (0.00) [0]
907	PANDHARPUR TO SANGOLA	7/2017	7/2019 (-) [0/0]	218.38 (-) [218.38]	168.75 (0.00) [0]
908	PARBHANI TO GANGKHED	3/2018	12/2019 (-) [12/2019]	238.19 (238.00) [238.19]	45.85 (0.00) [0]
909	PARLI PIMPLA DAHIGUDA	2/2017	6/2019 (-) [6/2020]	205.72 (205.72) [205.72]	30.42 (0.00) [12]
910	PARSHURAM GHAT TO ARAWALI	4/2016	12/2019 (-) [11/2019]	983.14 (983.00) [983.14]	655.15 (0.00) [-1]
911	PARTUR TO MAJALGAON	1/2017	7/2019 (-) [7/2019]	420.57 (420.57) [420.57]	176.39 (0.00) [0]
912	PATGAON KHOPOLI SECTION I	1/2018	12/2019 (-) [12/2019]	170.00 (-) [170.00]	56.57 (0.00) [0]

913	PEN TO KHOPOLI	3/2018	3/2018 (-) [12/2019]	301.39 (302.00) [301.39]	0.00 (0.00) [21]
914	PIMPLA TO MANJARSUMBHA	1/2017	8/2019 (-) [8/2019]	595.77 (595.77) [595.77]	151.44 (0.00) [0]
915	PUNE RAIGARH DISTRICT BORDER TO MANGAON	3/2018	12/2019 (-) [12/2019]	223.46 (-) [223.46]	21.42 (0.00) [0]
916	PUNE TO MALE VILLAGE	3/2018	12/2019 (-) [12/2019]	228.31 (-) [228.31]	13.50 (0.00) [0]
917	PUNE-SATARA(NH-4)	10/2010	3/2013 (-) [12/2019]	1,724.55 (-) [1,724.55]	2,401.00 (0.00) [81]
918	RALEGAON TO RAMTIRTH	1/2017	7/2019 (-) [0/0]	210.81 (-) [210.81]	114.69 (0.00) [0]
919	REHABILATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00	1/2014	/ (-) [0/0]	446.77 (-) [446.77]	278.50 (0.00) [0]
920	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM	1/2015	/ (-) [0/0]	225.81 (-) [225.81]	85.11 (0.00) [0]
921	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA	3/2016	12/2019 (-) [12/2019]	536.65 (356.00) [536.65]	465.20 (0.00) [0]
922	RISOD TO HINGOLI	2/2018	12/2019 (-) [12/2019]	355.99 (355.99) [355.99]	131.97 (0.00) [0]
923	SAKOLI TO BHANDARA	1/2017	6/2019 (-) [11/2019]	362.96 (362.96) [362.96]	37.83 (0.00) [5]
924	SALAIKHURD TO TIRORA	1/2018	12/2019 (-) [12/2019]	415.25 (415.25) [415.25]	96.22 (0.00) [0]
925	SANGOLA TO JATH	1/2018	12/2019 (-) [12/2019]	257.38 (257.00) [257.38]	84.15 (0.00) [0]
926	SARAD VANI PIMPALGAON	1/2017	7/2019 (-) [0/0]	250.46 (-) [250.46]	105.63 (0.00) [0]
927	SARSAM TO KOTHARI	2/2016	7/2019 (-) [0/0]	545.64 (-) [545.64]	99.01 (0.00) [0]
928	SATARA MURVAD PILLOV PANDHARPUR	1/2017	/ (-) [0/0]	388.44 (-) [388.44]	191.77 (0.00) [0]
929	SATARA TO MHASWAD	1/2017	7/2019 (-) [0/0]	653.46 (-) [653.46]	207.42 (0.00) [0]
930	SELDOH TO PANVAR	7/2018	5/2020 (-) [5/2020]	404.33 (404.00) [404.33]	30.19 (0.00) [0]
931	SHAHPUR PATGAON SECTION I	1/2018	12/2019 (-) [12/2019]	150.79 (150.79) [150.79]	21.42 (0.00) [0]
932	SHEGAON TO DEORI PHATA	2/2017	5/2019 (-) [12/2019]	373.10 (373.00) [373.10]	143.43 (0.00) [7]
933	SHIROD SHAHPURER TO NANDED	1/2017	7/2019	211.34	107.83

			(-) [7/2019]	(211.34) [211.34]	(0.00) [0]
934	SHIRUR TO KHARDA	2/2017	6/2019 (-) [0/0]	381.77 (-) [381.77]	156.79 (0.00) [0]
935	SHIVUR TO YEOLA	3/2018	12/2019 (-) [12/2019]	181.08 (-) [181.08]	7.50 (0.00) [0]
936	SILLOD TO FARDAPUR	2/2017	6/2019 (-) [0/0]	337.46 (-) [337.46]	39.22 (0.00) [0]
937	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH	12/2017	/ (-) [10/2020]	404.94 (448.18) [448.18]	165.51 (43.24) [-]
938	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE	11/2016	/ (3/2020) [3/2019]	290.73 (315.00) [315.00]	234.43 (24.27) [0]
939	TAKARKHED TO JALNA	9/2017	6/2019 (-) [12/2019]	417.90 (418.00) [417.90]	119.26 (0.00) [6]
940	TALEGAON TO GONAPUR	1/2018	3/2019 (-) [12/2019]	264.41 (264.00) [264.41]	36.71 (0.00) [9]
941	TALGAON TO KALMATH	10/2016	3/2020 (-) [3/2020]	904.70 (905.00) [904.70]	604.05 (0.00) [0]
942	TASGAON TO SHIRDHON	1/2017	11/2019 (-) [11/2019]	195.64 (196.00) [195.64]	169.73 (0.00) [0]
943	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI	2/2017	7/2019 (-) [0/0]	422.02 (422.00) [422.02]	247.01 (0.00) [0]
944	VADPALE TO BHOGAN KHURD	1/2017	11/2019 (-) [3/2020]	1,598.47 (1,560.00) [1,598.47]	751.91 (0.00) [4]
945	VITA TO NAGAJ	3/2018	12/2019 (-) [12/2019]	304.58 (305.00) [304.58]	24.16 (0.00) [0]
946	WADI TO ASOLA	1/2017	9/2019 (-) [9/2020]	363.82 (363.82) [363.82]	41.10 (0.00) [12]
947	WADIGODRI TO DHANGRIPIMPRI	3/2018	2/2020 (-) [2/2020]	194.23 (194.00) [194.23]	86.23 (0.00) [0]
948	WAKAN PALI KHOPOLI	1/2017	5/2019 (-) [5/2020]	376.19 (376.19) [376.19]	34.03 (0.00) [12]
949	WAKED TO TALEGAON	2/2016	2/2019 (-) [0/0]	1,244.75 (1,245.00) [1,244.75]	357.60 (0.00) [0]
950	WARDHA TO ARVI	2/2018	4/2020 (-) [4/2020]	313.58 (313.58) [313.58]	12.96 (0.00) [0]
951	WARDHA TO HINGAGHAT	1/2018	12/2019 (-) [12/2019]	216.90 (216.90) [216.90]	55.00 (0.00) [0]
952	WASHIM TO DASTAPUR	3/2018	12/2019 (-) [12/2019]	165.51 (-) [165.51]	34.45 (0.00) [0]
953	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16	10/2015	/ (-)	289.60 (-)	90.65 (0.00)

			[0/0]	[289.60]	[0]
954	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	5/2013	2/2014 (-) [0/0]	1,348.20 (-) [1,348.20]	1,792.90 (0.00) [0]
	Telecommunications				
955	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	1/2018	10/2018 (12/2019) [12/2019]	231.80 (240.10) [240.10]	117.63 (8.30) [14]
	Urban Development				
956	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI	1/2018	7/2020 (-) [11/2020]	223.37 (-) [223.37]	42.19 (0.00) [4]
957	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	7/2013	1/2015 (-) [5/2020]	23,136.00 (-) [23,136.00]	0.00 (0.00) [64]
958	NAGPUR METRO RAIL	8/2014	3/2018 (-) [12/2019]	8,680.00 (-) [8,680.00]	6,405.74 (0.00) [21]
959	PUNE METRO RAIL PROJECT (PHASE 1)	12/2016	11/2021 (3/2022) [3/2022]	11,420.00 (-) [11,420.00]	3,372.86 (0.00) [4]
960	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	6/2010	3/2012 (-) [12/2019]	205.00 (-) [205.00]	165.95 (0.00) [93]
	Water Resources				
961	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	3/2017	12/2019 (-) [12/2019]	233.57 (-) [233.57]	32.20 (0.00) [0]
	MANIPUR				
	Power				
962	LOKTAK D/S HEP(NHPC)	12/1999	6/2006 (-) [0/0]	578.62 (-) [578.62]	0.00 (0.00) [0]
	Railways				
963	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [3/2022]	4,454.17 (13,809.00) [12,524.00]	9,541.58 (8,069.83) [132]
	Road Transport And Highways				
964	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260.	10/2016	11/2020 (-) [11/2020]	235.31 (-) [235.31]	91.38 (0.00) [0]
965	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	8/2017	10/2018 (-) [10/2021]	517.57 (-) [457.77]	137.04 (-59.80) [36]
	Urban Development				
966	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	2/2014	3/2015 (-) [10/2020]	216.69 (-) [216.69]	52.00 (0.00) [67]
	MEGHALAYA				
	Health And Family Welfare				
967	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [7/2020]	363.99 (-) [363.99]	208.29 (0.00) [26]
	Human Resource Department				
968	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	9/2013	9/2014 (-) [12/2020]	484.32 (-) [626.26]	0.00 (141.94) [75]
	Railways				
969	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [3/2021]	906.46 (-) [6,000.00]	263.12 (5,093.54) [0]

	Road Transport And Highways				
970	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	3/2019	5/2019 (-) [0/0]	306.28 (-) [306.28]	42.66 (0.00) [0]
971	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	5/2018 (3/2018) [10/2019]	479.20 (-) [479.20]	711.38 (0.00) [0]
972	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (-) [9/2021]	553.51 (-) [553.51]	32.78 (0.00) [-]
	Urban Development				
973	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	4/2014	9/2017 (-) [0/0]	151.33 (-) [151.33]	7.15 (0.00) [0]
	MIZORAM				
	Railways				
974	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (3/2022) [3/2022]	2,393.47 (4,968.00) [5,021.45]	3,131.89 (2,627.98) [96]
	Road Transport And Highways				
975	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (-) [6/2020]	195.04 (-) [377.99]	305.38 (182.95) [116]
976	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	9/2014 (-) [12/2019]	186.96 (-) [305.61]	275.06 (118.65) [63]
977	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (-) [12/2019]	193.69 (-) [327.92]	254.24 (134.23) [110]
978	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	519.09 (-) [519.09]	0.00 (0.00) [0]
979	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	473.18 (-) [473.18]	0.00 (0.00) [0]
980	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	642.96 (-) [642.96]	0.00 (0.00) [0]
981	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	640.07 (-) [640.07]	0.00 (0.00) [0]
982	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	537.82 (-) [537.82]	0.00 (0.00) [0]
983	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	404.29 (-) [404.29]	0.00 (0.00) [0]
984	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	428.11 (-) [428.11]	0.00 (0.00) [0]
985	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	518.53 (-) [518.53]	0.00 (0.00) [0]
986	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (-) [12/2019]	624.41 (-) [992.67]	853.82 (368.26) [105]
	MULTI STATE				
	Coal				
987	DHANKASA UG (1.00 MTY)	9/2016	3/2022 (-) [3/2022]	458.07 (-) [458.07]	20.86 (0.00) [0]

988	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)	2/2017	3/2021 (-) [3/2021]	328.00 (-) [328.00]	167.00 (0.00) [0]
989	NILJAI EXPANSION (DEEP) OC (3.5 MTY)	8/2016	3/2022 (-) [3/2022]	319.76 (-) [319.76]	238.99 (0.00) [0]
	Petroleum				
990	50MW WIND ENERGY POWER PROJECT	11/2015	6/2017 (-) [0/0]	500.00 (-) [500.00]	0.00 (0.00) [0]
991	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	1/2015	12/2020 (-) [12/2020]	1,823.00 (3,027.90) [3,027.90]	955.36 (1,204.90) [0]
992	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II	9/2016	12/2019 (6/2020) [6/2020]	571.66 (-) [571.66]	297.66 (0.00) [6]
993	BARAUNI-GUWAHATI PIPELINE	6/2018	12/2021 (-) [12/2021]	3,308.00 (-) [3,308.00]	1,349.36 (0.00) [0]
994	BOKARO-ANGUL PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	3,437.00 (-) [3,437.00]	1,309.83 (0.00) [0]
995	DOBHI-DURGAPUR PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	2,433.00 (-) [2,433.00]	1,496.03 (0.00) [0]
996	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	9/2017	3/2021 (-) [3/2021]	2,677.00 (-) [2,677.00]	971.81 (0.00) [0]
997	JAIPUR-PANIPAT NAPTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE	2/2015	10/2019 (-) [12/2019]	890.00 (-) [887.00]	609.28 (-3.00) [2]
998	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	6/2009	12/2012 (2/2022) [2/2022]	2,915.00 (4,915.00) [4,915.00]	2,742.24 (2,000.00) [110]
999	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT	7/2015	12/2020 (-) [12/2020]	2,881.40 (-) [2,000.00]	1,293.26 (-881.40) [0]
1000	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION	9/2016	6/2020 (-) [6/2020]	1,879.00 (-) [1,879.00]	1,536.16 (0.00) [0]
1001	PARADIP HYDERABAD PIPLEINE	1/2015	12/2020 (-) [8/2020]	2,321.00 (3,338.00) [3,338.00]	1,912.90 (1,017.00) [-4]
1002	PARADIP LPG IMPORT FACILITY	1/2015	7/2018 (-) [10/2020]	690.00 (-) [690.00]	326.08 (0.00) [27]
1003	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I)	5/2016	10/2020 (-) [10/2020]	406.00 (-) [406.00]	91.19 (0.00) [0]
1004	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	7/2011	3/2017 (6/2020) [6/2020]	352.56 (-) [438.84]	249.73 (86.28) [39]
	Power				
1005	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION)	9/2017	9/2019 (2/2020) [2/2020]	198.49 (-) [198.49]	119.50 (0.00) [5]
1006	COMPREHENSIVE SCHEME FOR THE STRENGHTENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	12/2018 (-) [12/2020]	4,754.42 (-) [9,072.36]	1,352.46 (4,317.94) [24]
1007	EASTERN REGION STRENGTHENING SCHEME XX	11/2017	5/2020 (-)	358.83 (-)	166.27 (0.00)

			[5/2020]	[358.83]	[0]
1008	EASTERN REGION STRENGTHENING SCHEME-V	10/2013	4/2016 (8/2019) [12/2019]	1,364.52 (1,891.41) [1,891.41]	1,280.93 (526.89) [44]
1009	EASTERN REGION STRENGTHENING SCHEME-XII	5/2014	11/2016 (6/2020) [3/2020]	522.29 (546.36) [546.36]	470.50 (24.07) [40]
1010	EASTERN REGION STRENGTHENING SCHEME-XVIII	3/2017	7/2020 (-) [7/2020]	3,500.00 (3,500.00) [3,500.00]	1,949.00 (0.00) [0]
1011	EASTERN REGION STRENTHENING SCHEME XVII(PART B)	2/2017	6/2019 (-) [3/2020]	235.53 (-) [235.53]	130.55 (0.00) [9]
1012	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	2/2017	2/2019 (4/2020) [3/2020]	322.30 (-) [322.30]	164.09 (0.00) [13]
1013	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	3/2015	3/2018 (-) [12/2019]	197.40 (197.40) [197.40]	83.94 (0.00) [21]
1014	GREEN ENERGY CORRIDORS - INTER STATE TRANSSMISSION SCHEME PART-D	5/2016	5/2019 (-) [12/2019]	3,519.59 (-) [3,519.59]	2,534.01 (0.00) [7]
1015	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR	2/2017	4/2020 (-) [4/2020]	5,070.13 (-) [5,070.13]	3,042.59 (0.00) [0]
1016	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P	5/2016	11/2019 (-) [2/2020]	14,733.37 (-) [14,733.37]	9,317.26 (0.00) [3]
1017	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	8/2017	2/2020 (-) [2/2020]	1,931.39 (-) [1,931.39]	1,107.54 (0.00) [0]
1018	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	12/2014	12/2018 (-) [12/2020]	5,111.33 (-) [6,880.36]	1,779.00 (1,769.03) [24]
1019	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	2/2009	8/2013 (3/2022) [3/2022]	11,130.19 (14,719.10) [14,719.10]	12,816.90 (3,588.91) [103]
1020	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO	3/2017	11/2019 (-) [11/2019]	283.72 (-) [283.72]	196.10 (0.00) [0]
1021	SOUTHERN REGION STRENGTHENING SCHEME-XXI	9/2016	3/2019 (-) [12/2019]	562.25 (-) [562.25]	420.20 (0.00) [9]
1022	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	12/2015	4/2019 (-) [12/2019]	3,654.00 (-) [3,654.00]	3,485.19 (0.00) [8]
1023	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	10/2016	4/2019 (-) [12/2019]	608.24 (-) [608.24]	416.24 (0.00) [8]
1024	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	1/2015	7/2017 (6/2019) [11/2019]	203.28 (260.03) [260.03]	199.56 (56.75) [28]
1025	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII	3/2017	12/2019 (-) [3/2020]	379.95 (-) [379.95]	93.48 (0.00) [3]
1026	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII	3/2017	6/2019 (-) [12/2019]	337.75 (-) [337.75]	99.94 (0.00) [6]
1027	SYTEM STRENGTHENING XIII OF SR GRID	10/2011	6/2014 (9/2019) [12/2019]	487.49 (639.46) [639.46]	568.44 (151.97) [66]

1028	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	10/2008	10/2012 (12/2019) [3/2020]	4,824.12 (5,071.94) [5,071.94]	4,570.22 (247.82) [89]
1029	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP)	1/2015	10/2017 (9/2019) [11/2019]	871.62 (-) [871.62]	584.94 (0.00) [25]
1030	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II)	10/2016	1/2019 (9/2019) [1/2020]	408.46 (-) [408.46]	311.82 (0.00) [12]
1031	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH	6/2014	3/2018 (12/2019) [12/2019]	5,151.37 (5,151.37) [5,151.37]	3,216.41 (0.00) [21]
1032	TRANSMISSION SYSTEM STRENTHENNING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	3/2016	1/2018 (3/2020) [3/2020]	808.63 (-) [808.63]	534.82 (0.00) [26]
1033	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	1/2014	4/2016 (12/2017) [12/2019]	374.63 (374.63) [374.63]	214.62 (0.00) [44]
	Railways				
1034	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT	12/2015	12/2023 (12/2023) [12/2023]	1,08,000.00 (-) [1,08,000.00]	5,969.41 (0.00) [0]
1035	BANDEL-BOINCHI 3RD LINE	4/2011	/ (-) [3/2020]	288.35 (-) [393.00]	393.00 (104.65) [-]
1036	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT	4/2007	/ (-) [3/2025]	450.55 (-) [250.55]	20.12 (-200.00) [-]
1037	BHADRACHALAM ROAD-SATTUPALLI	4/2010	3/2020 (3/2020) [3/2020]	704.31 (952.16) [952.16]	303.24 (247.85) [0]
1038	BHADRACHALAM-KOVVUR	4/2012	/ (-) [0/0]	923.23 (2,184.83) [2,184.83]	2.46 (1,261.60) [0]
1039	BOINCHI-SHAKTIGARH 3RD LINE	4/2011	/ (-) [3/2021]	175.80 (-) [251.18]	251.18 (75.38) [-]
1040	CHANDIGARH-BADDI	4/2007	3/2023 (-) [3/2023]	328.14 (-) [1,540.00]	234.79 (1,211.86) [0]
1041	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA	4/2003	/ (-) [3/2025]	337.96 (-) [336.96]	70.20 (-1.00) [-]
1042	CHENNAI-CUDDALORE VIA MAMALLAPURAM	4/2008	/ (-) [0/0]	523.52 (-) [2,300.00]	2.28 (1,776.48) [0]
1043	CHHAPRA-BALLIA UP	3/2013	1/2019 (-) [1/2020]	295.00 (-) [477.31]	336.89 (182.31) [12]
1044	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	3/2007	12/2021 (-) [12/2021]	243.78 (-) [895.00]	106.55 (651.22) [0]
1045	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	4/2005	3/2017 (-) [3/2025]	595.51 (-) [769.40]	103.08 (173.89) [96]
1046	CHOTTAUDEPUR-DHAR(NL)	4/2007	3/2022 (3/2022) [3/2022]	1,347.26 (1,347.26) [1,347.26]	741.93 (0.00) [0]
1047	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	4/2007	3/2022 (3/2023) [3/2023]	1,640.04 (1,640.04) [1,640.04]	739.31 (0.00) [12]

1048	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	4/2010	3/2017 (-) [3/2025]	365.17 (-) [296.43]	248.70 (-68.74) [96]
1049	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	4/2007	/ (3/2022) [3/2022]	336.91 (791.39) [791.39]	517.05 (454.48) [-]
1050	DEOGHAR - SULTANGANJ (INL), ER	4/2000	2/2013 (-) [3/2024]	607.09 (-) [1,425.44]	637.54 (818.35) [133]
1051	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	4/2010	/ (-) [0/0]	2,030.50 (-) [2,030.50]	19.07 (0.00) [0]
1052	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	4/2010	3/2015 (3/2025) [3/2025]	651.00 (-) [1,009.00]	7.96 (358.00) [120]
1053	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	/ (-) [0/0]	11,589.00 (30,357.00) [28,181.00]	0.00 (16,592.00) [0]
1054	GAYA-CHATRA (NL)	4/2008	/ (-) [0/0]	415.67 (-) [549.75]	15.58 (134.08) [0]
1055	GONDIA-JABALPUR(GC),(SECR)	2/1997	4/2020 (1/2021) [1/2021]	511.86 (1,756.00) [1,756.00]	1,668.96 (1,244.14) [9]
1056	GOOTY-DHARMAVARAM-BANGLORE	4/2015	/ (-) [0/0]	636.38 (-) [636.38]	0.00 (0.00) [0]
1057	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	4/2011	3/2022 (-) [12/2024]	2,912.96 (-) [3,845.60]	148.26 (932.64) [33]
1058	HAJIPUR - BACHAWARA	5/2015	3/2019 (-) [2/2021]	678.54 (678.54) [678.54]	495.04 (0.00) [23]
1059	HANSDIHA-GODDA NL	4/2011	3/2020 (-) [3/2021]	542.18 (-) [693.80]	458.91 (151.62) [12]
1060	HANSNABAD-HINGALGANJ NEW BG LINE	4/2010	/ (-) [3/2025]	172.03 (-) [260.10]	10.73 (88.07) [-]
1061	HATHUA-BHATNI (N L) (NER)	4/2005	12/2022 (-) [12/2022]	230.03 (-) [230.03]	277.14 (0.00) [0]
1062	HOTGI-KUDGI-GADAG	3/2015	3/2019 (-) [3/2021]	1,614.59 (1,870.41) [1,870.41]	885.55 (255.82) [24]
1063	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS)	4/2010	11/2018 (-) [3/2021]	157.94 (-) [157.94]	51.75 (0.00) [28]
1064	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES	4/2011	/ (-) [3/2025]	166.89 (-) [166.89]	0.02 (0.00) [-]
1065	JALANDHAR-PATHANKOT-JAMMU TAWI	3/2002	3/2016 (-) [3/2021]	625.00 (781.00) [859.00]	835.35 (234.00) [60]
1066	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	4/2008	3/2014 (-) [3/2024]	2,132.77 (2,132.77) [2,132.77]	331.15 (0.00) [120]
1067	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	4/2001	3/2016 (-) [3/2025]	923.52 (-) [995.10]	501.00 (71.58) [108]
1068	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW	4/2010	/	174.56	71.42

	MM FOR RANAGHAT-DUTTAPHULIA NEW LINE		(-) [3/2025]	(-) [174.56]	(0.00) [-]
1069	KAZIPET-BALHRSHA	4/2015	3/2021 (-) [3/2023]	2,063.03 (2,063.03) [2,063.03]	792.70 (0.00) [24]
1070	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	4/2012	3/2023 (-) [3/2024]	1,856.95 (2,200.00) [2,200.00]	290.92 (343.05) [12]
1071	KURUPPANTHARA-CHINGAVANAM	4/2007	/ (-) [0/0]	270.14 (-) [457.08]	373.51 (186.94) [0]
1072	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	4/1987	3/2006 (-) [3/2025]	406.99 (-) [545.70]	148.48 (138.71) [228]
1073	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	9/1998	5/2008 (3/2022) [3/2023]	247.66 (6,672.85) [8,248.50]	1,986.78 (8,000.84) [178]
1074	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL	4/2009	3/2014 (-) [3/2025]	257.42 (-) [257.42]	107.49 (0.00) [132]
1075	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	4/2011	3/2019 (-) [12/2019]	120.70 (-) [1,800.00]	187.30 (1,679.30) [9]
1076	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	4/2009	2/2012 (-) [3/2025]	499.96 (-) [680.68]	159.45 (180.72) [157]
1077	MONIGRAM- NIMTITA	4/2012	/ (-) [3/2024]	250.93 (-) [310.70]	275.20 (59.77) [-]
1078	MUNEERABAD-MAHABOOBNAGAR(NL),SCR	4/1997	3/2000 (-) [3/2021]	1,723.00 (1,780.29) [1,780.09]	1,478.40 (57.09) [252]
1079	MURKONGSELEK-PASIGHAT NL	4/2011	3/2020 (-) [3/2020]	414.84 (-) [661.00]	122.93 (246.16) [0]
1080	NANGALDAM-TALWARA(NL),NR	3/1981	7/2012 (-) [3/2024]	450.00 (2,010.00) [2,200.00]	666.00 (1,750.00) [140]
1081	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	4/2010	3/2005 (-) [3/2025]	494.54 (-) [494.59]	32.00 (0.05) [240]
1082	NEW BG LINE FROM BALURGHAT TO HILLY NFR	4/2010	3/2020 (-) [3/2020]	242.22 (-) [471.00]	69.09 (228.78) [0]
1083	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	4/2010	/ (-) [6/2021]	241.52 (-) [373.87]	273.20 (132.35) [-]
1084	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	4/2013	3/2019 (-) [0/0]	1,798.00 (-) [2,496.67]	0.00 (698.67) [0]
1085	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	4/1999	/ (-) [0/0]	819.23 (-) [1,871.00]	1,082.01 (1,051.77) [0]
1086	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	4/2000	12/2008 (-) [3/2021]	1,180.19 (3,300.00) [4,541.00]	3,344.19 (3,360.81) [147]
1087	PHULERA - DIGANA DOUBLING	5/2015	3/2020 (-) [4/2022]	600.00 (-) [685.99]	74.80 (85.99) [25]
1088	PIRPAINTI-BHAGALPUR	4/2011	/ (-)	261.38 (-)	478.08 (216.70)

			[5/2019]	[478.08]	[0]
1089	PIRPAINTI-JASIDIH	4/2013	3/2022 (-) [3/2025]	915.98 (-) [2,137.81]	297.68 (1,221.83) [36]
1090	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY	4/2011	3/2017 (-) [3/2026]	299.60 (-) [335.62]	1.12 (36.02) [108]
1091	RATLAM-DUNGARPUR VIA BANSWARA (NL)	4/2011	/ (-) [0/0]	2,082.75 (-) [4,079.15]	185.30 (1,996.40) [0]
1092	RAYADURGA-TUMKUR NL	4/2007	/ (-) [3/2025]	2,062.30 (2,062.30) [2,062.30]	903.96 (0.00) [-]
1093	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL	4/2000	/ (-) [3/2025]	297.47 (-) [298.22]	52.09 (0.75) [-]
1094	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	4/2010	3/2016 (-) [3/2025]	277.28 (-) [266.32]	162.57 (-10.96) [108]
1095	SRINIVASA-PURA-MADANAPALLI NL	4/2013	/ (-) [12/2023]	296.00 (466.65) [466.65]	0.00 (170.65) [-]
1096	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	4/2007	/ (-) [3/2025]	450.00 (-) [1,261.34]	0.00 (811.34) [-]
1097	TARAKESHWAR-MAGRA NEW BG LINE	4/2010	/ (-) [3/2025]	365.17 (-) [527.54]	1.76 (162.37) [-]
1098	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	3/2020 (-) [3/2020]	16,592.00 (51,101.00) [51,101.00]	22,485.00 (34,509.00) [0]
1099	YELAHANKA-PENUKONDA	5/2015	3/2020 (-) [3/2020]	860.43 (-) [958.00]	756.85 (97.57) [0]
	Road Transport And Highways				
1100	4 LANING OF NAGPUR-BETUL	2/2011	8/2014 (-) [0/0]	2,498.76 (-) [2,498.76]	2,531.46 (0.00) [0]
1101	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	4/2015 (1/2017) [6/2020]	1,928.22 (-) [2,945.00]	2,467.00 (1,016.78) [62]
1102	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67.	3/2018	/ (-) [0/0]	1,294.47 (-) [1,296.00]	0.00 (1.53) [0]
1103	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE	3/2018	/ (-) [0/0]	998.70 (-) [962.00]	0.00 (-36.70) [0]
1104	GWALIOR-JHANSI, NH-75	12/2003	12/2009 (8/2020) [3/2020]	604.00 (364.59) [364.59]	215.58 (-239.41) [123]
1105	MUZAFFARNAGAR-HARIDWAR	9/2011	3/2013 (-) [12/2019]	754.00 (-) [754.00]	1,364.18 (0.00) [81]
1106	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP	9/2016	/ (-) [2/2020]	1,244.10 (-) [1,244.10]	1,394.00 (0.00) [-]
1107	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	2/2009	8/2011 (-) [0/0]	1,693.75 (2,848.49) [1,693.75]	2,848.49 (0.00) [0]
1108	VARANASI-AURANGABAD KM.786 TO KM.978.40	9/2011	3/2014 (4/2017)	2,848.00 (-)	1,159.10 (0.00)

			[6/2020]	[2,848.00]	[75]
	Shipping And Ports				
1109	JAL MARG VIKAS PROJECT	1/2018	3/2023 (3/2023) [3/2023]	4,200.00 (5,369.18) [5,369.18]	1,662.16 (1,169.18) [0]
	Telecommunications				
1110	NETWORK FOR SPECTRUM	3/2012	7/2015 (-) [5/2020]	13,334.00 (-) [24,664.00]	12,146.00 (11,330.00) [58]
1111	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY	9/2014	9/2014 (-) [0/0]	2,111.17 (-) [2,011.17]	253.90 (-100.00) [0]
	Urban Development				
1112	DELHI GHAZIABAD MEERUT RRTS CORRIDOR	3/2019	6/2025 (-) [6/2025]	30,274.00 (-) [30,274.00]	613.92 (0.00) [0]
	NAGALAND				
	Railways				
1113	DIMAPUR-TIZIT NL	4/2013	3/2020 (-) [3/2020]	4,274.00 (-) [4,274.00]	0.00 (0.00) [0]
1114	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (-) [10/2021]	2,326.52 (-) [4,600.00]	842.42 (2,273.48) [79]
	Road Transport And Highways				
1115	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (5/2019) [0/0]	239.30 (-) [239.30]	0.00 (0.00) [0]
1116	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [0/0]	285.68 (-) [285.68]	9.58 (0.00) [0]
1117	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (11/2018) [0/0]	282.98 (-) [282.98]	12.76 (0.00) [0]
1118	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [0/0]	387.00 (-) [387.00]	135.12 (0.00) [0]
1119	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [0/0]	500.09 (-) [500.09]	0.00 (0.00) [0]
1120	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN	3/2017	11/2020 (-) [11/2020]	217.35 (-) [217.35]	35.10 (0.00) [0]
1121	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683	2/2017	4/2017 (-) [0/0]	507.68 (-) [507.68]	129.13 (0.00) [0]
1122	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (7/2019) [0/0]	339.57 (233.35) [339.57]	0.00 (0.00) [0]
1123	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [0/0]	315.03 (-) [315.03]	18.60 (0.00) [0]
1124	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [0/0]	240.64 (-) [240.64]	17.29 (0.00) [0]
1125	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [0/0]	215.12 (-) [215.12]	12.45 (0.00) [0]
1126	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [0/0]	215.79 (-) [215.79]	10.21 (0.00) [0]

1127	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [0/0]	272.89 (-) [272.89]	0.00 (0.00) [0]
1128	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (-) [0/0]	323.98 (-) [323.98]	0.00 (0.00) [0]
1129	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (11/2018) [0/0]	251.97 (160.10) [251.97]	18.66 (0.00) [0]
1130	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (11/2018) [0/0]	237.72 (136.73) [237.72]	29.67 (0.00) [0]
1131	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [8/2019]	373.07 (387.00) [373.07]	211.16 (0.00) [0]
1132	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [6/2020]	396.52 (339.55) [396.52]	235.52 (0.00) [46]
1133	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [8/2019]	429.52 (340.00) [429.52]	167.54 (0.00) [0]
1134	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M	11/2016	9/2019 (-) [9/2019]	336.25 (-) [336.25]	62.64 (0.00) [0]
1135	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (-) [12/2020]	167.62 (-) [167.62]	42.15 (0.00) [0]
1136	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (-) [12/2020]	172.63 (-) [172.63]	45.02 (0.00) [0]
1137	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA	12/2010	2/2011 (-) [0/0]	1,296.00 (-) [1,296.00]	0.00 (0.00) [0]
1138	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH-	3/2019	12/2022 (-) [12/2022]	237.51 (-) [237.51]	0.00 (0.00) [0]
	ODISHA				
	Coal				
1139	ANANTA OC EXPANSION PH-III (15.0 MTY)	8/2008	3/2012 (-) [3/2021]	207.28 (-) [207.28]	296.22 (0.00) [108]
1140	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	3/2010 (-) [3/2022]	172.08 (-) [172.08]	347.93 (0.00) [144]
1141	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	5/2014	3/2019 (-) [3/2024]	479.15 (-) [479.15]	211.71 (0.00) [60]
1142	BHUBANESWARI OCP, MCL (20.0 MTY)	12/2007	3/2017 (-) [3/2021]	490.10 (-) [490.10]	508.91 (0.00) [48]
1143	GARJANBAHAL OCP	11/2014	3/2021 (-) [3/2021]	1,375.38 (-) [1,375.38]	445.39 (0.00) [0]
1144	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	3/2013 (-) [3/2021]	479.53 (-) [479.53]	389.52 (0.00) [96]
1145	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP	5/2018	3/2027 (-) [3/2027]	2,434.75 (-) [2,434.75]	123.99 (0.00) [0]
1146	JAGANNATH RE-ORGANISATION OC.(6.00 MTY)	5/2014	3/2019 (-)	337.66 (-)	188.48 (0.00)

			[3/2020]	[337.66]	[12]
1147	KANIHA OCP, MCL, (10.0 MTY)	12/2007	3/2013 (-) [3/2022]	457.77 (-) [457.77]	539.88 (0.00) [108]
1148	KULDA EXPN OC. (5.00 MTY)	6/2014	3/2018 (-) [3/2021]	289.03 (-) [289.03]	0.00 (0.00) [36]
1149	KULDA OCP (MAHANADI COALFIELDS LTD)	1/2005	3/2010 (-) [3/2020]	302.96 (-) [302.96]	272.73 (0.00) [120]
1150	REORGANISATION OF BHARATPUR OCP EXPANSION	11/2018	3/2029 (-) [3/2029]	2,838.87 (-) [2,838.87]	1,157.99 (0.00) [0]
1151	SIARMAL OCP (40.00MTY)	5/2014	3/2026 (-) [3/2026]	3,756.36 (-) [3,756.36]	1,205.32 (0.00) [0]
	Mines				
1152	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	4/2021 (4/2021) [4/2021]	5,540.00 (5,540.00) [5,540.00]	114.95 (0.00) [0]
1153	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	11/2020 (-) [11/2020]	355.00 (-) [355.00]	82.07 (0.00) [0]
1154	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	11/2017	4/2021 (4/2021) [4/2021]	483.00 (483.00) [483.00]	1.20 (0.00) [0]
1155	UTKAL D AND E COAL BLOCK	5/2016	1/2020 (-) [1/2020]	534.00 (-) [534.00]	320.18 (0.00) [0]
	Petroleum				
1156	2G ETHANOL BIO REFINERY AT BARGARH	8/2017	12/2020 (-) [12/2020]	750.00 (-) [750.00]	34.73 (0.00) [0]
1157	2ND GENERATION LIGNOCELLUOSIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA)	8/2019	8/2022 (-) [8/2022]	1,607.00 (-) [1,607.00]	37.49 (0.00) [0]
1158	ADDITIONAL STORAGE TANKS AT PARADIP	11/2018	9/2021 (-) [9/2021]	462.30 (-) [462.30]	0.00 (0.00) [0]
1159	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY	8/2017	12/2021 (-) [12/2020]	315.00 (-) [315.00]	116.26 (0.00) [-12]
1160	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR	7/2017	7/2022 (-) [7/2022]	243.53 (-) [243.53]	55.03 (0.00) [0]
1161	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK	7/2017	7/2022 (-) [7/2022]	182.20 (-) [182.20]	32.85 (0.00) [0]
1162	DHAMRA-ANGUL PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	1,933.00 (-) [1,933.00]	1,055.91 (0.00) [0]
1163	ETHYLENE GLYCOL PROJECT AT PARADIP	4/2018	10/2021 (-) [10/2021]	5,654.00 (-) [5,654.00]	467.39 (0.00) [0]
1164	Fuel Quality Upgradation Project at Paradip Refinery	5/2019	8/2021 (-) [8/2021]	3,361.00 (-) [3,361.00]	372.43 (0.00) [0]
1165	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY	5/2016	1/2019 (-) [6/2020]	429.00 (-) [429.00]	318.90 (0.00) [17]
1166	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD	6/2019	9/2022	371.00	0.00

	ALONGWITH INCINERATOR AT PARADIP REFINERY		(-) [9/2022]	(-) [371.00]	(0.00) [0]
1167	LPG BP PROJECT KHORDHA	12/2016	12/2019 (-) [7/2021]	161.59 (-) [161.59]	38.65 (0.00) [19]
1168	PARADIP SOMNATHPUR HALDIA PIPELINE	10/2018	10/2021 (-) [10/2021]	1,297.50 (-) [1,297.50]	18.30 (0.00) [0]
1169	POLYPROPYLENE PLANT AT PARADIP REFINERY	3/2014	9/2017 (-) [0/0]	3,150.00 (-) [3,150.00]	2,573.02 (0.00) [0]
	Power				
1170	DARLIPALLI STPP STAGE-I (2X800 MW)	2/2014	12/2018 (2/2020) [9/2020]	12,532.44 (-) [13,740.53]	9,944.45 (1,208.09) [21]
1171	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA	4/2016	4/2019 (4/2019) [11/2019]	844.64 (-) [844.64]	435.25 (0.00) [7]
1172	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL	5/2016	12/2018 (-) [3/2020]	1,885.13 (-) [1,885.13]	527.90 (0.00) [15]
	Railways				
1173	BANASPANI- JAKHPURA - DOUBLING	3/2009	3/2019 (-) [6/2022]	942.95 (-) [1,120.00]	1,028.76 (177.05) [39]
1174	BHADRAK - NERGUNDI 3RD LINE	3/2013	10/2020 (3/2023) [3/2023]	843.04 (843.04) [843.04]	141.96 (0.00) [29]
1175	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	4/2015	12/2018 (3/2022) [3/2022]	1,172.92 (1,172.92) [1,172.92]	546.12 (0.00) [39]
1176	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	4/2010	3/2015 (-) [0/0]	149.90 (-) [230.00]	54.46 (80.10) [0]
1177	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	4/2016	3/2020 (-) [6/2023]	5,200.00 (-) [1,700.43]	48.00 (-3,499.57) [39]
1178	HARIDASPUR-PARADEEP(NL)	4/1996	12/2017 (-) [3/2020]	1,185.64 (-) [1,844.47]	1,829.53 (658.83) [27]
1179	JAGADALPUR-KORAPUT DOUBLING	4/2015	3/2022 (-) [3/2023]	1,547.38 (1,547.38) [1,547.38]	366.66 (0.00) [12]
1180	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	4/2015	11/2018 (-) [3/2022]	701.61 (701.61) [810.02]	129.40 (108.41) [40]
1181	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	4/2000	3/2009 (3/2009) [6/2020]	133.41 (207.00) [385.00]	387.92 (251.59) [135]
1182	KHURDA ROAD-BOLANGIR(NL)ECOR	4/1994	3/2009 (-) [6/2024]	2,923.13 (3,791.66) [3,791.66]	1,243.45 (868.53) [183]
1183	KORAPUT - SINGAPUR ROAD DOUBLING	4/2015	3/2022 (-) [3/2025]	2,361.74 (2,361.74) [2,361.74]	208.19 (0.00) [36]
1184	ROURKELA JHARSUGUDA THIRD LINE 101 KM	11/2015	3/2020 (3/2020) [6/2020]	969.83 (1,312.96) [1,312.96]	562.50 (343.13) [3]
1185	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	3/2012	3/2020 (-) [3/2021]	155.81 (-) [238.03]	204.79 (82.22) [12]

1186	SAMBALPUR - TITLAGARH - DOUBLING	3/2006	3/2020 (-) [3/2021]	948.04 (-) [1,500.00]	1,374.96 (551.96) [12]
1187	SAMBALPUR-TALCHER DOUBLING	3/2011	2/2019 (-) [3/2022]	1,111.99 (1,539.28) [1,539.28]	937.49 (427.29) [37]
1188	SUKINDA ROAD - ANGUL (NL)(ECOR)	4/1998	2/2015 (-) [12/2021]	1,202.70 (-) [1,202.70]	947.96 (0.00) [82]
1189	TALCHER-BIMALAGARH(NL)(ECOR)	4/2005	6/2021 (-) [6/2024]	810.78 (198.07) [1,928.07]	770.82 (1,117.29) [36]
1190	VIZIANAGARAM -SAMABALPUR 3RD LINE	1/1991	12/2024 (-) [12/2024]	2,335.67 (-) [2,335.68]	647.54 (0.01) [0]
	Road Transport And Highways				
1191	4 LANING OF BAHARAGORA - SINGHARA	7/2015	/ (-) [3/2021]	1,282.94 (-) [1,282.94]	255.43 (0.00) [-]
1192	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S	9/2016	8/2019 (-) [3/2021]	2,510.04 (-) [2,510.04]	313.18 (0.00) [19]
1193	FOUR LANING WITH PS TALEBANI -SMBALPUR	12/2015	/ (-) [11/2019]	752.28 (-) [752.28]	76.78 (0.00) [-]
1194	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION	2/2016	/ (-) [3/2020]	1,069.65 (-) [1,069.65]	526.12 (0.00) [-]
1195	PANIKHOLI-RIMOLI	3/2012	9/2014 (-) [0/0]	1,410.00 (-) [1,410.00]	1,935.14 (0.00) [0]
1196	REHABILITAITON AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4	10/2016	/ (-) [3/2021]	1,008.96 (-) [1,008.96]	506.49 (0.00) [-]
1197	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS	1/2018	/ (-) [8/2021]	564.66 (-) [564.66]	46.76 (0.00) [-]
1198	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	7/2017	7/2017 (11/2020) [6/2021]	476.56 (-) [476.56]	0.00 (0.00) [47]
1199	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (	1/2018	/ (-) [0/0]	633.68 (-) [633.68]	0.00 (0.00) [0]
1200	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25	1/2018	/ (5/2020) [6/2021]	953.09 (-) [953.09]	126.71 (0.00) [-]
1201	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2	1/2018	/ (5/2020) [6/2021]	668.86 (-) [668.86]	134.42 (0.00) [-]
1202	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG	1/2018	/ (-) [8/2021]	614.48 (-) [614.48]	52.00 (0.00) [-]
1203	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH	7/2014	1/2017 (-) [0/0]	342.05 (-) [342.05]	258.91 (0.00) [0]
1204	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (	1/2018	/ (-) [6/2021]	503.88 (-) [503.88]	3.98 (0.00) [-]
1205	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	3/2017	3/2020 (-) [3/2021]	1,288.07 (-) [1,420.00]	446.76 (131.93) [12]

1206	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO	12/2017	/ (7/2020) [6/2021]	686.65 (-) [686.65]	91.47 (0.00) [-]
1207	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON	1/2018	/ (3/2020) [6/2021]	686.65 (-) [686.65]	89.80 (0.00) [-]
1208	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA	12/2017	/ (-) [6/2021]	417.51 (-) [417.51]	35.52 (0.00) [-]
1209	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN	7/2014	1/2017 (-) [0/0]	342.05 (342.00) [342.00]	258.91 (-0.05) [0]
1210	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141	1/2018	/ (-) [6/2021]	999.00 (-) [999.00]	0.00 (0.00) [-]
1211	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR	8/2013	6/2016 (-) [11/2019]	171.96 (172.00) [172.00]	88.30 (0.04) [41]
1212	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB	1/1991	10/2017 (-) [0/0]	218.63 (-) [218.63]	29.27 (0.00) [0]
1213	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK	1/1991	5/2018 (-) [0/0]	229.41 (-) [229.41]	6.65 (0.00) [0]
1214	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK	1/2018	/ (6/2021) [6/2021]	1,522.00 (-) [1,522.00]	132.24 (0.00) [-]
1215	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	12/2011	6/2014 (-) [3/2019]	1,047.00 (-) [1,047.00]	1,874.43 (0.00) [0]
1216	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000)	3/2018	/ (-) [4/2021]	806.11 (-) [806.11]	21.39 (0.00) [-]
1217	WIDENING AND STRENFTHENING OF EXISITNG SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO	3/2014	5/2016 (-) [12/2019]	191.50 (192.00) [192.00]	136.19 (0.50) [43]
1218	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM	2/2015	10/2017 (-) [0/0]	239.91 (240.00) [160.00]	147.25 (-79.91) [0]
1219	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W	1/2015	4/2018 (-) [0/0]	326.63 (327.00) [326.63]	249.26 (0.00) [0]
1220	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG	6/2016	6/2018 (-) [0/0]	157.30 (157.00) [157.30]	97.29 (0.00) [0]
1221	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA	12/2011	11/2017 (-) [0/0]	159.39 (-) [159.39]	210.29 (0.00) [0]
1222	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA	12/2011	8/2015 (-) [12/2019]	191.08 (-) [191.08]	99.98 (0.00) [52]
1223	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA.	8/2016	2/2017 (-) [0/0]	287.70 (-) [287.70]	153.90 (0.00) [0]
1224	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA	3/2018	8/2018 (-) [0/0]	214.23 (-) [214.23]	23.44 (0.00) [0]
1225	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26.	3/2016	12/2016 (-) [0/0]	165.06 (-) [165.06]	92.59 (0.00) [0]
1226	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57	12/2016	8/2018	223.50	44.52

	(NAYAGARH TO KHURDA) IN THE STATE OF ODISHA		(-) [0/0]	(-) [223.50]	(0.00) [0]
1227	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA	3/2018	8/2018 (-) [0/0]	199.16 (-) [199.16]	25.63 (0.00) [0]
1228	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA	9/2016	2/2017 (-) [0/0]	295.67 (-) [295.67]	127.75 (0.00) [0]
1229	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA	12/2016	4/2018 (-) [0/0]	206.88 (-) [206.88]	41.69 (0.00) [0]
	Steel				
1230	INSTALLATION OF NEW HOT STRIP MILL AT RSP	4/2015	4/2018 (11/2019) [1/2020]	3,127.30 (-) [3,127.30]	3,119.34 (0.00) [21]
	Urban Development				
1231	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR	1/2019	3/2022 (-) [6/2022]	790.79 (-) [800.00]	11.01 (9.21) [3]
	PUNJAB				
	Fertilisers				
1232	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA	1/2018	11/2019 (-) [11/2019]	218.83 (-) [218.83]	131.34 (0.00) [0]
1233	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL	1/2018	11/2019 (-) [11/2019]	239.81 (-) [239.81]	145.72 (0.00) [0]
	Health And Family Welfare				
1234	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	7/2016	6/2020 (8/2020) [10/2020]	703.00 (-) [557.48]	283.12 (-145.52) [4]
1235	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	7/2016	2/2018 (-) [3/2020]	152.95 (-) [177.92]	139.70 (24.97) [25]
	Railways				
1236	QADIAN-BEAS	4/2011	/ (-) [3/2024]	205.22 (-) [841.90]	1.73 (636.68) [-]
	Road Transport And Highways				
1237	4 LANING FROM PHAGWARA TO RUPNAGAR	8/2016	/ (-) [4/2020]	1,169.61 (1,367.00) [1,169.61]	1,151.18 (0.00) [-]
1238	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600	11/2015	/ (9/2019) [0/0]	847.02 (-) [847.02]	795.00 (0.00) [0]
1239	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00	11/2015	/ (12/2019) [0/0]	889.24 (-) [904.82]	739.41 (15.58) [0]
1240	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	8/2016	9/2019 (3/2020) [3/2020]	1,388.34 (2,541.32) [2,587.50]	1,449.00 (1,199.16) [6]
1241	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN	3/2017	3/2020 (-) [4/2020]	754.54 (-) [756.27]	181.12 (1.73) [1]
1242	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS	12/2015	/ (9/2019) [0/0]	766.36 (-) [766.36]	685.36 (0.00) [0]
1243	FOUR LANING OF CHANDIGARH - KHARAR	10/2015	12/2017 (6/2020) [12/2019]	447.29 (746.43) [746.43]	613.57 (299.14) [24]
1244	FOUR LANING OF EXISTING TWO LANE WITH PS FROM	2/2018	/	261.76	92.25

	TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB		(-) [1/2021]	(-) [207.00]	(-54.76) [-]
1245	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION	9/2014	/ (-) [3/2020]	479.00 (-) [479.00]	453.80 (0.00) [-]
1246	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200	10/2017	10/2019 (12/2020) [12/2020]	1,069.59 (-) [1,069.59]	663.50 (0.00) [14]
1247	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI	3/2018	/ (-) [1/2020]	196.05 (149.90) [196.05]	143.03 (0.00) [-]
1248	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN	3/2018	/ (-) [0/0]	199.90 (149.90) [199.90]	92.61 (0.00) [0]
1249	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000	3/2018	11/2020 (-) [5/2021]	170.57 (192.48) [170.57]	46.23 (0.00) [6]
1250	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF	3/2018	6/2020 (-) [6/2020]	173.24 (-) [173.24]	56.66 (0.00) [0]
1251	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH	3/2018	7/2020 (-) [7/2020]	322.48 (-) [322.48]	120.18 (0.00) [0]
1252	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES	3/2018	8/2020 (-) [8/2020]	293.64 (-) [293.64]	28.24 (0.00) [0]
1253	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES	3/2018	8/2020 (-) [8/2020]	293.64 (-) [293.64]	134.32 (0.00) [0]
1254	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA	3/2018	8/2020 (-) [8/2020]	293.10 (-) [293.10]	63.14 (0.00) [0]
1255	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA	6/2015	/ (-) [0/0]	892.17 (-) [892.17]	648.44 (0.00) [0]
	Urban Development				
1256	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	2/2014	5/2017 (-) [12/2019]	388.00 (-) [488.28]	440.59 (100.28) [31]
1257	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	1/2018	5/2020 (-) [1/2021]	430.00 (-) [430.00]	97.92 (0.00) [8]
1258	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	8/2016	4/2019 (-) [2/2020]	294.00 (-) [294.00]	208.99 (0.00) [10]
	RAJASTHAN				
	Atomic Energy				
1259	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016 (-) [12/2020]	12,320.00 (-) [17,079.00]	11,387.00 (4,759.00) [48]
	Coal				
1260	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	3/2015	12/2019 (-) [12/2019]	513.63 (-) [513.63]	175.30 (0.00) [0]
1261	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	3/2015	9/2019 (-) [0/0]	522.45 (-) [522.45]	9.88 (0.00) [0]
	Petroleum				
1262	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II	11/2011	3/2013 (-) [0/0]	310.00 (-) [370.00]	17.84 (60.00) [0]

1263	LPG BP PROJECT JODHPUR	3/2018	/ (-) [3/2021]	229.80 (-) [229.80]	74.26 (0.00) [-]
	Railways				
1264	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	5/2015	/ (-) [0/0]	873.71 (-) [1,980.21]	4.60 (1,106.50) [0]
1265	AJMER-BANGURGRAM	4/2011	11/2019 (-) [5/2020]	213.39 (-) [303.56]	274.18 (90.17) [6]
1266	AJMER-KOTA (NASIRABAD-JAUNDRI)	4/2013	/ (-) [0/0]	822.00 (-) [1,099.54]	0.00 (277.54) [0]
1267	ALWAR-BANDIKUI DOUBLING	4/2013	2/2019 (-) [3/2020]	242.09 (281.03) [410.00]	362.96 (167.91) [13]
1268	BANGURGRAM-GURIYA PATCH DOUBLING	4/2012	12/2019 (-) [6/2020]	246.08 (-) [348.55]	229.00 (102.47) [6]
1269	DAUSA-GANGAPUR CITY(NL),NWR	2/1997	2/2019 (-) [3/2021]	410.08 (780.98) [886.41]	559.84 (476.33) [25]
1270	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM)	8/2018	8/2022 (-) [9/2022]	808.85 (-) [808.85]	60.28 (0.00) [1]
1271	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR	4/2013	3/2020 (-) [6/2020]	420.18 (-) [420.18]	184.64 (0.00) [3]
1272	MULTI MODAL LOGISTICS PARK AT KATHUWAS	1/2011	3/2018 (-) [3/2020]	493.17 (-) [493.17]	441.09 (0.00) [24]
1273	PUSHKAR-MERTA	4/2013	/ (-) [0/0]	323.00 (-) [432.22]	0.00 (109.22) [0]
1274	THIYAT HAMIRA-SANU	4/2013	10/2018 (-) [12/2019]	236.93 (-) [294.90]	226.61 (57.97) [14]
	Road Transport And Highways				
1275	2 LANING WITH PS OF GULABPURA - UNIARA	10/2015	10/2017 (4/2018) [3/2020]	597.00 (-) [597.00]	587.64 (0.00) [29]
1276	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR	8/2016	1/2019 (-) [10/2019]	320.30 (-) [320.30]	237.81 (0.00) [0]
1277	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA	11/2012	8/2016 (-) [12/2019]	530.07 (-) [530.07]	556.02 (0.00) [40]
1278	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A	7/2016	/ (5/2017) [11/2019]	688.70 (881.00) [688.70]	701.76 (0.00) [-]
1279	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE-	12/2016	/ (-) [8/2020]	1,031.95 (-) [1,031.95]	367.00 (0.00) [-]
1280	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN.	3/2019	/ (-) [0/0]	178.13 (-) [178.13]	16.35 (0.00) [0]
1281	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM	8/2014	4/2018 (-) [0/0]	822.90 (-) [822.90]	844.08 (0.00) [0]
1282	CITTORGARH-NEEMACH (4L) OF NH-79 AND NIMBAHARA PRATAPGARH (2L+PS) OF NH-113 UNDER PPP.	10/2012	10/2013 (-)	511.21 (-)	814.79 (0.00)

			[0/0]	[511.21]	[0]
1283	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM	3/2018	/ (-) [0/0]	1,158.35 (-) [1,158.35]	369.55 (0.00) [0]
1284	CONSTRUCTION OF 4 LANING BY CC PAVEMENT ON KOTA-DARAH OF NH-12 FROM 256/550 TO 289/550 UNDER EPC.	12/2015	10/2016 (-) [0/0]	621.43 (-) [621.43]	426.67 (0.00) [0]
1285	CONSTRUCTION OF NAGAUR BYPASS FROM EXISTING KM 166/260 TO KM 180/500 OF NH-65 ON EPC MODE.	3/2016	9/2016 (-) [0/0]	155.77 (-) [155.77]	99.92 (0.00) [0]
1286	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709	11/2017	4/2018 (-) [0/0]	163.95 (-) [163.95]	67.93 (0.00) [0]
1287	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH.	2/2018	/ (-) [0/0]	716.76 (-) [716.76]	232.06 (0.00) [0]
1288	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA	2/2018	/ (-) [0/0]	741.86 (-) [741.86]	0.00 (0.00) [0]
1289	DEVELOPMENT AND OPERATION OF BIKANER-SURATGARH SECTION OF NH-15 BY 2L+PS IN THE STATE OF RAJASTHAN	3/2009	9/2013 (-) [0/0]	501.00 (671.54) [671.54]	659.98 (170.54) [0]
1290	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAUR ROAD) SECTIO	12/2017	/ (-) [12/2020]	1,308.73 (-) [1,308.73]	99.68 (0.00) [-]
1291	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM	6/2016	6/2019 (-) [11/2019]	763.23 (-) [763.23]	439.88 (0.00) [5]
1292	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM	6/2016	6/2019 (-) [9/2019]	649.00 (-) [649.00]	320.14 (0.00) [0]
1293	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540	10/2017	10/2017 (-) [11/2020]	964.17 (-) [964.17]	390.91 (0.00) [37]
1294	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	2/2008	10/2011 (-) [0/0]	1,673.70 (-) [1,673.70]	3,326.93 (0.00) [0]
1295	NAGAUR-BIKANER OF NH-11 (2L+PS) UNDER PPP.	1/2012	1/2014 (-) [0/0]	378.07 (478.73) [478.73]	188.98 (100.66) [0]
1296	NETRA VILLAGE TO MANDORE SECTION OF NH-65 KM 267+500 TO 296+070 (4L) UNDER EPC.	10/2014	1/2015 (-) [0/0]	382.81 (-) [382.81]	335.93 (0.00) [0]
1297	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING	9/2012	10/2013 (-) [0/0]	511.00 (-) [511.00]	492.00 (0.00) [0]
1298	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A	9/2012	10/2013 (-) [0/0]	511.00 (-) [511.00]	2,323.04 (0.00) [0]
1299	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS	10/2013	5/2014 (-) [0/0]	278.87 (-) [278.87]	0.00 (0.00) [0]
1300	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	1/1991	4/2014 (-) [0/0]	376.52 (-) [376.52]	0.00 (0.00) [0]
1301	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I	9/2016	/ (-) [5/2020]	1,100.19 (-) [1,145.31]	967.00 (45.12) [-]
1302	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (	9/2016	/ (-) [5/2020]	1,239.82 (-) [1,239.82]	1,363.85 (0.00) [-]

1303	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV	4/2017	4/2020 (-) [11/2019]	894.00 (-) [929.32]	750.00 (35.32) [-5]
1304	TWO LANING WITH PAVED SHOULDER OF KARAUII - DHOLPUR	9/2014	9/2016 (9/2014) [10/2019]	425.19 (-) [425.19]	276.40 (0.00) [0]
1305	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR	8/2015	/ (2/2016) [10/2019]	275.90 (-) [275.90]	257.52 (0.00) [0]
1306	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM	7/2016	10/2018 (-) [0/0]	331.46 (-) [331.46]	267.94 (0.00) [0]
1307	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR	6/2016	6/2019 (-) [9/2019]	637.18 (-) [637.18]	588.00 (0.00) [0]
1308	UP-GRADATION TO 2 LANE WITH PAVED SHOULDER FOR SECTION FROM KM 118.900 TO KM 156.955 BALOTRA TOSANDE	1/2017	7/2017 (-) [0/0]	163.54 (-) [163.54]	106.15 (0.00) [0]
1309	UP-GRADATION TO TWO LANE WITH PAVED SHOULDER FOR SECTION FROM KM 58.000 TO KM 91.600 (BALOTRA TO SAN	1/2017	11/2017 (-) [0/0]	179.32 (-) [179.32]	113.12 (0.00) [0]
1310	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE - DANTOUR-JA	3/2018	/ (-) [0/0]	874.25 (-) [874.25]	195.00 (0.00) [0]
1311	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	2/2018	6/2018 (-) [0/0]	370.30 (-) [370.30]	207.58 (0.00) [0]
1312	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION	2/2018	/ (-) [9/2020]	1,103.88 (-) [1,103.88]	344.06 (0.00) [-]
1313	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	2/2018	5/2018 (-) [0/0]	341.79 (-) [341.79]	120.47 (0.00) [0]
1314	WIDENING AND STRENGHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING	10/2014	1/2015 (-) [0/0]	257.09 (-) [257.09]	14.18 (0.00) [0]
1315	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24	2/2015	3/2015 (-) [0/0]	383.40 (-) [383.40]	244.68 (0.00) [0]
1316	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K	10/2014	1/2015 (-) [0/0]	269.22 (-) [269.22]	33.24 (0.00) [0]
1317	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH	12/2015	6/2018 (-) [0/0]	621.43 (-) [621.43]	387.22 (0.00) [0]
1318	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR	11/2017	4/2018 (-) [0/0]	187.82 (-) [187.82]	59.14 (0.00) [0]
	Urban Development				
1319	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS	5/2015	3/2017 (-) [0/0]	189.00 (-) [189.00]	0.00 (0.00) [0]
1320	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	7/2019 (12/2019) [4/2020]	549.31 (559.47) [559.47]	373.45 (10.16) [9]
	SIKKIM				
	Railways				
1321	SEVOK RANGPO, NEFR	4/2008	12/2015 (-) [0/0]	1,339.48 (-) [4,084.69]	332.23 (2,745.21) [0]
	Road Transport And Highways				

1322	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	1/2013	2/2013 (-) [12/2019]	182.28 (-) [269.14]	185.49 (86.86) [82]
1323	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	4/2013	8/2013 (-) [12/2019]	151.59 (-) [151.59]	196.76 (0.00) [76]
1324	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	4/2013	8/2013 (-) [0/0]	166.27 (-) [166.27]	132.27 (0.00) [0]
1325	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [0/0]	375.80 (-) [375.80]	77.39 (0.00) [0]
1326	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017 (-) [0/0]	290.05 (-) [290.05]	35.34 (0.00) [0]
1327	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA	4/2017	11/2017 (-) [0/0]	318.42 (-) [318.42]	66.63 (0.00) [0]
1328	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	0.00 (0.00) [0]
1329	RHENOK-RORAHTHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [447.37]	142.95 (59.37) [0]
	TAMIL NADU				
	Atomic Energy				
1330	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	3/2013	11/2020 (-) [11/2023]	39,849.00 (-) [39,849.00]	15,706.00 (0.00) [36]
1331	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	9/2003	9/2010 (-) [10/2021]	3,492.00 (-) [6,840.00]	5,837.84 (3,348.00) [133]
	Civil Aviation				
1332	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	6/2018	2/2022 (-) [8/2022]	2,467.00 (-) [2,467.00]	213.17 (0.00) [6]
1333	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI	8/2018	10/2021 (-) [10/2021]	951.28 (-) [951.28]	71.55 (0.00) [0]
	Coal				
1334	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	4/2013	6/2015 (-) [0/0]	1,458.17 (709.06) [709.06]	461.66 (-749.11) [0]
1335	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	6/2011	12/2015 (-) [12/2019]	5,907.11 (7,080.41) [7,080.41]	6,867.42 (1,173.30) [48]
	Mines				
1336	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU	9/2017	6/2019 (3/2020) [3/2020]	166.62 (163.17) [163.17]	135.00 (-3.45) [9]
	Petroleum				
1337	AUGMENTATION OF CTMPL	12/2016	6/2020 (-) [6/2020]	228.00 (-) [228.00]	24.50 (0.00) [0]
1338	BS-VI PROJECTS	9/2017	12/2019 (-) [12/2019]	1,858.00 (-) [1,858.00]	1,119.38 (0.00) [0]
1339	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	12/2017	10/2020 (-) [8/2021]	466.43 (-) [466.43]	35.01 (0.00) [10]
1340	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY	5/2016	12/2018	4,497.00	990.22

	NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE		(-) [2/2021]	(6,025.00) [6,025.00]	(1,528.00) [26]
1341	ENNORE-TRICHY-MADURAI LPG PIPELINE	5/2013	6/2020 (-) [6/2020]	711.00 (-) [711.00]	11.12 (0.00) [0]
1342	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	11/2015	3/2019 (5/2020) [5/2020]	650.82 (-) [650.82]	415.38 (0.00) [14]
1343	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	2/2017 (-) [10/2021]	678.00 (-) [678.00]	7.28 (0.00) [56]
1344	RE-LIQUIFIED NATURAL GAS	8/2017	8/2020 (-) [8/2020]	421.00 (-) [421.00]	159.94 (0.00) [0]
1345	RESID UPGRADATION PROJECT	3/2013	11/2015 (-) [0/0]	3,110.36 (-) [3,110.36]	2,915.00 (0.00) [0]
	Power				
1346	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	5/2005	11/2008 (-) [0/0]	1,779.29 (-) [2,187.32]	2,237.45 (408.03) [0]
1347	TRANSMISSION SYSTEM FOR EVACUTION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY	5/2017	7/2019 (-) [1/2020]	186.17 (-) [186.17]	110.60 (0.00) [6]
	Railways				
1348	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING	2/1999	3/2018 (-) [0/0]	257.00 (257.00) [257.00]	268.31 (0.00) [0]
1349	ATTIPPATTU PUTTUR	4/2008	2/2019 (-) [0/0]	151.84 (-) [1,105.00]	3.34 (953.16) [0]
1350	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	4/2007	/ (-) [3/2020]	931.98 (-) [951.24]	738.83 (19.26) [-]
1351	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	4/1999	/ (-) [0/0]	198.68 (-) [556.64]	304.22 (357.96) [0]
1352	ERODE-PALANI	4/2008	/ (-) [0/0]	288.57 (-) [1,140.00]	1.63 (851.43) [0]
1353	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	4/2006	6/2013 (-) [0/0]	495.74 (-) [734.01]	445.91 (238.27) [0]
1354	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	2/2015	3/2020 (-) [6/2021]	760.00 (-) [1,182.31]	446.00 (422.31) [15]
1355	MADURAI-BODINAYAKKANUR	4/2008	/ (-) [3/2020]	164.41 (-) [450.00]	167.49 (285.59) [-]
1356	MANIYACHI - NAGERCOIL (102 KM) DOUBLING	2/2015	3/2022 (-) [3/2022]	1,700.00 (-) [1,003.00]	252.02 (-697.00) [0]
1357	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	9/2007	2/2019 (-) [2/2020]	724.69 (-) [2,072.50]	1,440.83 (1,347.81) [12]
1358	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM	10/2013	4/2014 (-) [3/2020]	187.26 (-) [231.67]	162.06 (44.41) [71]
1359	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	4/2013	/ (-) [0/0]	839.00 (-) [1,500.00]	0.62 (661.00) [0]

1360	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	2/1996	3/2005 (-) [0/0]	268.87 (-) [950.00]	927.86 (681.13) [0]
1361	TIDIVANAM-NAGARI (NL)	9/2006	/ (-) [0/0]	582.83 (-) [2,300.00]	241.58 (1,717.17) [0]
1362	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	9/2006	/ (-) [0/0]	227.40 (-) [900.00]	63.28 (672.60) [0]
1363	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	9/1995	3/2020 (-) [3/2021]	303.98 (-) [980.00]	681.66 (676.02) [12]
1364	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	2/2017	3/2024 (-) [3/2026]	1,567.00 (-) [1,567.00]	0.00 (0.00) [24]
	Road Transport And Highways				
1365	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	9/2011	8/2013 (-) [0/0]	485.00 (-) [485.00]	406.68 (0.00) [0]
1366	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHTH 170 KM)	4/2012	4/2014 (-) [0/0]	624.00 (-) [624.00]	350.79 (0.00) [0]
1367	4-LANNING OF OTTANCHATRAM BYPASS	9/2017	9/2017 (-) [4/2020]	244.27 (-) [244.27]	168.40 (0.00) [31]
1368	4-LANNING OF STHIYATHOPU-CHOLOPURAM	9/2017	9/2017 (-) [8/2020]	1,227.87 (-) [1,227.87]	330.29 (0.00) [35]
1369	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT	3/2015	8/2015 (-) [0/0]	258.97 (-) [268.92]	0.00 (9.95) [0]
1370	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I-	11/2015	8/2015 (-) [0/0]	154.14 (-) [154.14]	0.00 (0.00) [0]
1371	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	6/2011	6/2013 (1/2019) [8/2020]	600.00 (-) [600.00]	329.92 (0.00) [86]
1372	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS	3/2018	/ (-) [4/2021]	1,016.92 (-) [1,071.00]	0.00 (54.08) [-]
1373	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120	5/2015	11/2017 (-) [7/2019]	1,387.11 (-) [1,387.11]	980.46 (0.00) [0]
1374	FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300)	3/2018	/ (-) [11/2020]	628.71 (-) [628.71]	106.92 (0.00) [-]
1375	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N	3/2018	/ (-) [0/0]	2,065.96 (-) [2,169.00]	0.00 (103.04) [0]
1376	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU	2/2018	/ (-) [2/2021]	1,166.26 (-) [1,166.26]	163.29 (0.00) [-]
1377	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	3/2016	7/2016 (-) [5/2020]	641.17 (-) [641.17]	369.23 (0.00) [46]
1378	FOUR LANINIG OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3	3/2018	/ (-) [11/2020]	505.35 (-) [505.35]	36.14 (0.00) [-]
1379	FOUR LANNING OF CHOLOPURAM-THANJAVUR	8/2017	8/2017 (-) [9/2020]	1,176.37 (-) [1,176.37]	193.39 (0.00) [37]

1380	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	2/2016	8/2018 (-) [3/2020]	707.82 (-) [707.82]	375.47 (0.00) [19]
1381	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65.	3/2017	3/2020 (-) [3/2020]	848.45 (-) [848.45]	87.01 (0.00) [0]
1382	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K	2/2016	7/2018 (-) [5/2020]	641.17 (-) [641.17]	369.23 (0.00) [22]
1383	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO	3/2015	7/2015 (-) [0/0]	157.18 (162.00) [162.00]	0.00 (4.82) [0]
1384	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE	12/2017	/ (-) [3/2020]	379.90 (-) [379.90]	112.41 (0.00) [-]
1385	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	9/2011	12/2013 (-) [6/2020]	1,250.00 (-) [1,250.00]	1,333.68 (0.00) [78]
1386	THIRUMAYAM - MANAMADURAI SECTION	7/2014	1/2017 (-) [0/0]	401.11 (-) [401.11]	273.89 (0.00) [0]
1387	TRICHY - KARUR	3/2007	7/2008 (-) [0/0]	516.00 (-) [516.00]	886.70 (0.00) [0]
1388	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	5/2010	5/2013 (-) [0/0]	374.00 (-) [374.00]	237.00 (0.00) [0]
1389	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N	3/2018	/ (-) [0/0]	633.55 (-) [482.04]	0.00 (-151.51) [0]
1390	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	6/2015	12/2017 (-) [0/0]	563.92 (-) [563.92]	93.53 (0.00) [0]
	Urban Development				
1391	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	10/2019 (-) [7/2020]	209.00 (-) [209.00]	150.71 (0.00) [9]
1392	CHENNAI METRO RAIL LTD (PHASE 1 EXT)	6/2016	3/2018 (6/2020) [6/2020]	3,770.00 (-) [3,770.00]	2,086.51 (0.00) [27]
1393	CHENNAI METRO RAIL LTD (PHASE 1)	2/2009	12/2015 (-) [0/0]	14,600.00 (-) [19,058.00]	16,352.87 (4,458.00) [0]
1394	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI	11/2017	/ (-) [11/2021]	348.77 (-) [348.77]	31.97 (0.00) [-]
	TELANGANA				
	Coal				
1395	KALYANIKHANI 6 INCLINE PROJECT	12/2015	3/2020 (-) [3/2020]	477.65 (-) [477.65]	2.11 (0.00) [0]
1396	KOYAGUDEM OPENCAST PROJECT	10/2015	3/2018 (-) [3/2020]	426.79 (-) [426.79]	0.72 (0.00) [24]
1397	JALAGAM VENGALA RAO OCP-II	7/2011	3/2015 (-) [3/2021]	447.06 (-) [473.22]	18.35 (26.16) [72]
1398	KAKATIYA LONGWALL	12/2008	12/2012 (-) [0/0]	453.63 (-) [453.63]	121.91 (0.00) [0]
1399	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1	3/2017	3/2019	413.84	56.86

			(-) [3/2022]	(-) [413.84]	(0.00) [36]
1400	KAKATIYAKHANI OPENCAST-2 PROJECT	5/2015	3/2019 (-) [3/2020]	397.09 (-) [442.42]	99.42 (45.33) [12]
1401	KALYANIKHANI OPENCAST PROJECT	7/2012	7/2016 (-) [3/2020]	417.33 (-) [384.32]	112.52 (-33.01) [44]
1402	KISTARAM OCP	11/2010	3/2015 (-) [3/2021]	242.29 (-) [164.04]	119.85 (-78.25) [72]
1403	MANUGURU OC-II EXTENSION PHASE-II	3/2010	3/2012 (-) [0/0]	181.19 (-) [181.19]	170.60 (0.00) [0]
1404	RAMAGUNDAM OC-II EXTENSION	12/2009	3/2012 (-) [3/2023]	418.97 (-) [489.62]	353.10 (70.65) [132]
1405	RAMPURAM SHAFT BLOCK	8/2016	/ (3/2023) [0/0]	431.92 (-) [431.92]	0.00 (0.00) [0]
1406	RCE OF INDARAM OCP(1.20 MTPA)	7/2011	3/2015 (-) [3/2021]	162.76 (-) [349.28]	7.49 (186.52) [72]
1407	RFR OF MANUGURU OC PROJECT	11/2012	3/2016 (-) [3/2020]	430.45 (-) [415.37]	187.89 (-15.08) [48]
1408	RG OC -III EXTENSION (PHASE -II) PROJECT	6/2012	6/2015 (-) [3/2020]	365.01 (-) [365.01]	159.81 (0.00) [57]
1409	RKP OCP PHASE-I	3/2010	3/2015 (-) [3/2020]	209.78 (-) [209.78]	143.61 (0.00) [60]
1410	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	3/2012 (-) [3/2024]	249.03 (-) [448.86]	296.17 (199.83) [144]
1411	SRAVANAPALLI OPENCAST PROJECT	2/2018	/ (3/2023) [0/0]	412.70 (-) [412.70]	0.11 (0.00) [0]
1412	SRP OC-II EXPANSION PROJECT	11/2016	/ (4/2017) [3/2020]	272.73 (-) [272.73]	162.62 (0.00) [-]
	Petroleum				
1413	GRASS ROOT TERMINAL AT MALKAPUR	12/2018	4/2022 (-) [4/2022]	611.00 (-) [611.00]	13.11 (0.00) [0]
	Power				
1414	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	1/2016	11/2020 (6/2021) [6/2021]	10,598.98 (-) [10,598.98]	5,851.67 (0.00) [7]
	Railways				
1415	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	4/2012	3/2016 (-) [12/2020]	632.68 (-) [816.55]	701.83 (183.87) [57]
1416	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY	3/2015	3/2021 (-) [3/2021]	636.38 (-) [636.38]	281.85 (0.00) [0]
1417	MACHERLA-NALGONDA(NL)(SCR)	7/1998	/ (-) [0/0]	458.25 (458.25) [458.26]	3.83 (0.01) [0]
1418	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION	4/2017	3/2022 (-)	119.73 (185.00)	342.54 (270.87)

	AVOIDANCE SYSTEM (958 K		[3/2022]	[390.60]	[0]
1419	MANOHARABAD-KOTHPALL NEW LINE(SCR)	4/2006	3/2010 (-) [3/2023]	1,160.48 (1,160.48) [1,160.48]	323.09 (0.00) [156]
1420	MANUGURU-RAMAGUNDAM	4/2013	/ (-) [0/0]	1,112.00 (2,911.84) [2,911.84]	0.92 (1,799.84) [0]
1421	SECUNDERABAD-MAHABUBNAGAR DOUBLING	4/2015	12/2024 (-) [12/2024]	773.94 (-) [773.94]	475.85 (0.00) [0]
	Road Transport And Highways				
1422	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	4/2014	9/2016 (-) [9/2019]	1,266.60 (1,544.00) [1,544.00]	1,446.45 (277.40) [0]
1423	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH	1/2018	5/2020 (-) [5/2020]	283.15 (-) [283.15]	42.22 (0.00) [0]
1424	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES	3/2018	7/2020 (-) [7/2020]	626.76 (-) [626.76]	80.66 (0.00) [0]
1425	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM	3/2015	1/2017 (-) [9/2019]	153.21 (-) [153.21]	100.10 (0.00) [0]
1426	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB	3/2017	3/2017 (-) [0/0]	4,429.00 (-) [4,429.00]	0.00 (0.00) [0]
1427	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3	3/2018	/ (-) [0/0]	857.62 (-) [857.62]	1.61 (0.00) [0]
1428	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K	3/2018	/ (-) [0/0]	802.65 (-) [802.65]	81.03 (0.00) [0]
1429	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM	3/2018	/ (-) [0/0]	950.63 (-) [950.63]	173.59 (0.00) [0]
1430	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT	3/2018	/ (11/2019) [0/0]	828.29 (998.89) [828.29]	0.00 (0.00) [0]
1431	FOUR LANING OF YADGIRI - WARANGAL	12/2015	11/2018 (7/2019) [3/2020]	1,423.96 (897.03) [897.03]	757.88 (-526.93) [16]
1432	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365	3/2018	7/2019 (-) [12/2019]	192.67 (-) [192.67]	107.37 (0.00) [5]
1433	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR	1/2017	10/2019 (-) [10/2019]	605.08 (-) [605.08]	273.88 (0.00) [0]
1434	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN	2/2018	4/2020 (-) [4/2020]	426.52 (-) [426.52]	225.51 (0.00) [0]
1435	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT	1/2014	3/2016 (-) [0/0]	270.00 (-) [270.00]	19.84 (0.00) [0]
1436	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT	2/2018	11/2019 (-) [11/2019]	294.13 (-) [294.13]	39.44 (0.00) [0]
1437	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS	2/2018	11/2019 (-) [11/2019]	220.28 (-) [220.28]	37.58 (0.00) [0]
1438	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO	3/2018	9/2020 (-)	322.81 (-)	1.66 (0.00)

	KODAD SEC		[9/2020]	[322.81]	[0]
1439	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ	10/2016	3/2019 (-) [3/2020]	248.83 (-) [248.83]	91.52 (0.00) [12]
1440	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON	10/2016	2/2019 (-) [6/2020]	298.32 (-) [298.32]	83.57 (0.00) [16]
1441	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4	1/2018	12/2019 (-) [12/2019]	230.03 (-) [230.03]	127.98 (0.00) [0]
1442	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59	2/2018	6/2020 (-) [6/2020]	206.13 (-) [206.13]	127.86 (0.00) [0]
1443	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR	1/2019	/ (-) [0/0]	193.19 (-) [193.19]	0.00 (0.00) [0]
1444	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH	1/2017	10/2019 (-) [12/2019]	196.52 (-) [196.52]	103.22 (0.00) [2]
1445	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI	1/2017	12/2019 (-) [12/2019]	283.00 (-) [283.00]	166.22 (0.00) [0]
1446	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE	1/2017	5/2019 (9/2019) [12/2019]	244.54 (-) [244.54]	138.52 (0.00) [7]
1447	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT	1/2017	5/2019 (-) [12/2019]	359.27 (-) [359.27]	237.90 (0.00) [7]
1448	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION	1/2017	5/2019 (-) [3/2020]	300.00 (-) [300.00]	100.33 (0.00) [10]
	Urban Development				
1449	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	10/2016	3/2020 (-) [5/2021]	209.84 (-) [209.84]	58.75 (0.00) [14]
	TRIPURA				
	Civil Aviation				
1450	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	9/2015	6/2019 (-) [12/2019]	338.93 (-) [339.00]	213.50 (0.07) [6]
	Railways				
1451	AGARTALA-AKHAURA NL	4/2012	3/2020 (9/2021) [9/2021]	569.63 (670.00) [670.00]	107.83 (100.37) [18]
	Road Transport And Highways				
1452	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (12/2019) [0/0]	369.00 (-) [369.00]	316.74 (0.00) [0]
1453	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C	10/2016	8/2020 (-) [8/2020]	171.90 (-) [171.90]	14.77 (0.00) [0]
	Urban Development				
1454	CONSTRUCTION AND MAINTEINANCE OF RURAL ROAD UNDER PMGSY PHASE V	3/2007	12/2015 (-) [0/0]	149.73 (173.00) [175.94]	176.65 (26.21) [0]
1455	CONSTRUCTION AND MAINTEINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016 (-) [0/0]	202.61 (227.00) [227.00]	199.95 (24.39) [0]
1456	CONSTRUCTION AND MAINTEINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016 (-) [0/0]	175.49 (206.71) [206.71]	141.28 (31.22) [0]

	UTTAR PRADESH				
	Civil Aviation				
1457	CCS INTERNATIONAL AIRPORT , LUCKNOW	6/2018	9/2021 (-) [9/2021]	1,383.00 (-) [1,383.00]	210.62 (0.00) [0]
	Coal				
1458	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	7/2016	11/2021 (-) [11/2021]	17,237.00 (-) [17,237.80]	8,032.77 (0.80) [0]
	Health And Family Welfare				
1459	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	7/2016	4/2020 (6/2020) [10/2020]	785.00 (-) [715.06]	345.41 (-69.94) [6]
1460	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI	3/2018	/ (-) [4/2020]	268.84 (-) [268.84]	157.76 (0.00) [-]
	Petroleum				
1461	120 TMTPA LPG BOTTLING PLANT AT GORAKHPUR UP	3/2014	9/2019 (-) [0/0]	204.00 (-) [204.00]	148.58 (0.00) [0]
1462	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A	3/2018	12/2021 (-) [12/2021]	676.00 (-) [676.00]	251.64 (0.00) [0]
1463	BS-VI PROJECT AT MATHURA REFINERY	1/2018	9/2019 (-) [1/2020]	666.64 (-) [666.64]	468.46 (0.00) [4]
1464	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI	4/2017	4/2022 (-) [4/2022]	287.49 (-) [287.49]	133.40 (0.00) [0]
1465	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY	8/2017	8/2020 (-) [8/2020]	255.40 (-) [255.40]	4.07 (0.00) [0]
1466	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL	12/2017	12/2021 (-) [12/2021]	1,524.06 (-) [1,524.06]	20.02 (0.00) [0]
1467	REDEVELOPMENT/ EXPANSION OF MEERUT DEPOT FOR ENHANCING PRODUCT HANDLING CAPACITY	8/2016	11/2019 (-) [11/2019]	154.84 (-) [154.84]	128.71 (0.00) [0]
1468	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR	8/2017	8/2021 (-) [11/2021]	318.80 (-) [318.80]	52.67 (0.00) [3]
	Power				
1469	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP	12/2018	9/2020 (-) [9/2020]	587.44 (-) [587.44]	250.00 (0.00) [0]
1470	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP	3/2019	11/2020 (-) [11/2020]	349.00 (-) [349.00]	125.00 (0.00) [0]
1471	DHUKWAN SMALL HYDRO PROJECT	5/2011	2/2014 (-) [12/2019]	195.42 (-) [294.60]	321.11 (99.18) [70]
1472	KHURJA SUPER THERMAL POWER PROJECT	3/2019	9/2023 (-) [9/2023]	11,089.42 (-) [11,089.42]	672.81 (0.00) [0]
1473	MUNPL-MEJA TPP - JV (2X660 MW)	4/2012	2/2017 (6/2020) [6/2020]	9,750.89 (-) [12,176.28]	10,032.00 (2,425.39) [40]
1474	TANDA TPP STAGE-II (2X660 MW)	9/2014	7/2019 (3/2020) [7/2020]	9,188.98 (-) [10,016.10]	6,633.23 (827.12) [12]
	Railways				

1475	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	3/2013	/ (-) [0/0]	307.00 (-) [1,409.09]	0.00 (1,102.09) [0]
1476	AUNRIHAR - JAUNPUR PATCH DOUBLING .	4/2016	1/2022 (-) [1/2022]	600.00 (-) [600.00]	31.72 (0.00) [0]
1477	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI.	4/2016	1/2022 (-) [1/2022]	1,900.00 (-) [1,277.06]	0.00 (-622.94) [0]
1478	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	3/2012	12/2020 (-) [12/2022]	1,183.25 (-) [1,183.25]	1,136.44 (0.00) [24]
1479	BURHWAL - GONDA - 3RD RUNNING LINE.	4/2016	/ (-) [0/0]	602.50 (-) [714.34]	18.40 (111.84) [0]
1480	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	2/2008	3/2012 (-) [0/0]	171.10 (-) [275.08]	141.55 (103.98) [0]
1481	ETAH - KASGANJ - NEW LINE	4/2017	4/2017 (-) [4/2022]	276.90 (-) [276.90]	0.00 (0.00) [60]
1482	ETAWAH-MAINPURI (NL),NCR	4/1997	12/2008 (-) [0/0]	120.00 (-) [346.00]	345.51 (226.00) [0]
1483	GHAZIPUR - AUNRIHAR (40 KM)	4/2014	/ (-) [0/0]	182.92 (-) [197.73]	0.00 (14.81) [0]
1484	INDARA - DOHRIGHAT GAUGE CONVERSION.	4/2016	4/2016 (-) [6/2020]	213.00 (-) [213.35]	9.62 (0.35) [50]
1485	JHANSI BINA DOUBLING	9/2016	3/2021 (-) [3/2021]	2,001.00 (-) [2,001.00]	416.59 (0.00) [0]
1486	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING	3/2018	3/2023 (-) [3/2023]	4,329.53 (-) [4,329.53]	3.90 (0.00) [0]
1487	KAPILVASTU-BASTI VIA BANSI SIDHARTHNAGAR BASTI NAUGARH UP	3/2013	/ (-) [0/0]	643.00 (-) [644.00]	0.00 (1.00) [0]
1488	KARAILA ROAD - SHAKTINAGAR DOUBLING	8/2015	3/2019 (-) [12/2019]	528.57 (-) [528.57]	118.49 (0.00) [9]
1489	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	4/2011	3/2019 (-) [3/2020]	927.01 (-) [1,200.00]	1,178.67 (272.99) [12]
1490	MATHURA-PLWAL 4TH LINE (80KM)	4/2015	3/2020 (-) [3/2020]	668.70 (668.00) [680.00]	330.00 (11.30) [0]
1491	MAU-GHAZIPUR-TARIGHAT NEW LINE	4/2015	3/2023 (-) [12/2024]	1,765.92 (-) [1,765.92]	650.11 (0.00) [21]
1492	NANPARA - NEPALGANJ GAUGE CONVERSION.	4/2017	4/2017 (-) [10/2022]	150.00 (-) [150.00]	0.00 (0.00) [66]
1493	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE	4/2017	1/2018 (-) [0/0]	1,343.00 (-) [1,476.15]	0.00 (133.15) [0]
1494	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION	4/2017	4/2017 (-) [1/2020]	622.50 (427.00) [426.74]	195.35 (-195.76) [33]
1495	RAMNA - SINGRAULI DOUBLING	8/2015	3/2020	2,436.21	597.94

			(-) [3/2021]	(-) [2,436.21]	(0.00) [12]
1496	ROSA-SITAPUR CANTT-BURHWAL DOUBLING	3/2015	3/2022 (-) [12/2019]	1,295.42 (-) [1,295.42]	350.85 (0.00) [-27]
1497	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	4/2016	12/2019 (-) [4/2021]	1,177.96 (-) [1,028.95]	26.06 (-149.01) [16]
1498	UNCHAHAR-AMETHI	4/2012	/ (-) [3/2023]	1,229.00 (-) [1,230.00]	103.72 (1.00) [-]
1499	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	4/2015	3/2022 (-) [12/2024]	943.60 (-) [750.56]	409.09 (-193.04) [33]
	Road Transport And Highways				
1500	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125	9/2015	9/2016 (3/2018) [3/2018]	368.73 (-) [368.73]	239.04 (0.00) [0]
1501	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE	11/2010	3/2017 (-) [0/0]	305.49 (-) [305.49]	131.08 (0.00) [0]
1502	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	4/2014	1/2016 (-) [0/0]	351.34 (-) [351.34]	433.68 (0.00) [0]
1503	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI	4/2014	1/2016 (-) [0/0]	495.78 (-) [495.78]	633.24 (0.00) [0]
1504	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	7/2012	1/2014 (-) [0/0]	291.36 (-) [291.36]	459.07 (0.00) [0]
1505	2-LANING WITH PS SITARGANJ BAREILY SECTION	6/2014	1/2016 (-) [0/0]	301.04 (-) [301.04]	207.94 (0.00) [0]
1506	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500	8/2016	4/2019 (-) [11/2019]	2,016.00 (-) [2,016.00]	1,996.00 (0.00) [7]
1507	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C	3/2018	/ (-) [0/0]	1,120.57 (1,332.00) [1,332.00]	183.54 (211.43) [0]
1508	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (	3/2016	/ (-) [1/2020]	1,668.00 (-) [1,668.00]	946.08 (0.00) [-]
1509	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	12/2015	6/2016 (-) [0/0]	611.65 (-) [611.65]	728.24 (0.00) [0]
1510	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00	3/2016	/ (-) [7/2020]	1,408.00 (-) [1,408.00]	442.70 (0.00) [-]
1511	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00	3/2016	/ (-) [4/2020]	1,737.00 (-) [1,737.00]	1,159.07 (0.00) [-]
1512	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKPUR)	3/2016	/ (3/2017) [0/0]	1,404.50 (3,267.94) [1,404.50]	2,977.58 (0.00) [0]
1513	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	3/2016	4/2019 (-) [0/0]	1,587.49 (-) [2,982.00]	276.87 (1,394.51) [0]
1514	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPU	3/2016	/ (-) [0/0]	1,396.74 (-) [1,396.74]	227.26 (0.00) [0]
1515	6 LANING OF AGRA - ETAWAH BYPASS	7/2015	1/2019	1,657.20	2,345.00

			(-) [0/0]	(-) [1,657.20]	(0.00) [0]
1516	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	3/2017	3/2020 (6/2020) [6/2020]	2,064.99 (-) [2,447.00]	1,896.03 (382.01) [3]
1517	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN	12/2017	/ (3/2020) [12/2020]	207.00 (-) [207.00]	34.77 (0.00) [-]
1518	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020	3/2016	4/2019 (-) [0/0]	676.73 (-) [676.73]	945.17 (0.00) [0]
1519	BAREILY-SITAPUR (NH-24)	3/2011	9/2013 (-) [0/0]	1,046.00 (-) [1,046.00]	805.19 (0.00) [0]
1520	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA	2/2018	/ (2/2019) [0/0]	972.77 (1,444.25) [972.77]	494.71 (0.00) [0]
1521	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T	12/2016	/ (-) [9/2019]	534.55 (-) [531.00]	433.62 (-3.55) [0]
1522	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O	12/2017	/ (-) [0/0]	305.00 (-) [305.00]	0.00 (0.00) [0]
1523	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO	3/2018	/ (-) [12/2021]	1,117.84 (-) [1,117.84]	0.00 (0.00) [-]
1524	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650	1/2017	/ (-) [0/0]	450.68 (-) [450.68]	397.62 (0.00) [0]
1525	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B	1/2014	3/2016 (-) [0/0]	282.41 (-) [282.41]	155.53 (0.00) [0]
1526	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM	1/2016	6/2019 (12/2016) [9/2019]	1,081.57 (-) [1,057.60]	1,024.76 (-23.97) [0]
1527	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM	12/2017	/ (2/2018) [5/2020]	1,232.21 (3,207.63) [1,087.00]	502.12 (-145.21) [-]
1528	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO	3/2017	3/2020 (11/2017) [5/2020]	1,989.00 (2,602.09) [1,989.00]	882.41 (0.00) [2]
1529	ETAWAH CHAKERI	3/2013	9/2015 (-) [0/0]	1,573.00 (-) [1,573.00]	2,078.25 (0.00) [0]
1530	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP	2/2018	/ (-) [0/0]	670.50 (-) [670.50]	25.44 (0.00) [0]
1531	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS	3/2018	/ (-) [0/0]	809.07 (1,065.70) [809.07]	107.50 (0.00) [0]
1532	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR.	3/2018	/ (-) [0/0]	925.40 (1,197.00) [1,197.00]	401.68 (271.60) [0]
1533	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	12/2015	6/2018 (-) [4/2020]	667.00 (3,007.86) [667.00]	549.07 (0.00) [22]
1534	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)	6/2016	7/2018 (-) [4/2020]	667.00 (2,257.49) [667.00]	464.05 (0.00) [21]
1535	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	1/2016	6/2018 (-)	1,027.53 (2,433.38)	601.13 (0.00)

			[6/2020]	[1,027.53]	[24]
1536	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II)	1/2016	6/2018 (-) [6/2020]	815.28 (2,182.03) [815.28]	520.89 (0.00) [24]
1537	FOUR LANING OF VARANASI BYPASS	5/2015	5/2017 (-) [0/0]	261.09 (275.00) [261.09]	240.96 (0.00) [0]
1538	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J	3/2018	8/2020 (-) [8/2020]	288.30 (-) [288.30]	0.34 (0.00) [0]
1539	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	3/2017	3/2020 (-) [11/2020]	1,373.28 (-) [1,373.28]	571.96 (0.00) [8]
1540	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	3/2017	3/2020 (-) [8/2020]	1,184.71 (-) [1,310.00]	563.15 (125.29) [5]
1541	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791	3/2016	4/2019 (7/2020) [7/2020]	899.00 (-) [899.00]	561.27 (0.00) [15]
1542	GHAZIABAD-ALIGARH NH-91	2/2011	8/2013 (-) [0/0]	1,141.00 (-) [1,141.00]	1,715.42 (0.00) [0]
1543	IMPROVEMENT AND UP-GRADATION OF EXISITING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T	11/2018	/ (-) [0/0]	281.45 (-) [281.45]	0.00 (0.00) [0]
1544	MEERUT-BULANDSHAHAR	1/2016	/ (10/2019) [2/2020]	683.24 (868.77) [987.94]	727.69 (304.70) [-]
1545	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404	12/2016	10/2019 (4/2020) [4/2020]	209.10 (-) [209.10]	159.51 (0.00) [6]
1546	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS	11/2016	/ (-) [0/0]	326.99 (327.00) [326.99]	0.00 (0.00) [0]
1547	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS	3/2016	9/2020 (-) [9/2020]	296.50 (-) [296.50]	40.27 (0.00) [0]
1548	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU	3/2018	/ (-) [0/0]	1,025.80 (-) [677.07]	156.01 (-348.73) [0]
1549	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA	3/2018	/ (-) [0/0]	1,115.28 (-) [770.04]	260.94 (-345.24) [0]
1550	REHABILITATION AND UPGRADATION OF ALLAHABAD - MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2-	10/2016	2/2019 (-) [7/2019]	239.63 (-) [239.63]	212.09 (0.00) [0]
1551	REHABILITATION AND UPGRADATION OF BARAICH - SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA	3/2016	12/2019 (-) [12/2019]	388.83 (-) [388.83]	304.47 (0.00) [0]
1552	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750	3/2018	4/2020 (-) [4/2020]	263.89 (242.05) [242.05]	139.38 (-21.84) [0]
1553	REHABILITATION AND UPGRADATION OF HARPALPUR - SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE	3/2016	11/2019 (-) [12/2019]	208.50 (-) [208.50]	139.97 (0.00) [1]
1554	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH	10/2013	3/2017 (-) [10/2019]	445.89 (653.00) [653.29]	464.07 (207.40) [0]
1555	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F	3/2016	1/2020 (-) [1/2020]	599.34 (-) [599.34]	485.53 (0.00) [0]

1556	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF	3/2018	2/2020 (-) [2/2020]	185.18 (-) [185.18]	65.66 (0.00) [0]
1557	REHABILITATION AND UPGRADATION OF TULSIPUR - BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730	3/2016	5/2019 (-) [3/2020]	249.50 (-) [249.50]	156.70 (0.00) [10]
1558	REHABILITATION AND UPGRADATION OF ALLAHABAD - MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT	10/2016	3/2020 (-) [3/2020]	218.90 (-) [218.90]	62.69 (0.00) [0]
1559	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230	3/2018	/ (-) [0/0]	306.59 (-) [306.59]	0.00 (0.00) [0]
1560	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P	11/2016	9/2019 (-) [10/2019]	215.16 (215.00) [215.16]	160.46 (0.00) [0]
1561	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH	3/2016	1/2020 (-) [1/2020]	240.30 (240.00) [240.30]	198.06 (0.00) [0]
1562	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA	10/2016	3/2020 (-) [3/2020]	218.94 (219.00) [218.94]	103.89 (0.00) [0]
1563	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO	10/2016	10/2018 (-) [9/2019]	176.94 (177.00) [176.94]	141.11 (0.00) [0]
1564	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO	7/2016	10/2019 (-) [12/2019]	208.88 (-) [208.88]	88.62 (0.00) [2]
1565	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	10/2013	3/2017 (-) [0/0]	445.89 (-) [653.29]	464.05 (207.40) [0]
1566	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH – 14	11/2017	1/2019 (-) [0/0]	2,159.00 (-) [2,159.00]	831.09 (0.00) [0]
1567	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA	3/2018	/ (-) [0/0]	2,140.93 (-) [2,140.93]	1,229.85 (0.00) [0]
1568	VARANASI RING ROAD PKG - I	1/2018	/ (-) [0/0]	450.77 (929.89) [450.77]	0.00 (0.00) [0]
1569	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH	5/2013	8/2015 (-) [0/0]	164.54 (165.00) [164.54]	89.14 (0.00) [0]
1570	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE	5/2013	8/2015 (-) [12/2019]	164.54 (-) [164.54]	126.41 (0.00) [52]
	Steel				
1571	FORGED WHEEL PLANT	4/2014	9/2018 (12/2019) [12/2019]	1,682.85 (-) [1,682.85]	1,270.63 (0.00) [15]
	Urban Development				
1572	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR	11/2017	3/2020 (-) [3/2020]	171.72 (-) [171.72]	32.00 (0.00) [0]
1573	LUCKNOW METRO RAIL CORPORATION LTD	1/2016	3/2019 (-) [0/0]	6,928.00 (6,928.00) [6,928.00]	2,536.77 (0.00) [0]
	Water Resources				
1574	FARRUKHABAD I AND D AND STP WORKS HAM	10/2017	3/2022 (-) [3/2022]	213.62 (-) [213.62]	0.00 (0.00) [0]
1575	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN	3/2018	9/2021	904.00	0.00

	ALLAHABAD ALONG WITH EXISTING ASSETS		(-) [9/2021]	(-) [904.00]	(0.00) [0]
1576	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH	1/2019	10/2021 (-) [10/2021]	206.05 (-) [206.05]	0.00 (0.00) [0]
1577	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH	1/2019	12/2021 (-) [12/2021]	231.79 (-) [231.79]	0.00 (0.00) [0]
1578	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH	3/2019	8/2021 (-) [8/2021]	271.39 (-) [271.39]	0.00 (0.00) [0]
1579	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH	3/2019	7/2021 (-) [7/2021]	298.12 (-) [298.12]	0.00 (0.00) [0]
1580	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA	5/2017	9/2021 (-) [9/2021]	767.59 (-) [767.59]	0.00 (0.00) [0]
1581	MATHURA SEWERAGE SCHEME	12/2017	12/2020 (-) [12/2020]	460.45 (-) [460.45]	0.00 (0.00) [0]
1582	REHABILITATION RENOVATION OF AGRA SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS IN AGRA UTTAR PR	12/2018	8/2021 (-) [8/2021]	857.26 (-) [857.26]	0.00 (0.00) [0]
1583	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA	2/2017	11/2019 (-) [11/2019]	161.31 (-) [161.31]	0.00 (0.00) [0]
1584	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH	2/2019	6/2022 (-) [6/2022]	681.78 (-) [681.78]	0.00 (0.00) [0]
1585	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS AT AGRA	2/2019	8/2021 (-) [8/2021]	317.19 (-) [317.19]	0.00 (0.00) [0]
1586	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	2/2011	12/2019 (-) [12/2019]	279.91 (-) [279.91]	0.00 (0.00) [0]
1587	SEWERAGE WORKS IN SEWERAGE DISTRICT A OF ALLAHABAD	2/2014	9/2019 (-) [9/2019]	288.94 (-) [288.94]	0.00 (0.00) [0]
1588	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR	10/2016	8/2020 (-) [8/2020]	370.40 (-) [370.40]	0.00 (0.00) [0]
1589	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS	3/2018	9/2021 (-) [9/2021]	967.23 (-) [967.23]	0.00 (0.00) [0]
	UTTARAKHAND				
	Civil Aviation				
1590	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN	7/2018	9/2020 (-) [9/2020]	353.27 (-) [353.27]	114.29 (0.00) [0]
	Petroleum				
1591	SITARGANJ LPG PROJECT	2/2017	2/2020 (-) [10/2020]	160.10 (-) [160.10]	51.57 (0.00) [8]
	Power				
1592	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	7/2012	8/2017 (-) [0/0]	1,527.00 (-) [1,801.07]	148.93 (274.07) [0]
1593	NAITWAR MORI HEP	10/2017	12/2021 (-) [12/2021]	648.33 (-) [648.33]	284.44 (0.00) [0]
1594	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	3/2013	2,978.48	4,264.84

			(12/2020) [1/2021]	(5,867.38) [5,867.38]	(2,888.90) [94]
1595	TEHRI PUMPED STORAGE PLANT(1000MW)	7/2006	2/2016 (-) [6/2022]	1,657.00 (-) [5,024.35]	3,118.00 (3,367.35) [76]
1596	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	8/2008	6/2013 (-) [12/2022]	2,491.58 (-) [4,397.80]	1,823.10 (1,906.22) [114]
	Railways				
1597	HARIDWAR-LAKSAR	4/2012	/ (-) [6/2020]	219.83 (346.63) [346.63]	233.23 (126.80) [-]
1598	KICHHA-KHATIMA (NL) - NER	4/2003	/ (-) [0/0]	142.45 (-) [228.40]	0.15 (85.95) [0]
1599	RISHIKESH - KARNAPRAYAG NEW LINE	4/2011	12/2024 (-) [3/2025]	16,216.00 (-) [16,216.00]	1,790.80 (0.00) [3]
	Road Transport And Highways				
1600	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI	3/2018	6/2018 (-) [0/0]	403.36 (-) [403.36]	99.65 (0.00) [0]
1601	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA	3/2018	5/2018 (-) [0/0]	417.24 (-) [417.24]	112.62 (0.00) [0]
1602	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	11/2012	7/2018 (12/2019) [2/2020]	605.84 (-) [722.46]	723.95 (116.62) [19]
1603	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900	3/2016	/ (-) [2/2020]	1,443.00 (-) [1,443.00]	1,246.85 (0.00) [-]
1604	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399	3/2018	5/2018 (-) [0/0]	274.31 (-) [274.31]	29.13 (0.00) [0]
1605	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK)	3/2018	7/2018 (-) [0/0]	1,383.78 (-) [1,383.78]	117.49 (0.00) [0]
1606	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN	5/2018	5/2020 (-) [5/2020]	248.00 (-) [248.00]	0.00 (0.00) [0]
1607	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88	3/2016	/ (10/2020) [10/2020]	720.00 (-) [720.00]	322.19 (0.00) [-]
1608	HARIDWAR DEHRADUN APPROVED LENGTH 69	11/2011	10/2013 (-) [2/2020]	478.51 (-) [478.00]	315.11 (-0.51) [76]
1609	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG	11/2017	11/2019 (-) [11/2019]	232.81 (-) [232.81]	59.44 (0.00) [0]
1610	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION	11/2017	11/2019 (-) [11/2019]	283.51 (-) [283.51]	126.38 (0.00) [0]
1611	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (-) [12/2019]	257.34 (-) [257.34]	62.79 (0.00) [0]
1612	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (-) [12/2019]	200.34 (-) [200.34]	31.00 (0.00) [0]
1613	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	6/2017	6/2019 (-) [12/2019]	282.08 (-) [282.08]	77.05 (0.00) [6]

1614	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR	2/2018	2/2020 (-) [2/2020]	418.88 (-) [418.88]	88.00 (0.00) [0]
1615	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (-) [11/2019]	266.52 (-) [266.52]	144.27 (0.00) [0]
1616	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER	8/2016	12/2017 (-) [12/2019]	234.88 (-) [208.89]	118.26 (-25.99) [24]
1617	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K	2/2018	/ (-) [0/0]	293.68 (-) [293.68]	11.57 (0.00) [0]
1618	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00	3/2018	/ (-) [0/0]	460.73 (-) [461.00]	0.00 (0.27) [0]
1619	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00	12/2017	12/2019 (-) [12/2019]	248.22 (-) [248.22]	57.20 (0.00) [0]
	Urban Development				
1620	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	12/2013 (-) [0/0]	114.26 (266.00) [266.00]	0.00 (151.74) [0]
	Water Resources				
1621	INTERCEPTION AND DIVERSION (I&D)WITH STP AT RISHIKESH	3/2017	11/2019 (-) [11/2019]	158.00 (-) [158.00]	0.00 (0.00) [0]
1622	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI	3/2017	8/2019 (-) [8/2019]	273.37 (-) [273.37]	0.00 (0.00) [0]
	WEST BENGAL				
	Civil Aviation				
1623	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA	1/2019	11/2021 (-) [11/2021]	264.99 (-) [264.99]	0.42 (0.00) [0]
1624	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	1/2016	3/2020 (-) [12/2020]	219.91 (-) [219.91]	65.45 (0.00) [9]
	Coal				
1625	JHANJRA COMBINED PR(3.50 MTY)	11/2015	3/2022 (-) [3/2022]	602.86 (-) [602.86]	317.12 (0.00) [0]
1626	NAKRAKONDA KUMARDIH B OCP	8/2018	3/2029 (-) [3/2029]	502.68 (-) [502.68]	0.00 (0.00) [0]
1627	RANIGANJ MASTER PLAN	8/2009	8/2019 (-) [8/2024]	2,661.73 (-) [5,173.26]	336.63 (2,511.53) [60]
1628	SIDULI MINE (OC AND UG)	5/2018	3/2026 (-) [3/2026]	535.18 (-) [535.18]	0.00 (0.00) [0]
1629	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	8/2012	3/2018 (-) [10/2020]	1,055.05 (-) [1,055.05]	528.96 (0.00) [31]
1630	TILABONI UG MINE	2/2019	3/2027 (-) [3/2027]	916.62 (-) [916.62]	0.00 (0.00) [0]
	Health And Family Welfare				
1631	CNCI KOLKATA WEST BENGAL	8/2016	9/2018 (-) [5/2019]	244.00 (-) [248.00]	224.92 (4.00) [0]
1632	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	5/2017	168.90	169.51

			(-) [7/2019]	(-) [191.20]	(22.30) [0]
1633	HOSPITAL AND TEACHING- AIIMS KALYANI	4/2018	/ (-) [7/2020]	651.99 (-) [651.99]	232.42 (0.00) [-]
1634	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	8/2017	3/2019 (-) [7/2020]	355.15 (-) [355.15]	217.00 (0.00) [16]
	Petroleum				
1635	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL	3/2018	9/2022 (-) [6/2021]	3,712.00 (-) [3,696.00]	683.33 (-16.00) [-15]
1636	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY	5/2018	9/2019 (-) [4/2020]	2,934.40 (-) [2,934.40]	1,780.52 (0.00) [7]
1637	DURGAPUR-HALDIA PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	1,740.00 (-) [1,740.00]	462.88 (0.00) [0]
1638	HALDIA BARAUNI PRODUCT PIPELINE	4/2016	12/2020 (-) [12/2020]	1,021.00 (-) [1,021.00]	4.45 (0.00) [0]
1639	HALDIA LPG IMPORT FACILITY	3/2015	10/2018 (12/2019) [12/2019]	694.00 (1,097.54) [1,097.54]	722.99 (403.54) [14]
1640	KHARAGPUR LPG BOTTLING PLANT	4/2017	4/2020 (-) [3/2021]	163.02 (-) [163.02]	54.53 (0.00) [11]
	Power				
1641	DURGAPUR PP-III (2X20 MW) - NSPCL	12/2016	11/2018 (-) [3/2020]	529.68 (-) [529.68]	140.10 (0.00) [16]
1642	EASTERN REGION STRENGTHENNING SCHEME-XV	4/2016	4/2018 (1/2020) [1/2020]	454.11 (-) [454.11]	297.16 (0.00) [21]
1643	RAMMAM-III HEPP (3X40 MW)	9/2014	9/2019 (5/2024) [5/2024]	1,381.84 (-) [1,592.34]	502.87 (210.50) [56]
	Railways				
1644	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	4/1998	3/2003 (3/2030) [3/2030]	1,027.40 (1,966.70) [2,373.00]	485.04 (1,345.60) [324]
1645	BARDHAMAN-KATWA (GC)	4/2007	12/2010 (12/2017) [3/2025]	1,106.62 (-) [1,091.59]	860.08 (-15.03) [171]
1646	BAZAR SAU -AZIMGANJ JN. DOUBLING	4/2012	/ (-) [9/2021]	255.64 (-) [272.20]	177.61 (16.56) [-]
1647	BOWAICHANDI-ARAMBAGH	4/2010	/ (3/2025) [3/2025]	267.37 (-) [620.00]	40.99 (352.63) [-]
1648	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSHPUR	4/2009	/ (-) [3/2025]	573.78 (-) [268.52]	0.03 (-305.26) [-]
1649	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	3/2013	3/2016 (-) [6/2021]	4,874.58 (-) [8,574.97]	5,892.72 (3,700.39) [63]
1650	HOWRAH-AMTA-CHAMPADANGA NL (SER)	4/1974	3/2007 (3/2007) [0/0]	393.46 (154.30) [1,026.00]	182.49 (632.54) [0]
1651	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	4/2010	/ (3/2022)	221.42 (-)	38.18 (158.58)

			[3/2022]	[380.00]	[-]
1652	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	4/1983	3/2019 (-) [3/2020]	297.32 (-) [614.00]	275.07 (316.68) [12]
1653	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN	2/1999	4/2010 (-) [0/0]	380.60 (-) [1,871.00]	1,087.60 (1,490.40) [0]
1654	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM)	4/2016	12/2021 (-) [3/2020]	602.27 (-) [612.00]	336.17 (9.73) [-21]
1655	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	4/2010	3/2014 (-) [12/2025]	2,298.42 (-) [2,733.86]	40.13 (435.44) [141]
1656	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	4/2010	3/2016 (-) [3/2025]	2,913.51 (-) [4,639.00]	855.74 (1,725.49) [108]
1657	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP)	4/2010	3/2016 (-) [0/0]	2,397.72 (-) [2,397.72]	197.20 (0.00) [0]
1658	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	4/2010	3/2016 (-) [3/2025]	3,951.98 (-) [4,724.30]	2,278.26 (772.32) [108]
1659	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	4/2000	3/2019 (12/2009) [3/2025]	1,188.91 (-) [1,619.48]	871.86 (430.57) [72]
1660	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	3/2000	12/2006 (-) [0/0]	1,049.69 (-) [3,404.92]	3,837.57 (2,355.23) [0]
	Road Transport And Highways				
1661	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	12/2015	6/2018 (-) [12/2019]	1,083.00 (-) [1,083.00]	1,487.87 (0.00) [18]
1662	4-LANING OF BRAHAMPORE-FARAKA	2/2011	8/2013 (-) [3/2021]	998.79 (-) [998.79]	1,807.21 (0.00) [91]
1663	4-LANING OF FARAKA-RAIGANJ	2/2011	8/2013 (-) [5/2020]	1,078.84 (-) [1,078.84]	2,181.00 (0.00) [81]
1664	6-LANING OF DHANKUNI-KHARAGPUR SECTION	4/2012	9/2014 (-) [3/2020]	1,396.18 (-) [1,396.18]	2,894.94 (0.00) [66]
1665	CONSTRUCTION OF ISLAMPUR BY PASS	10/2015	/ (-) [1/2020]	361.15 (-) [361.15]	186.64 (0.00) [-]
1666	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I	3/2017	6/2018 (-) [0/0]	158.65 (-) [158.65]	39.06 (0.00) [0]
1667	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H	3/2016	11/2018 (11/2019) [11/2019]	271.17 (291.20) [291.20]	89.25 (20.03) [12]
1668	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND	3/2016	8/2019 (-) [8/2021]	160.27 (213.97) [213.97]	20.11 (53.70) [24]
1669	CONSTRUCTION OF ROB –FLYOVER AT RANICHAK, HALDIA	3/2016	11/2018 (3/2020) [3/2020]	229.37 (-) [229.37]	110.52 (0.00) [16]
1670	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N	6/2016	8/2019 (-) [8/2021]	236.78 (263.26) [263.26]	59.92 (26.48) [24]
1671	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE,	3/2018	10/2020 (-)	254.30 (254.30)	53.02 (0.00)

	BAGDO		[10/2020]	[254.30]	[0]
1672	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA	9/2016	8/2018 (-) [9/2019]	767.03 (767.03) [767.03]	595.72 (0.00) [0]
1673	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O	8/2014	11/2017 (5/2019) [5/2019]	600.87 (720.97) [720.97]	652.08 (120.10) [0]
1674	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O	8/2014	11/2017 (6/2019) [6/2019]	823.20 (937.76) [937.76]	751.19 (114.56) [0]
1675	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA)	3/2018	/ (-) [7/2021]	1,261.98 (-) [1,261.98]	793.49 (0.00) [-]
1676	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	4/2014	8/2017 (7/2019) [7/2019]	279.70 (398.52) [398.52]	322.75 (118.82) [0]
1677	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN	1/2017	9/2019 (-) [0/0]	396.86 (396.86) [396.86]	185.31 (0.00) [0]
1678	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL	1/1991	3/2018 (-) [0/0]	322.00 (-) [322.00]	56.41 (0.00) [0]
1679	SIX-LANING OF BARWA ADDA-PANAGARH	4/2014	/ (-) [6/2019]	1,665.00 (-) [1,665.00]	4,357.89 (0.00) [0]
1680	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10	3/2017	11/2019 (-) [0/0]	202.69 (202.69) [202.69]	103.14 (0.00) [0]
1681	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4	2/2018	11/2020 (-) [0/0]	218.70 (218.70) [218.70]	38.81 (0.00) [0]
1682	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19.	2/2018	9/2020 (-) [0/0]	426.18 (426.18) [426.18]	224.05 (0.00) [0]
	Steel				
1683	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E	12/2018	9/2020 (-) [9/2020]	263.36 (-) [263.36]	15.67 (0.00) [0]
	Urban Development				
1684	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	2/2014	8/2016 (-) [0/0]	156.57 (-) [156.57]	159.35 (0.00) [0]
1685	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG	8/2012	3/2016 (-) [0/0]	185.37 (-) [185.37]	178.30 (0.00) [0]
1686	NSG AT KOLKATA	10/2014	4/2018 (6/2020) [6/2020]	162.88 (179.10) [162.88]	144.06 (0.00) [26]
	Water Resources				
1687	SEWERAGE SYSTEM & STP WORKS AT HALISHAHR	2/2014	12/2019 (-) [12/2019]	274.76 (-) [274.76]	0.00 (0.00) [0]
1688	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS	1/2019	4/2022 (-) [4/2022]	384.96 (-) [384.96]	0.00 (0.00) [0]
1689	I AND D AND STP WORKS AT BURDWAN WEST BENGAL	12/2018	4/2022 (-) [4/2022]	234.31 (-) [234.31]	0.00 (0.00) [0]
1690	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS	3/2018	6/2022 (-) [6/2022]	165.16 (-) [165.16]	0.00 (0.00) [0]

1691	INTERCEPTION DIVERSION AND TREATMENT WORKS AT TOLLY'S NULLAH ADI GANGA	8/2017	9/2022 (-) [9/2022]	307.12 (-) [307.12]	0.00 (0.00) [0]
1692	INTERCEPTION & DIVERSION WITH STP AT MAHESHTALA	5/2018	2/2022 (-) [2/2022]	198.43 (-) [198.43]	0.00 (0.00) [0]
1693	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH	5/2018	2/2022 (-) [2/2022]	160.00 (-) [160.00]	0.00 (0.00) [0]
1694	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPURL	3/2019	4/2022 (-) [4/2022]	287.53 (-) [287.53]	0.00 (0.00) [0]
1695	INTERCEPTION AND DIVERSION WITH STP AT BALLY	10/2017	12/2021 (-) [12/2021]	164.93 (-) [164.93]	0.00 (0.00) [0]
1696	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI	1/2018	12/2021 (-) [12/2021]	172.10 (-) [172.10]	0.00 (0.00) [0]
1697	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH	8/2017	12/2021 (-) [12/2021]	185.22 (-) [185.22]	0.00 (0.00) [0]
1698	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE	12/2014	4/2020 (-) [4/2020]	272.32 (-) [272.32]	0.00 (0.00) [0]
	Total			20,41,114.88 (6,61,297.01) [24,41,837.32]	10,50,331.59 (4,00,722.44)

North-East Central Sector Ongoing Project List

Annexure-XX

Details of Central Sector Projects Costing Rs.150 crore and above (as on 30.11.2019)					
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	ARUNACHAL PRADESH				
	Power				
1	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009 (10/2019) [10/2019]	2,496.90 (7,927.34) [7,927.34]	7,599.10 (5,430.44) [0]
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (-) [0/0]	6,285.33 (-) [19,496.34]	11,098.20 (13,211.01) [0]
	Road Transport And Highways				
3	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN	3/2015	/ (-) [0/0]	172.75 (-) [172.75]	118.30 (0.00) [0]
4	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [3/2020]	394.00 (-) [394.00]	272.92 (0.00) [21]
5	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59	3/2015	5/2018 (-) [8/2019]	194.11 (-) [194.11]	181.03 (0.00) [0]
6	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS	10/2015	1/2019 (-) [0/0]	179.82 (-) [179.82]	197.77 (0.00) [0]
7	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX	10/2015	/ (1/2016) [1/2019]	210.50 (210.50) [210.50]	120.60 (0.00) [0]
8	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROMKM.583.450	1/2016	11/2016 (-) [0/0]	183.65 (-) [183.65]	107.04 (0.00) [0]
9	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST	11/2016	/ (-) [9/2020]	243.89 (-) [243.89]	121.47 (0.00) [-]
10	BORDUMSA NAMCHIK (BURIDEHING - JAIRAMPUR) ROAD ON NH-52B (NEW NH-215) FROM KM. 0.15 (STARTING CHAIN	7/2015	/ (-) [0/0]	189.91 (-) [189.91]	154.43 (0.00) [0]
11	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM	5/2016	/ (-) [0/0]	259.52 (-) [259.52]	184.51 (0.00) [0]
12	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120.	12/2016	/ (-) [0/0]	200.44 (-) [200.44]	75.98 (0.00) [0]
13	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50	9/2016	/ (-) [0/0]	568.92 (-) [568.92]	134.41 (0.00) [0]
14	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI	12/2016	/	188.78	38.37

	ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5		(-) [0/0]	(-) [188.78]	(0.00) [0]
15	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	12/2016	1/2017 (-) [1/2020]	138.93 (155.00) [155.00]	75.99 (16.07) [36]
16	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/ (-) [9/2020]	245.79 (-) [245.79]	105.26 (0.00) [-]
17	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	4/2016	10/2016 (-) [10/2019]	198.00 (-) [198.00]	184.62 (0.00) [0]
18	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	7/2015	10/2018 (9/2015) [9/2018]	197.16 (197.16) [197.16]	75.57 (0.00) [0]
19	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF	3/2017	/ (-) [0/0]	1,718.59 (-) [1,718.59]	158.90 (0.00) [0]
20	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	1/2017	3/2017 (-) [3/2022]	1,253.10 (-) [1,253.10]	158.90 (0.00) [60]
21	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	4/2017 (2/2018) [2/2021]	167.28 (167.28) [167.28]	19.83 (0.00) [46]
22	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS	2/2017	4/2017 (2/2018) [2/2021]	216.71 (216.71) [216.71]	19.67 (0.00) [46]
23	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/ (-) [0/0]	392.60 (-) [392.60]	0.00 (0.00) [0]
24	FUNDED)CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH	11/2015	/ (-) [12/2020]	434.06 (-) [434.06]	133.38 (0.00) [-]
25	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017 (3/2018) [3/2021]	284.09 (284.09) [284.09]	77.42 (0.00) [47]
26	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017 (-) [0/0]	195.23 (-) [195.23]	49.25 (0.00) [0]
27	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017 (-) [0/0]	203.36 (-) [203.36]	62.53 (0.00) [0]
28	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	194.66 (-) [194.66]	83.66 (0.00) [0]
29	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	198.22 (-) [198.22]	83.66 (0.00) [0]
30	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	3/2012	5/2012 (5/2015) [12/2019]	207.03 (389.45) [389.45]	291.55 (182.42) [91]
31	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	4/2017 (2/2018) [2/2021]	180.57 (180.57) [180.57]	14.27 (0.00) [46]
32	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS	2/2017	4/2017 (2/2018) [2/2021]	168.32 (168.32) [168.32]	34.87 (0.00) [46]
33	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	2/2012 (-) [0/0]	156.63 (276.00) [276.00]	147.65 (119.37) [0]
34	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL	11/2010	3/2011 (-)	305.49 (-)	131.08 (0.00)

	PRADESH P		[0/0]	[305.49]	[0]
35	TWO-LANING OF HAYULIANG– HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI	1/2017	/ (-) [0/0]	256.66 (-) [256.66]	24.14 (0.00) [0]
36	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0	2/2017	/ (4/2019) [4/2022]	175.06 (175.06) [175.06]	14.08 (0.00) [-]
37	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1	2/2017	/ (4/2019) [4/2022]	176.12 (176.12) [176.12]	14.79 (0.00) [-]
38	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D	2/2017	/ (2/2018) [2/2021]	199.02 (199.02) [199.02]	11.87 (0.00) [-]
39	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D	2/2017	/ (2/2018) [2/2021]	184.88 (184.88) [184.88]	97.50 (0.00) [-]
40	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU	9/2011	/ (3/2020) [0/0]	1,979.00 (-) [1,979.00]	1,143.00 (0.00) [0]
	ASSAM				
	Civil Aviation				
41	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	3/2021 (-) [3/2021]	859.86 (-) [860.00]	232.44 (0.14) [0]
	Health And Family Welfare				
42	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (10/2021) [10/2021]	875.00 (-) [747.80]	110.70 (-127.20) [5]
	Petroleum				
43	ASSAM RENEWAL PROJECT FOR GROUP A	3/2009	3/2013 (12/2019) [12/2019]	2,465.15 (-) [2,378.86]	2,147.00 (-86.29) [81]
44	BS VI PROJECT AT GUWAHATI REFINERY	8/2018	2/2020 (-) [6/2020]	557.00 (-) [557.00]	249.46 (0.00) [4]
45	BS-VI PROJECT AT BONGAIGAON REFINERY	5/2018	9/2019 (-) [4/2020]	1,222.00 (-) [1,222.00]	606.24 (0.00) [7]
46	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN	6/2016	8/2020 (-) [8/2020]	224.75 (-) [224.75]	69.99 (0.00) [0]
47	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	7/2011	1/2019 (-) [0/0]	350.00 (-) [350.00]	2.06 (0.00) [0]
48	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	6/2010	1/2014 (-) [11/2019]	202.94 (345.92) [345.92]	155.61 (142.98) [70]
49	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	6/2016	8/2019 (-) [12/2020]	423.00 (-) [423.00]	282.50 (0.00) [16]
50	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (6/2020) [6/2020]	543.91 (-) [682.90]	71.46 (138.99) [4]
51	INDMAX PROJECT AT BONGAIGAON REFINERY	2/2016	11/2019 (-) [2/2020]	2,582.00 (-) [2,582.00]	1,613.96 (0.00) [3]
52	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020 (-) [5/2020]	249.85 (265.49) [265.49]	180.20 (15.64) [0]
53	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	9/2012	3/2015 (-)	871.35 (-)	565.63 (328.65)

			[0/0]	[1,200.00]	[0]
	Railways				
54	AMBARI FALAKATA TO NEW MAYNAGURI	4/2011	3/2019 (-) [3/2020]	314.00 (728.00) [728.00]	727.55 (414.00) [12]
55	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2020]	2,232.32 (-) [2,182.00]	756.32 (-50.32) [-24]
56	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-) [3/2021]	870.96 (-) [2,136.01]	580.01 (1,265.05) [0]
57	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2020]	385.20 (1,532.00) [1,532.00]	642.09 (1,146.80) [12]
	Road Transport And Highways				
58	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (-) [0/0]	268.08 (-) [268.08]	203.15 (0.00) [0]
59	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	11/2010	2/2011 (-) [0/0]	470.20 (-) [630.36]	344.32 (160.16) [0]
60	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS	12/2015	12/2018 (-) [0/0]	225.02 (-) [159.20]	26.00 (-65.82) [0]
61	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	12/2015	6/2018 (-) [0/0]	223.30 (-) [223.30]	73.39 (0.00) [0]
62	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [0/0]	520.01 (-) [520.01]	50.38 (0.00) [0]
63	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [0/0]	588.95 (-) [588.95]	382.22 (0.00) [0]
64	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [0/0]	289.99 (-) [289.99]	13.26 (0.00) [0]
65	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (12/2021) [12/2021]	252.00 (-) [252.00]	4.74 (0.00) [71]
66	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (12/2020) [12/2021]	437.39 (-) [437.39]	9.30 (0.00) [42]
67	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (2/2019) [4/2021]	294.17 (-) [294.17]	63.00 (0.00) [63]
68	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	4/2010 (-) [7/2019]	217.61 (-) [360.84]	453.70 (143.23) [0]
69	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM	11/2010	2/2014 (-) [12/2019]	197.37 (-) [197.37]	88.86 (0.00) [70]
70	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	5/2008 (-) [6/2019]	160.00 (-) [167.98]	223.81 (7.98) [0]
71	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52	6/2016	1/2019 (-) [0/0]	829.00 (-) [829.00]	304.25 (0.00) [0]
72	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [0/0]	168.39 (-) [168.39]	73.37 (0.00) [0]
73	FOUR LANING OF BALACHERA-HARANGAJAO SECTION	10/2017	/	818.00	62.91

	OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE		(-) [6/2020]	(-) [818.00]	(0.00) [-]
74	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (1/2021) [12/2021]	463.49 (-) [463.49]	22.32 (0.00) [42]
75	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [0/0]	829.00 (-) [829.00]	304.27 (0.00) [0]
76	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (5/2020) [12/2020]	454.89 (-) [454.89]	123.20 (0.00) [31]
77	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (7/2019) [7/2019]	280.00 (490.00) [525.00]	492.41 (245.00) [0]
78	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (10/2018) [10/2018]	196.00 (655.17) [655.17]	655.17 (459.17) [0]
79	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (1/2011) [8/2013]	155.04 (255.23) [255.23]	251.39 (100.19) [0]
80	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (3/2011) [8/2019]	199.81 (340.14) [340.14]	319.96 (140.33) [0]
81	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (7/2011) [1/2014]	167.64 (408.77) [408.77]	395.78 (241.13) [0]
82	NALBARI T BIJNI (AS-7)	12/2003	4/2008 (-) [3/2020]	208.00 (-) [230.00]	339.22 (22.00) [143]
83	NALBARI TO BIJNI (AS-6)	12/2003	6/2008 (-) [9/2019]	225.00 (-) [225.00]	328.47 (0.00) [0]
84	OUR LANNNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST	3/2017	/ (-) [0/0]	1,049.51 (-) [1,049.51]	89.16 (0.00) [0]
85	SONAPUR TO GUWAHTI (AS-3)	12/2003	3/2008 (-) [8/2020]	245.00 (-) [174.34]	225.34 (-70.66) [149]
86	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ	11/2014	2/2018 (-) [0/0]	218.31 (-) [307.47]	263.85 (89.16) [0]
87	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN	9/2018	9/2021 (-) [9/2021]	160.00 (-) [160.00]	0.50 (0.00) [0]
	MANIPUR				
	Power				
88	LOKTAK D/S HEP(NHPC)	12/1999	6/2006 (-) [0/0]	578.62 (-) [578.62]	0.00 (0.00) [0]
	Railways				
89	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [3/2022]	4,454.17 (13,809.00) [12,524.00]	9,541.58 (8,069.83) [132]
	Road Transport And Highways				
90	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260.	10/2016	11/2020 (-) [11/2020]	235.31 (-) [235.31]	91.38 (0.00) [0]
91	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	8/2017	10/2018 (-) [10/2021]	517.57 (-) [457.77]	137.04 (-59.80) [36]
	Urban Development				

92	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	2/2014	3/2015 (-) [10/2020]	216.69 (-) [216.69]	52.00 (0.00) [67]
	MEGHALAYA				
	Health And Family Welfare				
93	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [7/2020]	363.99 (-) [363.99]	208.29 (0.00) [26]
	Human Resource Department				
94	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	9/2013	9/2014 (-) [12/2020]	484.32 (-) [626.26]	0.00 (141.94) [75]
	Railways				
95	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [3/2021]	906.46 (-) [6,000.00]	263.12 (5,093.54) [0]
	Road Transport And Highways				
96	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	3/2019	5/2019 (-) [0/0]	306.28 (-) [306.28]	42.66 (0.00) [0]
97	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	5/2018 (3/2018) [10/2019]	479.20 (-) [479.20]	711.38 (0.00) [0]
98	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (-) [9/2021]	553.51 (-) [553.51]	32.78 (0.00) [-]
	Urban Development				
99	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	4/2014	9/2017 (-) [0/0]	151.33 (-) [151.33]	7.15 (0.00) [0]
	MIZORAM				
	Railways				
100	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (3/2022) [3/2022]	2,393.47 (4,968.00) [5,021.45]	3,131.89 (2,627.98) [96]
	Road Transport And Highways				
101	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (-) [6/2020]	195.04 (-) [377.99]	305.38 (182.95) [116]
102	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	9/2014 (-) [12/2019]	186.96 (-) [305.61]	275.06 (118.65) [63]
103	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (-) [12/2019]	193.69 (-) [327.92]	254.24 (134.23) [110]
104	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	519.09 (-) [519.09]	0.00 (0.00) [0]
105	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	537.82 (-) [537.82]	0.00 (0.00) [0]
106	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	404.29 (-) [404.29]	0.00 (0.00) [0]
107	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	428.11 (-) [428.11]	0.00 (0.00) [0]
108	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	518.53 (-) [518.53]	0.00 (0.00) [0]
109	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED	4/2017	9/2019	473.18	0.00

	SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO		(-) [9/2019]	(-) [473.18]	(0.00) [0]
110	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	640.07 (-) [640.07]	0.00 (0.00) [0]
111	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	642.96 (-) [642.96]	0.00 (0.00) [0]
112	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (-) [12/2019]	624.41 (-) [992.67]	853.82 (368.26) [105]
	NAGALAND				
	Railways				
113	DIMAPUR-TIZIT NL	4/2013	3/2020 (-) [3/2020]	4,274.00 (-) [4,274.00]	0.00 (0.00) [0]
114	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (-) [10/2021]	2,326.52 (-) [4,600.00]	842.42 (2,273.48) [79]
	Road Transport And Highways				
115	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (5/2019) [0/0]	239.30 (-) [239.30]	0.00 (0.00) [0]
116	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [0/0]	285.68 (-) [285.68]	9.58 (0.00) [0]
117	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (11/2018) [0/0]	282.98 (-) [282.98]	12.76 (0.00) [0]
118	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [0/0]	387.00 (-) [387.00]	135.12 (0.00) [0]
119	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [0/0]	500.09 (-) [500.09]	0.00 (0.00) [0]
120	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN	3/2017	11/2020 (-) [11/2020]	217.35 (-) [217.35]	35.10 (0.00) [0]
121	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683	2/2017	4/2017 (-) [0/0]	507.68 (-) [507.68]	129.13 (0.00) [0]
122	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (7/2019) [0/0]	339.57 (233.35) [339.57]	0.00 (0.00) [0]
123	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [0/0]	315.03 (-) [315.03]	18.60 (0.00) [0]
124	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [0/0]	240.64 (-) [240.64]	17.29 (0.00) [0]
125	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [0/0]	215.12 (-) [215.12]	12.45 (0.00) [0]
126	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [0/0]	215.79 (-) [215.79]	10.21 (0.00) [0]
127	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [0/0]	272.89 (-) [272.89]	0.00 (0.00) [0]
128	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING	3/2018	9/2018 (-)	323.98 (-)	0.00 (0.00)

	KM 60.345 TO		[0/0]	[323.98]	[0]
129	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (11/2018) [0/0]	251.97 (160.10) [251.97]	18.66 (0.00) [0]
130	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (11/2018) [0/0]	237.72 (136.73) [237.72]	29.67 (0.00) [0]
131	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [8/2019]	373.07 (387.00) [373.07]	211.16 (0.00) [0]
132	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [6/2020]	396.52 (339.55) [396.52]	235.52 (0.00) [46]
133	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [8/2019]	429.52 (340.00) [429.52]	167.54 (0.00) [0]
134	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M	11/2016	9/2019 (-) [9/2019]	336.25 (-) [336.25]	62.64 (0.00) [0]
135	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (-) [12/2020]	167.62 (-) [167.62]	42.15 (0.00) [0]
136	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (-) [12/2020]	172.63 (-) [172.63]	45.02 (0.00) [0]
137	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA	12/2010	2/2011 (-) [0/0]	1,296.00 (-) [1,296.00]	0.00 (0.00) [0]
138	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH-	3/2019	12/2022 (-) [12/2022]	237.51 (-) [237.51]	0.00 (0.00) [0]
	SIKKIM				
	Railways				
139	SEVOK RANGPO, NEFR	4/2008	12/2015 (-) [0/0]	1,339.48 (-) [4,084.69]	332.23 (2,745.21) [0]
	Road Transport And Highways				
140	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	1/2013	2/2013 (-) [12/2019]	182.28 (-) [269.14]	185.49 (86.86) [82]
141	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	4/2013	8/2013 (-) [12/2019]	151.59 (-) [151.59]	196.76 (0.00) [76]
142	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	4/2013	8/2013 (-) [0/0]	166.27 (-) [166.27]	132.27 (0.00) [0]
143	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [0/0]	375.80 (-) [375.80]	77.39 (0.00) [0]
144	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017 (-) [0/0]	290.05 (-) [290.05]	35.34 (0.00) [0]
145	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA	4/2017	11/2017 (-) [0/0]	318.42 (-) [318.42]	66.63 (0.00) [0]
146	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	0.00 (0.00) [0]
147	RHENOK-RORAHTHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [447.37]	142.95 (59.37) [0]

	TRIPURA				
	Civil Aviation				
148	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	9/2015	6/2019 (-) [12/2019]	338.93 (-) [339.00]	213.50 (0.07) [6]
	Railways				
149	AGARTALA-AKHAURA NL	4/2012	3/2020 (9/2021) [9/2021]	569.63 (670.00) [670.00]	107.83 (100.37) [18]
	Road Transport And Highways				
150	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (12/2019) [0/0]	369.00 (-) [369.00]	316.74 (0.00) [0]
151	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C	10/2016	8/2020 (-) [8/2020]	171.90 (-) [171.90]	14.77 (0.00) [0]
	Urban Development				
152	CONSTRUCTION AND MAINTEINANCE OF RURAL ROAD UNDER PMGSY PHASE V	3/2007	12/2015 (-) [0/0]	149.73 (173.00) [175.94]	176.65 (26.21) [0]
153	CONSTRUCTION AND MAINTEINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016 (-) [0/0]	202.61 (227.00) [227.00]	199.95 (24.39) [0]
154	CONSTRUCTION AND MAINTEINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016 (-) [0/0]	175.49 (206.71) [206.71]	141.28 (31.22) [0]
	Total			85,137.06 (37,578.66) [1,30,781.44]	59,081.06 (45,644.38)
